Owner Monthly Dashboard

March 2025

Tri-County RVTHS

147 Pond Street, Franklin, MA 02038

CONSIGLI

FINANCIAL

Change Order & Contract Status

Original Contract Amount:	$	53,468,521.00
Previously Approved Change Orders:	$	-
Current Contract Amount:	$	53,468,521.00
Verbally Approved Changes:	$	-
Submitted Changes:	$	-
Pending Changes:	$	-
Total Potential Changes:	$	-
Projected Contract Amount:	$	53,468,521.00

Billing Status



Billed to Date	$ 13,154,195	Retainage Held	$ 657,710
Paid to Date	$ 10,809,456	Amount Outstanding	$ 1,687,023

Allowance Status

Original Allowance Budget	$1,906,682.00
Added/(Expended) to Date	$ 533,994.00
Remaining Allowances	$2,440,676.00

Holds Status

Original Holds Budget	$ 587,328.00
Added/(Expended) to Date	$ 1,295,321.00
Remaining Holds	$ 1,882,649.00

Contingency Status

Original Cont. Amount:	$	1,061,170
Added/(Expended) to Date	$	(118,127)
Remaining Contingency:	$	943,043

Procurement Overview

Percent Complete:	20.0%
Buyout Savings / (Bust)	N/A
Buyout Savings / (Bust) %	N/A

EXECUTIVE OVERVIEW

The Tri-County Regional High School project is making steady progress, with a significant portion of footings and walls having been poured in Building A. Excavation for Buildings B and C foundations is also in full swing, preparing the eastern and westernmost sections of the building pad for the forming of footings. Site utility work continues, with efforts focused on completing all utility installation and backfill activities around the site perimeter—key steps that will allow for paving of the loop road binder course. The electric ductbank mains have been successfully installed around the building, while sanitary and water line installations are nearing completion. Additionally, preparations for the geothermal system are well underway. In February, a detailed survey was conducted along the roadway behind the school to pinpoint the exact locations of existing utilities, ensuring no conflicts arise when the new mains are installed in the summer of 2025. Looking ahead, geothermal well drilling crews are set to mobilize on-site in early March.

SCHEDULE

Project Milestones

Milestone	Target	Actual	Variance
Enabling Sitework Complete	4/1/2025	-	-
Foundations Complete	7/18/2025	-	-
Structural Steel Complete	8/11/2025	-	-
Roofing Complete	9/15/2025	-	-
Exterior Façade Complete	11/4/2025	-	-
Courtyard Façade Complete [Weathertight]	12/26/2025	-	-
Geothermal System Complete	12/30/2025	-	-
Equipment Start Up Complete	2/18/2027	-	-
Building Turnover (C of O)	7/14/2027	-	-
Punchlist Complete	8/17/2027	-	-
Project Completion (Fields/Landscaping Complete)	8/10/2028	-	-

Roadblocks

Item	Ball In Court	Due Date
Site Conditions due to Thawing	CCC	4/1/2025

QUALITY

Construction Submittal Status



RFI Status



Observation Review

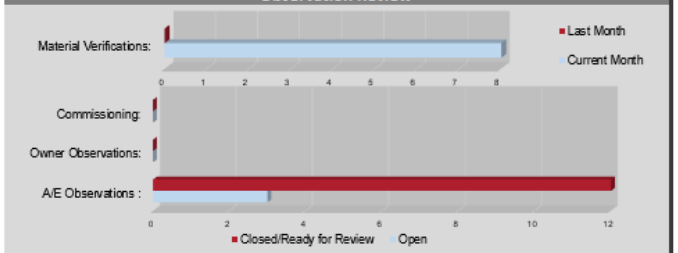

Safety Update

Current Project Safety Score:	97.7%
Total Man Hours to Date:	37,824
OSHA Recordables to Date/Month:	0/0

PROGRESS PHOTOS

Tri-County RVTHS

Owner Monthly Report March 2025

Table Of Contents

Section 1	**Executive Summary**
Section 2	**Antipicated Cost Report**
Section 3	**Change Request Log**
Section 4	**Holds, Contingencies, & Allowances Log**
Section 5	**Requisition Summary Report**
Section 6	**Schedule & Manpower Log**
Section 7	**Submittal Log**
Section 8	**RFI Log**
Section 9	**Progress Photos**

CONSIGLI

Est. 1905

Section 1 - Executive Summary

Tri-County RVTHS

Executive Summary

Project Overview Update:

As of February 2025, the Tri-County Regional High School project has made significant progress in excavation and foundation installation. During excavation for the foundations of Buildings B and C, additional pockets of topsoil were discovered beneath the building footprint. These areas are being carefully removed and replaced with structural fill to ensure a stable foundation.

The majority of concrete submittals have been reviewed and approved, with only the rebar shop drawings for Building E remaining outstanding. The release of materials for this final submittal is targeted for early March. Meanwhile, the project team has begun reviewing and approving structural steel submittals and has already received anchor bolt deliveries for Buildings A, B, and C.

As winter comes to an end, site thawing has presented challenges for the continuation of foundation installation. To address this, the project team has shifted their focus to installing utilities and constructing an accessible roadway around the site. The goal is to complete both by early April 2025, ensuring foundation work can resume at full capacity.

Additionally, preparations are underway for the geothermal subcontractor's mobilization, with their arrival scheduled for early March. The final step in site preparation is completing the sedimentation pond, located north of the existing football field, to support dewatering efforts.

Financial Status Update:

The current contract value is $53,468,521 and the amount of work completed and stored through February 28, 2025 is $13,314,194 pending approval of the February 2025 Application for Payment. The team is in the process of preparing Pre-GMP Amendment #5, which will formalize the remaining scopes of work outlined in the Bid Package #8, the 100% construction drawings.

Schedule Summary Update:

The project team is actively refining the construction schedule for the next phases. Foundation work is currently expected to extend four weeks beyond the original timeline. However, Consigli is implementing accelerated measures in steel construction and other tasks to recover this time. As a result, the substantial completion date remains July 14, 2027, with Owner Move-In scheduled for the following month. Full project completion is expected by August 10, 2028.

All critical path milestones are on track, including the start of architectural pre-cast concrete fabrication and the mobilization of geothermal well drilling teams. Steel installation is set to begin in May 2025.

Roadblocks Update:

One roadblock arose at the end of February. The site conditions due to thawing has been a challenge for installing foundations. Therefore Consigli and the subcontractors are working on installing accesible roadways around the site to continue concrete pours.

Quality Update:

The team is in ongoing communications with the Civil Engineer of Record (Samiotes), Structural Engineer of Record (Engineers Design Group), the Building Commissioner and the Town of Franklin's Third-Party Testing Agency (Yankee) to inspect compaction and concrete testing.

Safety Update:

There have been 0 lost-time or recordable incidents on the project to-date. The project has safely worked over 37,824 man hours and has received a February safety score of 97.7 based on audits conducted by Consigli's internal safety team.

CONSIGLI
Est. 1905

Section 2 - Antipicated Cost Report

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

Print GC Backup:	Yes		
Print Permit Detail:	No	Print SDI Detail:	No
Print P&P Bond Detail:	No	Print Sub Bonds Detail:	No
Print Builder's Risk Detail:	No	Print Cost Detail:	Yes
Print GL Detail:	No	Include PreCon:	No
Print CCIP Detail:	No	Exclude Fee Detail:	Yes

OFFICE = MILFORD

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
GMP																
1 - GENERAL CONDITIONS																
1-001 Project superintendent																
CONSIGLI LABOR											146,880					
Base	755,140	0	0	755,140	0	0	0	0	**755,140**	0	146,880	146,880	608,260	**755,140**	**0**	-755,140
1-001 TOTAL	755,140	0	0	755,140	0	0	0	0	**755,140**	0	146,880	146,880	608,260	**755,140**	**0**	-755,140
1-002 Project manager																
CONSIGLI LABOR											14,245					
Base	455,060	0	0	455,060	0	0	0	0	**455,060**	0	14,245	14,245	440,815	**455,060**	**0**	-455,060
BT008-PreGMP #3 - GC Reconciliation	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-25,330*	***-25,330***	*0*	*0*	*0*	*-25,330*	***-25,330***	***0***	*25,330*
1-002 TOTAL	455,060	0	0	455,060	0	0	0	-25,330	**429,730**	0	14,245	14,245	415,485	**429,730**	**0**	-429,730
1-003 Project engineer																
CONSIGLI LABOR											60,000					
Base	424,500	0	0	424,500	0	0	0	0	**424,500**	0	60,000	60,000	364,500	**424,500**	**0**	-424,500
1-003 TOTAL	424,500	0	0	424,500	0	0	0	0	**424,500**	0	60,000	60,000	364,500	**424,500**	**0**	-424,500
1-004 Project executive																
CONSIGLI LABOR											143,585					
Base	402,413	0	0	402,413	0	0	0	0	**402,413**	0	143,585	143,585	258,828	**402,413**	**0**	-402,413
1-004 TOTAL	402,413	0	0	402,413	0	0	0	0	**402,413**	0	143,585	143,585	258,828	**402,413**	**0**	-402,413
1-005 Assistant superintendent																
CONSIGLI LABOR											161,000					
Base	494,200	0	0	494,200	0	0	0	0	**494,200**	0	161,000	161,000	333,200	**494,200**	**0**	-494,200
1-005 TOTAL	494,200	0	0	494,200	0	0	0	0	**494,200**	0	161,000	161,000	333,200	**494,200**	**0**	-494,200
1-006 Assistant project manager																
CONSIGLI LABOR											183,280					
Base	446,600	0	0	446,600	0	0	0	0	**446,600**	0	183,280	183,280	263,320	**446,600**	**0**	-446,600
1-006 TOTAL	446,600	0	0	446,600	0	0	0	0	**446,600**	0	183,280	183,280	263,320	**446,600**	**0**	-446,600
1-007 MEP coordinator																
CONSIGLI LABOR											44,570					
Base	300,622	0	0	300,622	0	0	0	0	**300,622**	0	44,570	44,570	256,052	**300,622**	**0**	-300,622
1-007 TOTAL	300,622	0	0	300,622	0	0	0	0	**300,622**	0	44,570	44,570	256,052	**300,622**	**0**	-300,622
1-008 Purchasing / procurement																
CONSIGLI LABOR											41,305					
Base	239,295	0	0	239,295	0	0	0	0	**239,295**	0	41,305	41,305	197,990	**239,295**	**0**	-239,295
1-008 TOTAL	239,295	0	0	239,295	0	0	0	0	**239,295**	0	41,305	41,305	197,990	**239,295**	**0**	-239,295
1-010 Design services / architect																
CONSIGLI LABOR											25,330					
Base	0	0	0	0	0	0	0	0	**0**	0	25,330	25,330	-25,330	**0**	**0**	0
BT008-PreGMP #3 - GC Reconciliation	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*25,330*	***25,330***	*0*	*0*	*0*	*25,330*	***25,330***	***0***	*-25,330*
1-010 TOTAL	0	0	0	0	0	0	0	25,330	**25,330**	0	25,330	25,330	0	**25,330**	**0**	-25,330
1-011 Project scheduler																
CONSIGLI LABOR											32,160					
Base	63,239	0	0	63,239	0	0	0	0	**63,239**	0	32,160	32,160	31,079	**63,239**	**0**	-63,239
1-011 TOTAL	63,239	0	0	63,239	0	0	0	0	**63,239**	0	32,160	32,160	31,079	**63,239**	**0**	-63,239

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
1-013 General superintendent																
CONSIGLI LABOR											22,325					
Base	66,129	0	0	66,129	0	0	0	0	**66,129**	0	22,325	22,325	43,804	**66,129**	**0**	-66,129
1-013 TOTAL	66,129	0	0	66,129	0	0	0	0	**66,129**	0	22,325	22,325	43,804	**66,129**	**0**	-66,129
1-014 Safety inspections																
CONSIGLI LABOR											19,980					
Base	45,888	0	0	45,888	0	0	0	0	**45,888**	0	19,980	19,980	25,908	**45,888**	**0**	-45,888
1-014 TOTAL	45,888	0	0	45,888	0	0	0	0	**45,888**	0	19,980	19,980	25,908	**45,888**	**0**	-45,888
1-016 Project administrator																
CONSIGLI LABOR											13,178					
Base	20,076	0	0	20,076	0	0	0	0	**20,076**	0	13,178	13,178	6,899	**20,076**	**0**	-20,076
1-016 TOTAL	20,076	0	0	20,076	0	0	0	0	**20,076**	0	13,178	13,178	6,899	**20,076**	**0**	-20,076
1-017 Project accountant																
CONSIGLI LABOR											14,740					
Base	38,924	0	0	38,924	0	0	0	0	**38,924**	0	14,740	14,740	24,184	**38,924**	**0**	-38,924
1-017 TOTAL	38,924	0	0	38,924	0	0	0	0	**38,924**	0	14,740	14,740	24,184	**38,924**	**0**	-38,924
1-030 BIM modeler																
CONSIGLI LABOR											34,130					
Base	141,234	0	0	141,234	0	0	0	0	**141,234**	0	34,130	34,130	107,104	**141,234**	**0**	-141,234
1-030 TOTAL	141,234	0	0	141,234	0	0	0	0	**141,234**	0	34,130	34,130	107,104	**141,234**	**0**	-141,234
1-050 Outreach Coordinator																
CONSIGLI LABOR											14,310					
Base	23,112	0	0	23,112	0	0	0	0	**23,112**	0	14,310	14,310	8,802	**23,112**	**0**	-23,112
1-050 TOTAL	23,112	0	0	23,112	0	0	0	0	**23,112**	0	14,310	14,310	8,802	**23,112**	**0**	-23,112
1-053 Quality Control																
CONSIGLI LABOR											12,760					
Base	21,188	0	0	21,188	0	0	0	0	**21,188**	0	12,760	12,760	8,428	**21,188**	**0**	-21,188
1-053 TOTAL	21,188	0	0	21,188	0	0	0	0	**21,188**	0	12,760	12,760	8,428	**21,188**	**0**	-21,188
1-099 Riggs General Requirements																
RIGGS CONTRACTING INC.											181,711					
Base	2,496,828	0	0	2,496,828	0	0	0	0	**2,496,828**	16	181,711	181,727	2,315,101	**2,496,828**	**0**	-2,496,828
AT030-Winter Conditions #1	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*23,875*	***23,875***	*0*	*0*	*0*	*23,875*	***23,875***	***0***	*-23,875*
AT041-Winter Conditions #2 - Feb '25	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*69,236*	***69,236***	*0*	*0*	*0*	*69,236*	***69,236***	***0***	*-69,236*
BT004-Temp Trailer Setup #1 SOE/Swr	*0*	*0*	*-26,573*	*-26,573*	*0*	*0*	*0*	*0*	***-26,573***	*0*	*0*	*0*	*-26,573*	***-26,573***	***0***	*26,573*
1-099 TOTAL	2,496,828	0	-26,573	2,470,255	0	0	0	93,111	**2,563,366**	16	181,711	181,727	2,381,638	**2,563,366**	**0**	-2,563,366
1-120 Office furniture																
AMAZON WEB SERVICES LLC											8,758					
COLONY HARDWARE SUPPLY CO INC											145					
GRAINGER											6,602					
HOME DEPOT RECEIPTS - CC											687					
W.B. MASON CO., INC.											4,929					
WEBSTAURANT STORE - CC											1,354					
Base	43,487	0	0	43,487	0	0	0	0	**43,487**	19,864	22,475	23,451	20,036	**43,487**	**0**	-43,487
1-120 TOTAL	43,487	0	0	43,487	0	0	0	0	**43,487**	19,864	22,475	23,451	20,036	**43,487**	**0**	-43,487
1-125 Office supplies																
AMAZON WEB SERVICES LLC											1,099					
COLONY HARDWARE SUPPLY CO INC											508					
NHS PRINT											786					
W.B. MASON CO., INC.											3,526					
WILLIAM FERACO											16					
Base	13,380	0	0	13,380	0	0	0	0	**13,380**	6,107	5,935	7,061	6,319	**13,380**	**0**	-13,380
1-125 TOTAL	13,380	0	0	13,380	0	0	0	0	**13,380**	6,107	5,935	7,061	6,319	**13,380**	**0**	-13,380
1-126 Office Costs																
Base	4,550	0	0	4,550	0	0	0	0	**4,550**	0	0	0	4,550	**4,550**	**0**	-4,550

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
1-126 TOTAL	4,550	0	0	4,550	0	0	0	0	**4,550**	0	0	0	4,550	**4,550**	**0**	-4,550
1-130 Computers & communications																
AMAZON MKTPLACE -CC											1,265					
AMAZON WEB SERVICES LLC											167					
CDW DIRECT, LLC											5,182					
COMCAST											216					
CONSIGLI CONSTRUCTION CO, INC.											3,140					
KYOCERA											395					
LINQ SERVICES											650					
STARLINK INTERNET - CC											3,706					
WELLS FARGO -GE											10,104					
WILLIAM FERACO											396					
Base	150,342	0	0	150,342	0	0	0	0	**150,342**	6,020	25,222	25,686	124,656	**150,342**	**0**	-150,342
BT007-PreGMP #3 - GR Reconciliation	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-30,722*	***-30,722***	*0*	*0*	*0*	*-30,722*	***-30,722***	***0***	*30,722*
1-130 TOTAL	150,342	0	0	150,342	0	0	0	-30,722	**119,620**	6,020	25,222	25,686	93,934	**119,620**	**0**	-119,620
1-140 Temporary Power																
CONSIGLI CONSTRUCTION CO, INC.											4,950					
FABIANO OIL CORP.											17,772					
GRAINGER											2,756					
HERC RENTALS INC.											22,863					
TRISTEN MOORE											32					
Base	28,403	0	0	28,403	0	0	0	0	**28,403**	2,073	48,373	48,373	-19,970	**28,403**	**0**	-28,403
AT027-Temp Lighting at Gym Lot	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*6,134*	***6,134***	*0*	*6,134*	*6,134*	*0*	***6,134***	***0***	*-6,134*
AT039-Utility Pole NGrid Shutdown	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*3,622*	***3,622***	*0*	*3,622*	*3,622*	*0*	***3,622***	***0***	*-3,622*
BT007-PreGMP #3 - GR Reconciliation	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*22,918*	***22,918***	*0*	*0*	*0*	*22,918*	***22,918***	***0***	*-22,918*
1-140 TOTAL	28,403	0	0	28,403	0	0	0	32,675	**61,078**	2,073	58,130	58,130	2,948	**61,078**	**0**	-61,078
1-150 Toilets																
UNITED SITE SERVICES NORTHEAST											10,310					
WASTED PBC											3,404					
Base	50,526	0	0	50,526	0	0	0	0	**50,526**	0	13,714	13,714	36,812	**50,526**	**0**	-50,526
1-150 TOTAL	50,526	0	0	50,526	0	0	0	0	**50,526**	0	13,714	13,714	36,812	**50,526**	**0**	-50,526
1-153 Drinking Water																
COLONY HARDWARE SUPPLY CO INC											66					
READY REFRESH BY NESTLE											1,546					
Base	3,649	0	0	3,649	0	0	0	0	**3,649**	66	1,611	1,611	2,038	**3,649**	**0**	-3,649
1-153 TOTAL	3,649	0	0	3,649	0	0	0	0	**3,649**	66	1,611	1,611	2,038	**3,649**	**0**	-3,649
1-156 Safety & first aid																
COLONY HARDWARE SUPPLY CO INC											7,569					
KNOX COMPANY											360					
RB SUPPLY											763					
SIGNIFY ENTERPRISES INC DBA											1,068					
Base	13,574	0	0	13,574	0	0	0	0	**13,574**	8,173	9,759	9,759	3,815	**13,574**	**0**	-13,574
1-156 TOTAL	13,574	0	0	13,574	0	0	0	0	**13,574**	8,173	9,759	9,759	3,815	**13,574**	**0**	-13,574
1-160 Project photos																
Base	18,440	0	0	18,440	0	0	0	0	**18,440**	0	0	0	18,440	**18,440**	**0**	-18,440
1-160 TOTAL	18,440	0	0	18,440	0	0	0	0	**18,440**	0	0	0	18,440	**18,440**	**0**	-18,440
1-161 Onsite Live Web Cameras																
AMAZON MKTPLACE -CC											818					
Base	25,500	0	0	25,500	0	0	0	0	**25,500**	770	818	818	24,682	**25,500**	**0**	-25,500
1-161 TOTAL	25,500	0	0	25,500	0	0	0	0	**25,500**	770	818	818	24,682	**25,500**	**0**	-25,500
1-165 Permits																
1-165 TOTAL	0	0	0	0	0	0	0	102	**102**	0	102	102	0	**102**	**0**	-102
1-172 Surveying																
BRENNAN CONSULTING											25,000					
Base	25,000	0	0	25,000	0	0	0	0	**25,000**	25,000	25,000	25,000	0	**25,000**	**0**	-25,000

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
1-172 Surveying (cont.)																
AT021-Survey Reconciliation - Oct 24	*0*	*0*	*26,855*	*26,855*	*0*	*0*	*0*	*0*	***26,855***	*26,855*	*26,855*	*26,855*	*0*	***26,855***	***0***	*-26,855*
AT034-Survey Reconciliation - Nov 24	*0*	*0*	*11,305*	*11,305*	*0*	*0*	*0*	*0*	***11,305***	*11,305*	*11,305*	*11,305*	*0*	***11,305***	***0***	*-11,305*
AT038-Survey Reconciliation - Dec 24	*0*	*0*	*10,333*	*10,333*	*0*	*0*	*0*	*0*	***10,333***	*10,333*	*10,333*	*10,333*	*0*	***10,333***	***0***	*-10,333*
1-172 TOTAL	25,000	0	48,493	73,493	0	0	0	0	**73,493**	73,493	73,493	73,493	0	**73,493**	**0**	-48,493
1-180 Postage / shipping																
UNITED PARCEL SERVICE											67					
Base	1,502	0	0	1,502	0	0	0	0	**1,502**	0	67	67	1,435	**1,502**	**0**	-1,502
1-180 TOTAL	1,502	0	0	1,502	0	0	0	0	**1,502**	0	67	67	1,435	**1,502**	**0**	-1,502
1-185 Blueprints																
ALLEGRA FRANKLIN											685					
ARCHIMEDIA SOLUTIONS GROUP LLC											5,051					
Base	18,087	0	0	18,087	0	0	0	0	**18,087**	0	5,736	5,736	12,351	**18,087**	**0**	-18,087
1-185 TOTAL	18,087	0	0	18,087	0	0	0	0	**18,087**	0	5,736	5,736	12,351	**18,087**	**0**	-18,087
1-205 Project Logistical Support																
CONSIGLI EQUIPMENT											7,650					
WEX BANK											18					
WEX BANK (SHELL)											421					
Base	0	0	0	0	0	0	0	0	**0**	0	8,089	8,089	-8,089	**0**	**0**	0
BT007-PreGMP #3 - GR Reconciliation	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*8,089*	***8,089***	*0*	*0*	*0*	*8,089*	***8,089***	***0***	*-8,089*
1-205 TOTAL	0	0	0	0	0	0	0	8,089	**8,089**	0	8,089	8,089	0	**8,089**	**0**	-8,089
1-210 Storage trailers																
ARIES BUILDING SYSTEMS, LLC											3,188					
Base	5,200	0	0	5,200	0	0	0	0	**5,200**	68	3,188	3,188	2,012	**5,200**	**0**	-5,200
1-210 TOTAL	5,200	0	0	5,200	0	0	0	0	**5,200**	68	3,188	3,188	2,012	**5,200**	**0**	-5,200
1-213 Office trailers																
ARIES BUILDING SYSTEMS, LLC											120,387					
Base	215,467	0	0	215,467	0	0	0	0	**215,467**	24,415	120,387	144,802	70,665	**215,467**	**0**	-215,467
1-213 TOTAL	215,467	0	0	215,467	0	0	0	0	**215,467**	24,415	120,387	144,802	70,665	**215,467**	**0**	-215,467
1-215 Office Trailer Cleaning																
COLONY HARDWARE SUPPLY CO INC											867					
THOMAS SMITH											264					
Base	26,745	0	0	26,745	0	0	0	0	**26,745**	1,044	1,131	1,131	25,614	**26,745**	**0**	-26,745
1-215 TOTAL	26,745	0	0	26,745	0	0	0	0	**26,745**	1,044	1,131	1,131	25,614	**26,745**	**0**	-26,745
1-216 Setup trailer																
Base	45,780	0	0	45,780	0	0	0	0	**45,780**	0	0	0	45,780	**45,780**	**0**	-45,780
1-216 TOTAL	45,780	0	0	45,780	0	0	0	0	**45,780**	0	0	0	45,780	**45,780**	**0**	-45,780
1-248 Pest control																
Base	18,850	0	0	18,850	0	0	0	0	**18,850**	18,850	0	18,850	0	**18,850**	**0**	-18,850
1-248 TOTAL	18,850	0	0	18,850	0	0	0	0	**18,850**	18,850	0	18,850	0	**18,850**	**0**	-18,850
1-438 Fire ext setup/maintenance																
COLONY HARDWARE SUPPLY CO INC											-1,410					
Base	0	0	0	0	0	0	0	0	**0**	0	-1,410	-1,410	1,410	**0**	**0**	0
1-438 TOTAL	0	0	0	0	0	0	0	0	**0**	0	-1,410	-1,410	1,410	**0**	**0**	0
1-810 Dumpsters																
NORTHEAST RECYCLING											7,871					
Base	135,199	0	0	135,199	0	0	0	0	**135,199**	0	7,871	7,871	127,328	**135,199**	**0**	-135,199
BT007-PreGMP #3 - GR Reconciliation	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-387*	***-387***	*0*	*0*	*0*	*-387*	***-387***	***0***	*387*
1-810 TOTAL	135,199	0	0	135,199	0	0	0	-387	**134,812**	0	7,871	7,871	126,941	**134,812**	**0**	-134,812
1-840 Indoor air quality monitoring																
Base	15,600	0	0	15,600	0	0	0	0	**15,600**	0	0	0	15,600	**15,600**	**0**	-15,600
1-840 TOTAL	15,600	0	0	15,600	0	0	0	0	**15,600**	0	0	0	15,600	**15,600**	**0**	-15,600
1-845 3rd Party Abatement Review																

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
1-845 3rd Party Abatement Review (cont.)																
Base	10,000	0	0	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
1-845 TOTAL	10,000	0	0	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
1-910 Consigli payment & perf bond																
1-910 TOTAL	390,856	0	0	390,856	0	0	0	0	**390,856**	0	98,400	98,400	292,456	**390,856**	**0**	-390,856
1-920 Builder's risk insurance																
1-920 TOTAL	534,567	0	0	534,567	0	0	0	0	**534,567**	0	534,567	534,567	0	**534,567**	**0**	-534,567
1-930 General liability insurance																
1-930 TOTAL	588,153	0	0	588,153	0	0	0	0	**588,153**	0	192,435	192,435	395,718	**588,153**	**0**	-588,153
1-940 Subcontractor default insurnce																
1-940 TOTAL	514,479	0	0	514,479	0	0	0	0	**514,479**	0	174,755	174,755	339,724	**514,479**	**0**	-514,479
1-970 Owner purchases																
DASILVA MOTOR SPORTS											29,598					
Base	29,598	0	0	29,598	0	0	0	0	**29,598**	0	29,598	29,598	0	**29,598**	**0**	-29,598
1-970 TOTAL	29,598	0	0	29,598	0	0	0	0	**29,598**	0	29,598	29,598	0	**29,598**	**0**	-29,598
1-980 Legal / professional services																
CODE RED CONSULTANTS											9,750					
Base	35,250	0	0	35,250	0	0	0	0	**35,250**	35,250	9,750	35,250	0	**35,250**	**0**	-35,250
1-980 TOTAL	35,250	0	0	35,250	0	0	0	0	**35,250**	35,250	9,750	35,250	0	**35,250**	**0**	-35,250
1-985 Textura Project Fees																
ORACLE AMERICA											6,006					
Base	30,000	0	0	30,000	0	0	0	0	**30,000**	0	6,006	6,006	23,994	**30,000**	**0**	-30,000
1-985 TOTAL	30,000	0	0	30,000	0	0	0	0	**30,000**	0	6,006	6,006	23,994	**30,000**	**0**	-30,000
1-999 PreGMP #3 H/C/A Reconciliation																
Base	1,371,560	0	0	1,371,560	0	0	0	0	**1,371,560**	0	0	0	1,371,560	**1,371,560**	**0**	-1,371,560
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-1,371,560*	***-1,371,560***	*0*	*0*	*0*	*-1,371,560*	***-1,371,560***	***0***	*1,371,560*
1-999 TOTAL	1,371,560	0	0	1,371,560	0	0	0	-1,371,560	**0**	0	0	0	0	**0**	**0**	0
1 - GENERAL CONDITIONS TOTAL	***10,798,192***	***0***	***21,919***	***10,820,111***	***0***	***0***	***0***	***-1,268,693***	***9,551,419***	*196,209*	*2,567,317*	*2,638,664*	*6,912,755*	***9,551,419***	***0***	-9,551,419
2 - SITEWORK & DEMOLITION																
2-304 Temporary fencing																
EHJJ PARTNERS, LLC											309,075					
Base	0	0	0	0	0	0	0	0	**0**	326,550	309,075	326,550	-326,550	**0**	**0**	0
HT001-BP#1 - Temporary Fencing	*0*	*0*	*326,550*	*326,550*	*0*	*0*	*0*	*0*	***326,550***	*0*	*0*	*0*	*326,550*	***326,550***	***0***	*-326,550*
HT002-OFR: East Courtyard Temp Fence	*0*	*0*	*3,439*	*3,439*	*0*	*0*	*0*	*0*	***3,439***	*3,439*	*3,439*	*3,439*	*0*	***3,439***	***0***	*-3,439*
HT004-OFR: Wetland Retention Fence	*0*	*0*	*5,450*	*5,450*	*0*	*0*	*0*	*0*	***5,450***	*5,450*	*5,450*	*5,450*	*0*	***5,450***	***0***	*-5,450*
HT005-Softball Fence Relocation	*0*	*0*	*2,095*	*2,095*	*0*	*0*	*0*	*0*	***2,095***	*2,095*	*2,095*	*2,095*	*0*	***2,095***	***0***	*-2,095*
HT006-Temporary 6' Jobsite Fence	*0*	*0*	*27,081*	*27,081*	*0*	*0*	*0*	*0*	***27,081***	*27,081*	*27,081*	*27,081*	*0*	***27,081***	***0***	*-27,081*
HT007-Tennis Stockpile Fence Reloc	*0*	*0*	*22,972*	*22,972*	*0*	*0*	*0*	*0*	***22,972***	*22,972*	*22,972*	*22,972*	*0*	***22,972***	***0***	*-22,972*
HT009-Temp Generator Fence	*0*	*0*	*4,289*	*4,289*	*0*	*0*	*0*	*0*	***4,289***	*4,289*	*4,289*	*4,289*	*0*	***4,289***	***0***	*-4,289*
HT010-Temp Fence Maint - Jan '25	*0*	*0*	*10,305*	*10,305*	*0*	*0*	*0*	*0*	***10,305***	*10,305*	*0*	*10,305*	*0*	***10,305***	***0***	*-10,305*
HT013-F&I Football Stockpile Fence	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*21,311*	***21,311***	*0*	*0*	*0*	*21,311*	***21,311***	***0***	*-21,311*
2-304 TOTAL	0	0	402,180	402,180	0	0	0	21,311	**423,491**	402,180	374,400	402,180	21,311	**423,491**	**0**	-423,491
2-401 General site excavation sub																
NORTHEAST CONTRACTORS, INC.											6,855,449					
Base	9,900,650	0	0	9,900,650	0	0	0	0	**9,900,650**	9,900,650	6,855,449	9,900,650	0	**9,900,650**	**0**	-9,900,650
AT001-TCD Water Main Ledge Removal	*0*	*0*	*19,009*	*19,009*	*0*	*0*	*0*	*0*	***19,009***	*19,009*	*19,009*	*19,009*	*0*	***19,009***	***0***	*-19,009*
AT002-CorBuilt GPRS Utility Survey	*0*	*0*	*6,670*	*6,670*	*0*	*0*	*0*	*0*	***6,670***	*6,670*	*6,670*	*6,670*	*0*	***6,670***	***0***	*-6,670*
AT004-ASI #1: ConCom Civil Revisions	*0*	*0*	*147,739*	*147,739*	*0*	*0*	*0*	*0*	***147,739***	*147,739*	*99,709*	*147,739*	*0*	***147,739***	***0***	*-147,739*
AT005-ASI #1 - Parking Lot T&M	*0*	*0*	*33,273*	*33,273*	*0*	*0*	*0*	*0*	***33,273***	*33,273*	*33,273*	*33,273*	*0*	***33,273***	***0***	*-33,273*
AT006-Gate Valve at Utility Access	*0*	*0*	*3,966*	*3,966*	*0*	*0*	*0*	*0*	***3,966***	*3,966*	*3,966*	*3,966*	*0*	***3,966***	***0***	*-3,966*
AT007-DPW: Gate Valve at Vault Pit	*0*	*0*	*7,322*	*7,322*	*0*	*0*	*0*	*0*	***7,322***	*7,322*	*7,322*	*7,322*	*0*	***7,322***	***0***	*-7,322*
AT008-OFR: East Access Road Ext.	*0*	*0*	*39,817*	*39,817*	*0*	*0*	*0*	*0*	***39,817***	*39,817*	*39,817*	*39,817*	*0*	***39,817***	***0***	*-39,817*
AT009-Added Pre-Blast Surveys	*0*	*0*	*18,769*	*18,769*	*0*	*0*	*0*	*0*	***18,769***	*18,769*	*18,769*	*18,769*	*0*	***18,769***	***0***	*-18,769*

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
2-401 General site excavation sub (cont.)																
AT010-ASI #1: Water Quality Units	0	0	216,213	216,213	0	0	0	0	**216,213**	216,213	127,000	216,213	0	**216,213**	**0**	-216,213
AT011-TCD Water Main Ledge Removal 2	0	0	39,189	39,189	0	0	0	0	**39,189**	39,189	39,189	39,189	0	**39,189**	**0**	-39,189
AT012-OFR: Added Temp Parking Spaces	0	0	33,173	33,173	0	0	0	0	**33,173**	33,173	33,173	33,173	0	**33,173**	**0**	-33,173
AT013-OTO Test Pit Excavation	0	0	4,805	4,805	0	0	0	0	**4,805**	4,805	4,805	4,805	0	**4,805**	**0**	-4,805
AT014-OFR: Tennis Stockpile Expansio	0	0	41,140	41,140	0	0	0	0	**41,140**	41,140	0	41,140	0	**41,140**	**0**	-41,140
AT015-Goat Path Ledge Removal	0	0	327,131	327,131	0	0	0	0	**327,131**	327,131	0	327,131	0	**327,131**	**0**	-327,131
AT018-BP #1 Hydroseeding	0	0	2,751	2,751	0	0	0	0	**2,751**	2,751	2,751	2,751	0	**2,751**	**0**	-2,751
AT019-Stump Removal & Export	0	0	178,773	178,773	0	0	0	0	**178,773**	178,773	178,773	178,773	0	**178,773**	**0**	-178,773
AT020-Utility Road Premium Time T&M	0	0	18,631	18,631	0	0	0	0	**18,631**	18,631	0	18,631	0	**18,631**	**0**	-18,631
AT024-Loading Dock Rock Removal	0	0	105,934	105,934	0	0	0	0	**105,934**	105,934	105,934	105,934	0	**105,934**	**0**	-105,934
AT025-Topsoil Screening	0	0	797,114	797,114	0	0	0	0	**797,114**	797,114	260,000	797,114	0	**797,114**	**0**	-797,114
AT028-F&I Softball Outfield Sod	0	0	24,111	24,111	0	0	0	0	**24,111**	24,111	24,111	24,111	0	**24,111**	**0**	-24,111
AT030-Winter Conditions #1	0	0	0	0	0	0	0	62,457	**62,457**	0	0	0	62,457	**62,457**	**0**	-62,457
AT031-Ex. Football Field Soil & Demo	0	0	0	0	0	0	0	64,794	**64,794**	0	0	0	64,794	**64,794**	**0**	-64,794
AT032-Badger Vac for Ductbank	0	0	5,485	5,485	0	0	0	0	**5,485**	5,485	0	5,485	0	**5,485**	**0**	-5,485
AT041-Winter Conditions #2 - Feb '25	0	0	0	0	0	0	0	102,009	**102,009**	0	0	0	102,009	**102,009**	**0**	-102,009
AT042-F&I Contractor Parking	0	0	0	0	0	0	0	12,271	**12,271**	0	0	0	12,271	**12,271**	**0**	-12,271
AT043-Earthwork Material Credit	0	0	0	0	0	0	0	-229,360	**-229,360**	0	0	0	-229,360	**-229,360**	**0**	229,360
AT045-GeoT Sediment Pond	0	0	0	0	0	0	0	11,993	**11,993**	0	0	0	11,993	**11,993**	**0**	-11,993
BT004-Temp Trailer Setup #1 SOE/Swr	0	0	26,573	26,573	0	0	0	0	**26,573**	26,573	0	26,573	0	**26,573**	**0**	-26,573
CT001-Reconcile Backstop & Netting	0	0	94,841	94,841	0	0	0	0	**94,841**	94,841	94,841	94,841	0	**94,841**	**0**	-94,841
CT003-Access Path DG Expansion	0	0	0	0	0	0	0	11,351	**11,351**	0	0	0	11,351	**11,351**	**0**	-11,351
HT003-F&I Jersey Barriers - Nov '24	0	0	3,950	3,950	0	0	0	0	**3,950**	3,950	3,950	3,950	0	**3,950**	**0**	-3,950
HT011-Jersey Barriers - Jan '25	0	0	0	0	0	0	0	8,748	**8,748**	0	0	0	8,748	**8,748**	**0**	-8,748
2-401 TOTAL	9,900,650	0	2,196,377	12,097,027	0	0	0	44,264	**12,141,291**	12,097,027	7,958,510	12,097,027	44,264	**12,141,291**	**0**	-1,964,077
2-790 Geothermal Well & Drilling																
Base	4,332,583	0	0	4,332,583	0	0	0	0	**4,332,583**	2,798,207	0	2,798,207	1,534,376	**4,332,583**	**0**	-4,332,583
RB001-OAL 05 - BP#3 Geothermal RB	0	0	-1,534,376	-1,534,376	0	0	0	0	**-1,534,376**	0	0	0	-1,534,376	**-1,534,376**	**0**	1,534,376
2-790 TOTAL	4,332,583	0	-1,534,376	2,798,207	0	0	0	0	**2,798,207**	2,798,207	0	2,798,207	0	**2,798,207**	**0**	-2,798,207
2-976 Hold - Add'l Test & Cleaning																
RB001-OAL 05 - BP#3 Geothermal RB	0	0	45,000	45,000	0	0	0	0	**45,000**	0	0	0	45,000	**45,000**	**0**	-45,000
2-976 TOTAL	0	0	45,000	45,000	0	0	0	0	**45,000**	0	0	0	45,000	**45,000**	**0**	-45,000
2-977 Seeding																
RB001-OAL 05 - BP#3 Geothermal RB	0	0	50,000	50,000	0	0	0	0	**50,000**	0	0	0	50,000	**50,000**	**0**	-50,000
2-977 TOTAL	0	0	50,000	50,000	0	0	0	0	**50,000**	0	0	0	50,000	**50,000**	**0**	-50,000
2-978 Hold - Concrete Pad at Vault																
RB001-OAL 05 - BP#3 Geothermal RB	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
2-978 TOTAL	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
2-979 Hold - Add'l Verticality Tests																
RB001-OAL 05 - BP#3 Geothermal RB	0	0	23,750	23,750	0	0	0	0	**23,750**	0	0	0	23,750	**23,750**	**0**	-23,750
2-979 TOTAL	0	0	23,750	23,750	0	0	0	0	**23,750**	0	0	0	23,750	**23,750**	**0**	-23,750
2-980 Plantings - shrubs, sm trees																
RB001-OAL 05 - BP#3 Geothermal RB	0	0	40,000	40,000	0	0	0	0	**40,000**	0	0	0	40,000	**40,000**	**0**	-40,000
2-980 TOTAL	0	0	40,000	40,000	0	0	0	0	**40,000**	0	0	0	40,000	**40,000**	**0**	-40,000
2-981 Hold - Vault Tiedown Straps																
RB001-OAL 05 - BP#3 Geothermal RB	0	0	15,000	15,000	0	0	0	0	**15,000**	0	0	0	15,000	**15,000**	**0**	-15,000
2-981 TOTAL	0	0	15,000	15,000	0	0	0	0	**15,000**	0	0	0	15,000	**15,000**	**0**	-15,000
2-982 Hold - Grout Backfill at Mains																
RB001-OAL 05 - BP#3 Geothermal RB	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
2-982 TOTAL	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
2-983 Plantings - trees																
RB001-OAL 05 - BP#3 Geothermal RB	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
2-983 TOTAL	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
2-984 Hold - Boxout for FND Sleeves																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*6,000*	*6,000*	*0*	*0*	*0*	*0*	***6,000***	*0*	*0*	*0*	*6,000*	***6,000***	***0***	*-6,000*
2-984 TOTAL	0	0	6,000	6,000	0	0	0	0	**6,000**	0	0	0	6,000	**6,000**	**0**	-6,000
2-985 Hold - Concrete pad on Vault																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*15,000*	*15,000*	*0*	*0*	*0*	*0*	***15,000***	*0*	*0*	*0*	*15,000*	***15,000***	***0***	*-15,000*
2-985 TOTAL	0	0	15,000	15,000	0	0	0	0	**15,000**	0	0	0	15,000	**15,000**	**0**	-15,000
2-986 Mulch/wood chips																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*4,000*	*4,000*	*0*	*0*	*0*	*0*	***4,000***	*0*	*0*	*0*	*4,000*	***4,000***	***0***	*-4,000*
2-986 TOTAL	0	0	4,000	4,000	0	0	0	0	**4,000**	0	0	0	4,000	**4,000**	**0**	-4,000
2-987 Hold - Sleeves & Link Seal																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*8,000*	*8,000*	*0*	*0*	*0*	*0*	***8,000***	*0*	*0*	*0*	*8,000*	***8,000***	***0***	*-8,000*
2-987 TOTAL	0	0	8,000	8,000	0	0	0	0	**8,000**	0	0	0	8,000	**8,000**	**0**	-8,000
2-988 Hold - F&I Peastone																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*6,000*	*6,000*	*0*	*0*	*0*	*0*	***6,000***	*0*	*0*	*0*	*6,000*	***6,000***	***0***	*-6,000*
2-988 TOTAL	0	0	6,000	6,000	0	0	0	0	**6,000**	0	0	0	6,000	**6,000**	**0**	-6,000
2-989 Hold - F&I Bentonite Chips																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*6,000*	*6,000*	*0*	*0*	*0*	*0*	***6,000***	*0*	*0*	*0*	*6,000*	***6,000***	***0***	*-6,000*
2-989 TOTAL	0	0	6,000	6,000	0	0	0	0	**6,000**	0	0	0	6,000	**6,000**	**0**	-6,000
2-990 Temporary Fence- Hold																
Base	587,328	0	0	587,328	0	0	0	0	**587,328**	0	0	0	587,328	**587,328**	**0**	-587,328
HT001-BP#1 - Temporary Fencing	*0*	*0*	*-459,550*	*-459,550*	*0*	*0*	*0*	*0*	***-459,550***	*0*	*0*	*0*	*-459,550*	***-459,550***	***0***	*459,550*
HT002-OFR: East Courtyard Temp Fence	*0*	*0*	*-3,439*	*-3,439*	*0*	*0*	*0*	*0*	***-3,439***	*0*	*0*	*0*	*-3,439*	***-3,439***	***0***	*3,439*
HT004-OFR: Wetland Retention Fence	*0*	*0*	*-5,450*	*-5,450*	*0*	*0*	*0*	*0*	***-5,450***	*0*	*0*	*0*	*-5,450*	***-5,450***	***0***	*5,450*
HT005-Softball Fence Relocation	*0*	*0*	*-2,095*	*-2,095*	*0*	*0*	*0*	*0*	***-2,095***	*0*	*0*	*0*	*-2,095*	***-2,095***	***0***	*2,095*
HT006-Temporary 6' Jobsite Fence	*0*	*0*	*-25,335*	*-25,335*	*0*	*0*	*0*	*0*	***-25,335***	*0*	*0*	*0*	*-25,335*	***-25,335***	***0***	*25,335*
HT008-Goat Path OH Line Protection	*0*	*0*	*-87,171*	*-87,171*	*0*	*0*	*0*	*0*	***-87,171***	*0*	*0*	*0*	*-87,171*	***-87,171***	***0***	*87,171*
HT009-Temp Generator Fence	*0*	*0*	*-4,289*	*-4,289*	*0*	*0*	*0*	*0*	***-4,289***	*0*	*0*	*0*	*-4,289*	***-4,289***	***0***	*4,289*
HT013-F&I Football Stockpile Fence	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-21,311*	***-21,311***	*0*	*0*	*0*	*-21,311*	***-21,311***	***0***	*21,311*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*96,408*	***96,408***	*0*	*0*	*0*	*96,408*	***96,408***	***0***	*-96,408*
2-990 TOTAL	587,328	0	-587,328	0	0	0	0	75,097	**75,097**	0	0	0	75,097	**75,097**	**0**	-75,097
2-991 F&I Jersey Barrier - HOLD																
FREMONT TRUCKING - CC											980					
Base	0	0	0	0	0	0	0	0	**0**	0	980	980	-980	**0**	**0**	0
HT001-BP#1 - Temporary Fencing	*0*	*0*	*94,000*	*94,000*	*0*	*0*	*0*	*0*	***94,000***	*0*	*0*	*0*	*94,000*	***94,000***	***0***	*-94,000*
HT003-F&I Jersey Barriers - Nov '24	*0*	*0*	*-3,950*	*-3,950*	*0*	*0*	*0*	*0*	***-3,950***	*0*	*0*	*0*	*-3,950*	***-3,950***	***0***	*3,950*
HT011-Jersey Barriers - Jan '25	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-8,748*	***-8,748***	*0*	*25,856*	*25,856*	*-34,604*	***-8,748***	***0***	*8,748*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*90,050*	***90,050***	*0*	*0*	*0*	*90,050*	***90,050***	***0***	*-90,050*
2-991 TOTAL	0	0	90,050	90,050	0	0	0	81,302	**171,352**	0	26,836	26,836	144,516	**171,352**	**0**	-171,352
2-992 Temp Fence Maintenance - Hold																
HT001-BP#1 - Temporary Fencing	*0*	*0*	*39,000*	*39,000*	*0*	*0*	*0*	*0*	***39,000***	*0*	*0*	*0*	*39,000*	***39,000***	***0***	*-39,000*
HT006-Temporary 6' Jobsite Fence	*0*	*0*	*-1,746*	*-1,746*	*0*	*0*	*0*	*0*	***-1,746***	*0*	*0*	*0*	*-1,746*	***-1,746***	***0***	*1,746*
HT007-Tennis Stockpile Fence Reloc	*0*	*0*	*-22,972*	*-22,972*	*0*	*0*	*0*	*0*	***-22,972***	*0*	*0*	*0*	*-22,972*	***-22,972***	***0***	*22,972*
HT010-Temp Fence Maint - Jan '25	*0*	*0*	*-10,305*	*-10,305*	*0*	*0*	*0*	*0*	***-10,305***	*0*	*0*	*0*	*-10,305*	***-10,305***	***0***	*10,305*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*36,905*	***36,905***	*0*	*0*	*0*	*36,905*	***36,905***	***0***	*-36,905*
2-992 TOTAL	0	0	3,977	3,977	0	0	0	36,905	**40,882**	0	0	0	40,882	**40,882**	**0**	-40,882
2-993 Hold - F&I EZ Seal																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*3,000*	*3,000*	*0*	*0*	*0*	*0*	***3,000***	*0*	*0*	*0*	*3,000*	***3,000***	***0***	*-3,000*
2-993 TOTAL	0	0	3,000	3,000	0	0	0	0	**3,000**	0	0	0	3,000	**3,000**	**0**	-3,000
2-994 Hold - NEMA3R Electrical																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*15,000*	*15,000*	*0*	*0*	*0*	*0*	***15,000***	*0*	*0*	*0*	*15,000*	***15,000***	***0***	*-15,000*
2-994 TOTAL	0	0	15,000	15,000	0	0	0	0	**15,000**	0	0	0	15,000	**15,000**	**0**	-15,000
2-995 Hold - Sitework Coordination																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*20,000*	*20,000*	*0*	*0*	*0*	*0*	***20,000***	*0*	*0*	*0*	*20,000*	***20,000***	***0***	*-20,000*

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
2-995 TOTAL	0	0	20,000	20,000	0	0	0	0	**20,000**	0	0	0	20,000	**20,000**	**0**	-20,000
2-996 Hold - Building Valves																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*30,000*	*30,000*	*0*	*0*	*0*	*0*	***30,000***	*0*	*0*	*0*	*30,000*	***30,000***	***0***	*-30,000*
2-996 TOTAL	0	0	30,000	30,000	0	0	0	0	**30,000**	0	0	0	30,000	**30,000**	**0**	-30,000
2-997 Hold - Union Labor Support																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*87,200*	*87,200*	*0*	*0*	*0*	*0*	***87,200***	*0*	*0*	*0*	*87,200*	***87,200***	***0***	*-87,200*
2-997 TOTAL	0	0	87,200	87,200	0	0	0	0	**87,200**	0	0	0	87,200	**87,200**	**0**	-87,200
2-998 Rented equipment																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*254,100*	*254,100*	*0*	*0*	*0*	*0*	***254,100***	*0*	*0*	*0*	*254,100*	***254,100***	***0***	*-254,100*
2-998 TOTAL	0	0	254,100	254,100	0	0	0	0	**254,100**	0	0	0	254,100	**254,100**	**0**	-254,100
2-999 Owned equipment - idle																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*207,276*	*207,276*	*0*	*0*	*0*	*0*	***207,276***	*0*	*0*	*0*	*207,276*	***207,276***	***0***	*-207,276*
2-999 TOTAL	0	0	207,276	207,276	0	0	0	0	**207,276**	0	0	0	207,276	**207,276**	**0**	-207,276
2 - SITEWORK & DEMOLITION TOTAL	***14,820,561***	***0***	***1,436,206***	***16,256,767***	***0***	***0***	***0***	***258,879***	***16,515,646***	*15,297,415*	*8,359,746*	*15,324,251*	*1,191,396*	***16,515,646***	***0***	-16,515,646
3 - CONCRETE																
3-110 Concrete subcontractor																
Base	6,916,055	0	0	6,916,055	0	0	0	0	**6,916,055**	6,450,000	0	6,450,000	466,055	**6,916,055**	**0**	-6,916,055
AT035-Foundation MEP Sleeves	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*25,597*	***25,597***	*0*	*0*	*0*	*25,597*	***25,597***	***0***	*-25,597*
AT041-Winter Conditions #2 - Feb '25	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*6,666*	***6,666***	*0*	*0*	*0*	*6,666*	***6,666***	***0***	*-6,666*
HT014-Add'l Rebar MEP Sleeves (A)	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*3,166*	***3,166***	*0*	*0*	*0*	*3,166*	***3,166***	***0***	*-3,166*
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*-450,000*	*-450,000*	*0*	*0*	*0*	*0*	***-450,000***	*0*	*0*	*0*	*-450,000*	***-450,000***	***0***	*450,000*
3-110 TOTAL	6,916,055	0	-450,000	6,466,055	0	0	0	35,429	**6,501,484**	6,450,000	0	6,450,000	51,484	**6,501,484**	**0**	-6,501,484
3-820 Precast concrete wall panels																
CORESLAB STRUCTURES (CONN) INC											327,259					
Base	3,161,950	0	0	3,161,950	0	0	0	0	**3,161,950**	3,161,950	327,259	3,161,950	0	**3,161,950**	**0**	-3,161,950
3-820 TOTAL	3,161,950	0	0	3,161,950	0	0	0	0	**3,161,950**	3,161,950	327,259	3,161,950	0	**3,161,950**	**0**	-3,161,950
3-825 Precast concrete planks																
Base	376,400	0	0	376,400	0	0	0	0	**376,400**	198,000	0	198,000	178,400	**376,400**	**0**	-376,400
RB004-OAL 08 - BP#3 Precast Plank	*0*	*0*	*-178,400*	*-178,400*	*0*	*0*	*0*	*0*	***-178,400***	*0*	*0*	*0*	*-178,400*	***-178,400***	***0***	*178,400*
3-825 TOTAL	376,400	0	-178,400	198,000	0	0	0	0	**198,000**	198,000	0	198,000	0	**198,000**	**0**	-198,000
3-895 Hold - Bonding Agent																
RB004-OAL 08 - BP#3 Precast Plank	*0*	*0*	*10,000*	*10,000*	*0*	*0*	*0*	*0*	***10,000***	*0*	*0*	*0*	*10,000*	***10,000***	***0***	*-10,000*
3-895 TOTAL	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
3-896 Hold - Plank Grouting																
RB004-OAL 08 - BP#3 Precast Plank	*0*	*0*	*94,000*	*94,000*	*0*	*0*	*0*	*0*	***94,000***	*0*	*0*	*0*	*94,000*	***94,000***	***0***	*-94,000*
3-896 TOTAL	0	0	94,000	94,000	0	0	0	0	**94,000**	0	0	0	94,000	**94,000**	**0**	-94,000
3-897 Hold - Grout Access Point																
RB004-OAL 08 - BP#3 Precast Plank	*0*	*0*	*15,000*	*15,000*	*0*	*0*	*0*	*0*	***15,000***	*0*	*0*	*0*	*15,000*	***15,000***	***0***	*-15,000*
3-897 TOTAL	0	0	15,000	15,000	0	0	0	0	**15,000**	0	0	0	15,000	**15,000**	**0**	-15,000
3-898 Hold - Add'l T&E																
RB004-OAL 08 - BP#3 Precast Plank	*0*	*0*	*5,000*	*5,000*	*0*	*0*	*0*	*0*	***5,000***	*0*	*0*	*0*	*5,000*	***5,000***	***0***	*-5,000*
3-898 TOTAL	0	0	5,000	5,000	0	0	0	0	**5,000**	0	0	0	5,000	**5,000**	**0**	-5,000
3-899 Hold - Stamped Erection Plans																
RB004-OAL 08 - BP#3 Precast Plank	*0*	*0*	*10,000*	*10,000*	*0*	*0*	*0*	*0*	***10,000***	*0*	*0*	*0*	*10,000*	***10,000***	***0***	*-10,000*
3-899 TOTAL	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
3-994 Hold - Add'l Rebar Deliveries																
HT014-Add'l Rebar MEP Sleeves (A)	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-3,166*	***-3,166***	*0*	*0*	*0*	*-3,166*	***-3,166***	***0***	*3,166*
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*25,000*	*25,000*	*0*	*0*	*0*	*0*	***25,000***	*0*	*0*	*0*	*25,000*	***25,000***	***0***	*-25,000*
3-994 TOTAL	0	0	25,000	25,000	0	0	0	-3,166	**21,834**	0	0	0	21,834	**21,834**	**0**	-21,834
3-995 Hold - Undefined Embed Install																
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*30,000*	*30,000*	*0*	*0*	*0*	*0*	***30,000***	*0*	*0*	*0*	*30,000*	***30,000***	***0***	*-30,000*

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
3-995 TOTAL	0	0	30,000	30,000	0	0	0	0	**30,000**	0	0	0	30,000	**30,000**	**0**	-30,000
3-996 Hold - Wash-out Dumpster																
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*10,000*	*10,000*	*0*	*0*	*0*	*0*	***10,000***	*0*	*0*	*0*	*10,000*	***10,000***	***0***	*-10,000*
3-996 TOTAL	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
3-997 Hold - Add'l B&G CW-PC Clips																
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*75,000*	*75,000*	*0*	*0*	*0*	*0*	***75,000***	*0*	*0*	*0*	*75,000*	***75,000***	***0***	*-75,000*
3-997 TOTAL	0	0	75,000	75,000	0	0	0	0	**75,000**	0	0	0	75,000	**75,000**	**0**	-75,000
3-998 Add'l Gym Slab Floor Prep																
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*110,000*	*110,000*	*0*	*0*	*0*	*0*	***110,000***	*0*	*0*	*0*	*110,000*	***110,000***	***0***	*-110,000*
3-998 TOTAL	0	0	110,000	110,000	0	0	0	0	**110,000**	0	0	0	110,000	**110,000**	**0**	-110,000
3-999 Hold - Add'l Floor Protection																
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*40,000*	*40,000*	*0*	*0*	*0*	*0*	***40,000***	*0*	*0*	*0*	*40,000*	***40,000***	***0***	*-40,000*
3-999 TOTAL	0	0	40,000	40,000	0	0	0	0	**40,000**	0	0	0	40,000	**40,000**	**0**	-40,000
3 - CONCRETE TOTAL	***10,454,405***	***0***	***-204,400***	***10,250,005***	***0***	***0***	***0***	***32,263***	***10,282,268***	*9,809,950*	*327,259*	*9,809,950*	*472,318*	***10,282,268***	***0***	-10,282,268
4 - MASONRY																
4-601 Masonry TC (Bearing)																
Base	724,000	0	0	724,000	0	0	0	0	**724,000**	0	0	0	724,000	**724,000**	**0**	-724,000
4-601 TOTAL	724,000	0	0	724,000	0	0	0	0	**724,000**	0	0	0	724,000	**724,000**	**0**	-724,000
4 - MASONRY TOTAL	***724,000***	***0***	***0***	***724,000***	***0***	***0***	***0***	***0***	***724,000***	*0*	*0*	*0*	*724,000*	***724,000***	***0***	-724,000
5 - METALS																
5-120 Structural steel																
Base	11,388,828	0	0	11,388,828	0	0	0	0	**11,388,828**	0	0	0	11,388,828	**11,388,828**	**0**	-11,388,828
RB003-OAL 07 - BP#3 SS	*0*	*0*	*-1,062,828*	*-1,062,828*	*0*	*0*	*0*	*0*	***-1,062,828***	*0*	*0*	*0*	*-1,062,828*	***-1,062,828***	***0***	*1,062,828*
5-120 TOTAL	11,388,828	0	-1,062,828	10,326,000	0	0	0	0	**10,326,000**	0	0	0	10,326,000	**10,326,000**	**0**	-10,326,000
5-990 Hold - Elevator Guiderails																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*20,000*	*20,000*	*0*	*0*	*0*	*0*	***20,000***	*0*	*0*	*0*	*20,000*	***20,000***	***0***	*-20,000*
5-990 TOTAL	0	0	20,000	20,000	0	0	0	0	**20,000**	0	0	0	20,000	**20,000**	**0**	-20,000
5-991 Hold - Add'l Engineering																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*20,000*	*20,000*	*0*	*0*	*0*	*0*	***20,000***	*0*	*0*	*0*	*20,000*	***20,000***	***0***	*-20,000*
5-991 TOTAL	0	0	20,000	20,000	0	0	0	0	**20,000**	0	0	0	20,000	**20,000**	**0**	-20,000
5-992 Hold - Post-Erection Survey																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*25,000*	*25,000*	*0*	*0*	*0*	*0*	***25,000***	*0*	*0*	*0*	*25,000*	***25,000***	***0***	*-25,000*
5-992 TOTAL	0	0	25,000	25,000	0	0	0	0	**25,000**	0	0	0	25,000	**25,000**	**0**	-25,000
5-993 Hold - Abrasion Touchups																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*50,000*	*50,000*	*0*	*0*	*0*	*0*	***50,000***	*0*	*0*	*0*	*50,000*	***50,000***	***0***	*-50,000*
5-993 TOTAL	0	0	50,000	50,000	0	0	0	0	**50,000**	0	0	0	50,000	**50,000**	**0**	-50,000
5-994 Hold - Uniformed Fire Watch																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*15,000*	*15,000*	*0*	*0*	*0*	*0*	***15,000***	*0*	*0*	*0*	*15,000*	***15,000***	***0***	*-15,000*
5-994 TOTAL	0	0	15,000	15,000	0	0	0	0	**15,000**	0	0	0	15,000	**15,000**	**0**	-15,000
5-995 Hold - Add'l Trade Layout																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*40,000*	*40,000*	*0*	*0*	*0*	*0*	***40,000***	*0*	*0*	*0*	*40,000*	***40,000***	***0***	*-40,000*
5-995 TOTAL	0	0	40,000	40,000	0	0	0	0	**40,000**	0	0	0	40,000	**40,000**	**0**	-40,000
5-996 Hold - Cable & Rail Removal																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*80,500*	*80,500*	*0*	*0*	*0*	*0*	***80,500***	*0*	*0*	*0*	*80,500*	***80,500***	***0***	*-80,500*
5-996 TOTAL	0	0	80,500	80,500	0	0	0	0	**80,500**	0	0	0	80,500	**80,500**	**0**	-80,500
5-997 Hold - Blowoff Decks																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*17,328*	*17,328*	*0*	*0*	*0*	*0*	***17,328***	*0*	*0*	*0*	*17,328*	***17,328***	***0***	*-17,328*
5-997 TOTAL	0	0	17,328	17,328	0	0	0	0	**17,328**	0	0	0	17,328	**17,328**	**0**	-17,328
5-998 Hold - Punchlist Stairs																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*30,000*	*30,000*	*0*	*0*	*0*	*0*	***30,000***	*0*	*0*	*0*	*30,000*	***30,000***	***0***	*-30,000*

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
5-998 TOTAL	0	0	30,000	30,000	0	0	0	0	**30,000**	0	0	0	30,000	**30,000**	**0**	-30,000
5-999 Hold - Shop Weld Couplers																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*35,000*	*35,000*	*0*	*0*	*0*	*0*	***35,000***	*0*	*0*	*0*	*35,000*	***35,000***	***0***	*-35,000*
5-999 TOTAL	0	0	35,000	35,000	0	0	0	0	**35,000**	0	0	0	35,000	**35,000**	**0**	-35,000
5 - METALS TOTAL	***11,388,828***	***0***	***-730,000***	***10,658,828***	***0***	***0***	***0***	***0***	***10,658,828***	*0*	*0*	*0*	*10,658,828*	***10,658,828***	***0***	-10,658,828
7 - THERMAL / MOISTURE PROTECTION																
7-102 Early Waterproofing																
Base	102,780	0	0	102,780	0	0	0	0	**102,780**	102,780	0	102,780	0	**102,780**	**0**	-102,780
7-102 TOTAL	102,780	0	0	102,780	0	0	0	0	**102,780**	102,780	0	102,780	0	**102,780**	**0**	-102,780
7 - THERMAL / MOISTURE PROTECTION TOTAL	***102,780***	***0***	***0***	***102,780***	***0***	***0***	***0***	***0***	***102,780***	*102,780*	*0*	*102,780*	*0*	***102,780***	***0***	-102,780
14 - CONVEYING SYSTEMS																
14-001 Elevator																
Base	770,000	0	0	770,000	0	0	0	0	**770,000**	770,000	0	770,000	0	**770,000**	**0**	-770,000
14-001 TOTAL	770,000	0	0	770,000	0	0	0	0	**770,000**	770,000	0	770,000	0	**770,000**	**0**	-770,000
14 - CONVEYING SYSTEMS TOTAL	***770,000***	***0***	***0***	***770,000***	***0***	***0***	***0***	***0***	***770,000***	*770,000*	*0*	*770,000*	*0*	***770,000***	***0***	-770,000
16 - ELECTRICAL																
16-002 Early Site Electrical																
WAYNE J. GRIFFIN ELECTRIC, INC											256,000					
Base	393,500	0	0	393,500	0	0	0	0	**393,500**	393,500	256,000	393,500	0	**393,500**	**0**	-393,500
AT022-Temp Power Exploratory T&M	*0*	*0*	*855*	*855*	*0*	*0*	*0*	*0*	***855***	*855*	*0*	*855*	*0*	***855***	***0***	*-855*
AT026-Utility Road Pole Support	*0*	*0*	*7,907*	*7,907*	*0*	*0*	*0*	*0*	***7,907***	*7,907*	*0*	*7,907*	*0*	***7,907***	***0***	*-7,907*
CT006-F&D Precast Electrical Materia	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*16,860*	***16,860***	*0*	*0*	*0*	*16,860*	***16,860***	***0***	*-16,860*
CT008-RFI #7 Credit	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-4,925*	***-4,925***	*0*	*0*	*0*	*-4,925*	***-4,925***	***0***	*4,925*
HT008-Goat Path OH Line Protection	*0*	*0*	*87,171*	*87,171*	*0*	*0*	*0*	*0*	***87,171***	*87,171*	*87,171*	*87,171*	*0*	***87,171***	***0***	*-87,171*
16-002 TOTAL	393,500	0	95,933	489,433	0	0	0	11,935	**501,368**	489,433	343,171	489,433	11,935	**501,368**	**0**	-501,368
16 - ELECTRICAL TOTAL	***393,500***	***0***	***95,933***	***489,433***	***0***	***0***	***0***	***11,935***	***501,368***	*489,433*	*343,171*	*489,433*	*11,935*	***501,368***	***0***	-501,368
19 - CONTINGENCY																
19-001 Construction Contingency																
Base	1,061,170	0	0	1,061,170	0	0	0	0	**1,061,170**	0	0	0	1,061,170	**1,061,170**	**0**	-1,061,170
CT001-Reconcile Backstop & Netting	*0*	*0*	*-94,841*	*-94,841*	*0*	*0*	*0*	*0*	***-94,841***	*0*	*0*	*0*	*-94,841*	***-94,841***	***0***	*94,841*
CT003-Access Path DG Expansion	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-11,351*	***-11,351***	*0*	*0*	*0*	*-11,351*	***-11,351***	***0***	*11,351*
CT006-F&D Precast Electrical Materia	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-16,860*	***-16,860***	*0*	*0*	*0*	*-16,860*	***-16,860***	***0***	*16,860*
CT008-RFI #7 Credit	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*4,925*	***4,925***	*0*	*0*	*0*	*4,925*	***4,925***	***0***	*-4,925*
19-001 TOTAL	1,061,170	0	-94,841	966,329	0	0	0	-23,286	**943,043**	0	0	0	943,043	**943,043**	**0**	-943,043
19 - CONTINGENCY TOTAL	***1,061,170***	***0***	***-94,841***	***966,329***	***0***	***0***	***0***	***-23,286***	***943,043***	*0*	*0*	*0*	*943,043*	***943,043***	***0***	-943,043
24 - CONTRACT ALLOWANCES																
24-001 Survey -Layout- Allowance																
Base	130,000	0	0	130,000	0	0	0	0	**130,000**	0	0	0	130,000	**130,000**	**0**	-130,000
AT002-CorBuilt GPRS Utility Survey	*0*	*0*	*-6,670*	*-6,670*	*0*	*0*	*0*	*0*	***-6,670***	*0*	*0*	*0*	*-6,670*	***-6,670***	***0***	*6,670*
AT021-Survey Reconciliation - Oct 24	*0*	*0*	*-26,855*	*-26,855*	*0*	*0*	*0*	*0*	***-26,855***	*0*	*0*	*0*	*-26,855*	***-26,855***	***0***	*26,855*
AT025-Topsoil Screening	*0*	*0*	*-111,000*	*-111,000*	*0*	*0*	*0*	*0*	***-111,000***	*0*	*0*	*0*	*-111,000*	***-111,000***	***0***	*111,000*
AT034-Survey Reconciliation - Nov 24	*0*	*0*	*-11,305*	*-11,305*	*0*	*0*	*0*	*0*	***-11,305***	*0*	*0*	*0*	*-11,305*	***-11,305***	***0***	*11,305*
AT035-Foundation MEP Sleeves	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-15,597*	***-15,597***	*0*	*0*	*0*	*-15,597*	***-15,597***	***0***	*15,597*
AT038-Survey Reconciliation - Dec 24	*0*	*0*	*-10,333*	*-10,333*	*0*	*0*	*0*	*0*	***-10,333***	*0*	*0*	*0*	*-10,333*	***-10,333***	***0***	*10,333*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*90,990*	***90,990***	*0*	*0*	*0*	*90,990*	***90,990***	***0***	*-90,990*
24-001 TOTAL	130,000	0	-166,163	-36,163	0	0	0	75,393	**39,230**	0	0	0	39,230	**39,230**	**0**	-39,230
24-002 Winter Conditions- Allowance																
Base	325,000	0	0	325,000	0	0	0	0	**325,000**	0	0	0	325,000	**325,000**	**0**	-325,000
AT025-Topsoil Screening	*0*	*0*	*-25,000*	*-25,000*	*0*	*0*	*0*	*0*	***-25,000***	*0*	*0*	*0*	*-25,000*	***-25,000***	***0***	*25,000*
AT030-Winter Conditions #1	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-86,332*	***-86,332***	*0*	*0*	*0*	*-86,332*	***-86,332***	***0***	*86,332*
AT041-Winter Conditions #2 - Feb '25	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-177,911*	***-177,911***	*0*	*0*	*0*	*-177,911*	***-177,911***	***0***	*177,911*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*25,000*	***25,000***	*0*	*0*	*0*	*25,000*	***25,000***	***0***	*-25,000*
24-002 TOTAL	325,000	0	-25,000	300,000	0	0	0	-239,242	**60,758**	0	0	0	60,758	**60,758**	**0**	-60,758

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
24-003 Traffic Controls- Allowance																
Base	36,000	0	0	36,000	0	0	0	0	**36,000**	0	0	0	36,000	**36,000**	**0**	-36,000
AT008-OFR: East Access Road Ext.	*0*	*0*	*-20,000*	*-20,000*	*0*	*0*	*0*	*0*	***-20,000***	*0*	*0*	*0*	*-20,000*	***-20,000***	***0***	*20,000*
AT014-OFR: Tennis Stockpile Expansio	*0*	*0*	*-8,980*	*-8,980*	*0*	*0*	*0*	*0*	***-8,980***	*0*	*0*	*0*	*-8,980*	***-8,980***	***0***	*8,980*
AT022-Temp Power Exploratory T&M	*0*	*0*	*-855*	*-855*	*0*	*0*	*0*	*0*	***-855***	*0*	*0*	*0*	*-855*	***-855***	***0***	*855*
AT027-Temp Lighting at Gym Lot	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-6,134*	***-6,134***	*0*	*0*	*0*	*-6,134*	***-6,134***	***0***	*6,134*
AT028-F&I Softball Outfield Sod	*0*	*0*	*-6,165*	*-6,165*	*0*	*0*	*0*	*0*	***-6,165***	*0*	*0*	*0*	*-6,165*	***-6,165***	***0***	*6,165*
AT042-F&I Contractor Parking	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-12,271*	***-12,271***	*0*	*0*	*0*	*-12,271*	***-12,271***	***0***	*12,271*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*36,000*	***36,000***	*0*	*0*	*0*	*36,000*	***36,000***	***0***	*-36,000*
24-003 TOTAL	36,000	0	-36,000	0	0	0	0	17,594	**17,594**	0	0	0	17,594	**17,594**	**0**	-17,594
24-004 Added Dust Control- Allowance																
Base	50,000	0	0	50,000	0	0	0	0	**50,000**	0	0	0	50,000	**50,000**	**0**	-50,000
AT008-OFR: East Access Road Ext.	*0*	*0*	*-19,817*	*-19,817*	*0*	*0*	*0*	*0*	***-19,817***	*0*	*0*	*0*	*-19,817*	***-19,817***	***0***	*19,817*
AT010-ASI #1: Water Quality Units	*0*	*0*	*-30,183*	*-30,183*	*0*	*0*	*0*	*0*	***-30,183***	*0*	*0*	*0*	*-30,183*	***-30,183***	***0***	*30,183*
AT031-Ex. Football Field Soil & Demo	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-42,000*	***-42,000***	*0*	*0*	*0*	*-42,000*	***-42,000***	***0***	*42,000*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*50,000*	***50,000***	*0*	*0*	*0*	*50,000*	***50,000***	***0***	*-50,000*
24-004 TOTAL	50,000	0	-50,000	0	0	0	0	8,000	**8,000**	0	0	0	8,000	**8,000**	**0**	-8,000
24-005 Fire Details- Allowance																
Base	20,000	0	0	20,000	0	0	0	0	**20,000**	0	0	0	20,000	**20,000**	**0**	-20,000
AT018-BP #1 Hydroseeding	*0*	*0*	*-2,751*	*-2,751*	*0*	*0*	*0*	*0*	***-2,751***	*0*	*0*	*0*	*-2,751*	***-2,751***	***0***	*2,751*
AT028-F&I Softball Outfield Sod	*0*	*0*	*-17,249*	*-17,249*	*0*	*0*	*0*	*0*	***-17,249***	*0*	*0*	*0*	*-17,249*	***-17,249***	***0***	*17,249*
AT039-Utility Pole NGrid Shutdown	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-3,622*	***-3,622***	*0*	*0*	*0*	*-3,622*	***-3,622***	***0***	*3,622*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*20,000*	***20,000***	*0*	*0*	*0*	*20,000*	***20,000***	***0***	*-20,000*
24-005 TOTAL	20,000	0	-20,000	0	0	0	0	16,378	**16,378**	0	0	0	16,378	**16,378**	**0**	-16,378
24-006 Dewatering- Allowance																
Base	200,000	0	0	200,000	0	0	0	0	**200,000**	0	0	0	200,000	**200,000**	**0**	-200,000
AT004-ASI #1: ConCom Civil Revisions	*0*	*0*	*-147,739*	*-147,739*	*0*	*0*	*0*	*0*	***-147,739***	*0*	*0*	*0*	*-147,739*	***-147,739***	***0***	*147,739*
AT010-ASI #1: Water Quality Units	*0*	*0*	*-52,261*	*-52,261*	*0*	*0*	*0*	*0*	***-52,261***	*0*	*0*	*0*	*-52,261*	***-52,261***	***0***	*52,261*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*150,000*	***150,000***	*0*	*0*	*0*	*150,000*	***150,000***	***0***	*-150,000*
24-006 TOTAL	200,000	0	-200,000	0	0	0	0	150,000	**150,000**	0	0	0	150,000	**150,000**	**0**	-150,000
24-007 Street Sweeping- Allowance																
Base	20,000	0	0	20,000	0	0	0	0	**20,000**	0	0	0	20,000	**20,000**	**0**	-20,000
AT010-ASI #1: Water Quality Units	*0*	*0*	*-20,000*	*-20,000*	*0*	*0*	*0*	*0*	***-20,000***	*0*	*0*	*0*	*-20,000*	***-20,000***	***0***	*20,000*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*20,000*	***20,000***	*0*	*0*	*0*	*20,000*	***20,000***	***0***	*-20,000*
24-007 TOTAL	20,000	0	-20,000	0	0	0	0	20,000	**20,000**	0	0	0	20,000	**20,000**	**0**	-20,000
24-008 Temp. Water Bypass- Allowance																
Base	100,000	0	0	100,000	0	0	0	0	**100,000**	0	0	0	100,000	**100,000**	**0**	-100,000
AT006-Gate Valve at Utility Access	*0*	*0*	*-3,966*	*-3,966*	*0*	*0*	*0*	*0*	***-3,966***	*0*	*0*	*0*	*-3,966*	***-3,966***	***0***	*3,966*
AT007-DPW: Gate Valve at Vault Pit	*0*	*0*	*-7,322*	*-7,322*	*0*	*0*	*0*	*0*	***-7,322***	*0*	*0*	*0*	*-7,322*	***-7,322***	***0***	*7,322*
AT010-ASI #1: Water Quality Units	*0*	*0*	*-88,713*	*-88,713*	*0*	*0*	*0*	*0*	***-88,713***	*0*	*0*	*0*	*-88,713*	***-88,713***	***0***	*88,713*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*100,000*	***100,000***	*0*	*0*	*0*	*100,000*	***100,000***	***0***	*-100,000*
24-008 TOTAL	100,000	0	-100,000	0	0	0	0	100,000	**100,000**	0	0	0	100,000	**100,000**	**0**	-100,000
24-009 Temp. Sewer Bypass- Allowance																
Base	75,000	0	0	75,000	0	0	0	0	**75,000**	0	0	0	75,000	**75,000**	**0**	-75,000
AT005-ASI #1 - Parking Lot T&M	*0*	*0*	*-33,273*	*-33,273*	*0*	*0*	*0*	*0*	***-33,273***	*0*	*0*	*0*	*-33,273*	***-33,273***	***0***	*33,273*
AT010-ASI #1: Water Quality Units	*0*	*0*	*-25,056*	*-25,056*	*0*	*0*	*0*	*0*	***-25,056***	*0*	*0*	*0*	*-25,056*	***-25,056***	***0***	*25,056*
AT012-OFR: Added Temp Parking Spaces	*0*	*0*	*-16,671*	*-16,671*	*0*	*0*	*0*	*0*	***-16,671***	*0*	*0*	*0*	*-16,671*	***-16,671***	***0***	*16,671*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*75,000*	***75,000***	*0*	*0*	*0*	*75,000*	***75,000***	***0***	*-75,000*
24-009 TOTAL	75,000	0	-75,000	0	0	0	0	75,000	**75,000**	0	0	0	75,000	**75,000**	**0**	-75,000
24-010 Temp. Storm Relocation- Allow																
Base	50,000	0	0	50,000	0	0	0	0	**50,000**	0	0	0	50,000	**50,000**	**0**	-50,000
AT012-OFR: Added Temp Parking Spaces	*0*	*0*	*-16,501*	*-16,501*	*0*	*0*	*0*	*0*	***-16,501***	*0*	*0*	*0*	*-16,501*	***-16,501***	***0***	*16,501*
AT019-Stump Removal & Export	*0*	*0*	*-33,499*	*-33,499*	*0*	*0*	*0*	*0*	***-33,499***	*0*	*0*	*0*	*-33,499*	***-33,499***	***0***	*33,499*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*50,000*	***50,000***	*0*	*0*	*0*	*50,000*	***50,000***	***0***	*-50,000*
24-010 TOTAL	50,000	0	-50,000	0	0	0	0	50,000	**50,000**	0	0	0	50,000	**50,000**	**0**	-50,000

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
24-011 Video Inspections- Allowance																
Base	22,630	0	0	22,630	0	0	0	0	**22,630**	0	0	0	22,630	**22,630**	**0**	-22,630
AT014-OFR: Tennis Stockpile Expansio	*0*	*0*	*-3,557*	*-3,557*	*0*	*0*	*0*	*0*	***-3,557***	*0*	*0*	*0*	*-3,557*	***-3,557***	***0***	*3,557*
AT025-Topsoil Screening	*0*	*0*	*-18,364*	*-18,364*	*0*	*0*	*0*	*0*	***-18,364***	*0*	*0*	*0*	*-18,364*	***-18,364***	***0***	*18,364*
AT031-Ex. Football Field Soil & Demo	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-22,794*	***-22,794***	*0*	*0*	*0*	*-22,794*	***-22,794***	***0***	*22,794*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*22,630*	***22,630***	*0*	*0*	*0*	*22,630*	***22,630***	***0***	*-22,630*
24-011 TOTAL	22,630	0	-21,921	709	0	0	0	-164	**545**	0	0	0	545	**545**	**0**	-545
24-012 R&D UG Fuel Tanks- Allowance																
Base	25,000	0	0	25,000	0	0	0	0	**25,000**	0	0	0	25,000	**25,000**	**0**	-25,000
AT025-Topsoil Screening	*0*	*0*	*-32,750*	*-32,750*	*0*	*0*	*0*	*0*	***-32,750***	*0*	*0*	*0*	*-32,750*	***-32,750***	***0***	*32,750*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*25,000*	***25,000***	*0*	*0*	*0*	*25,000*	***25,000***	***0***	*-25,000*
24-012 TOTAL	25,000	0	-32,750	-7,750	0	0	0	25,000	**17,250**	0	0	0	17,250	**17,250**	**0**	-17,250
24-013 T&D Contaminated Soil- Allow																
Base	10,000	0	0	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
AT013-OTO Test Pit Excavation	*0*	*0*	*-4,805*	*-4,805*	*0*	*0*	*0*	*0*	***-4,805***	*0*	*0*	*0*	*-4,805*	***-4,805***	***0***	*4,805*
AT014-OFR: Tennis Stockpile Expansio	*0*	*0*	*-4,498*	*-4,498*	*0*	*0*	*0*	*0*	***-4,498***	*0*	*0*	*0*	*-4,498*	***-4,498***	***0***	*4,498*
AT028-F&I Softball Outfield Sod	*0*	*0*	*-697*	*-697*	*0*	*0*	*0*	*0*	***-697***	*0*	*0*	*0*	*-697*	***-697***	***0***	*697*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*5,195*	***5,195***	*0*	*0*	*0*	*5,195*	***5,195***	***0***	*-5,195*
24-013 TOTAL	10,000	0	-10,000	0	0	0	0	5,195	**5,195**	0	0	0	5,195	**5,195**	**0**	-5,195
24-014 Drilling-Blasting- Allowance																
Base	843,052	0	0	843,052	0	0	0	0	**843,052**	0	0	0	843,052	**843,052**	**0**	-843,052
AT001-TCD Water Main Ledge Removal	*0*	*0*	*-19,009*	*-19,009*	*0*	*0*	*0*	*0*	***-19,009***	*0*	*0*	*0*	*-19,009*	***-19,009***	***0***	*19,009*
AT009-Added Pre-Blast Surveys	*0*	*0*	*-18,769*	*-18,769*	*0*	*0*	*0*	*0*	***-18,769***	*0*	*0*	*0*	*-18,769*	***-18,769***	***0***	*18,769*
AT011-TCD Water Main Ledge Removal 2	*0*	*0*	*-39,189*	*-39,189*	*0*	*0*	*0*	*0*	***-39,189***	*0*	*0*	*0*	*-39,189*	***-39,189***	***0***	*39,189*
AT014-OFR: Tennis Stockpile Expansio	*0*	*0*	*-24,105*	*-24,105*	*0*	*0*	*0*	*0*	***-24,105***	*0*	*0*	*0*	*-24,105*	***-24,105***	***0***	*24,105*
AT015-Goat Path Ledge Removal	*0*	*0*	*-327,131*	*-327,131*	*0*	*0*	*0*	*0*	***-327,131***	*0*	*0*	*0*	*-327,131*	***-327,131***	***0***	*327,131*
AT019-Stump Removal & Export	*0*	*0*	*-145,274*	*-145,274*	*0*	*0*	*0*	*0*	***-145,274***	*0*	*0*	*0*	*-145,274*	***-145,274***	***0***	*145,274*
AT020-Utility Road Premium Time T&M	*0*	*0*	*-18,631*	*-18,631*	*0*	*0*	*0*	*0*	***-18,631***	*0*	*0*	*0*	*-18,631*	***-18,631***	***0***	*18,631*
AT024-Loading Dock Rock Removal	*0*	*0*	*-105,934*	*-105,934*	*0*	*0*	*0*	*0*	***-105,934***	*0*	*0*	*0*	*-105,934*	***-105,934***	***0***	*105,934*
AT025-Topsoil Screening	*0*	*0*	*-610,000*	*-610,000*	*0*	*0*	*0*	*0*	***-610,000***	*0*	*0*	*0*	*-610,000*	***-610,000***	***0***	*610,000*
AT026-Utility Road Pole Support	*0*	*0*	*-7,907*	*-7,907*	*0*	*0*	*0*	*0*	***-7,907***	*0*	*0*	*0*	*-7,907*	***-7,907***	***0***	*7,907*
AT032-Badger Vac for Ductbank	*0*	*0*	*-5,485*	*-5,485*	*0*	*0*	*0*	*0*	***-5,485***	*0*	*0*	*0*	*-5,485*	***-5,485***	***0***	*5,485*
AT043-Earthwork Material Credit	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*229,360*	***229,360***	*0*	*0*	*0*	*229,360*	***229,360***	***0***	*-229,360*
RB005-Pre-GMP #3: H/A Reconc.	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*478,382*	***478,382***	*0*	*0*	*0*	*478,382*	***478,382***	***0***	*-478,382*
24-014 TOTAL	843,052	0	-1,321,434	-478,382	0	0	0	707,742	**229,360**	0	0	0	229,360	**229,360**	**0**	-229,360
24-015 Dewatering - Allowance																
AT045-GeoT Sediment Pond	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-11,993*	***-11,993***	*0*	*0*	*0*	*-11,993*	***-11,993***	***0***	*11,993*
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*150,000*	*150,000*	*0*	*0*	*0*	*0*	***150,000***	*0*	*0*	*0*	*150,000*	***150,000***	***0***	*-150,000*
24-015 TOTAL	0	0	150,000	150,000	0	0	0	-11,993	**138,007**	0	0	0	138,007	**138,007**	**0**	-138,007
24-016 High Pressure Air - Allowance																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*138,500*	*138,500*	*0*	*0*	*0*	*0*	***138,500***	*0*	*0*	*0*	*138,500*	***138,500***	***0***	*-138,500*
24-016 TOTAL	0	0	138,500	138,500	0	0	0	0	**138,500**	0	0	0	138,500	**138,500**	**0**	-138,500
24-017 Additional Ground - Allowance																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*212,850*	*212,850*	*0*	*0*	*0*	*0*	***212,850***	*0*	*0*	*0*	*212,850*	***212,850***	***0***	*-212,850*
24-017 TOTAL	0	0	212,850	212,850	0	0	0	0	**212,850**	0	0	0	212,850	**212,850**	**0**	-212,850
24-018 Additional Casing - Allowance																
RB001-OAL 05 - BP#3 Geothermal RB	*0*	*0*	*167,700*	*167,700*	*0*	*0*	*0*	*0*	***167,700***	*0*	*0*	*0*	*167,700*	***167,700***	***0***	*-167,700*
24-018 TOTAL	0	0	167,700	167,700	0	0	0	0	**167,700**	0	0	0	167,700	**167,700**	**0**	-167,700
24-019 Add'l Concrete Win Con - Allow																
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*105,000*	*105,000*	*0*	*0*	*0*	*0*	***105,000***	*0*	*0*	*0*	*105,000*	***105,000***	***0***	*-105,000*
24-019 TOTAL	0	0	105,000	105,000	0	0	0	0	**105,000**	0	0	0	105,000	**105,000**	**0**	-105,000
24-020 Monument Sign. Footing - Allow																
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*10,000*	*10,000*	*0*	*0*	*0*	*0*	***10,000***	*0*	*0*	*0*	*10,000*	***10,000***	***0***	*-10,000*
24-020 TOTAL	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A Original Budget	B1 Approved Change Orders	B2 Approved Transfers	C (A+B) Current Budget	D1 Pending Change Orders (Verbal Okay)	D2 Pending Change Orders (Submitted)	D3 Pending Change Orders (Other)	D4 Pending Transfers	E (C+D) Projected Budget	F Total Committed	G JTD Cost Incurred	H Total Costs	I (J-H) Costs to Complete	J Total Anticipated Costs	K (E-J) Budget Variance	M Last Month vs. This Month
24-021 Add'l Concrete Pads - Allow																
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*15,000*	*15,000*	*0*	*0*	*0*	*0*	***15,000***	*0*	*0*	*0*	*15,000*	***15,000***	***0***	*-15,000*
24-021 TOTAL	0	0	15,000	15,000	0	0	0	0	**15,000**	0	0	0	15,000	**15,000**	**0**	-15,000
24-022 Add'l MEP Sleeves																
AT035-Foundation MEP Sleeves	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*-10,000*	***-10,000***	*0*	*0*	*0*	*-10,000*	***-10,000***	***0***	*10,000*
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*10,000*	*10,000*	*0*	*0*	*0*	*0*	***10,000***	*0*	*0*	*0*	*10,000*	***10,000***	***0***	*-10,000*
24-022 TOTAL	0	0	10,000	10,000	0	0	0	-10,000	**0**	0	0	0	0	**0**	**0**	0
24-023 Add'l Field Beam Pens - Allow																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*100,000*	*100,000*	*0*	*0*	*0*	*0*	***100,000***	*0*	*0*	*0*	*100,000*	***100,000***	***0***	*-100,000*
24-023 TOTAL	0	0	100,000	100,000	0	0	0	0	**100,000**	0	0	0	100,000	**100,000**	**0**	-100,000
24-024 CP&R Openings - Allow																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*317,500*	*317,500*	*0*	*0*	*0*	*0*	***317,500***	*0*	*0*	*0*	*317,500*	***317,500***	***0***	*-317,500*
24-024 TOTAL	0	0	317,500	317,500	0	0	0	0	**317,500**	0	0	0	317,500	**317,500**	**0**	-317,500
24-025 Mech Unit Support - Allow																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*108,000*	*108,000*	*0*	*0*	*0*	*0*	***108,000***	*0*	*0*	*0*	*108,000*	***108,000***	***0***	*-108,000*
24-025 TOTAL	0	0	108,000	108,000	0	0	0	0	**108,000**	0	0	0	108,000	**108,000**	**0**	-108,000
24-026 Mockups - Allowance																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*10,000*	*10,000*	*0*	*0*	*0*	*0*	***10,000***	*0*	*0*	*0*	*10,000*	***10,000***	***0***	*-10,000*
24-026 TOTAL	0	0	10,000	10,000	0	0	0	0	**10,000**	0	0	0	10,000	**10,000**	**0**	-10,000
24-027 Stair Leave Outs - Allow																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*35,000*	*35,000*	*0*	*0*	*0*	*0*	***35,000***	*0*	*0*	*0*	*35,000*	***35,000***	***0***	*-35,000*
24-027 TOTAL	0	0	35,000	35,000	0	0	0	0	**35,000**	0	0	0	35,000	**35,000**	**0**	-35,000
24-028 Joist Loading - Allowance																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*50,000*	*50,000*	*0*	*0*	*0*	*0*	***50,000***	*0*	*0*	*0*	*50,000*	***50,000***	***0***	*-50,000*
24-028 TOTAL	0	0	50,000	50,000	0	0	0	0	**50,000**	0	0	0	50,000	**50,000**	**0**	-50,000
24-029 Cut & Repair Decking - Allow																
RB003-OAL 07 - BP#3 SS	*0*	*0*	*109,500*	*109,500*	*0*	*0*	*0*	*0*	***109,500***	*0*	*0*	*0*	*109,500*	***109,500***	***0***	*-109,500*
24-029 TOTAL	0	0	109,500	109,500	0	0	0	0	**109,500**	0	0	0	109,500	**109,500**	**0**	-109,500
24-030 Add'l Opening Support - Allow																
RB004-OAL 08 - BP#3 Precast Plank	*0*	*0*	*44,400*	*44,400*	*0*	*0*	*0*	*0*	***44,400***	*0*	*0*	*0*	*44,400*	***44,400***	***0***	*-44,400*
24-030 TOTAL	0	0	44,400	44,400	0	0	0	0	**44,400**	0	0	0	44,400	**44,400**	**0**	-44,400
24-031 Wrap Seal Radon Pens - Allow																
RB002-OAL 06 - BP#3 Concrete	*0*	*0*	*20,000*	*20,000*	*0*	*0*	*0*	*0*	***20,000***	*0*	*0*	*0*	*20,000*	***20,000***	***0***	*-20,000*
24-031 TOTAL	0	0	20,000	20,000	0	0	0	0	**20,000**	0	0	0	20,000	**20,000**	**0**	-20,000
24 - CONTRACT ALLOWANCES TOTAL	***1,906,682***	***0***	***-524,818***	***1,381,864***	***0***	***0***	***0***	***988,901***	***2,370,766***	*0*	*0*	*0*	*2,370,766*	***2,370,766***	***0***	-2,370,766
25 - CONTRACTORS FEE																
25-001 Contractor's Fee																
25-001 TOTAL	1,048,403	0	0	1,048,403	0	0	-7,038	0	**1,041,365**	0	0	0	1,041,365	**1,041,365**	**0**	-1,041,365
25-999 Non-Reimbursable Cost																
EMILY RAMOS											19					
ETHAN TIEGER											54					
JOHN BONIN											43					
OLIVA' S, INC.											1,833					
SIEM YEBIO											17					
TRISTEN MOORE											4,934					
WILLIAM FERACO											136					
25-999 TOTAL	0	0	0	0	0	0	7,038	0	**7,038**	0	7,037	7,037	1	**7,038**	**0**	-7,038
25 - CONTRACTORS FEE TOTAL	***1,048,403***	***0***	***0***	***1,048,403***	***0***	***0***	***0***	***0***	***1,048,403***	*0*	*7,037*	*7,037*	*1,041,366*	***1,048,403***	***0***	-1,048,403
GMP TOTAL	**53,468,521**	**0**	**0**	**53,468,521**	**0**	**0**	**0**	**0**	**53,468,521**	**26,665,786**	**11,604,530**	**29,142,115**	**24,326,406**	**53,468,521**	**0**	**-53,468,521**
Job 2983 Total	53,468,521	0	0	53,468,521	0	0	0	0	**53,468,521**	26,665,786	11,604,530	29,142,115	24,326,406	53,468,521	0	-53,468,521

2983 Tri County Reg. Voc. Tech. HS

Anticipated Cost Report

	A	B1	B2	C	D1	D2	D3	D4	E	F	G	H	I	J	K	M
				(A+B)					(C+D)				(J-H)		(E-J)	
	Original Budget	Approved Change Orders	Approved Transfers	Current Budget	Pending Change Orders (Verbal Okay)	Pending Change Orders (Submitted)	Pending Change Orders (Other)	Pending Transfers	Projected Budget	Total Committed	JTD Cost Incurred	Total Costs	Costs to Complete	Total Anticipated Costs	Budget Variance	Last Month vs. This Month

Section 3 - Change Request Log

Change Request Log by Status

Consigli Construction Co., Inc. 03/07/25

2983 Tri County Reg. Voc. Tech. HS

Number	Date	Description	Amount	CO
CONTINGENCY GROUP				
Contingency				
Not issued				
CT005	01/30/25	Submittal #003300.001 Elevator Clarifications and Pier Revisions	0.00	
CT007	03/03/25	Submittal 033000-004.0 - Building D Foundation Revisions	0.00	
CT008	03/04/25	RFI #7 - Temporary Lighting Clarifications	0.00	
		Not issued Total	**0.00**	
Submitted				
CT003	01/28/25	Utility Corridor Dense Grade Expansion	0.00	
CT006	02/27/25	Prefab & Deliver Electrical Conduit/Boxes for Arch. Precast	0.00	
		Submitted Total	**0.00**	
Approved				
CT001	08/26/24	Submittal 323100-001.1: Softball Backstop & Netting Reconciliation	0.00	2
		Approved Total	**0.00**	
		Original Contingency Amount:	0.00	
		Approved Contingency Items:	0.00	
		Remaining Contingency Amount:	0.00	
		Pending Contingency Items:	0.00	
		CONTINGENCY GROUP TOTAL	**0.00**	
ALLOWANCES				
Allowance				
Not issued				
AT023	10/28/24	Unforeseen Loam Below Subgrade - T&M	0.00	
AT029	11/07/24	Probing for Rock at Main Geothermal Route	0.00	
AT033	01/22/25	Temporary Power Setup - T&M	0.00	
AT036	01/28/25	Added Drop Footings - Building A	0.00	
AT040	02/04/25	ASI #004 - Foundation Changes	0.00	
AT041	02/04/25	Winter Conditions through 2/28/2025 - T&M	0.00	
AT043	02/24/25	Site Enabling Earthwork Material Credit	0.00	
AT044	02/25/25	Temporary Access Path: Building A Concrete Pour	0.00	
AT046	03/04/25	Winter Conditions #3 - through 03/31/2025	0.00	
AT047	03/04/25	Survey Budget Reconciliation #4 - February 2025 - T&M	0.00	
AT048	03/05/25	Unforeseen Topsoil in Building Pad 2/20/25 through -	0.00	
		Not issued Total	**0.00**	
Submitted				
AT027	11/07/24	Temporary Lighting at Existing Gym Parking Lot	0.00	
AT030	11/19/24	Winter Conditions #1 through 1/31/2025 - T&M	0.00	
AT031	12/09/24	Existing Football Field Soils & Demo - T&M	0.00	
AT035	01/24/25	Foundation Wall MEP Sleeves Material	0.00	
AT039	02/08/25	National Grid Shutdown Reconciliation	0.00	
AT042	02/19/25	Furnish & Install Contractor Parking Lot	0.00	
AT045	02/26/25	Geothermal Sedimentation Basin	0.00	
		Submitted Total	**0.00**	
Approved				
AT001	08/16/24	Ledge Removal for Water Line Installation at Tri-County Drive - Unforeseen Condition - T&M	0.00	1
AT002	08/20/24	GPRS Utility Surveys for Excavation	0.00	1
AT004	08/16/24	ASI #001: Civil Revisions Subsequent to ConCom Comments	0.00	1
AT005	08/20/24	ASI #001: Associated Premium Time to Achieve Schedule - T&M	0.00	2
AT006	08/06/24	RFI #002: Added Gate Valve at Utility Access Road	0.00	1
AT007	08/06/24	RFI #005: Added Gate Valve at Vault Pit (DPW Requirement)	0.00	1
AT008	08/20/24	Owner Field Request: Temporary Access Road Extension (East Road)	0.00	1

2983 Tri County Reg. Voc. Tech. HS

Number	Date	Description	Amount	CO
ALLOWANCES (continued)				
Allowance (continued)				
Approved (continued)				
AT009	08/27/24	Additional Pre-Blast Surveys & Pre-Blast Notifications	0.00	4
AT010	09/05/24	ASI #001: Water Quality Units	0.00	2
AT011	09/05/24	Hoe Ram for Water Line Installation at Tri-County Drive #2 - Unforeseen Condition - T&M	0.00	2
AT012	09/25/24	Owner Field Request: Added Parking Spaces in West Lot - T&M	0.00	2
AT013	09/25/24	OTO Solar Field Test Pit Excavation - T&M	0.00	2
AT014	09/25/24	Owner Field Request: Tennis Court Stockpile Clearing and Expansion	0.00	5
AT015	09/25/24	Utility Access Path Ledge Removal	0.00	5
AT018	10/04/24	Hydroseeding & Stabilization - T&M	0.00	3
AT019	10/04/24	Stump Removal & Export - T&M	0.00	4
AT020	10/16/24	Utility Access Road Premium Time - T&M	0.00	5
AT021	10/16/24	Survey Budget Reconciliation - October 2024	0.00	3
AT022	10/28/24	Temporary Power Exploratory Investigation - T&M	0.00	3
AT024	10/28/24	Additional Foundation Blasting and Rock Removal	0.00	4
AT025	10/31/24	Topsoil Screening at Stockpile - Unforeseen Condition - T&M	0.00	6
AT026	11/06/24	Pole Support in Utility Access Corridor	0.00	3
AT028	11/07/24	Furnish & Install Softball Sod	0.00	4
AT032	12/18/24	Badger Vacuum for Electrical Ductbank Installation	0.00	5
AT034	01/21/25	Survey Budget Reconciliation #2 - November 2024 - T&M	0.00	6
AT038	01/28/25	Survey Budget Reconciliation #3 - December 2024 - T&M	0.00	6
		Approved Total	**0.00**	
		ALLOWANCES TOTAL	**0.00**	
HOLD TRANSFER				
Hold Transfer				
Not issued				
HT014	02/25/25	Submittal 200000-001: Additional Reinforcement for MEP Sleeves (Building A)	0.00	
HT015	02/25/25	Submittal 200000-002: Additional Reinforcement for MEP Sleeves (Buildings B&C)	0.00	
HT016	02/25/25	Submittal 200000-002: Additional Reinforcement for MEP Sleeves (Buildings D&E)	0.00	
HT017	02/25/25	ASI-006: Restaurant Canopy Column Revisions	0.00	
		Not issued Total	**0.00**	
Submitted				
HT011	01/03/25	Jersey Barrier Reconciliation through 1/31/2025	0.00	
HT013	02/25/25	AT031 Reconciliation: F&I Football Stockpile Fence	0.00	
		Submitted Total	**0.00**	
Approved				
HT001	08/02/24	OAL #2 Temporary Fencing Hold Reconciliation	0.00	1
HT002	08/16/24	Owner Field Request: Additional Temporary Fencing	0.00	2
HT003	09/05/24	Jersey Barrier Relocation Through November 2024	0.00	4
HT004	09/25/24	Owner Field Request: Stormwater Basin Fence Protection - T&M	0.00	2
HT005	09/25/24	Softball Field Fence Relocation - T&M	0.00	2
HT006	09/25/24	Temporary Jobsite Fence - T&M	0.00	4
HT007	09/25/24	Tennis Court Stockpile Fence Relocation	0.00	4
HT008	09/26/24	Utility Access Path - Overhead Wire Protection	0.00	2
HT009	09/26/24	Temporary Generator Enclosure & Sound Barrier	0.00	2
HT010	01/03/25	Temporary Fence Maintenance through 12/19/24	0.00	6
		Approved Total	**0.00**	
		HOLD TRANSFER TOTAL	**0.00**	

Section 4 - Holds, Contingencies, & Allowances Log

2983 Tri County Reg. Voc. Tech. HS

Hold/Contingency/Allowance Log

	A Original Budget	B Approved COs and Transfers	C Current Budget	D Pending	E (C+D-TotalCosts) Remaining Unallocated
PROJECT HOLDS					
2-976 Hold - Add'l Tests & Cleaning	0	45,000	45,000	0	45,000
2-977 Hold - Add'l Mobilizations	0	50,000	50,000	0	50,000
2-978 Hold - Concrete Pad over Vault	0	10,000	10,000	0	10,000
2-979 Hold - Add'l Verticality Tests	0	23,750	23,750	0	23,750
2-980 Hold - Additional Surveying	0	40,000	40,000	0	40,000
2-981 Hold - Vault Tie-Down Straps	0	15,000	15,000	0	15,000
2-982 Hold - Grout Backfill at Mains	0	10,000	10,000	0	10,000
2-983 Hold - DEP-NPDES Permit Fees	0	10,000	10,000	0	10,000
2-984 Hold - Sleeve Boxout at Fnds	0	6,000	6,000	0	6,000
2-985 Hold- Concrete Pad Above Vault	0	15,000	15,000	0	15,000
2-986 Hold - Install Tracer Wire	0	4,000	4,000	0	4,000
2-987 Hold - Sleeve at Fnd Wall	0	8,000	8,000	0	8,000
2-988 Hold - F&I Peastone	0	6,000	6,000	0	6,000
2-989 Hold - F&I Bentonite Chips	0	6,000	6,000	0	6,000
2-990 Temporary Fence- Hold	587,328	-587,328	0	75,097	75,097
2-991 F&I Jersey Barrier - HOLD	0	90,050	90,050	81,302	**144,516**
2-992 Temp Fence Maintenance - HOLD	0	3,977	3,977	36,905	40,882
2-993 Hold - F&I EZ Seal	0	3,000	3,000	0	3,000
2-994 Hold - NEMA3R Electrical	0	15,000	15,000	0	15,000
2-995 Hold - Add'll Sitework Coord.	0	20,000	20,000	0	20,000
2-996 Hold - Flushing Valves	0	30,000	30,000	0	30,000
2-997 Hold - Union Labor Support	0	87,200	87,200	0	87,200
2-998 Hold - Import Trench Sand	0	254,100	254,100	0	254,100
2-999 Hold - T&D Excess Trench	0	207,276	207,276	0	207,276
3-895 Hold - Bonding Agent	0	10,000	10,000	0	10,000
3-896 Hold - Plank Grouting	0	94,000	94,000	0	94,000
3-897 Hold - Grout Access Point	0	15,000	15,000	0	15,000
3-898 Hold - Add'l T&E	0	5,000	5,000	0	5,000
3-899 Hold - Stamped Erection Plans	0	10,000	10,000	0	10,000
3-994 Hold - Add'l Rebar Deliveries	0	25,000	25,000	-3,166	21,834
3-995 Hold - Undefined Embed Install	0	30,000	30,000	0	30,000
3-996 Hold - Wash-out Dumpster	0	10,000	10,000	0	10,000
3-997 Hold - Add'l B&G CW-PC Clips	0	75,000	75,000	0	75,000
3-998 Add'l Gym Slab Floor Prep	0	110,000	110,000	0	110,000
3-999 Hold - Add'l Floor Protection	0	40,000	40,000	0	40,000
5-990 Hold - Elevator Guiderails	0	20,000	20,000	0	20,000
5-991 Hold - Add'l Engineering	0	20,000	20,000	0	20,000
5-992 Hold - Post-Erection Survey	0	25,000	25,000	0	25,000
5-993 Hold - Abrasion Touchups	0	50,000	50,000	0	50,000
5-994 Hold - Uniformed Fire Watch	0	15,000	15,000	0	15,000
5-995 Hold - Add'l Trade Layout	0	40,000	40,000	0	40,000
5-996 Hold - Cable & Rail Removal	0	80,500	80,500	0	80,500
5-997 Hold - Blowoff Decks	0	17,328	17,328	0	17,328
5-998 Hold - Punchlist Stairs	0	30,000	30,000	0	30,000
5-999 Hold - Shop Weld Couplers	0	35,000	35,000	0	35,000
PROJECT HOLDS TOTAL	587,328	1,128,853	1,716,181	190,138	1,879,483
PROJECT CONTINGENCIES					
19-001 Construction Contingency	1,061,170	-94,841	966,329	-23,286	943,043
PROJECT CONTINGENCIES TOTAL	1,061,170	-94,841	966,329	-23,286	943,043
PROJECT ALLOWANCES					
24-001 Survey -Layout- Allowance	130,000	-166,163	-36,163	75,393	39,230
24-002 Winter Conditions- Allowance	325,000	-25,000	300,000	-239,242	60,758
24-003 Traffic Controls- Allowance	36,000	-36,000	0	17,594	17,594
24-004 Added Dust Control- Allowance	50,000	-50,000	0	8,000	8,000
24-005 Fire Details- Allowance	20,000	-20,000	0	16,378	16,378
24-006 Dewatering- Allowance	200,000	-200,000	0	150,000	150,000
24-007 Street Sweeping- Allowance	20,000	-20,000	0	20,000	20,000
24-008 Temp. Water Bypass- Allowance	100,000	-100,000	0	100,000	100,000
24-009 Temp. Sewer Bypass- Allowance	75,000	-75,000	0	75,000	75,000
24-010 Temp. Storm Relocation- Allow	50,000	-50,000	0	50,000	50,000
24-011 Video Inspections- Allowance	22,630	-21,921	709	-164	545

2983 Tri County Reg. Voc. Tech. HS

Hold/Contingency/Allowance Log

	A Original Budget	B Approved COs and Transfers	C Current Budget	D Pending	E (C+D-TotalCosts) Remaining Unallocated
PROJECT ALLOWANCES					
24-012 R&D UG Fuel Tanks- Allowance	25,000	-32,750	-7,750	25,000	17,250
24-013 T&D Contaminated Soil- Allow	10,000	-10,000	0	5,195	5,195
24-014 Drilling-Blasting- Allowance	843,052	-1,321,434	-478,382	707,742	229,360
24-015 Dewatering - Allowance	0	150,000	150,000	-11,993	138,007
24-016 High Pressure Air - Allowance	0	138,500	138,500	0	138,500
24-017 Additional Grout - Allowance	0	212,850	212,850	0	212,850
24-018 Additional Casing - Allowance	0	167,700	167,700	0	167,700
24-019 Add'l Concrete Win Con - Allow	0	105,000	105,000	0	105,000
24-020 Monument Sign. Footing - Allow	0	10,000	10,000	0	10,000
24-021 Add'l Concrete Pads - Allow	0	15,000	15,000	0	15,000
24-022 Add'l MEP Sleeves	0	10,000	10,000	-10,000	0
24-023 Add'l Field Beam Pens - Allow	0	100,000	100,000	0	100,000
24-024 CP&R Openings - Allow	0	317,500	317,500	0	317,500
24-025 Mech Unit Support - Allow	0	108,000	108,000	0	108,000
24-026 Mockups - Allowance	0	10,000	10,000	0	10,000
24-027 Stair Leave Outs - Allow	0	35,000	35,000	0	35,000
24-028 Joist Loading - Allowance	0	50,000	50,000	0	50,000
24-029 Cut & Repair Decking - Allow	0	109,500	109,500	0	109,500
24-030 Add'l Opening Support - Allow	0	44,400	44,400	0	44,400
24-031 Wrap Seal Radon Pens - Allow	0	20,000	20,000	0	20,000
PROJECT ALLOWANCES TOTAL	1,906,682	-524,818	1,381,864	988,901	2,370,766
Job 2983 Total	3,555,180	509,194	4,064,374	1,155,754	5,193,292

~**Bold** amounts indicate costs~

Section 5 - Requisition Summary Report

CONSIGLI

Requisition Summary

2983-01 - Tri County Reg. Voc. Tech. HS

Req/Inv Number	Invoice Date	Invoice Amount Current	Invoice Amount JTD	Retainage Current	Retainage JTD	Net Paid Current	Net Paid JTD		Date Paid	Days Outstdg
Contract: 2983-01	**Contract: Tri County Reg. Voc. Tech. HS**					Contract Value: Original:	**$53,468,521**		Revised:	**$53,468,521**
REQUISITIONS										
1	07/31/24	962,052.84	962,052.84	48,102.66	48,102.66	913,950.18	913,950.18	1.7%	09/03/24	33
2	08/31/24	1,323,107.87	2,285,160.71	66,155.40	114,258.06	1,256,952.47	2,170,902.65	4.1%	09/24/24	24
3	09/30/24	1,865,463.12	4,150,623.83	93,273.17	207,531.23	1,772,189.95	3,943,092.60	7.4%	10/21/24	21
4	10/31/24	1,915,870.15	6,066,493.98	95,793.52	303,324.75	1,820,076.63	5,763,169.23	10.8%	11/25/24	25
5	11/30/24	1,648,651.79	7,715,145.77	82,432.59	385,757.34	1,566,219.20	7,329,388.43	13.7%	12/26/24	26
6	12/31/24	1,221,315.97	8,936,461.74	61,065.80	446,823.14	1,160,250.17	8,489,638.60	15.9%	01/27/25	27
7	01/31/25	2,441,913.40	11,378,375.14	122,095.69	568,918.83	2,319,817.71	10,809,456.31	20.2%	03/03/25	31
TOTALS:						**Contract Value: Original:**	**$53,468,521**		**Revised:**	**$53,468,521**

REQUISITIONS:	**11,378,375.14**	**568,918.83**	**10,809,456.31**	**20.2%**
INVOICES:	**0.00**	**0.00**	**0.00**	Average Days Outstanding: 26.7
TOTAL:	**11,378,375.14**	**568,918.83**	**10,809,456.31**	

Section 6 - Schedule & Manpower Log

Daily Log Manpower Report

MANPOWER GRAPH

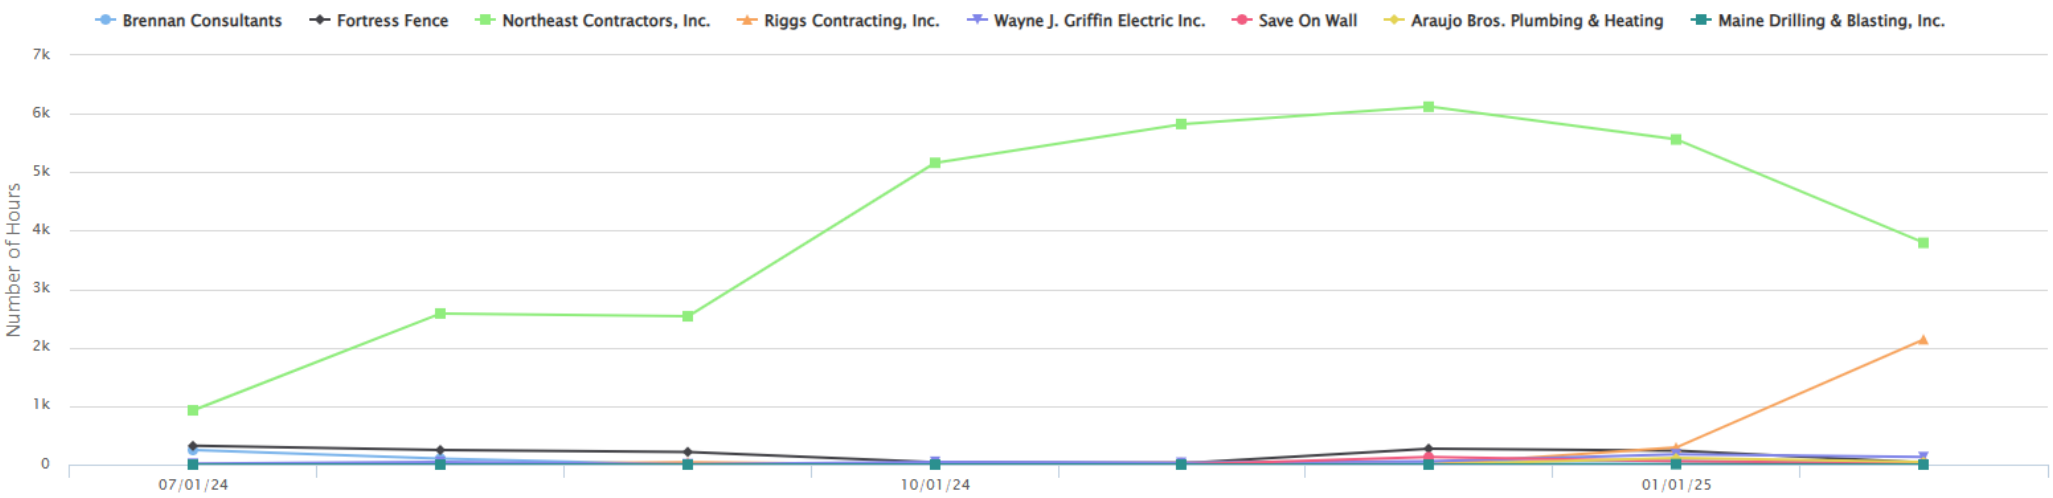

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
Tri-County Vocational Technical HS					
MILESTONES					
A1090	RFP Submitted	0d	0d	08-Mar-23 A	
A1100	Funding Approved (District Wide Vote)	0d	0d	24-Oct-23 A	
A1120	Start Construction [07-08-24]	0d	0d	08-Jul-24 A	
A1730	Issue Final Construction Documents	0d	0d		03-Mar-25
A1110	C of O [07/14/27]	0d	0d		14-Jul-27*
A1150	Fields / Landscaping Complete [08/10/2028]	0d	0d		10-Aug-28*
PROJECT MILESTONES					
A192650	First Foundation Complete	0d	0d		21-Mar-25
A192670	Start Structural Steel	0d	0d	27-May-25	
A1740	Start MEP Underground Rough-In	0d	0d	09-Jul-25	
A192680	Start MEP Overhead Rough-In	0d	0d	15-Sep-25	
A192660	Buyout Complete	0d	0d		19-Sep-25
A192700	Start Interior Finishes	0d	0d	06-Oct-25	
A192690	MEP Coordination Complete	0d	0d		23-Oct-25
A44100	CX Kick-Off Meeting / Establish Commissioning Schedule	0d	0d		23-Oct-25
A192710	Building Weather-Tight	0d	0d		13-Apr-26
A192730	Complete Vertical Transportation	0d	0d		08-Jul-26
A192560	Permanent Power Live	0d	0d		16-Sep-26
A192760	Building Commissioned	0d	0d		03-May-27
A192750	Owner Move In	0d	0d	26-Aug-27	
A1710	Project Closeout Complete	0d	0d		10-Aug-28
A192740	Finish Sitework	0d	0d		10-Aug-28
CONSTRUCTION MILESTONES					
Foundations / Structural					
A23900	Complete Foundations - Bldg A	0d	0d		21-Mar-25
A23910	Complete Foundations - Bldg B	0d	0d		31-Mar-25
A24110	Complete Damproofing - Bldg A	0d	0d		04-Apr-25
A24120	Complete Damproofing - Bldg B	0d	0d		10-Apr-25
A24160	Complete Foundation Backfill - Bldg A	0d	0d		11-Apr-25
A24170	Complete Foundation Backfill - Bldg B	0d	0d		15-Apr-25
A23920	Complete Foundations - Bldg C	0d	0d		21-May-25
A24340	Complete Mezz Precast Plank - Bldg A - East	0d	0d		30-May-25
A24350	Complete Mezz Precast Plank - Bldg B	0d	0d		03-Jun-25
A23930	Complete Foundations - Bldg D	0d	0d		04-Jun-25
A24130	Complete Damproofing - Bldg C	0d	0d		05-Jun-25
A24360	Complete Mezz Precast Plank - Bldg C	0d	0d		06-Jun-25
A24180	Complete Foundation Backfill - Bldg C	0d	0d		12-Jun-25
A24140	Complete Damproofing - Bldg D	0d	0d		16-Jun-25
A24190	Complete Foundation Backfill - Bldg D	0d	0d		19-Jun-25
A24380	Complete Mezz Precast Plank- Bldg D	0d	0d		19-Jun-25
A24370	Complete Mezz Precast Plank - Bldg E	0d	0d		30-Jun-25

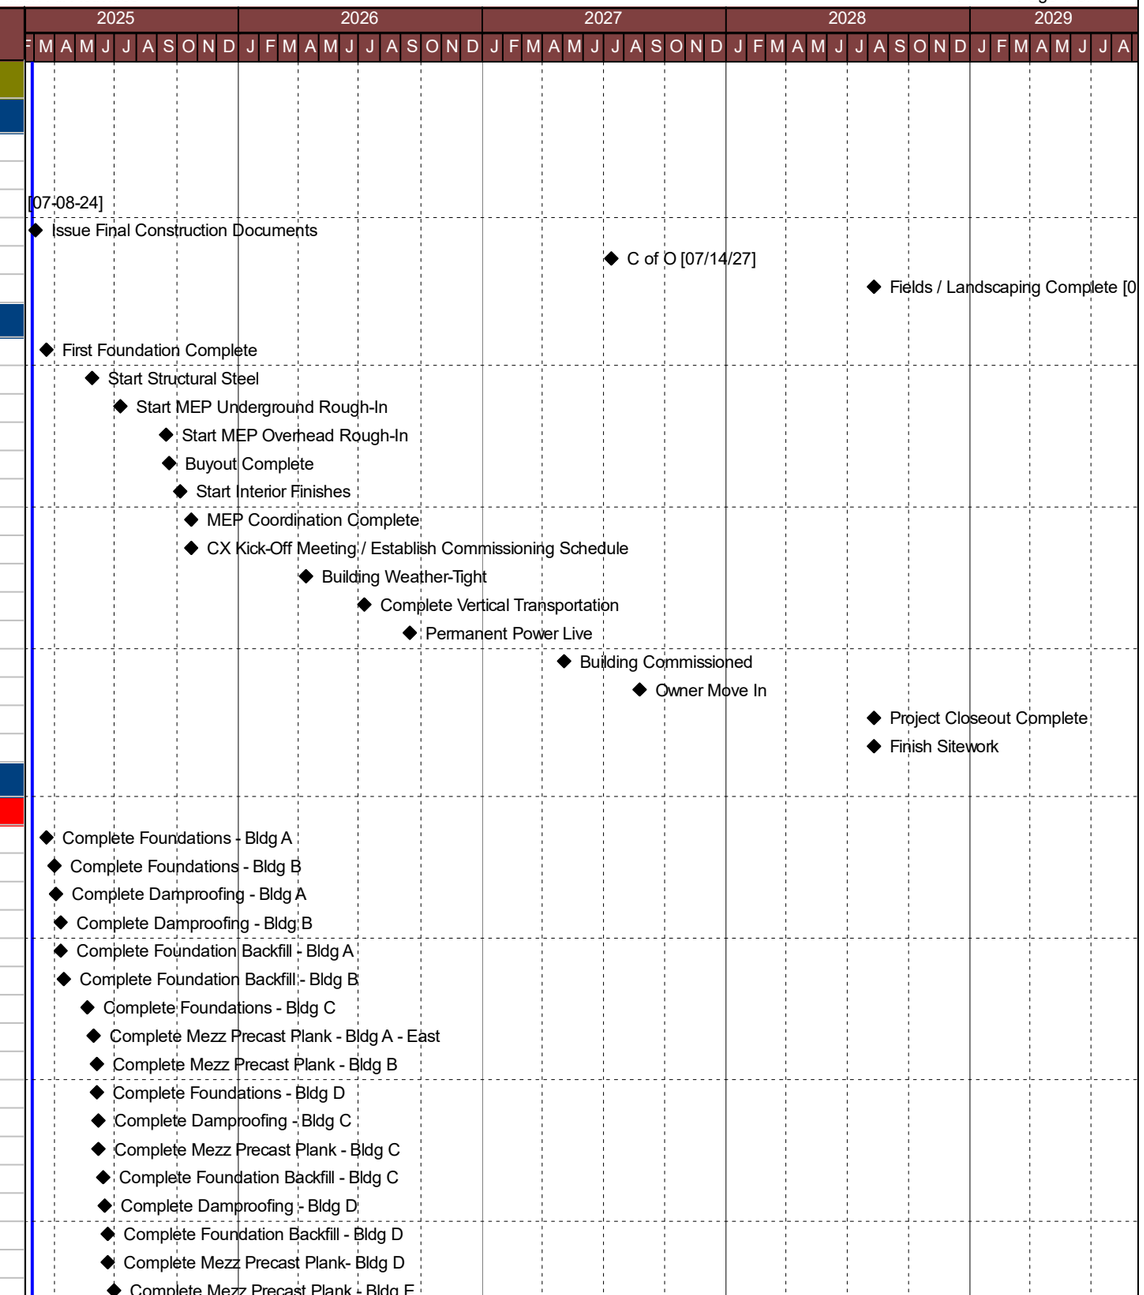

Start Date 02-Mar-23
Finish Date 05-Sep-28
Data Date 27-Feb-25
Run Date 28-Feb-25 14:56

© *Primavera Systems, Inc.*

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Consigli Construction Co., Inc.
Tri-County Vocational Technical HS
Project Schedule - Updated 27-Feb-25

CONSIGLI
Est. 1905

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A24210	Complete Steel Deck & Detail - Bldg A	0d	0d		08-Jul-25
A23940	Complete Foundations - Bldg E	0d	0d		11-Jul-25
A23950	Complete SOD - Bldg A	0d	0d		24-Jul-25
A24150	Complete Damproofing - Bldg E	0d	0d		25-Jul-25
A24220	Complete Steel Deck & Detail- Bldg B	0d	0d		25-Jul-25
A24070	Complete Mezz Topping Slab - Bldg A - East	0d	0d		29-Jul-25
A24200	Complete Foundation Backfill - Bldg E	0d	0d		01-Aug-25
A24240	Complete Steel Deck & Detail- Bldg D	0d	0d		04-Aug-25
A23960	Complete SOD - Bldg B - 2nd Fl	0d	0d		12-Aug-25
A24310	Complete Mezz Topping Slab - Bldg B	0d	0d		15-Aug-25
A24230	Complete Steel Deck & Detail- Bldg C	0d	0d		22-Aug-25
A24000	Complete SOD - Bldg B - 3rd Fl	0d	0d		27-Aug-25
A24250	Complete Steel Deck & Detail- Bldg E	0d	0d		04-Sep-25
A24010	Complete SOG - Bldg A	0d	0d		09-Sep-25
A23970	Complete SOD - Bldg C	0d	0d		10-Sep-25
A24020	Complete SOG - Bldg B	0d	0d		16-Sep-25
A24080	Complete Mezz Topping Slab - Bldg C	0d	0d		17-Sep-25
A23990	Complete SOD - Bldg E	0d	0d		22-Sep-25
A23980	Complete SOD - Bldg D	0d	0d		29-Sep-25
A24100	Complete Mezz Topping Slab - Bldg E	0d	0d		29-Sep-25
A24090	Complete Mezz Topping Slab- Bldg D	0d	0d		02-Oct-25
A24040	Complete SOG - Bldg C	0d	0d		06-Oct-25
A24060	Complete SOG - Bldg E	0d	0d		21-Oct-25
A24050	Complete SOG - Bldg D	0d	0d		28-Oct-25
Envelope					
A176620	External Framing, Sheathing & Window Blocking Complete - Building A	0d	0d		05-Aug-25
A192910	Facade Precast Complete - Building A	0d	0d		20-Aug-25
A176420	Masonry Facade Complete - Building A	0d	0d		27-Aug-25
A176470	Roofing Complete - Building A	0d	0d		17-Sep-25
A176640	Facade Precast Complete - Building C	0d	0d		18-Sep-25
A176660	Facade Precast Complete - Building E	0d	0d		02-Oct-25
A176650	External Framing, Sheathing & Window Blocking Complete - Building D	0d	0d		06-Oct-25
A192920	Facade Precast Complete - Building D	0d	0d		09-Oct-25
A176600	AVB Complete - Building D	0d	0d		14-Oct-25
A176480	Roofing Complete - Building B	0d	0d		16-Oct-25
A176450	Masonry Facade Complete - Building D	0d	0d		20-Oct-25
A176570	AVB Complete - Building A	0d	0d		21-Oct-25
A176560	Curtainwall / External Storefront Complete - Building E	0d	0d		24-Oct-25
A176630	External Framing, Sheathing & Window Blocking Complete - Building B	0d	0d		28-Oct-25
A176550	Curtainwall / External Storefront Complete - Building D	0d	0d		29-Oct-25
A176500	Roofing Complete - Building D	0d	0d		30-Oct-25
A176490	Roofing Complete - Building C	0d	0d		04-Nov-25
A176520	Curtainwall / External Storefront Complete - Building A	0d	0d		05-Nov-25
A176590	AVB Complete - Building C	0d	0d		07-Nov-25
A176540	Curtainwall / External Storefront Complete - Building C	0d	0d		01-Dec-25
A176510	Roofing Complete - Building E	0d	0d		04-Dec-25
A176580	AVB Complete - Building B	0d	0d		11-Dec-25
A176530	Curtainwall / External Storefront Complete - Building B	0d	0d		13-Apr-26
Interiors					
A175580	Drywall Complete - Building A 3rd Floor	0d	0d		09-Oct-25

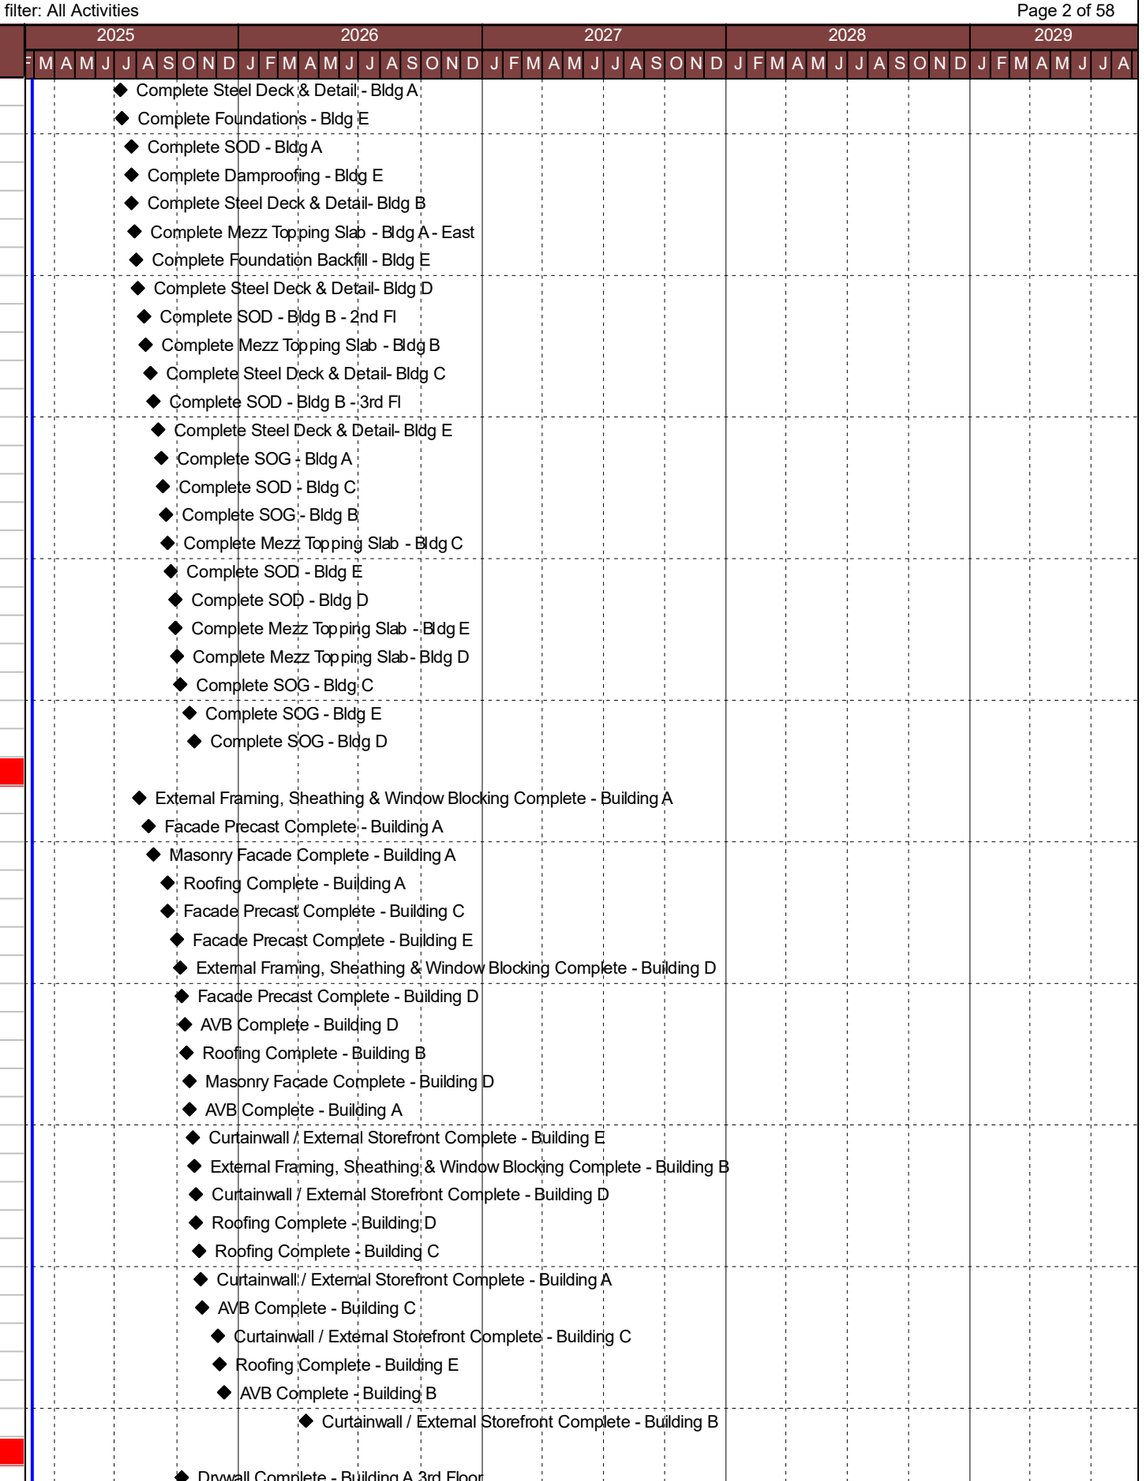

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A175750	Prime / 1st Coat Paint Complete - Building A 3rd Floor	0d	0d		10-Oct-25
A192930	Above Ceiling Inspections Complete - Building A 3rd Floor	0d	0d		24-Oct-25
A175380	MEP/FP OH Rough-In Complete - Building A 3rd Floor	0d	0d		17-Nov-25
A175420	MEP/FP OH Rough-In Complete - Building B 3rd Floor	0d	0d		12-Dec-25
A175430	MEP/FP OH Rough-In Complete - Building B 2nd Floor	0d	0d		06-Jan-26
A177260	MEP/FP OH Rough-In Complete - Building A 2ndFloor	0d	0d		06-Jan-26
A175400	MEP/FP OH Rough-In Complete - Building A 1st Floor	0d	0d		13-Jan-26
A175440	MEP/FP OH Rough-In Complete - Building B 1st Floor	0d	0d		21-Jan-26
A193390	Prime / 1st Coat Paint Complete - Auditorium	0d	0d		21-Jan-26
A193400	Prime / 1st Coat Paint Complete - Gym	0d	0d		21-Jan-26
A175590	Drywall Complete - Building A 2nd Floor	0d	0d		28-Jan-26
A175460	MEP/FP OH Rough-In Complete - Building C 2nd Floor	0d	0d		04-Feb-26
A175470	MEP/FP OH Rough-In Complete - Building C 1st Floor	0d	0d		19-Feb-26
A175620	Drywall Complete - Building B 3rd Floor	0d	0d		19-Feb-26
A175760	Prime / 1st Coat Paint Complete - Building A 2nd Floor	0d	0d		19-Feb-26
A193380	MEP/FP OH Rough-In Complete - Building D 2nd Floor	0d	0d		05-Mar-26
A175790	Prime / 1st Coat Paint Complete - Building B 3rd Floor	0d	0d		12-Mar-26
A175500	MEP/FP OH Rough-In Complete - Building D 1st Floor	0d	0d		19-Mar-26
A175520	MEP/FP OH Rough-In Complete - Building E 2nd Floor	0d	0d		19-Mar-26
A175630	Drywall Complete - Building B 2nd Floor	0d	0d		19-Mar-26
A175930	Above Ceiling Inspections Complete - Building A 2nd Floor	0d	0d		25-Mar-26
A175610	Drywall Complete - Building B 1st Floor	0d	0d		06-Apr-26
A176100	Casework / Millwork Complete - Building A 2nd Floor	0d	0d		07-Apr-26
A175800	Prime / 1st Coat Paint Complete - Building B 2nd Floor	0d	0d		09-Apr-26
A176020	Above Ceiling Inspections Complete - Building B 3rd Floor	0d	0d		10-Apr-26
A175780	Prime / 1st Coat Paint Complete - Building B 1st Floor	0d	0d		13-Apr-26
A175530	MEP/FP OH Rough-In Complete - Building E 1st Floor	0d	0d		16-Apr-26
A192980	Drywall Complete - Building C 1st Floor	0d	0d		16-Apr-26
A175840	Prime / 1st Coat Paint Complete - Building C 1st Floor	0d	0d		23-Apr-26
A177870	Controls Complete - Main Mechanical Room	0d	0d		23-Apr-26
A176120	Casework / Millwork Complete - Building B 3rd Floor	0d	0d		24-Apr-26
A175740	Prime / 1st Coat Paint Complete - Building A 1st Floor	0d	0d		01-May-26
A175560	High Ceiling MEPs Complete - Auditorium	0d	0d		08-May-26
A175690	Drywall Complete - Building D 2nd Floor	0d	0d		08-May-26
A175860	Prime / 1st Coat Paint Complete - Building D 2nd Floor	0d	0d		11-May-26
A175970	Above Ceiling Inspections Complete - Building B 2nd Floor	0d	0d		11-May-26
A175980	Above Ceiling Inspections Complete - Building B 1st Floor	0d	0d		11-May-26
A176270	Flooring Complete - Building A 2nd Floor	0d	0d		12-May-26
A176010	Above Ceiling Inspections Complete - Building C 1st Floor	0d	0d		13-May-26
A175660	Drywall Complete - Building C 2nd Floor	0d	0d		14-May-26
A176030	Above Ceiling Inspections Complete - Building D 2nd Floor	0d	0d		19-May-26
A176080	Casework / Millwork Complete - Building A 1st Floor	0d	0d		20-May-26
A175830	Prime / 1st Coat Paint Complete - Building C 2nd Floor	0d	0d		22-May-26
A176130	Casework / Millwork Complete - Building B 2nd Floor	0d	0d		22-May-26
A24320	Complete Elevator #1 - Bldg A	0d	0d		27-May-26
A175720	Drywall Complete - Building E 2nd Floor	0d	0d		28-May-26
A175940	Above Ceiling Inspections Complete - Building A 1st Floor	0d	0d		29-May-26
A176300	Flooring Complete - Building B 3rd Floor	0d	0d		01-Jun-26
A175890	Prime / 1st Coat Paint Complete - Building E 2nd Floor	0d	0d		05-Jun-26
A193310	Flooring Complete - Building B 2nd Floor	0d	0d		15-Jun-26

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A176150	Casework / Millwork Complete - Building B 1st Floor	0d	0d		17-Jun-26
A176290	Flooring Complete - Building B 1st Floor	0d	0d		24-Jun-26
A175600	Drywall Complete - Building A 1st Floor	0d	0d		29-Jun-26
A176050	Above Ceiling Inspections Complete - Building E 2nd Floor	0d	0d		30-Jun-26
A175990	Above Ceiling Inspections Complete - Building C 2nd Floor	0d	0d		02-Jul-26
A175730	Drywall Complete - Building E 1st Floor	0d	0d		06-Jul-26
A24330	Complete Elevator #2 - Bldg D	0d	0d		08-Jul-26
A175700	Drywall Complete - Building D 1st Floor	0d	0d		09-Jul-26
A176070	Above Ceiling Inspections Complete - Building E 1st Floor	0d	0d		10-Jul-26
A175900	Prime / 1st Coat Paint Complete - Building E 1st Floor	0d	0d		13-Jul-26
A192940	Casework / Millwork Complete - Building C 2nd Floor	0d	0d		15-Jul-26
A175870	Prime / 1st Coat Paint Complete - Building D 1st Floor	0d	0d		17-Jul-26
A193370	Flooring Complete - Building E 2nd Floor	0d	0d		21-Jul-26
A176160	Casework / Millwork Complete - Building C 1st Floor	0d	0d		05-Aug-26
A176040	Above Ceiling Inspections Complete - Building D 1st Floor	0d	0d		06-Aug-26
A193330	Flooring Complete - Building C 2nd Floor	0d	0d		11-Aug-26
A192970	Casework / Millwork Complete - Building D 2nd Floor	0d	0d		12-Aug-26
A193350	Flooring Complete - Building D 2nd Floor	0d	0d		18-Aug-26
A192950	Casework / Millwork Complete - Building E 2nd Floor	0d	0d		26-Aug-26
A193320	Flooring Complete - Building C 1st Floor	0d	0d		08-Sep-26
A176210	Casework / Millwork Complete - Building D 1st Floor	0d	0d		14-Sep-26
A176260	Flooring Complete - Building A 3rd Floor	0d	0d		22-Sep-26
A192960	Casework / Millwork Complete - Building E 1st Floor	0d	0d		22-Sep-26
A193300	Flooring Complete - Building A 1st Floor	0d	0d		22-Sep-26
A193340	Flooring Complete - Building D 1st Floor	0d	0d		23-Sep-26
A193360	Flooring Complete - Building E 1st Floor	0d	0d		24-Sep-26
A175770	Low Voltage Start-up / Programming / Testing Complete	0d	0d		03-May-27
Demoltion & Abatement					
A193410	Complete Demoltion & Abatement	0d	0d		15-Dec-27
Fields					
A193420	Geothermal Well Drilling & Laterials Complete	0d	0d		25-Aug-25
A193430	Under-Field Drainage, Track / Soccer (Northwest)	0d	0d		23-Sep-25
A193440	Track & Sod Complete Track / Soccer (Northwest)	0d	0d		29-Oct-25
A193450	Field Complete Track / Soccer (Northwest)	0d	0d		15-May-26
A193490	Light Pole Bases & Under Conduit Complete, Entry Drive	0d	0d		08-Jul-27
A193460	Subgrade & Collector Drain Complete, Baseball	0d	0d		15-Jul-27
A193500	Binder Complete, Entry Drive	0d	0d		18-Aug-27
A193470	Athletic Top Soil & Infield Complete, Baseball	0d	0d		26-Aug-27
A193510	Line Striping Complete, Entry Drive	0d	0d		26-Aug-27
A193480	Field Complete, Baseball	0d	0d		10-Sep-27
A193520	Infiltration System Complete, Central Parking	0d	0d		31-Dec-27
A193570	Subgrade & Collector Drain Complete, Football	0d	0d		12-Jan-28
A193640	Light Pole Bases & Under Conduit Complete, Central Parking	0d	0d		24-Jan-28
A193610	Subgrade & Collector Drain Complete, Multi-Purpose	0d	0d		10-Feb-28
A193620	Athletic Top Soil Complete, Multi-Purpose	0d	0d		27-Mar-28
A193580	Athletic Top Soil Complete, Football	0d	0d		30-Mar-28
A193670	Seeding Complete, Multi-Purpose	0d	0d		03-Apr-28
A193600	Press Box & Bleachers Complete, Football	0d	0d		14-Apr-28
A193650	Binder Complete, Central Parking	0d	0d		26-Apr-28
A193590	Field Complete, Football	0d	0d		18-May-28

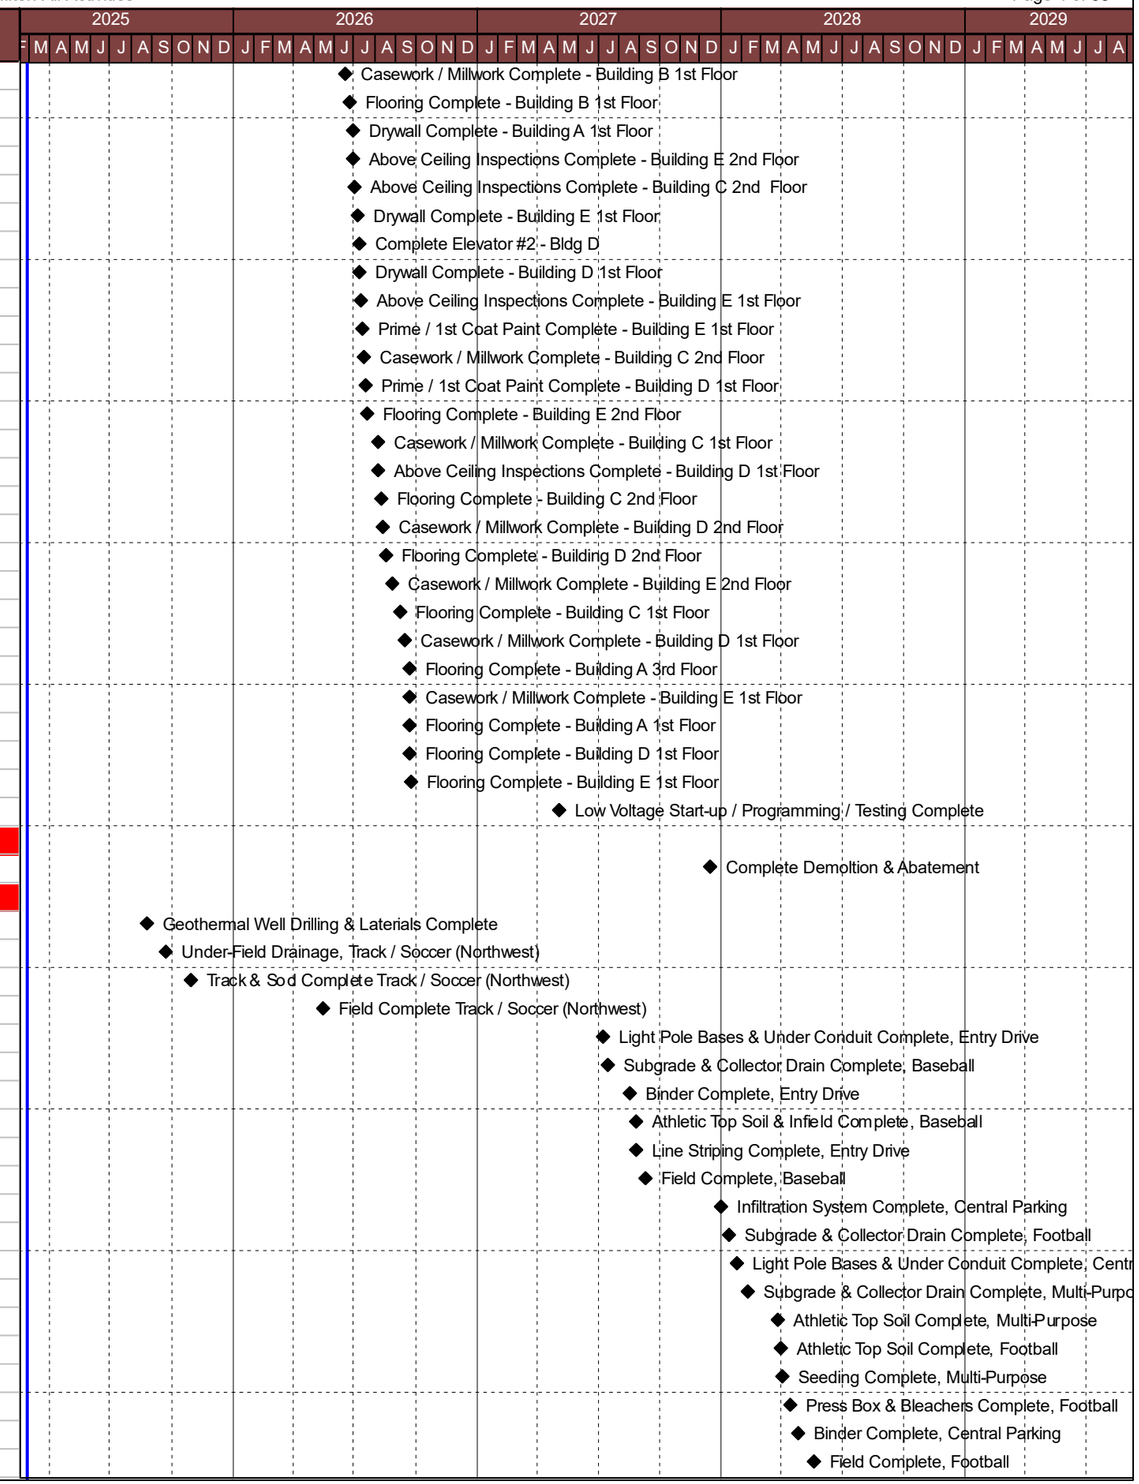

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A193660	Line Striping Complete, Central Parking	0d	0d		24-May-28
A193630	Field Complete, Multi-Purpose	0d	0d		09-Aug-28
ACADEMIC CALENDAR					
A49320	First Day of School - 2024	0d	0d	03-Sep-24 A	
A49330	Thanksgiving Break - 2024	4d	0d	28-Nov-24 A	01-Dec-24 A
A49340	December Vacation - 2024-2025	12d	0d	21-Dec-24 A	01-Jan-25 A
A49350	February Vacation - 2025	9d	0d	15-Feb-25 A	23-Feb-25 A
A49750	MCAS	2d	2d	25-Mar-25*	26-Mar-25
A49360	April Vacation - 2025	10d	10d	18-Apr-25*	27-Apr-25
A49790	MCAS	2d	2d	20-May-25*	21-May-25
A191030	MCAS	2d	2d	04-Jun-25*	05-Jun-25
A49370	Last Day of School - 2025 (TBD)	0d	0d	17-Jun-25*	
A49380	First Day of School - 2025	0d	0d	02-Sep-25*	
A49390	Thanksgiving Break - 2025	4d	4d	27-Nov-25*	30-Nov-25
A49400	December Vacation - 2025-2026	13d	13d	20-Dec-25*	01-Jan-26
A49410	February Vacation - 2026	9d	9d	14-Feb-26*	22-Feb-26
A49420	April Vacation - 2026	10d	10d	17-Apr-26*	26-Apr-26
A49430	Last Day of School - 2026 (TBD)	0d	0d	16-Jun-26*	
A49440	First Day of School - 2026	0d	0d	08-Sep-26*	
A49450	Thanksgiving Break - 2026	4d	4d	26-Nov-26*	29-Nov-26
A49460	December Vacation - 2026-2027	14d	14d	19-Dec-26*	01-Jan-27
A49470	February Vacation - 2027	9d	9d	13-Feb-27*	21-Feb-27
A49480	April Vacation - 2027	10d	10d	16-Apr-27*	25-Apr-27
A49490	Last Day of School - 2027 (TBD)	0d	0d	17-Jun-27*	
A49500	First Day of School - 2027	0d	0d	07-Sep-27*	
A49510	Thanksgiving Break - 2027	4d	4d	25-Nov-27*	28-Nov-27
A49520	December Vacation - 2027-2028	12d	12d	21-Dec-27*	01-Jan-28
A49530	February Vacation - 2028	9d	9d	12-Feb-28*	20-Feb-28
A49540	April Vacation - 2028	10d	10d	14-Apr-28*	23-Apr-28
A49550	Last Day of School - 2028 (TBD)	0d	0d	16-Jun-28*	
A49560	First Day of School - 2028	0d	0d	05-Sep-28*	
SCHEDULE IMPACTS					
Weather Impacts					
A192800	Snow, Rain, Ice (all operations) 02/18/25 - 02/19/25	2d	0d	18-Feb-25 A	19-Feb-25 A
CR004 - Owner Field Request - Temporary Maintenance Access Road Extension					
A10590	Owner & CCC Walk for Egress Analysis	1d	0d	05-Aug-24 A	05-Aug-24 A
A10600	Develop Pricing - CR004	5d	0d	06-Aug-24 A	23-Aug-24 A
A10610	Review & Approve Pricing - CR004	2d	0d	23-Aug-24 A	26-Aug-24 A
ConComm Delays					
A10640	ConComm Delay (Order of Conditions)	37d	0d	24-Jun-24 A	15-Aug-24 A
A10650	Implement Order of Conditions	14d	0d	16-Aug-24 A	12-Sep-24 A
Addition of Geothermal (delays HVAC Bidding)					
A10660	Addition of Geothermal (delays HVAC Bidding)	0d	0d	22-Aug-24 A	
Unforeseen Ledge at Utility Corridor					
A23580	Unforeseen Ledge at Utility Corridor	1d	0d	12-Sep-24 A	12-Sep-24 A
A23590	Coordination & Mobilization of Maine Drilling & Blasting	5d	0d	13-Sep-24 A	20-Sep-24 A
Stop Work Order for 6" Material					
A192820	Stop Work Order for 6" Material Received on 02/06/25 at 11:09am	0d	0d	06-Feb-25 A	
A192830	3rd Party Testing Took Samples of Material to Run Testing	0d	0d	12-Feb-25 A	

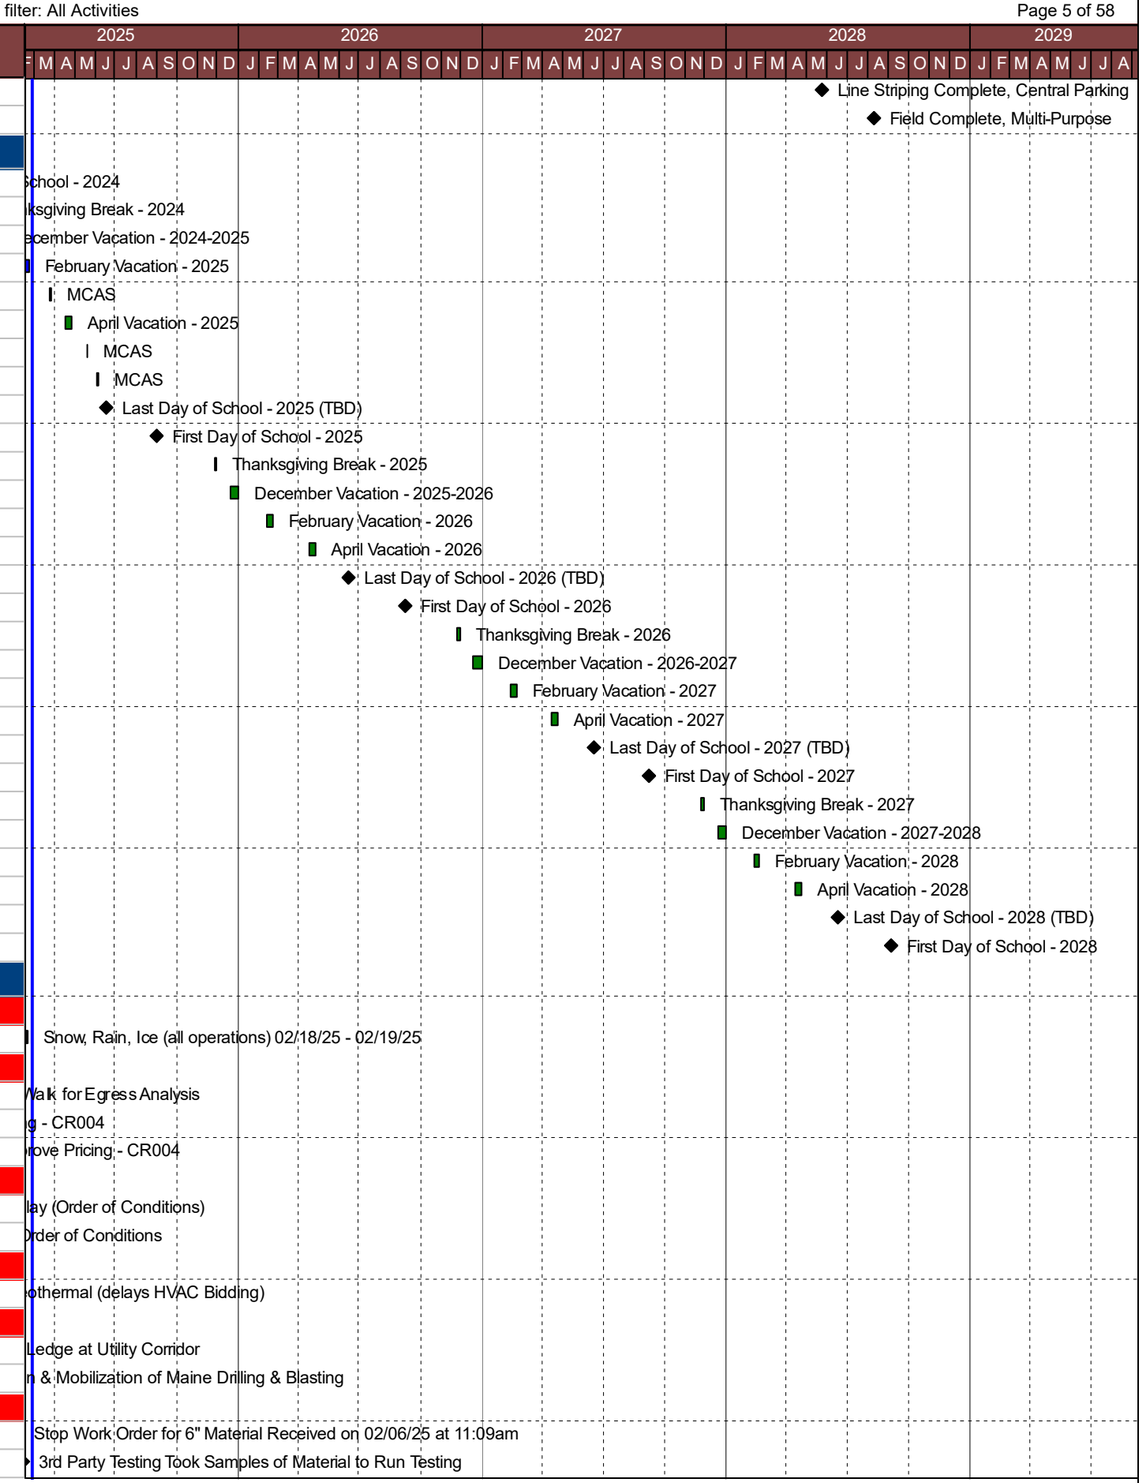

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A192840	Meeting to Review Path Forward	0d	0d	18-Feb-25 A	
A192850	CCC Met with NCI to Review Options and Provided Response Email	1d	0d	21-Feb-25 A	21-Feb-25 A
A192860	OTO Back On Site to Review Backfill Operations	1d	0d	26-Feb-25 A	26-Feb-25 A
A192870	2nd Meeting to Review Path Forward	0d	0d	04-Mar-25*	
Site Thaw, Melting and Mud					
A192810	Site Thaw, Melting & Mud - Starting 02/24/25	0d	0d	24-Feb-25 A	
A192880	Concrete Placement Canceled - 02/26/25	0d	0d	26-Feb-25 A	
A192900	Site Crew Diveted From Footing Excavation to Mucking	2d	1d	26-Feb-25 A	27-Feb-25
A192890	Concrete Placement Canceled - 02/28/25	0d	0d	28-Feb-25	
DESIGN / PRECONSTRUCTION					
Schematic Design					
A6890	Schematic Design	54d	0d	02-Mar-23 A	17-May-23 A
A6900	SD Estimate / Reconciliation / VE	19d	0d	18-May-23 A	15-Jun-23 A
Design Development					
A1790	Design Development	133d	0d	31-Aug-23 A	14-Mar-24 A
A2040	DD Estimate / Reconciliation / VE	23d	0d	15-Mar-24 A	17-Apr-24 A
Construction Documents					
A2050	60% Construction Documents	97d	0d	15-Mar-24 A	28-Aug-24 A
A2080	Issue Early Release Package #1 - Sitework Enabling	0d	0d	08-May-24 A	
A8810	Issue Early Release Package #2 - Precast Design Assist	0d	0d	08-Jul-24 A	
A2060	60% CD Estimate	14d	0d	29-Aug-24 A	20-Sep-24 A
A1800	90% Construction Documents	48d	0d	29-Aug-24 A	13-Nov-24 A
A2280	60% Estimate Reconciliation	3d	0d	23-Sep-24 A	24-Sep-24 A
A2450	Issue Bid Package #3 - Foundations / Steel / Sitework for Foundations / Geothermal	0d	0d	16-Oct-24 A	
A185340	Issue Bid Package #4 - Waterproofing	0d	0d	28-Oct-24 A	
A185350	Issue Bid Package #5 - Elevators	0d	0d	28-Oct-24 A	
A1870	90% CD Estimate	13d	0d	14-Nov-24 A	03-Dec-24 A
A2210	Bid Documents - Bid Package #7	79d	3d	14-Nov-24 A	03-Mar-25
A1810	90% CD Estimate Reconciliation / VE	2d	0d	04-Dec-24 A	05-Dec-24 A
A7830	Issue Bid Package #6 - Switchgear & Generator	0d	0d	24-Jan-25 A	
A10620	Issue Bid Package #8 - HVAC	0d	0d	03-Apr-25*	
GMP					
A2270	Bidding	16d	16d	04-Mar-25	25-Mar-25
A2250	Develop GMP	12d	12d	26-Mar-25	10-Apr-25
A2260	Review & Approve GMP	10d	10d	11-Apr-25	25-Apr-25
PERMITTING					
A8720	Approval from Planning/ConComm/Building Inspector	0d	0d	24-Jun-24 A	
A8710	July Hearing - Planning/ConComm/Building Inspector/ Town Engineer	0d	0d	08-Jul-24 A	
ConComm Meetings (meetings 1st & 3rd meetings of every month - typ 3-4 month process)					
A1780	NOI Submitted	0d	0d	21-Mar-24 A	
A1820	NOI Peer Review	5d	0d	21-Mar-24 A	27-Mar-24 A
A1830	First NOI Hearing	0d	0d	18-Apr-24 A	
A1840	SW Work Session	0d	0d	25-Apr-24 A	
A1850	Wetlands Work Session	0d	0d	02-May-24 A	
A1860	May Hearing (likely to continue to address peer review)	0d	0d	02-May-24 A	
A8610	May Hearing	0d	0d	16-May-24 A	
A8620	June Hearing (may continue based on speed of 2nd peer review)	0d	0d	13-Jun-24 A	
A8650	ConComm Order of Conditions	22d	0d	24-Jun-24 A	15-Aug-24 A
A8630	June Hearing	0d	0d	27-Jun-24 A	

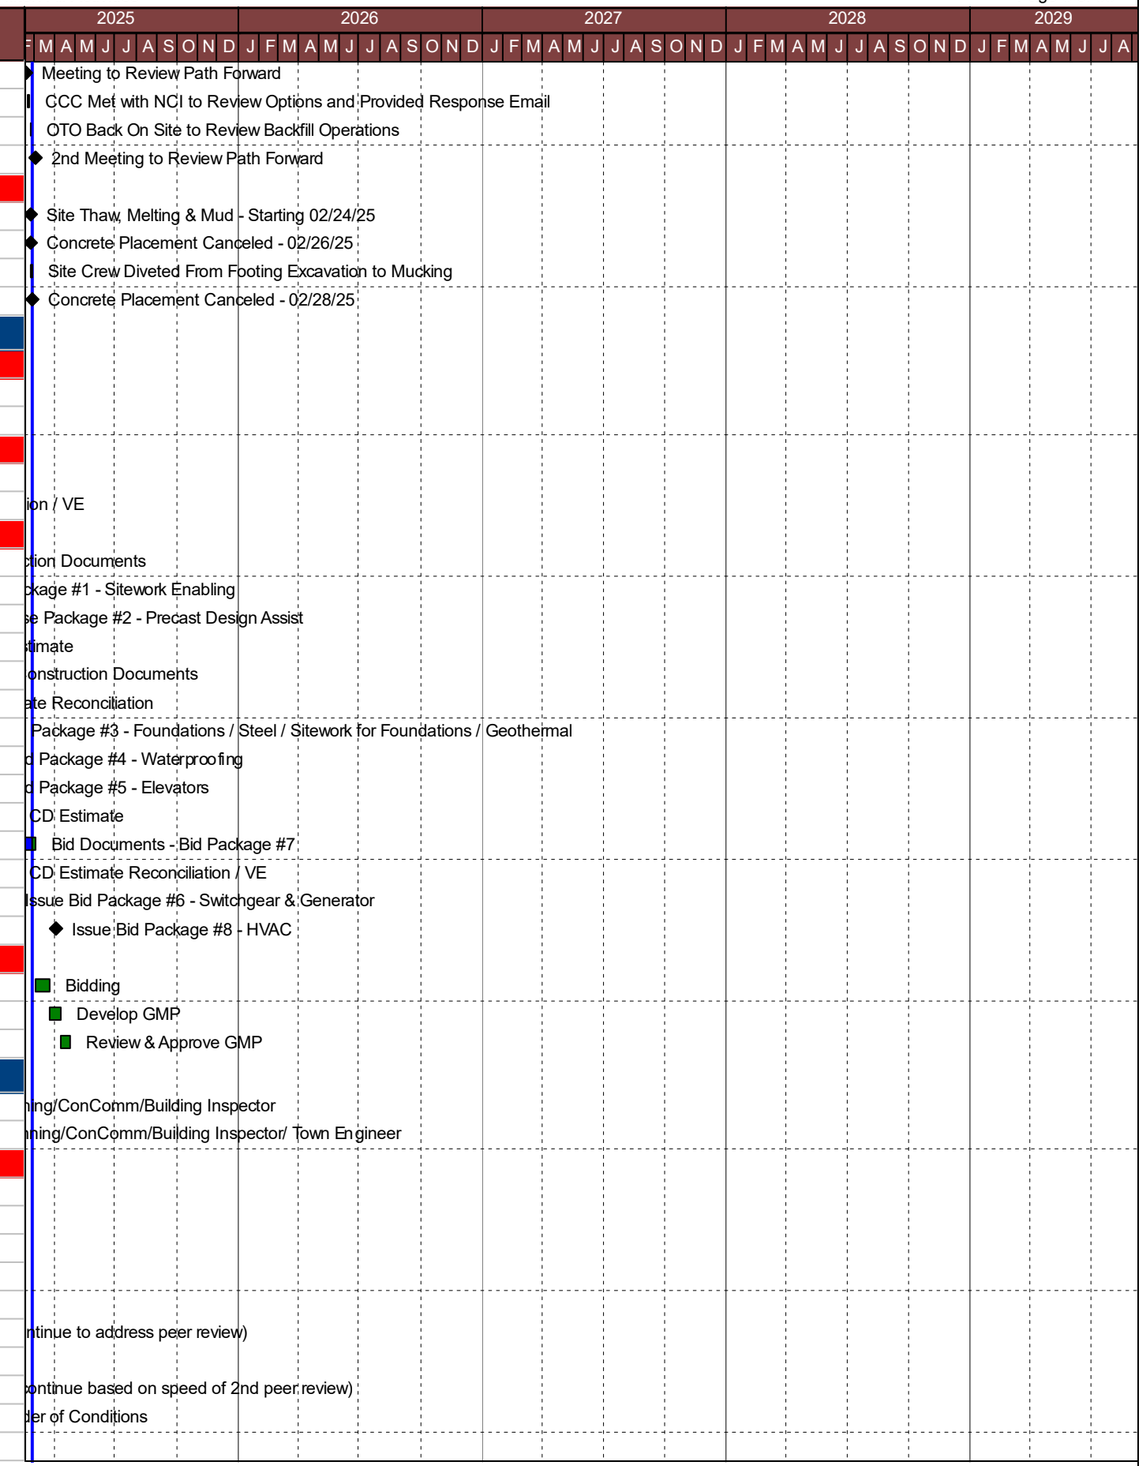

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A10150	10 Day Appeal Period - ConComm Order of Conditions	10d	0d	15-Aug-24 A	25-Aug-24 A
Planning Board Meetings (1st & 3rd Mondays of each month - typ 3-4 month process)					
A8660	Package Submitted to Planning Board Meeting	0d	0d	08-Apr-24 A	
A8670	May Hearing (first one & into to project)	0d	0d	06-May-24 A	
A8680	May Hearing	0d	0d	20-May-24 A	
A8690	June Hearing	0d	0d	03-Jun-24 A	
A8700	June Hearing	0d	0d	17-Jun-24 A	
Design Review Board (Hearing scheduled as needed - run concurrent with Planning Board - typ 2 months					
A8730	Package Submitted	0d	0d	08-May-24 A	
A8740	May Hearing	0d	0d	14-May-24 A	
Building Permit					
A1760	Building Permit	20d	0d	19-Jun-24 A	27-Sep-24 A
A1890	Blasting Permit	4d	0d	09-Sep-24 A	18-Sep-24 A
A1900	Community Town Hall Meeting	0d	0d	18-Sep-24 A	
PREQUALIFICATION					
A1880	Prequalify Filed Sub Bidders (FSB)	35d	0d	14-Nov-24 A	06-Jan-25 A
A2070	Notify Prequalified Bidders	0d	0d	07-Jan-25 A	
PROCUREMENT					
BP #1 Site Enabling					
Sitework Enabling					
A1400	Bid & Award - Sitework Enabling	30d	0d	08-May-24 A	14-Jun-24 A
A10540	Prepare Submittals - Softball Netting & Padding System	10d	0d	14-Jun-24 A	26-Jul-24 A
A1410	Prepare Submittals - Sitework Enabling	10d	0d	14-Jun-24 A	20-Aug-24 A
A10950	Prepare Submittals - WQUs	10d	0d	14-Jun-24 A	06-Sep-24 A
A1420	Approve Submittals - Sitework Enabling	10d	0d	11-Jul-24 A	23-Aug-24 A
A1430	Fabricate - Sitework Enabling	5d	0d	11-Jul-24 A	30-Aug-24 A
A1440	Deliver - Sitework Enabling	1d	0d	12-Jul-24 A	19-Sep-24 A
A10550	Review & Approve Submittals - Softball Netting & Padding System	5d	0d	29-Jul-24 A	08-Aug-24 A
A10530	Deliver - Water Retention System	1d	0d	02-Aug-24 A	19-Aug-24 A
A10560	Revise & Resubmit - Softball Netting & Padding System	5d	0d	09-Aug-24 A	20-Aug-24 A
A10570	Review & Approve R1 Revised Submittals - Softball Netting & Padding System	7d	0d	21-Aug-24 A	28-Aug-24 A
A10580	Fabricate & Deliver - Softball Netting & Padding System	35d	0d	29-Aug-24 A	05-Nov-24 A
A10960	Approve Submittals - WQUs	10d	0d	09-Sep-24 A	09-Sep-24 A
A10980	Fabricate - WQUs	32d	0d	09-Sep-24 A	16-Jan-25 A
A10970	Deliver - WQUs	1d	0d	16-Jan-25 A	16-Jan-25 A
BP #2 Precast Design Assist					
Precast Design Assist					
A8820	Bidding - Precast Design Assist	20d	0d	09-Jul-24 A	09-Aug-24 A
A8830	Descope - Precast Design Assist	4d	0d	12-Aug-24 A	14-Aug-24 A
A8840	Review / Award - Precast Design Assist	5d	0d	15-Aug-24 A	23-Aug-24 A
A8850	Precast Design Assist / Development	65d	0d	26-Aug-24 A	12-Nov-24 A
A9150	Precast D/A Submittal Review	18d	0d	12-Nov-24 A	05-Dec-24 A
A9700	Precast D/A Revise & Resubmit	10d	0d	09-Dec-24 A	31-Dec-24 A
A8860	Submittals & Shop Drawings - Precast	56d	0d	02-Jan-25 A	16-Jan-25 A
A8870	Fabrication - Precast Exterior Wall	85d	85d	10-Mar-25*	09-Jul-25
BP #3 Concrete, Steel, Site, Geothermal					
02 Geothermal					
A10670	Bid & Award - Geothermal	20d	0d	16-Oct-24 A	11-Dec-24 A
A10690	Prepare Submittals - Geothermal	15d	0d	13-Dec-24 A	21-Jan-25 A

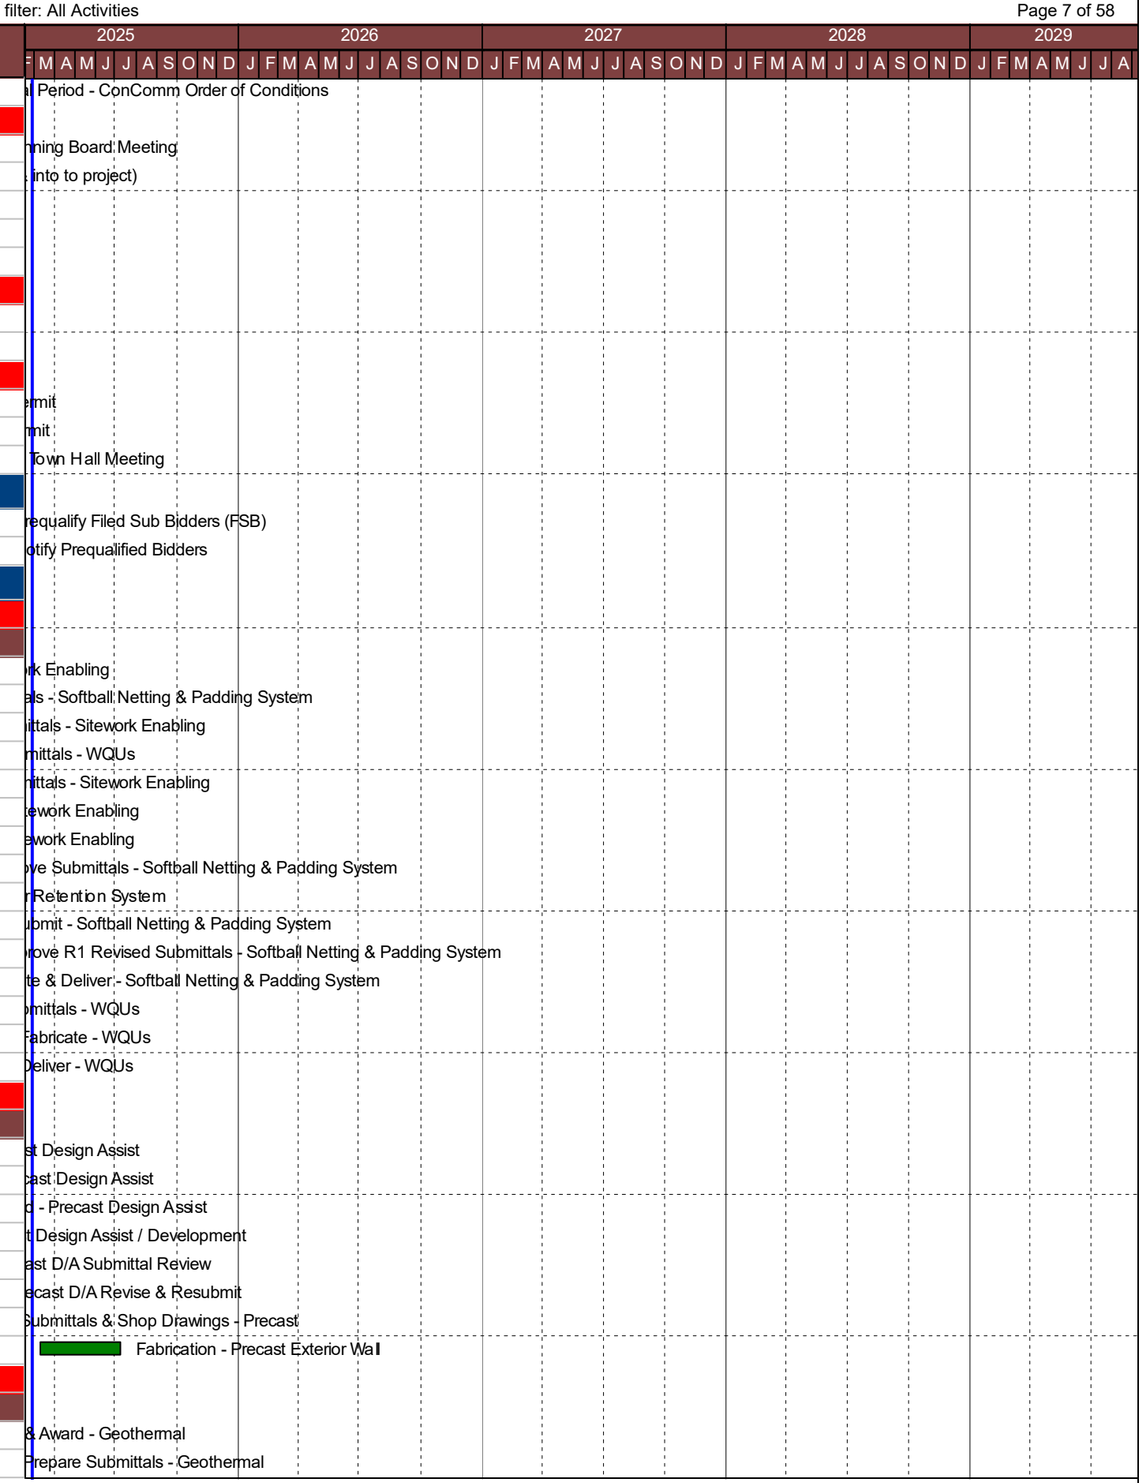

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A10700	Approve Submittals - Geothermal	15d	2d	21-Jan-25 A	28-Feb-25
A10710	Fabricate & Deliver - Geothermal	11d	11d	03-Mar-25	17-Mar-25
A10720	Mobilize to Site / Layout - Geothermal	3d	3d	17-Mar-25	19-Mar-25
02 Sitework for Foundations					
A8750	Bid & Award - Sitework for Foundations	30d	0d	16-Sep-24 A	11-Dec-24 A
03 Concrete Foundations					
A1520	Bid & Award - Concrete Foundations	30d	0d	16-Oct-24 A	11-Dec-24 A
A1530	Prepare Submittals - Concrete Foundations	10d	0d	12-Dec-24 A	10-Jan-25 A
A1540	Approve Submittals - Concrete Foundations - Bldg A	5d	0d	10-Jan-25 A	23-Jan-25 A
A190200	Approve Submittals - Concrete Foundations - Bldg B	5d	0d	14-Jan-25 A	29-Jan-25 A
A190230	Approve Submittals - Concrete Foundations - Bldg C	5d	0d	14-Jan-25 A	12-Feb-25 A
A190260	Approve Submittals - Concrete Foundations - Bldg D	5d	2d	14-Jan-25 A	28-Feb-25
A190290	Approve Submittals - Concrete Foundations - Bldg E	5d	7d	14-Jan-25 A	07-Mar-25
A190320	R1 Prepare Submittals - Concrete Foundations - Bldg A	10d	0d	24-Jan-25 A	30-Jan-25 A
A1550	Fabricate & Deliver - Rebar Footings - Bldg A	10d	0d	27-Jan-25 A	05-Feb-25 A
A190210	Fabricate - Concrete Foundations - Bldg B	10d	0d	29-Jan-25 A	19-Feb-25 A
A190330	R1 Approve Submittals - Concrete Foundations - Bldg A	5d	0d	30-Jan-25 A	06-Feb-25 A
A1720	Fabrication & Deliver - Rebar Walls - Bldg A	1d	0d	06-Feb-25 A	12-Feb-25 A
A190240	Fabricate - Concrete Foundations - Bldg C	10d	0d	12-Feb-25 A	26-Feb-25 A
A190220	Deliver - Concrete Foundations - Bldg B	1d	0d	19-Feb-25 A	19-Feb-25 A
A190250	Deliver - Concrete Foundations - Bldg C	1d	1d	27-Feb-25	27-Feb-25
A190270	Fabricate - Concrete Foundations - Bldg D	10d	10d	03-Mar-25	14-Mar-25
A190300	Fabricate - Concrete Foundations - Bldg E	10d	10d	10-Mar-25	21-Mar-25
A190280	Deliver - Concrete Foundations - Bldg D	1d	1d	14-Mar-25	14-Mar-25
A190310	Deliver - Concrete Foundations - Bldg E	1d	1d	21-Mar-25	21-Mar-25
03 Precast Plank					
A189310	Bid & Award - Precast Plank	30d	0d	16-Oct-24 A	16-Jan-25 A
A189320	Prepare Submittals - Precast Plank	20d	0d	27-Jan-25 A	14-Feb-25 A
A192770	Prepare SD - Precast Plank	20d	7d	27-Jan-25 A	07-Mar-25
A189330	Approve Submittals - Precast Plank	10d	2d	14-Feb-25 A	28-Feb-25
A192780	Approve SD - Precast Plank	10d	10d	10-Mar-25	21-Mar-25
A9200	Fabrication - Precast Planks	40d	40d	24-Mar-25	19-May-25
05 Steel					
A1560	Bid & Award - Steel	30d	0d	16-Oct-24 A	11-Dec-24 A
A1570	Prepare Submittals - Steel (Bldg A)	30d	0d	12-Dec-24 A	07-Jan-25 A
A189210	Prepare Submittals - Anchor Bolts (Bldg A)	30d	0d	12-Dec-24 A	07-Jan-25 A
A189240	Prepare Submittals - Anchor Bolts (Bldg B &C)	30d	0d	12-Dec-24 A	17-Jan-25 A
A189270	Prepare Submittals - Anchor Bolts (Bldg D&E)	30d	0d	12-Dec-24 A	27-Jan-25 A
A189220	Approve Submittals - Anchor Bolts (Bldg A)	15d	0d	07-Jan-25 A	24-Jan-25 A
A1580	Approve Submittals - Steel (Bldg A)	15d	2d	07-Jan-25 A	28-Feb-25
A190950	Prepare Submittals - Steel (Bldg B&C)	30d	16d	08-Jan-25 A	20-Mar-25
A190980	Prepare Submittals - Steel (Bldg D&E)	30d	40d	08-Jan-25 A	24-Apr-25
A189250	Approve Submittals - Anchor Bolts (Bldg B &C)	15d	0d	17-Jan-25 A	14-Feb-25 A
A189230	Fabricate - Anchor Bolts (Bldg A)	5d	0d	27-Jan-25 A	05-Feb-25 A
A189280	Approve Submittals - Anchor Bolts (Bldg D&E)	15d	2d	27-Jan-25 A	28-Feb-25
A189260	Fabricate - Anchor Bolts (Bldg B &C)	10d	0d	14-Feb-25 A	26-Feb-25 A
A189290	Fabricate - Anchor Bolts (Bldg D&E)	10d	10d	03-Mar-25	14-Mar-25
A1590	Fabricate & Deliver - Steel (Bldg A)	50d	50d	03-Mar-25	12-May-25
A190960	Approve Submittals - Steel (Bldg B&C)	10d	10d	21-Mar-25	03-Apr-25
A190970	Fabricate & Deliver - Steel (Bldg B&C)	40d	40d	04-Apr-25	02-Jun-25

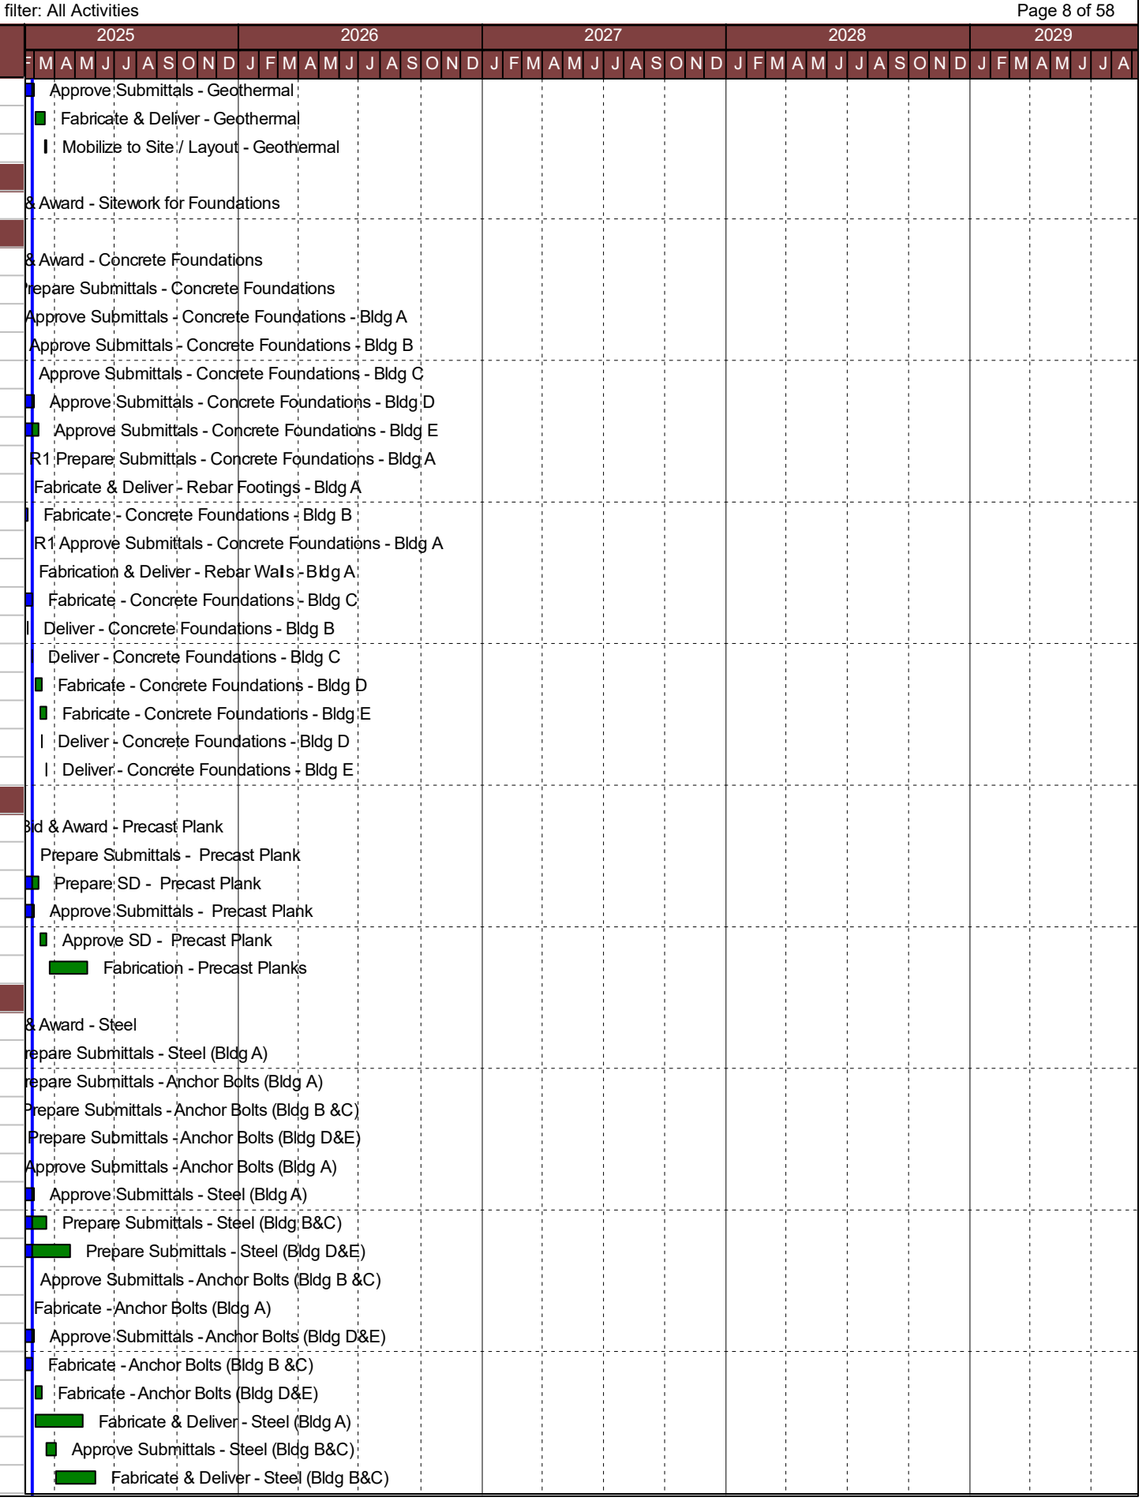

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A190990	Approve Submittals - Steel (Bldg D&E)	10d	10d	25-Apr-25	08-May-25
A191000	Fabricate & Deliver - Steel (Bldg D&E)	40d	40d	09-May-25	07-Jul-25
07.01 Waterproofing & Joint Sealants [TS]					
A2170	Bid & Award- Waterproofing [TS]	30d	0d	29-Oct-24 A	10-Jan-25 A
A2180	Prepare Submittals - Waterproofing	15d	0d	13-Jan-25 A	28-Jan-25 A
A2190	Approve Submittals - Waterproofing	10d	2d	17-Jan-25 A	28-Feb-25
A2200	Fabricate - Waterproofing	20d	20d	03-Mar-25	28-Mar-25
A2230	Deliver - Waterproofing	1d	1d	28-Mar-25	28-Mar-25
14.02 Elevator [TS]					
A2130	Bid & Award- Elevator [TS]	30d	0d	29-Oct-24 A	13-Jan-25 A
A2140	Prepare Submittals - Elevator	30d	0d	14-Jan-25 A	25-Feb-25 A
A2150	Approve Submittals - Elevator	15d	14d	25-Feb-25 A	18-Mar-25
A2160	Fabricate - Elevator	80d	80d	19-Mar-25	11-Jul-25
A2240	Deliver - Elevator	1d	1d	11-Jul-25	11-Jul-25
BP Early Masonry					
A188950	Issue Early Masonry RFQ	0d	0d	12-Dec-24 A	
A188960	Prequalify Early Masonry Sub Bidders	20d	0d	12-Dec-24 A	10-Jan-25 A
A188970	Issue RFP for Early Masonry	0d	0d	15-Jan-25 A	
A188980	Bid & Award - Early Masonry	15d	0d	15-Jan-25 A	26-Feb-25 A
A188990	Prepare Submittals - Early Masonry	14d	14d	27-Feb-25	18-Mar-25
A189000	Approve Submittals - Early Masonry	10d	10d	19-Mar-25	01-Apr-25
A189010	Fabricate - Early Masonry	10d	10d	02-Apr-25	15-Apr-25
BP #6 Switchgear & Generator					
A7820	Bid & Award - Switchgear & Generator	30d	7d	30-Jan-25 A	07-Mar-25
A7760	Prepare Submittals - Generator - Electrical - Equipment	20d	20d	10-Mar-25	04-Apr-25
A7770	Prepare Submittals - Switch Gear - Electrical - Equipment	20d	20d	10-Mar-25	04-Apr-25
A7780	Approve Submittals - Switch Gear - Electrical - Equipment	11d	11d	07-Apr-25	22-Apr-25
A7790	Approve Submittals - Generator - Electrical - Equipment	11d	11d	07-Apr-25	22-Apr-25
A7710	Fabricate - Generator - Electrical - Equipment	270d	270d	23-Apr-25	20-May-26
A7700	Fabricate - Switch Gear - Electrical - Equipment [58 weeks]	290d	290d	23-Apr-25	18-Jun-26
A7730	Deliver Generator - Electrical - Equipment	1d	1d	21-May-26	21-May-26
A7720	Deliver Switch Gear - Electrical - Equipment	1d	1d	19-Jun-26	19-Jun-26
BP #7 Balance of Procurement					
A2220	Bids Due	0d	0d		03-Apr-25
02.41 Selective Demolition					
A193180	OAL & Award- Demolition	10d	10d	23-Jun-25	07-Jul-25
A193140	Prepare Submittals - Demolition	20d	20d	08-Jul-25	04-Aug-25
A193150	Approve Submittals - Demolition	15d	15d	05-Aug-25	25-Aug-25
A193160	Mobilization - Demolition	10d	10d	10-Jun-27	23-Jun-27
02.82 Hazardous Material Abatement					
A193230	OAL & Award- Abatement	10d	10d	23-Jun-25	07-Jul-25
A193190	Prepare Submittals - Abatement	20d	20d	08-Jul-25	04-Aug-25
A193200	Approve Submittals - Abatement	15d	15d	05-Aug-25	25-Aug-25
A193210	10 Day Notification - Abatement	10d	10d	10-Jun-27	23-Jun-27
04.02 Masonry [TS]					
A5760	OAL & Award- Masory [TS]	10d	10d	07-Apr-25	18-Apr-25
A5770	Prepare Submittals - Exterior Wall Veneer	20d	20d	22-Apr-25	19-May-25
A9070	Prepare Submittals - CMU	20d	20d	22-Apr-25	19-May-25
A5780	Approve Submittals - Exterior Wall Veneer	20d	20d	20-May-25	17-Jun-25
A9080	Approve Submittals - CMU	20d	20d	20-May-25	17-Jun-25

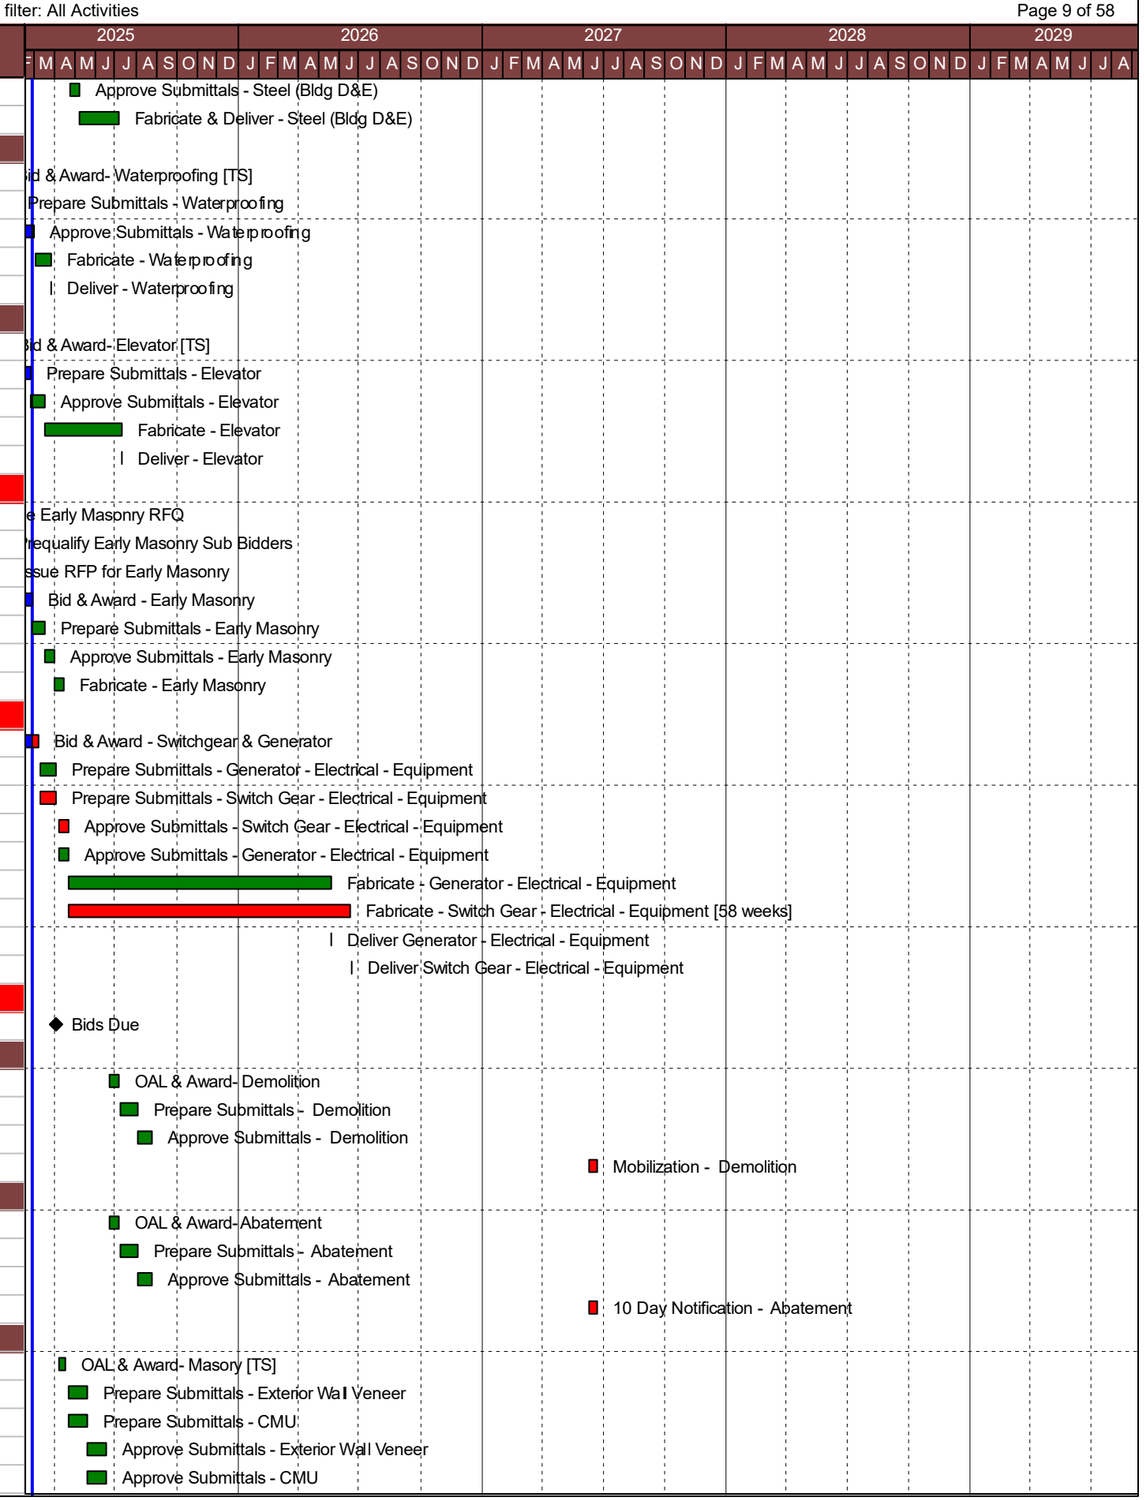

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A9090	Fabricate - CMU	10d	10d	18-Jun-25	01-Jul-25
A5790	Fabricate - Exterior Wall Veneer	40d	40d	18-Jun-25	13-Aug-25
A5800	Deliver - Exterior Wall Veneer	1d	1d	13-Aug-25	13-Aug-25
05.05 Misc. Metals [TS]					
A49110	OAL & Award- Misc. Metals [TS]	10d	10d	07-Apr-25	18-Apr-25
A48710	Prepare Submittals - Misc. Metals	20d	20d	22-Apr-25	19-May-25
A43650	Prepare Submittals - Stairs	20d	20d	22-Apr-25	19-May-25
A48720	Approve Submittals - Misc. Metals	15d	15d	20-May-25	10-Jun-25
A43660	Approve Submittals - Stairs	15d	15d	20-May-25	10-Jun-25
A48730	Fabricate - Misc. Metals	30d	30d	11-Jun-25	23-Jul-25
A43670	Fabricate - Stairs	30d	30d	11-Jun-25	23-Jul-25
A48740	Deliver - Misc. Metals	1d	1d	23-Jul-25	23-Jul-25
A43680	Deliver - Stairs	1d	1d	23-Jul-25	23-Jul-25
06.25 Millwork					
A49120	OAL & Award- Millwork	10d	10d	30-Jun-25	14-Jul-25
A5320	Prepare Submittals - Millwork	20d	20d	15-Jul-25	11-Aug-25
A5330	Approve Submittals - Millwork	15d	15d	12-Aug-25	02-Sep-25
A5340	Fabricate - Millwork	20d	20d	03-Sep-25	30-Sep-25
A5350	Deliver - Millwork	1d	1d	02-Apr-26	02-Apr-26
07.05 Roofing [TS]					
A1640	OAL & Award- Roofing [TS]	10d	10d	07-Apr-25	18-Apr-25
A1650	Prepare Submittals - Roofing	15d	15d	22-Apr-25	12-May-25
A1660	Approve Submittals - Roofing	10d	10d	13-May-25	27-May-25
A1670	Fabricate - Roofing	40d	40d	28-May-25	23-Jul-25
A1770	Deliver - Roofing	1d	1d	23-Jul-25	23-Jul-25
07.42 Metal Panels					
A5810	OAL & Award- Metal Panels	10d	10d	09-Jun-25	20-Jun-25
A5820	Prepare Submittals - Metal Panels	40d	40d	23-Jun-25	18-Aug-25
A5830	Approve Submittals - Metal Panels	20d	20d	19-Aug-25	16-Sep-25
A5840	Fabricate - Metal Panels	60d	60d	17-Sep-25	12-Dec-25
A5850	Deliver - Metal Panels	1d	1d	12-Dec-25	12-Dec-25
07.95 Expansion Joint Covers					
A193240	OAL & Award- Expansion Joint Covers	10d	10d	08-Sep-25	19-Sep-25
A193250	Prepare Submittals - Expansion Joint Covers	30d	30d	22-Sep-25	03-Nov-25
A193260	Approve Submittals - Expansion Joint Covers	20d	20d	04-Nov-25	03-Dec-25
A193270	Fabricate - Expansion Joint Covers	60d	60d	04-Dec-25	03-Mar-26
A193280	Deliver - Expansion Joint Covers	1d	1d	09-Apr-26	09-Apr-26
07.10 Waterproofing & Joint Sealant [TS]					
A192990	OAL & Award- Waterproofing & Joint Sealants	10d	10d	07-Apr-25	18-Apr-25
A193000	Prepare Submittals - Waterproofing & Joint Sealants	15d	15d	22-Apr-25	12-May-25
A193010	Approve Submittals - Waterproofing & Joint Sealants	15d	15d	13-May-25	03-Jun-25
A193020	Fabricate - Waterproofing & Joint Sealants	15d	15d	04-Jun-25	24-Jun-25
A193030	Deliver - Waterproofing & Joint Sealants	1d	1d	22-Jul-25	22-Jul-25
07.81 Spray Fireproofing					
A23530	OAL & Award- Spray Fireproofing	10d	10d	28-Apr-25	09-May-25
A23540	Prepare Submittals - Spray Fireproofing	15d	15d	12-May-25	02-Jun-25
A23550	Approve Submittals - Spray Fireproofing	15d	15d	03-Jun-25	23-Jun-25
A23560	Fabricate - Spray Fireproofing	15d	15d	24-Jun-25	15-Jul-25
A23570	Deliver - Spray Fireproofing	1d	1d	15-Jul-25	15-Jul-25
08.01 Doors / Frames / Hardware					

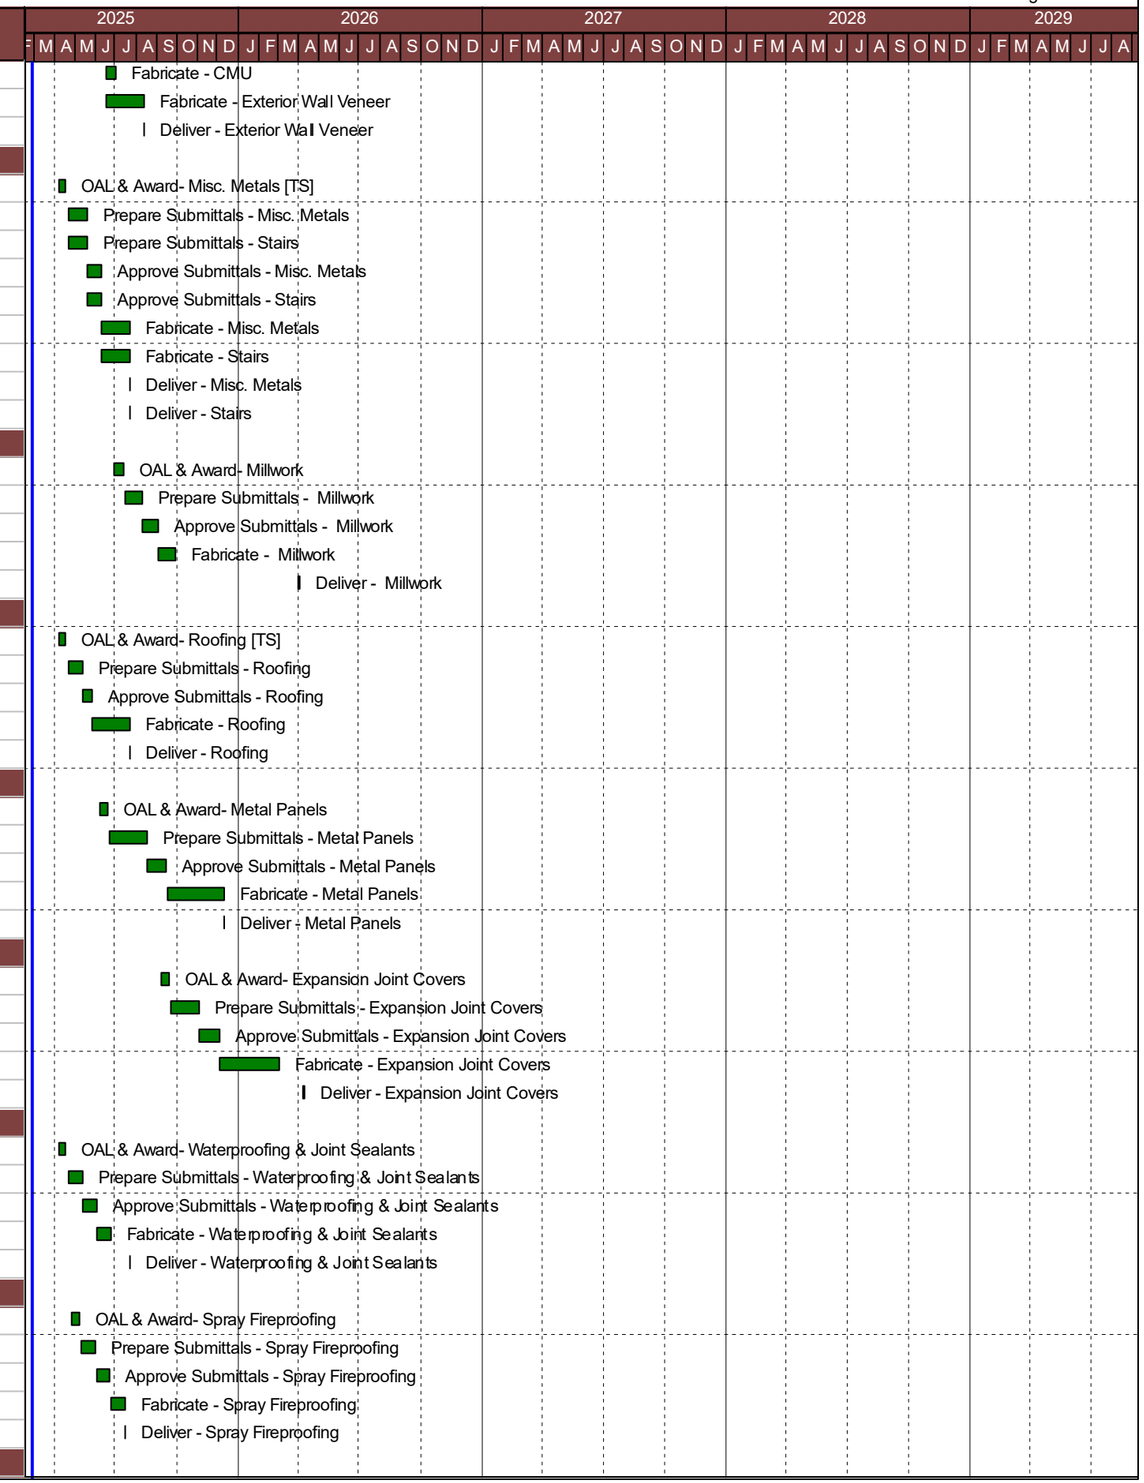

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A5460	OAL & Award- Doors / Frames / Hardware	10d	10d	27-May-25	09-Jun-25
A5470	Prepare Submittals - Doors / Frames / Hardware	20d	20d	10-Jun-25	08-Jul-25
A5480	Approve Submittals - Doors / Frames / Hardware	15d	15d	09-Jul-25	29-Jul-25
A5490	Fabricate - Doors / Frames / Hardware	40d	40d	30-Jul-25	24-Sep-25
A5500	Deliver - Doors / Frames / Hardware	1d	1d	24-Sep-25	24-Sep-25
08.36 Overhead Doors					
A49130	OAL & Award- Overhead Doors	10d	10d	14-Jul-25	25-Jul-25
A48790	Prepare Submittals - Overhead Doors	20d	20d	28-Jul-25	22-Aug-25
A48800	Approve Submittals - Overhead Doors	15d	15d	25-Aug-25	15-Sep-25
A48810	Field Measure & Fabricate - Overhead Doors	40d	40d	16-Sep-25	12-Nov-25
A46480	Fabricate - Vertical Doors [s]	50d	50d	16-Sep-25	26-Nov-25
A48820	Deliver - Overhead Doors	1d	1d	12-Nov-25	12-Nov-25
08.41 Windows / Curtainwall [TS]					
A5710	OAL & Award- Windows / Curtainwall [TS]	10d	10d	07-Apr-25	18-Apr-25
A5720	Prepare Submittals - Windows / Curtainwall	40d	40d	22-Apr-25	17-Jun-25
A5730	Approve Submittals - Windows / Curtainwall	15d	15d	18-Jun-25	09-Jul-25
A5740	Fabricate - Windows / Curtainwall	70d	70d	10-Jul-25	17-Oct-25
A5750	Deliver - Windows / Curtainwall	1d	1d	17-Oct-25	17-Oct-25
08.80 Glass & Glazing [TS]					
A193040	OAL & Award- Glass & Glazing [TS]	10d	10d	07-Apr-25	18-Apr-25
A193050	Prepare Submittals - Glass & Glazing	40d	40d	22-Apr-25	17-Jun-25
A193060	Approve Submittals - Glass & Glazing	15d	15d	18-Jun-25	09-Jul-25
A193070	Fabricate - Glass & Glazing	35d	35d	10-Jul-25	27-Aug-25
A193080	Deliver - Glass & Glazing	1d	1d	27-Aug-25	27-Aug-25
09.03 Flooring - Tile/Stone [TS]					
A4810	OAL & Award- Tile [TS]	10d	10d	07-Apr-25	18-Apr-25
A4820	Prepare Submittals - Tile	20d	20d	22-Apr-25	19-May-25
A4830	Approve Submittals - Tile	15d	15d	20-May-25	10-Jun-25
A4840	Fabricate - Tile	40d	40d	11-Jun-25	06-Aug-25
A4850	Deliver - Tile	1d	1d	06-Aug-25	06-Aug-25
09.04 Terrazzo [TS]					
A25840	OAL & Award- Terrazzo [TS]	10d	10d	07-Apr-25	18-Apr-25
A25850	Prepare Submittals - Terrazzo	20d	20d	22-Apr-25	19-May-25
A25860	Approve Submittals - Terrazzo	15d	15d	20-May-25	10-Jun-25
A25870	Fabricate - Precast Terrazzo	40d	40d	21-Oct-25	17-Dec-25
A25880	Deliver - Precast Terrazzo	1d	1d	17-Dec-25	17-Dec-25
09.08 Acoustical Wall & Ceiling Panels					
A49140	OAL & Award- Acoustical Wall & Ceiling Panels	10d	10d	06-Jun-25	19-Jun-25
A5120	Prepare Submittals - Acoustical Wall & Ceiling Panels	20d	20d	20-Jun-25	18-Jul-25
A5130	Approve Submittals - Acoustical Wall & Ceiling Panels	15d	15d	21-Jul-25	08-Aug-25
A5140	Fabricate - Acoustical Wall & Ceiling Panels	30d	30d	11-Aug-25	22-Sep-25
A5150	Deliver - Acoustical Wall & Ceiling Panels	1d	1d	22-Sep-25	22-Sep-25
09.09 Painting [TS]					
A49150	OAL & Award- Paint [TS]	10d	10d	07-Apr-25	18-Apr-25
A5070	Prepare Submittals - Paint	20d	20d	22-Apr-25	19-May-25
A5080	Approve Submittals - Paint	15d	15d	20-May-25	10-Jun-25
A5100	Deliver - Paint	1d	1d	09-Oct-25	09-Oct-25
09.21 Drywall					
A49160	OAL & Award- Drywall	10d	10d	22-Apr-25	05-May-25
A48750	Prepare Submittals - Drywall	20d	20d	06-May-25	03-Jun-25

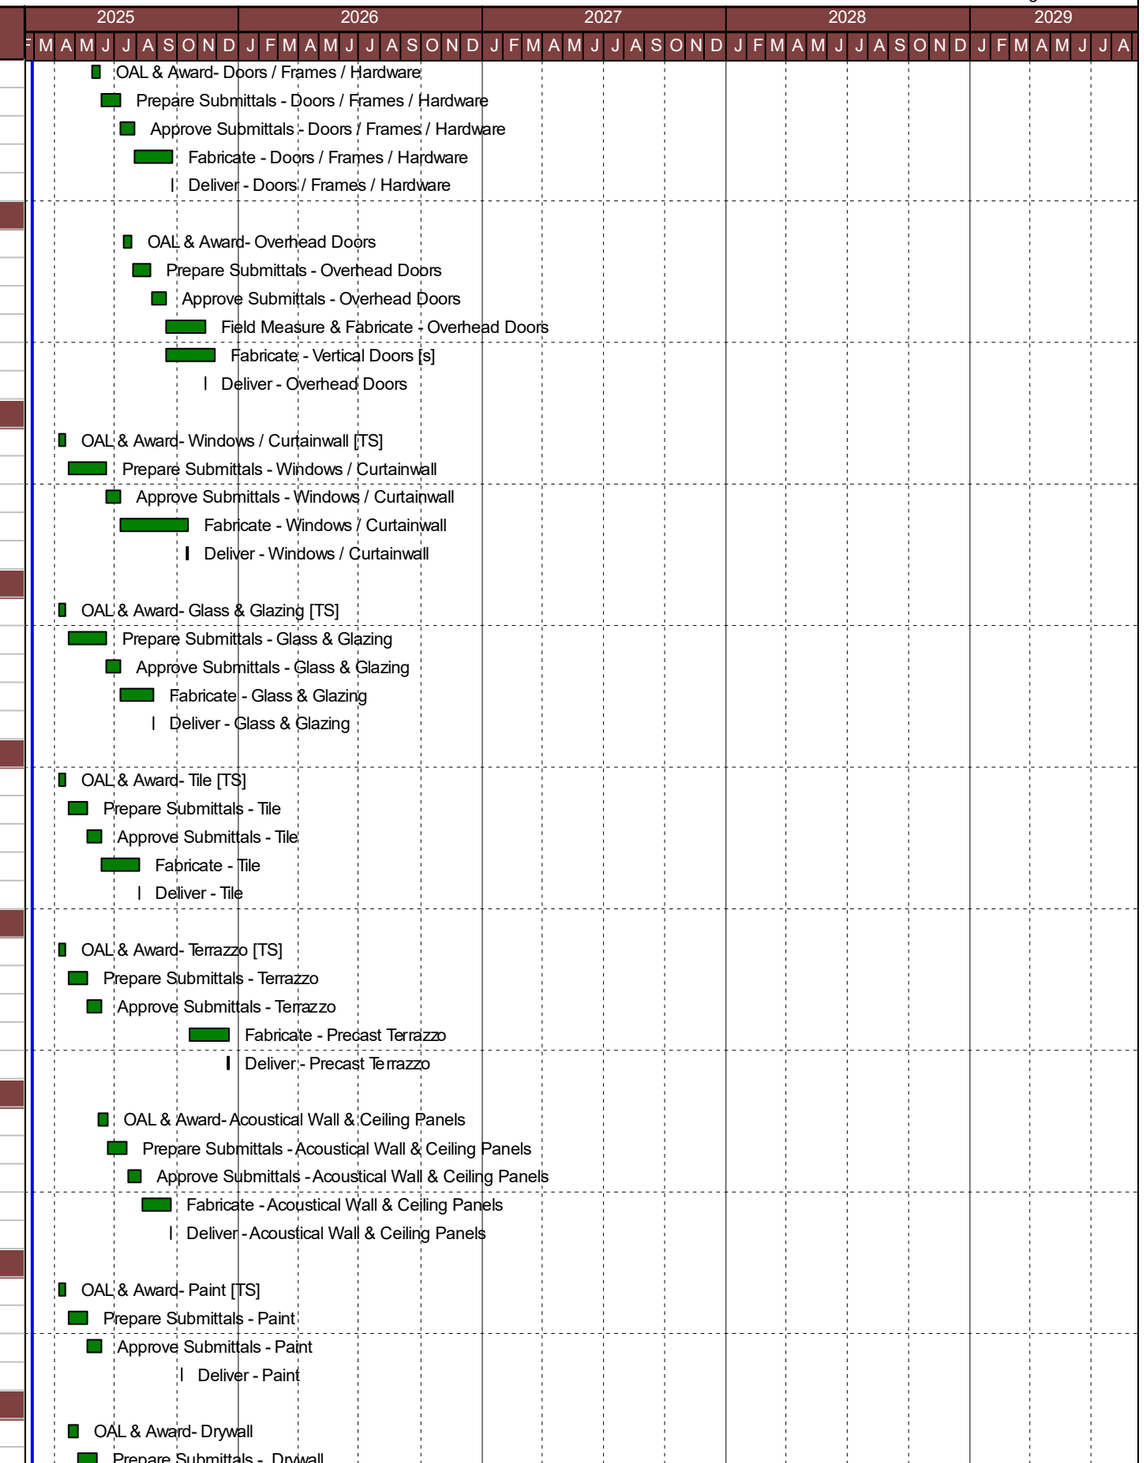

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A48760	Approve Submittals - Drywall	15d	15d	04-Jun-25	24-Jun-25
A48770	Fabricate - Drywall	20d	20d	25-Jun-25	23-Jul-25
A48780	Deliver - Drywall	1d	1d	03-Oct-25	03-Oct-25
09.51 ACT [TS]					
A4760	OAL & Award- ACT [TS]	10d	10d	07-Apr-25	18-Apr-25
A4770	Prepare Submittals - ACT	15d	15d	22-Apr-25	12-May-25
A4780	Approve Submittals - ACT	10d	10d	13-May-25	27-May-25
A4790	Fabricate - ACT	15d	15d	28-May-25	17-Jun-25
A4800	Deliver - ACT	1d	1d	17-Jun-25	17-Jun-25
09.62 Wood Flooring					
A4960	OAL & Award- Wood Flooring	10d	10d	11-Aug-25	22-Aug-25
A4970	Prepare Submittals - Wood Flooring	20d	20d	25-Aug-25	22-Sep-25
A4980	Approve Submittals - Wood Flooring	15d	15d	23-Sep-25	14-Oct-25
A4990	Fabricate - Wood Flooring	50d	50d	15-Oct-25	26-Dec-25
A5000	Deliver - Wood Flooring	1d	1d	26-Dec-25	26-Dec-25
09.65 Flooring - Resilient [TS]					
A49170	OAL & Award- Resilient Flooring [TS]	10d	10d	07-Apr-25	18-Apr-25
A5020	Prepare Submittals - Resilient Flooring	15d	15d	22-Apr-25	12-May-25
A5030	Approve Submittals - Resilient Flooring	15d	15d	13-May-25	03-Jun-25
A5040	Fabricate - Resilient Flooring	20d	20d	07-Aug-28	01-Sep-28
A5050	Deliver - Resilient Flooring [s]	1d	1d	01-Sep-28	01-Sep-28
09.64 Athletic Wood Flooring					
A4910	OAL & Award- Athletic Wood Flooring	10d	10d	21-Jul-25	01-Aug-25
A4920	Prepare Submittals - Athletic Wood Flooring	20d	20d	04-Aug-25	29-Aug-25
A4930	Approve Submittals - Athletic Wood Flooring	15d	15d	02-Sep-25	22-Sep-25
A4940	Fabricate - Athletic Wood Flooring	50d	50d	23-Sep-25	04-Dec-25
A4950	Deliver - Athletic Wood Flooring	1d	1d	04-Dec-25	04-Dec-25
09.68 Carpet					
A49180	OAL & Award- Carpet	10d	10d	18-Aug-25	29-Aug-25
A4870	Prepare Submittals - Carpet	15d	15d	02-Sep-25	22-Sep-25
A4880	Approve Submittals - Carpet	10d	10d	23-Sep-25	06-Oct-25
A4890	Fabricate - Carpet	20d	20d	07-Oct-25	04-Nov-25
A4900	Deliver - Carpet	1d	1d	04-Nov-25	04-Nov-25
10.14 Signage					
A5860	OAL & Award- Signage	10d	10d	18-Aug-25	29-Aug-25
A5670	Prepare Submittals - Signage	20d	20d	02-Sep-25	29-Sep-25
A5680	Approve Submittals - Signage	15d	15d	30-Sep-25	21-Oct-25
A5690	Fabricate - Signage	15d	15d	22-Oct-25	12-Nov-25
A5700	Deliver - Signage	1d	1d	15-Apr-26	15-Apr-26
10.24 Operable Partitions					
A49190	OAL & Award- Operable Partitions	10d	10d	04-Aug-25	15-Aug-25
A48830	Prepare Submittals - Operable Partitions	20d	20d	18-Aug-25	15-Sep-25
A48840	Approve Submittals - Operable Partitions	15d	15d	16-Sep-25	06-Oct-25
A48850	Fabricate - Operable Partitions	100d	100d	07-Oct-25	04-Mar-26
A48860	Deliver - Operable Partitions	1d	1d	31-Mar-26	31-Mar-26
10.51 Lockers					
A49200	OAL & Award- Lockers	10d	10d	04-Aug-25	15-Aug-25
A5620	Prepare Submittals - Lockers	20d	20d	18-Aug-25	15-Sep-25
A5630	Approve Submittals - Lockers	15d	15d	16-Sep-25	06-Oct-25
A5640	Fabricate - Lockers	40d	40d	07-Oct-25	04-Dec-25

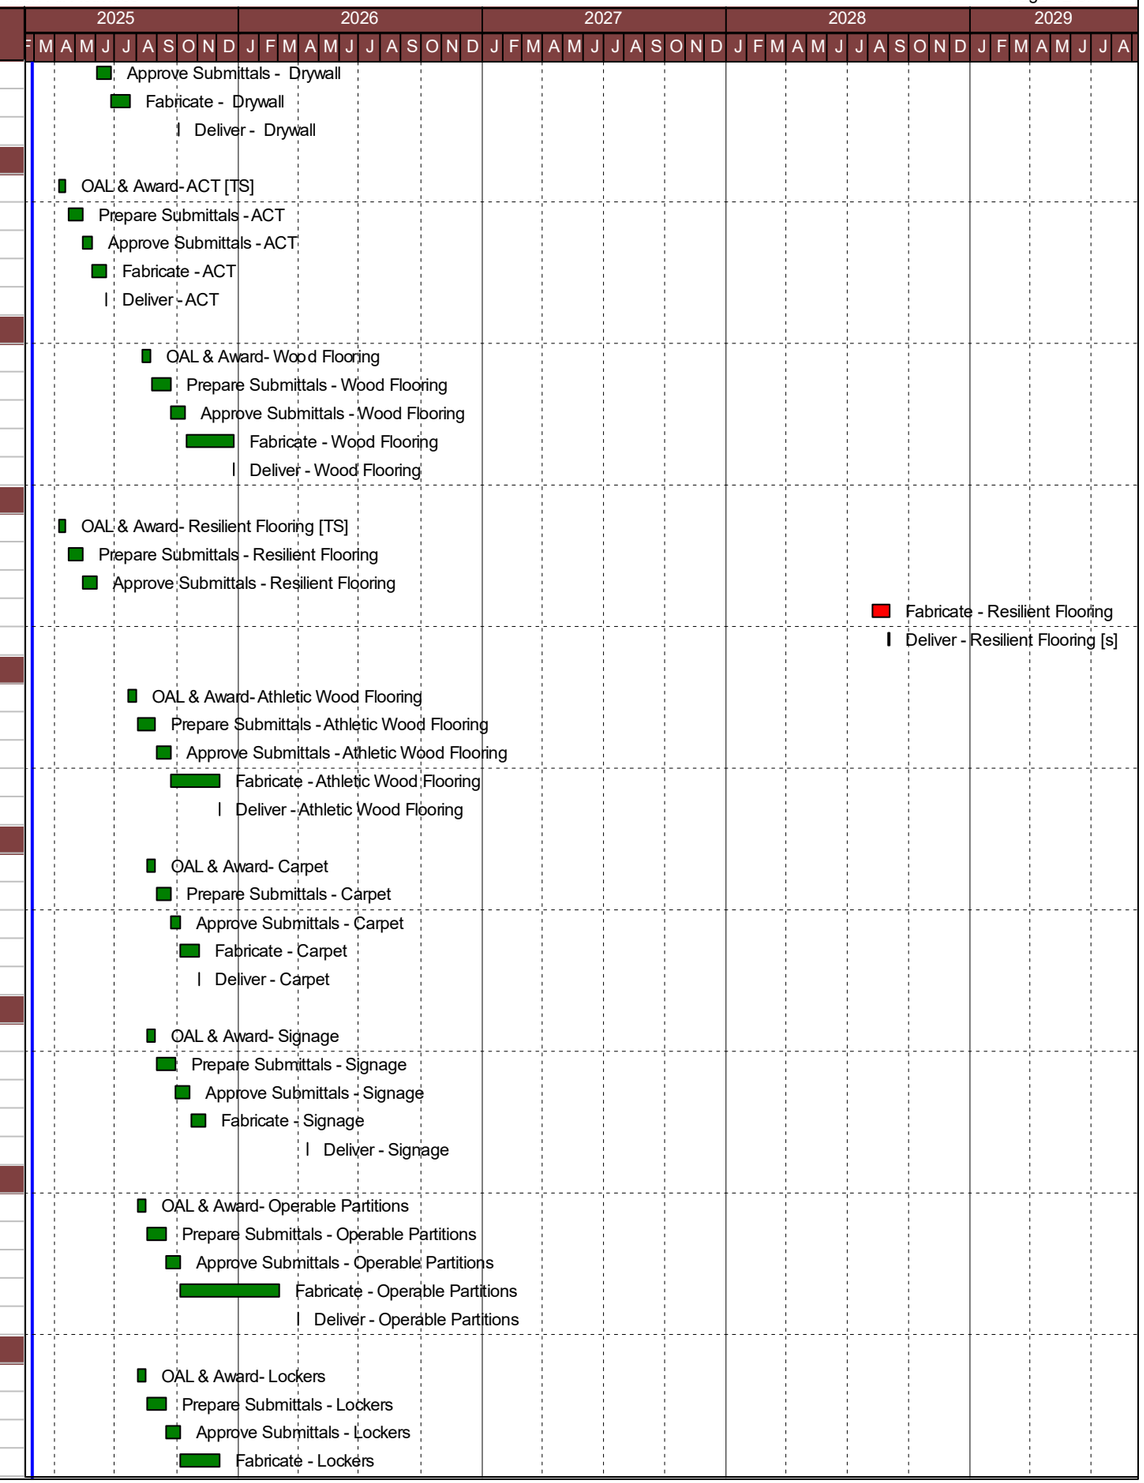

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A5650	Deliver - Lockers [s]	1d	1d	29-Apr-26	29-Apr-26
10.95 Toilet Partitions / Accessories					
A49210	OAL & Award- Toilet Partitions / Accessories	10d	10d	04-Aug-25	15-Aug-25
A5520	Prepare Submittals - Toilet Partitions / Accessories	20d	20d	18-Aug-25	15-Sep-25
A5530	Approve Submittals - Toilet Partitions / Accessories	15d	15d	16-Sep-25	06-Oct-25
A5540	Fabricate - Toilet Partitions / Accessories	20d	20d	07-Oct-25	04-Nov-25
A5550	Deliver - Toilet Partitions / Accessories	1d	1d	10-Mar-26	10-Mar-26
11.04 Food Service Equipment					
A5160	OAL & Award- Food Service Equipment	10d	10d	16-Jun-25	27-Jun-25
A5170	Prepare Submittals - Food Service Equipment	20d	20d	30-Jun-25	28-Jul-25
A5180	Approve Submittals - Food Service Equipment	15d	15d	29-Jul-25	18-Aug-25
A5190	Fabricate - Food Service Equipment	60d	60d	19-Aug-25	13-Nov-25
A5200	Deliver - Food Service Equipment	1d	1d	13-Nov-25	13-Nov-25
11.31 Residential Appliances					
A49220	OAL & Award- Residential Appliances	10d	10d	08-Sep-25	19-Sep-25
A48870	Prepare Submittals - Residential Appliances	10d	10d	22-Sep-25	03-Oct-25
A48880	Approve Submittals - Residential Appliances	15d	15d	06-Oct-25	27-Oct-25
A48890	Fabricate - Residential Appliances	60d	60d	28-Oct-25	26-Jan-26
A48900	Deliver - Residential Appliances [s]	1d	1d	26-Jan-26	26-Jan-26
11.52 Projection Screens					
A49230	OAL & Award- Projection Screens	10d	10d	18-Aug-25	29-Aug-25
A48910	Prepare Submittals - Projection Screens	20d	20d	02-Sep-25	29-Sep-25
A48920	Approve Submittals - Projection Screens	15d	15d	30-Sep-25	21-Oct-25
A48930	Fabricate - Projection Screens	40d	40d	22-Oct-25	18-Dec-25
A48940	Deliver - Projection Screens [s]	1d	1d	01-Sep-28	01-Sep-28
11.53 Lab Equipment					
A49240	OAL & Award- Lab Equipment	10d	10d	30-Jun-25	14-Jul-25
A5220	Prepare Submittals - Lab Equipment	20d	20d	15-Jul-25	11-Aug-25
A5230	Approve Submittals - Lab Equipment	15d	15d	12-Aug-25	02-Sep-25
A5240	Fabricate - Lab Equipment	60d	60d	03-Sep-25	28-Nov-25
A5250	Deliver - Lab Equipment [s]	1d	1d	01-Sep-28	01-Sep-28
11.61 Theater & Stage Equipment					
A49250	OAL & Award- Theater & Stage Equipment	10d	10d	21-Jul-25	01-Aug-25
A43730	Submittals - Theater & Stage Equipment	10d	10d	04-Aug-25	15-Aug-25
A48950	Prepare Submittals - Theater & Stage Equipment	20d	20d	04-Aug-25	29-Aug-25
A43740	Approve Submittals - Theater & Stage Equipment	15d	15d	18-Aug-25	08-Sep-25
A48960	Approve Submittals - Theater & Stage Equipment	15d	15d	02-Sep-25	22-Sep-25
A48970	Fabricate - Theater & Stage Equipment	60d	60d	23-Sep-25	18-Dec-25
A48980	Deliver - Theater & Stage Equipment	1d	1d	18-Dec-25	18-Dec-25
11.65 Athletic / Recreational Equipment					
A49260	OAL & Award- Athletic / Recreational Equipment	10d	10d	14-Jul-25	25-Jul-25
A48990	Prepare Submittals - Athletic / Recreational Equipment	20d	20d	28-Jul-25	22-Aug-25
A49000	Approve Submittals - Athletic / Recreational Equipment	15d	15d	25-Aug-25	15-Sep-25
A49010	Fabricate - Athletic / Recreational Equipment	60d	60d	16-Sep-25	11-Dec-25
A49020	Deliver - Athletic / Recreational Equipment	1d	1d	11-Dec-25	11-Dec-25
12.02 Window Treatments					
A49270	OAL & Award- Window Treatments	10d	10d	02-Sep-25	15-Sep-25
A5570	Prepare Submittals - Window Treatments	20d	20d	16-Sep-25	14-Oct-25
A5580	Approve Submittals - Window Treatments	15d	15d	15-Oct-25	04-Nov-25
A5590	Fabricate - Window Treatments	20d	20d	05-Nov-25	04-Dec-25

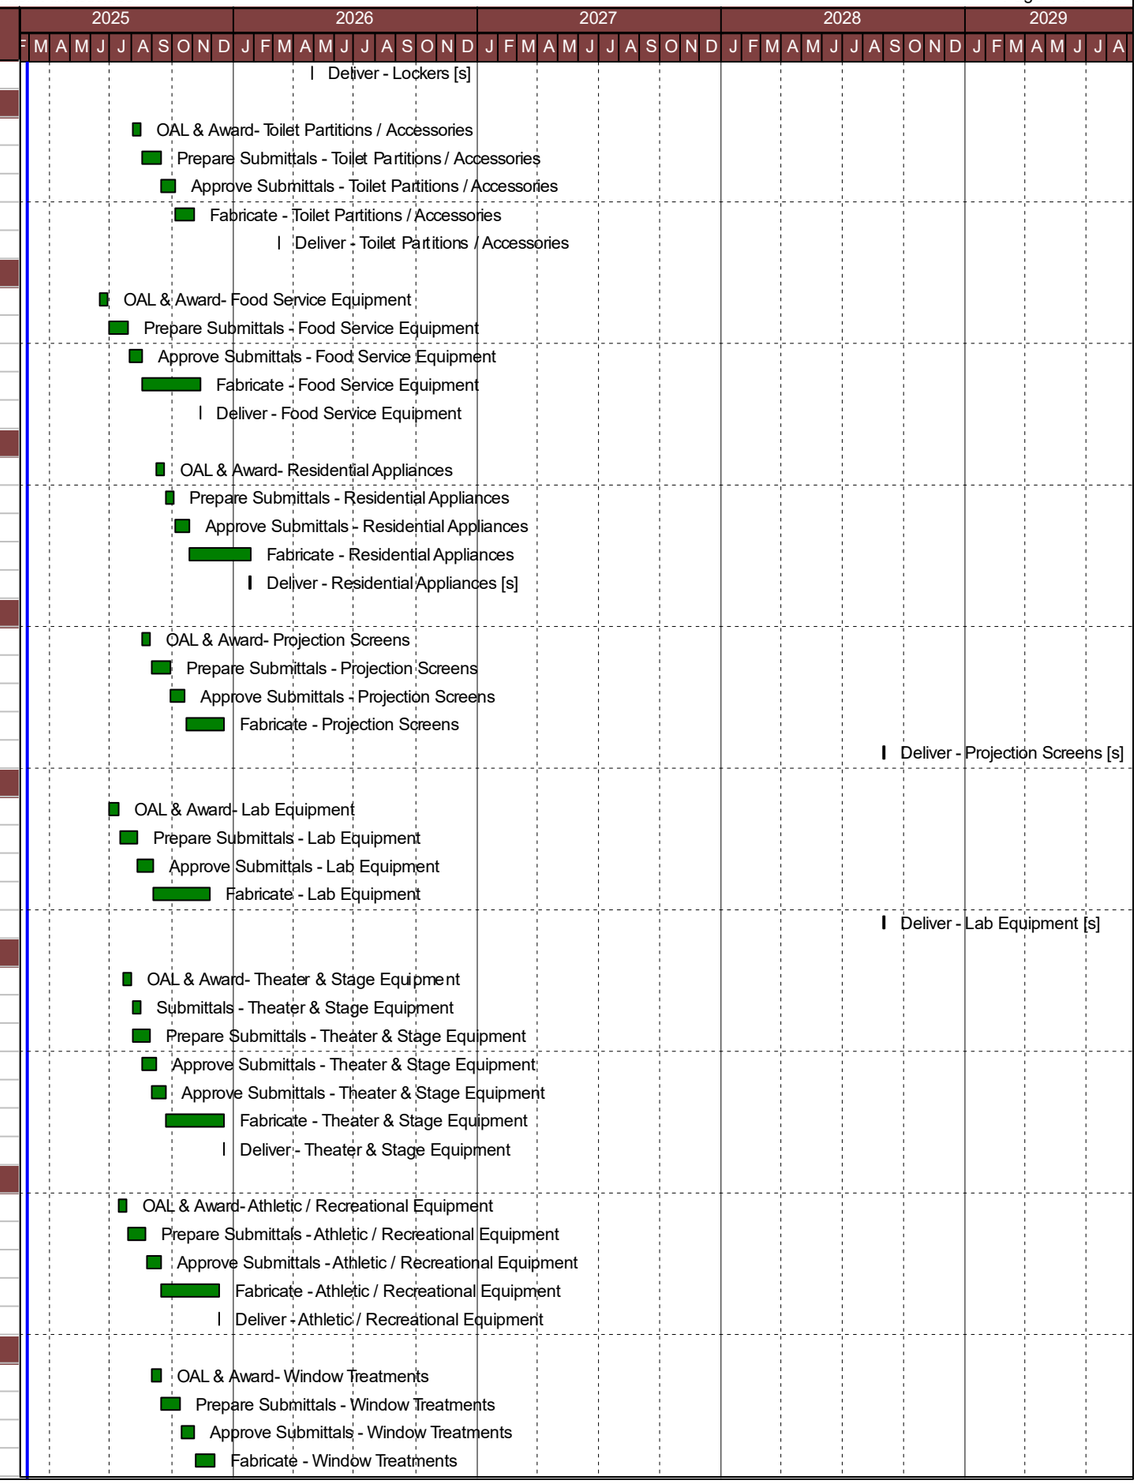

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A5600	Deliver - Window Treatments [s]	1d	1d	01-Sep-28	01-Sep-28
12.06 Theater Seating					
A5360	OAL & Award- Theater Seating	10d	10d	28-Jul-25	08-Aug-25
A5370	Prepare Submittals - Theater Seating	30d	30d	11-Aug-25	22-Sep-25
A5380	Approve Submittals - Theater Seating	15d	15d	23-Sep-25	14-Oct-25
A5390	Fabricate - Theater Seating	50d	50d	15-Oct-25	26-Dec-25
A5400	Deliver - Theater Seating	1d	1d	26-Dec-25	26-Dec-25
12.35 Lab Casework					
A49280	OAL & Award- Lab Casework	10d	10d	30-Jun-25	14-Jul-25
A5270	Prepare Submittals - Lab Casework	20d	20d	15-Jul-25	11-Aug-25
A5280	Approve Submittals - Lab Casework	15d	15d	12-Aug-25	02-Sep-25
A5290	Fabricate - Lab Casework	50d	50d	03-Sep-25	13-Nov-25
A5300	Deliver - Lab Casework [s]	1d	1d	01-Sep-28	01-Sep-28
12.48 Flooring - Entrance Mats					
A49290	OAL & Award- Entrance Mats	10d	10d	18-Aug-25	29-Aug-25
A49070	Prepare Submittals - Entrance Mats	15d	15d	02-Sep-25	22-Sep-25
A49080	Approve Submittals - Entrance Mats	15d	15d	23-Sep-25	14-Oct-25
A49090	Fabricate - Entrance Mats	40d	40d	15-Oct-25	11-Dec-25
A49100	Deliver - Entrance Mats [s]	1d	1d	01-Sep-28	01-Sep-28
12.07 Bleachers					
A5410	OAL & Award- Bleachers	10d	10d	25-Aug-25	08-Sep-25
A5420	Prepare Submittals - Bleachers	15d	15d	09-Sep-25	29-Sep-25
A5430	Approve Submittals - Bleachers	15d	15d	30-Sep-25	21-Oct-25
A5440	Fabricate - Bleachers	40d	40d	22-Oct-25	18-Dec-25
A5450	Deliver - Bleachers	1d	1d	18-Dec-25	18-Dec-25
14.20 Elevator [TS]					
A193090	OAL & Award- Elevators [TS]	10d	10d	07-Apr-25	18-Apr-25
A193100	Prepare Submittals - Elevators	30d	30d	22-Apr-25	03-Jun-25
A193110	Approve Submittals - Elevators	15d	15d	04-Jun-25	24-Jun-25
A193120	Fabricate - Elevators	70d	70d	25-Jun-25	02-Oct-25
A193130	Deliver - Elevators	1d	1d	02-Oct-25	02-Oct-25
21.01 Fire Protection [TS]					
A4470	OAL & Award- Fire Protection [TS]	10d	10d	07-Apr-25	18-Apr-25
Basic Material					
A4480	Prepare Submittals - Fire Protection - Basic Material	15d	15d	22-Apr-25	12-May-25
A4490	Approve Submittals - Fire Protection - Basic Material	15d	15d	13-May-25	03-Jun-25
A4500	Fabricate - Fire Protection - Basic Material	15d	15d	04-Jun-25	24-Jun-25
A4510	Deliver - Fire Protection - Basic Material	1d	1d	24-Jun-25	24-Jun-25
Equipment					
A4680	Prepare Submittals - Fire Protection - Equipment	20d	20d	22-Apr-25	19-May-25
A4690	Approve Submittals - Fire Protection - Equipment	15d	15d	20-May-25	10-Jun-25
A4700	Fabricate - Fire Protection - Equipment	65d	65d	11-Jun-25	11-Sep-25
A4710	Deliver - Fire Protection - Equipment	1d	1d	11-Sep-25	11-Sep-25
22.01 Plumbing [TS]					
A4420	OAL & Award- Plumbing [TS]	10d	10d	07-Apr-25	18-Apr-25
Basic Material					
A4430	Prepare Submittals - Plumbing - Basic Material	15d	15d	22-Apr-25	12-May-25
A4440	Approve Submittals - Plumbing - Basic Material	15d	15d	13-May-25	03-Jun-25
A4450	Fabricate - Plumbing - Basic Material	15d	15d	04-Jun-25	24-Jun-25
A4460	Deliver - Plumbing - Basic Material	1d	1d	24-Jun-25	24-Jun-25

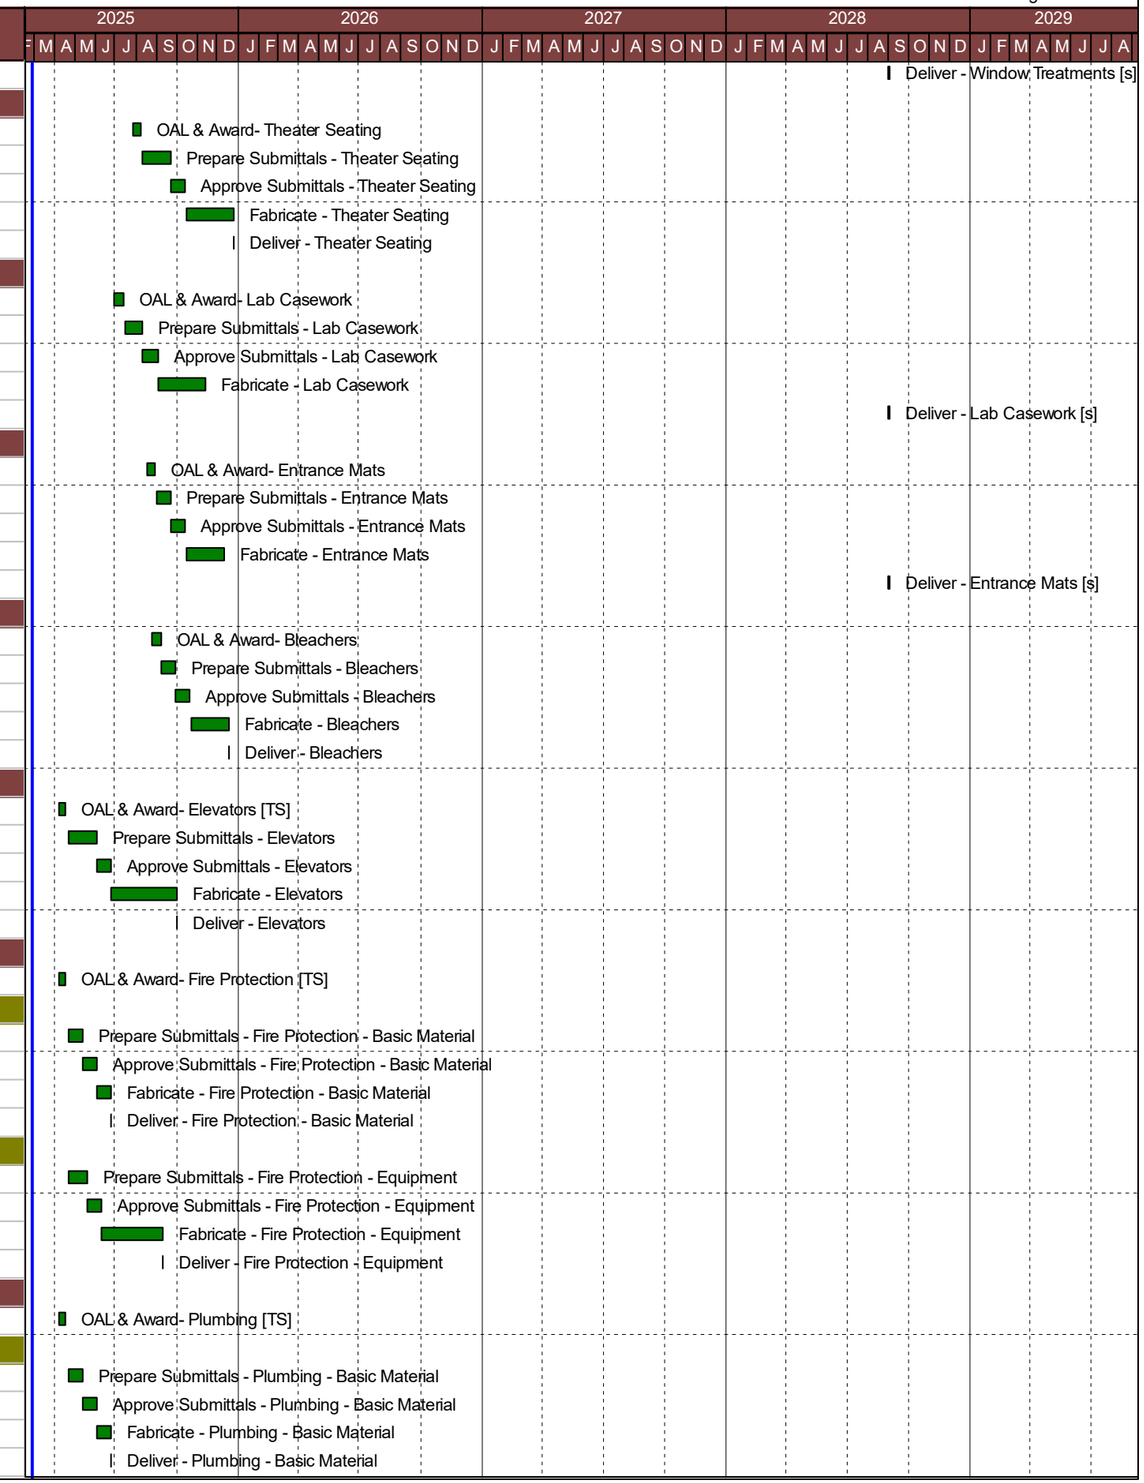

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
Equipment					
A4640	Prepare Submittals - Plumbing - Equipment	20d	20d	22-Apr-25	19-May-25
A4650	Approve Submittals - Plumbing - Equipment	15d	15d	20-May-25	10-Jun-25
A4660	Fabricate - Plumbing - Equipment	65d	65d	11-Jun-25	11-Sep-25
A4670	Deliver - Plumbing - Equipment	1d	1d	11-Sep-25	11-Sep-25
Fixtures					
A4720	Prepare Submittals - Plumbing - Fixtures	20d	20d	22-Apr-25	19-May-25
A4730	Approve Submittals - Plumbing - Fixtures	15d	15d	20-May-25	10-Jun-25
A4740	Fabricate - Plumbing - Fixtures	60d	60d	11-Jun-25	04-Sep-25
A4750	Deliver - Plumbing - Fixtures	1d	1d	04-Sep-25	04-Sep-25
26.01 Electrical [TS]					
A4370	OAL & Award- Electrical [TS]	10d	10d	07-Apr-25	18-Apr-25
Basic Material					
A4380	Prepare Submittals - Electrical - Basic Material	15d	15d	22-Apr-25	12-May-25
A4390	Approve Submittals - Electrical - Basic Material	15d	15d	13-May-25	03-Jun-25
A4400	Fabricate - Electrical - Basic Material	15d	15d	04-Jun-25	24-Jun-25
A4410	Deliver - Electrical - Basic Material	1d	1d	24-Jun-25	24-Jun-25
Equipment					
A4560	Prepare Submittals - Electrical - Equipment	20d	20d	22-Apr-25	19-May-25
A4570	Approve Submittals - Electrical - Equipment	15d	15d	20-May-25	10-Jun-25
A4580	Fabricate - Electrical - Equipment	65d	65d	11-Jun-25	11-Sep-25
A4590	Deliver - Electrical - Equipment	1d	1d	11-Sep-25	11-Sep-25
Lighting					
A4600	Prepare Submittals - Electrical - Lighting	20d	20d	22-Apr-25	19-May-25
A4610	Approve Submittals - Electrical - Lighting	15d	15d	20-May-25	10-Jun-25
A4620	Fabricate - Electrical - Lighting	65d	65d	11-Jun-25	11-Sep-25
A4630	Deliver - Electrical - Lighting	1d	1d	11-Sep-25	11-Sep-25
31.01 - Sitework (Balance)					
A10990	OAL & Award - Site / Utilities	10d	10d	05-May-25	16-May-25
A11000	Prepare Submittals - Site / Utilities	10d	10d	19-May-25	02-Jun-25
A11010	Approve Submittals - Site / Utilities	10d	10d	03-Jun-25	16-Jun-25
A11020	Fabricate - Site / Utilities	5d	5d	17-Jun-25	23-Jun-25
A11030	Deliver - Site / Utilities	1d	1d	23-Jun-25	23-Jun-25
32.01 Landscaping					
A49300	OAL & Award- Landscaping	10d	10d	19-May-25	02-Jun-25
A25950	Prepare Submittals - Landscaping	10d	10d	03-Jun-25	16-Jun-25
A25960	Approve Submittals - Landscaping	15d	15d	17-Jun-25	08-Jul-25
A48640	Fabricate - Natural Fields	10d	10d	09-Jul-25	22-Jul-25
A48700	Deliver - Natural Fields	1d	1d	01-Sep-28	01-Sep-28
32.30 Site Improvement					
A49310	OAL & Award- Site Improvements	10d	10d	19-May-25	02-Jun-25
A49030	Prepare Submittals - Site Improvements	15d	15d	03-Jun-25	23-Jun-25
A49040	Approve Submittals - Site Improvements	15d	15d	24-Jun-25	15-Jul-25
A49050	Fabricate - Site Improvements	40d	40d	16-Jul-25	10-Sep-25
A49060	Deliver - Site Improvements [s]	1d	1d	10-Sep-25	10-Sep-25
BP #6 HVAC					
23.01 HVAC [TS]					
A1600	Bidding - Mechanical [TS]	21d	21d	03-Apr-25	02-May-25
A193290	OAL & Award- Mechanical	10d	10d	05-May-25	16-May-25
Basic Material					

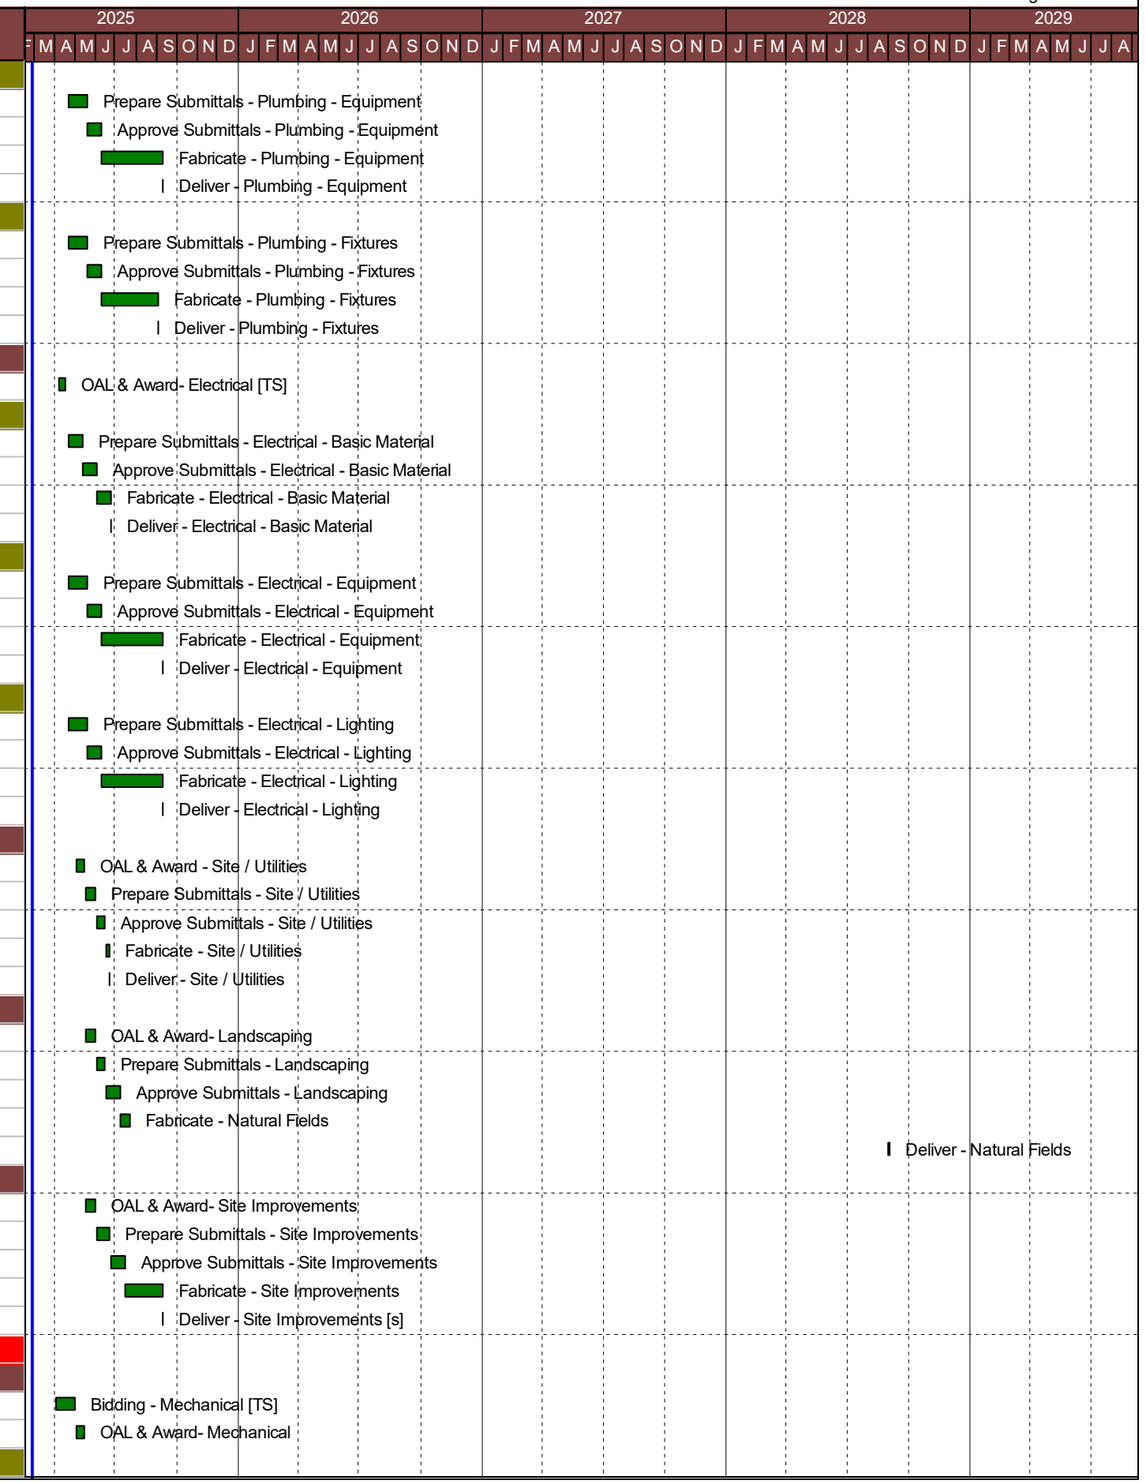

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A1610	Prepare Submittals - Mechanical - Basic Material	15d	15d	05-May-25	23-May-25
A1620	Approve Submittals - Mechanical - Basic Material	15d	15d	27-May-25	16-Jun-25
A1630	Fabricate - Mechanical - Basic Material	15d	15d	17-Jun-25	08-Jul-25
A192450	Fabricate - Mechanical - Equipment Curbs	40d	40d	17-Jun-25	12-Aug-25
A1750	Deliver - Mechanical - Basic Material	1d	1d	08-Jul-25	08-Jul-25
Equipment					
A4520	Prepare Submittals - Mechanical - Equipment	20d	20d	19-May-25	16-Jun-25
A7800	Prepare Submittals - AHU - Chillers - Mechanical- Equipment	20d	20d	19-May-25	16-Jun-25
A4530	Approve Submittals - Mechanical - Equipment	15d	15d	17-Jun-25	08-Jul-25
A7810	Approve Submittals - AHU - Chillers - Mechanical- Equipment	15d	15d	17-Jun-25	08-Jul-25
A4540	Fabricate - Mechanical - Equipment	80d	80d	09-Jul-25	30-Oct-25
A7740	Fabricate - Mechanical - AHU - Chillers - Equipment	150d	150d	09-Jul-25	12-Feb-26
A4550	Deliver - Mechanical - Equipment	1d	1d	30-Oct-25	30-Oct-25
A7750	Deliver - Mechanical - AHU - Chillers - Equipment	1d	1d	13-Feb-26	13-Feb-26
MOCK-UPS					
Procurement					
Damproofing / Waterproofing					
A190600	Prepare Submittals - Mock-up - Damproofing / Waterproofing	10d	10d	03-Mar-25	14-Mar-25
A190610	Approve Submittals - Mock-up - Damproofing / Waterproofing	10d	10d	17-Mar-25	28-Mar-25
A190620	Fabricate & Deliver - Mock-up - Damproofing / Waterproofing	10d	10d	31-Mar-25	11-Apr-25
Joint Sealants					
A190840	Prepare Submittals - Mock-up - Joint Sealant	10d	10d	03-Mar-25	14-Mar-25
A190850	Approve Submittals - Mock-up - Joint Sealant	10d	10d	17-Mar-25	28-Mar-25
A190860	Fabricate & Deliver - Mock-up - Joint Sealant	10d	10d	31-Mar-25	11-Apr-25
Framing					
A190630	Prepare Submittals - Mock-up - Framing	10d	10d	06-May-25	19-May-25
A190640	Approve Submittals - Mock-up - Framing	10d	10d	20-May-25	03-Jun-25
A190650	Fabricate & Deliver - Mock-up - Framing	10d	10d	04-Jun-25	17-Jun-25
Granite / CMU					
A190900	Prepare Submittals - Mock-up - Granite / CMU	20d	20d	22-Apr-25	19-May-25
A190910	Approve Submittals - Mock-up - Granite / CMU	10d	10d	20-May-25	03-Jun-25
A190920	Fabricate & Deliver - Mock-up - Granite / CMU	40d	40d	04-Jun-25	30-Jul-25
Precast					
A190870	Prepare Submittals - Mock-up - Precast	30d	30d	03-Mar-25	11-Apr-25
A190880	Approve Submittals - Mock-up - Precast	10d	10d	14-Apr-25	28-Apr-25
A190890	Fabricate & Deliver - Mock-up - Precast (confirm duration)	50d	50d	29-Apr-25	09-Jul-25
Windows					
A190660	Prepare Submittals - Mock-up - Windows	30d	30d	22-Apr-25	03-Jun-25
A190670	Approve Submittals - Mock-up - Windows	10d	10d	04-Jun-25	17-Jun-25
A190680	Fabricate & Deliver - Mock-up - Windows	70d	70d	18-Jun-25	25-Sep-25
Curtainwall					
A190690	Prepare Submittals - Mock-up - Curtainwall	30d	30d	22-Apr-25	03-Jun-25
A190700	Approve Submittals - Mock-up - Curtainwall	10d	10d	04-Jun-25	17-Jun-25
A190710	Fabricate & Deliver - Mock-up - Curtainwall	70d	70d	18-Jun-25	25-Sep-25
ACM Metal Metal Panel					
A190720	Prepare Submittals - Mock-up - ACM Metal Panel	20d	20d	23-Jun-25	21-Jul-25
A190730	Approve Submittals - Mock-up - ACM Metal Panel	10d	10d	22-Jul-25	04-Aug-25
A190740	Fabricate & Deliver - Mock-up - ACM Metal Panel	60d	60d	05-Aug-25	29-Oct-25
Insulated Metal Panel					

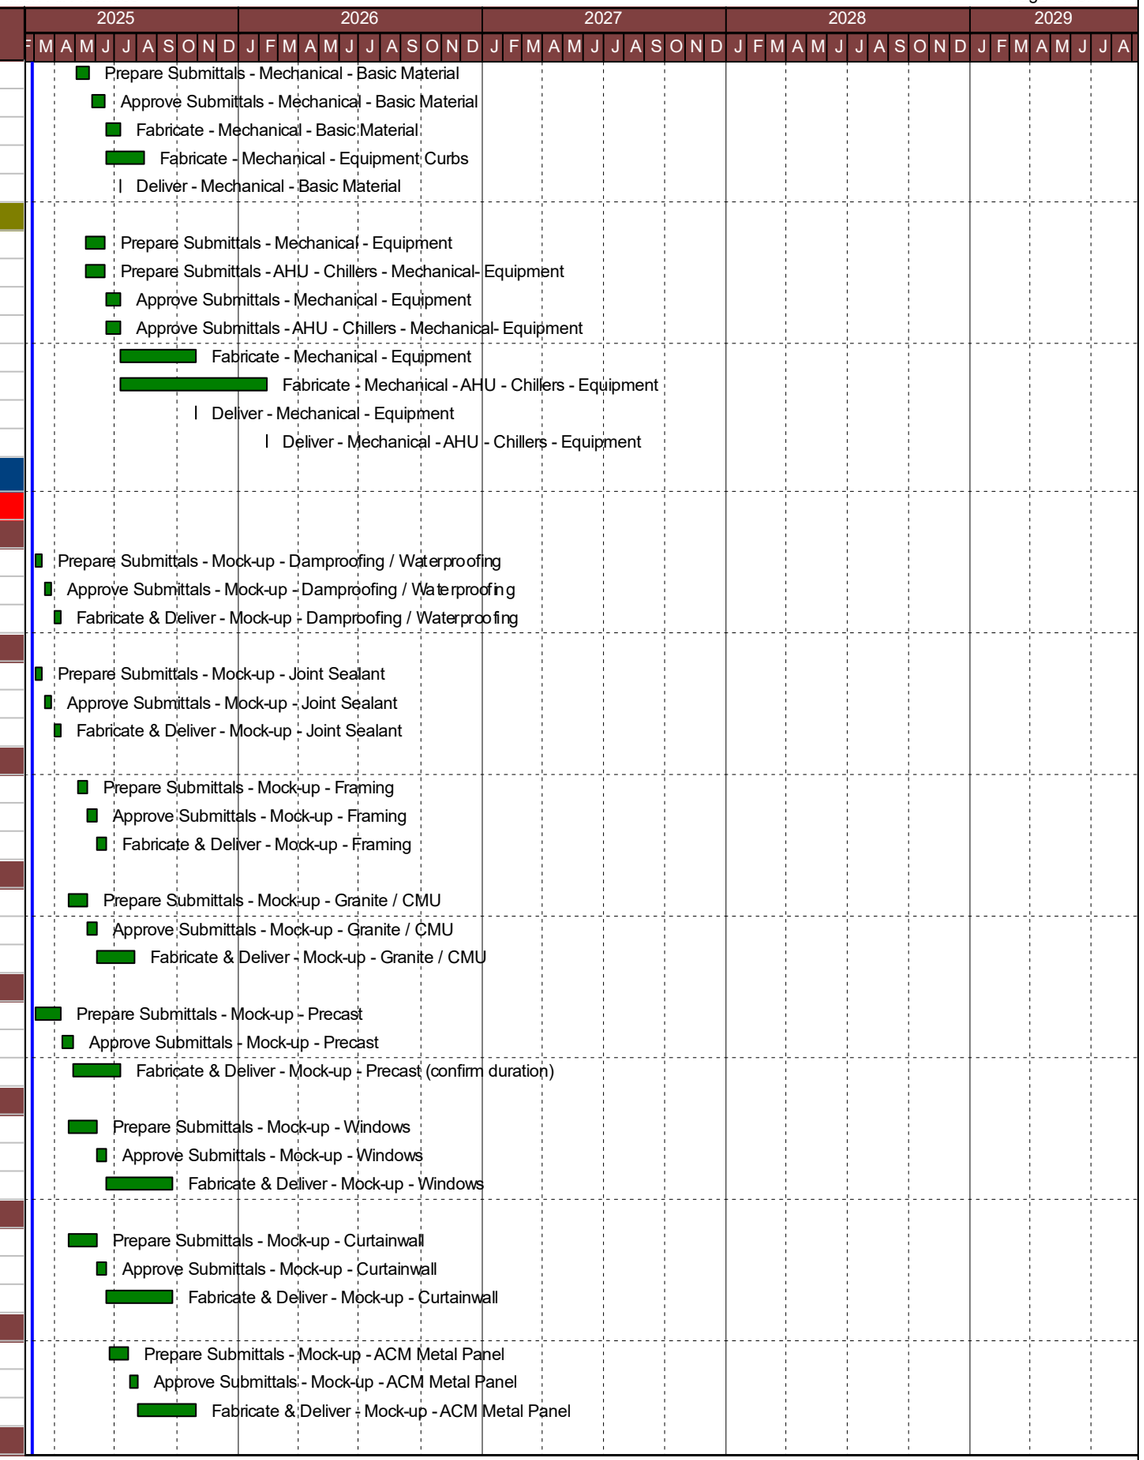

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A190750	Prepare Submittals - Mock-up - Insulated Metal Panel	20d	20d	23-Jun-25	21-Jul-25
A190760	Approve Submittals - Mock-up - Insulated Metal Panel	10d	10d	22-Jul-25	04-Aug-25
A190770	Fabricate & Deliver - Mock-up - Insulated Metal Panel	60d	60d	05-Aug-25	29-Oct-25
Flatlock Metal Panel					
A190780	Prepare Submittals - Mock-up - Flatlock Metal Panel	20d	20d	23-Jun-25	21-Jul-25
A190790	Approve Submittals - Mock-up - Flatlock Metal Panel	10d	10d	22-Jul-25	04-Aug-25
A190800	Fabricate & Deliver - Mock-up - Flatlock Metal Panel	30d	30d	05-Aug-25	16-Sep-25
Roof Edge					
A190810	Prepare Submittals - Mock-up - Roof Edge	20d	20d	22-Apr-25	19-May-25
A190820	Approve Submittals - Mock-up - Roof Edge	10d	10d	20-May-25	03-Jun-25
A190830	Fabricate & Deliver - Mock-up - Roof Edge	20d	20d	04-Jun-25	01-Jul-25
Construction					
Precast					
A190440	Prepare SD - Precast Mock-up	22d	0d	20-Jan-25 A	30-Jan-25 A
A192790	Approve SD - Precast Mock-up	10d	2d	30-Jan-25 A	28-Feb-25
A190450	Place Concrete Slabs - Precast Mock-up	3d	3d	01-Apr-25*	03-Apr-25
A190460	Install / Connect / Support Precast Panels - Precast Mock-up	5d	5d	10-Jul-25	16-Jul-25
A190570	Approve Precast Panels - Precast Mock-up	5d	5d	17-Jul-25	23-Jul-25
A190470	Install & Waterproofing Windows - Precast Mock-up	3d	3d	26-Sep-25	30-Sep-25
A190480	Joint Sealants - Precast Mock-up	2d	2d	01-Oct-25	02-Oct-25
A190580	Approve Waterproofing Windows - Precast Mock-up	5d	5d	01-Oct-25	07-Oct-25
A190590	Approve Joint Sealants - Precast Mock-up	5d	5d	03-Oct-25	09-Oct-25
General Facade					
A190430	Prepare Drawing - Facade Mock-up	22d	2d	20-Jan-25 A	28-Feb-25
A190340	Place Concrete Slabs - Facade Mock-up	3d	3d	01-Apr-25*	03-Apr-25
A190345	Install Damproofing / Waterproofing on Foundation - Facade Mock-up	2d	2d	14-Apr-25	15-Apr-25
A190350	Framing / Sheathing / Blocking - Facade Mock-up	5d	5d	18-Jun-25	24-Jun-25
A190490	Approve Frame & Sheath - Facade Mock-up	5d	5d	25-Jun-25	01-Jul-25
A190360	Install Granite & CMU - Facade Mock-up	5d	5d	31-Jul-25	06-Aug-25
A190500	Approve Granite & CMU - Facade Mock-up	5d	5d	07-Aug-25	13-Aug-25
A190370	Install Windows - Facade Mock-up	3d	3d	26-Sep-25	30-Sep-25
A190380	Install Curtainwall - Facade Mock-up	5d	5d	01-Oct-25	07-Oct-25
A190510	Approve Windows - Facade Mock-up	5d	5d	01-Oct-25	07-Oct-25
A190520	Approve Curtainwall - Facade Mock-up	5d	5d	08-Oct-25	15-Oct-25
A190390	Install ACM Metal Panel - Facade Mock-up	4d	4d	30-Oct-25	04-Nov-25
A190400	Install Insulated Metal Panel - Facade Mock-up	2d	2d	05-Nov-25	06-Nov-25
A190530	Approve ACM Metal Panel - Facade Mock-up	5d	5d	05-Nov-25	12-Nov-25
A190410	Install Flat Lock Metal Panel - Facade Mock-up	3d	3d	07-Nov-25	12-Nov-25
A190540	Approve Insulated Metal Panel - Facade Mock-up	5d	5d	07-Nov-25	14-Nov-25
A190420	Install Roof Edge Detail - Facade Mock-up	2d	2d	13-Nov-25	14-Nov-25
A190930	Joint Sealants - Facade Mock-up	2d	2d	13-Nov-25	14-Nov-25
A190550	Approve Flat Lock Metal Panel - Facade Mock-up	5d	5d	13-Nov-25	19-Nov-25
A190560	Approve Roof Edge Detail - Facade Mock-up	5d	5d	17-Nov-25	21-Nov-25
A190940	Approve Joint Sealants - Facade Mock-up	5d	5d	17-Nov-25	21-Nov-25
MEP/FP COORDINATION					
MEP/FP-140	Enhanced Coordination - Kick-Off Meeting	0d	0d	09-Oct-24 A	
MEP/FP-130	Enhanced Coordination	96d	30d	20-Nov-24 A	09-Apr-25
MEP/FP-100	MEP/FP Coordination - Underground & Risers	30d	30d	06-May-25	17-Jun-25
MEP/FP-110	MEP/FP Coordination - Bldg A - L2 & L3 + Auditorium + Gym	40d	40d	19-May-25	15-Jul-25

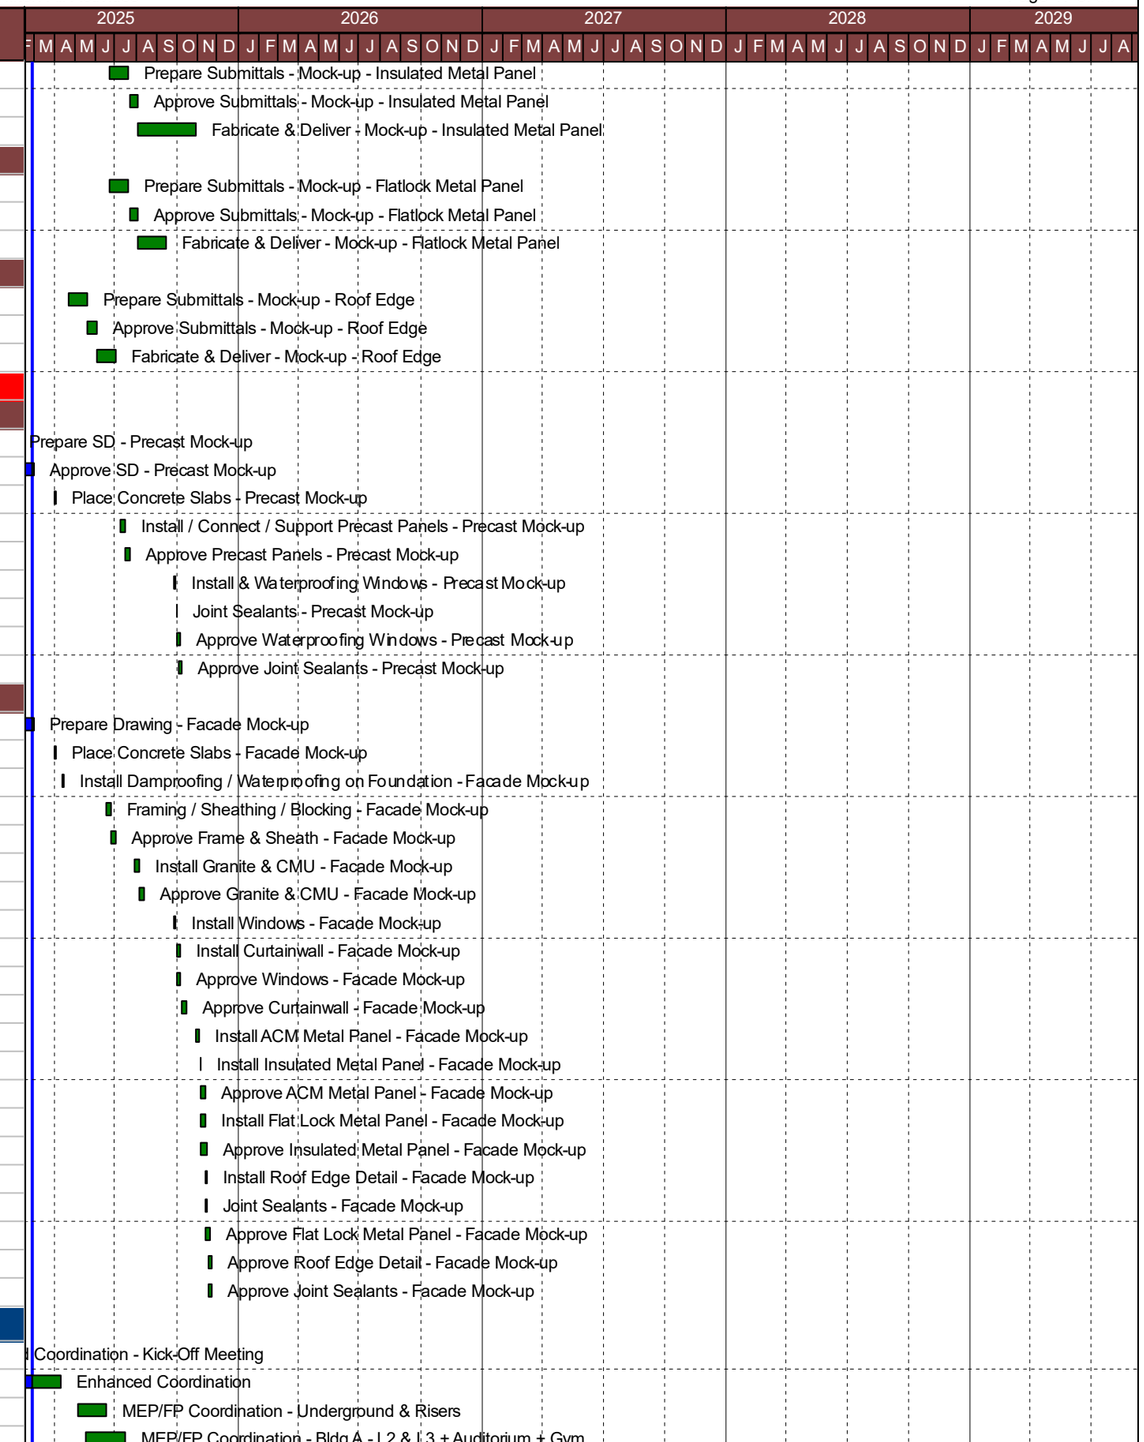

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
MEP/FP-160	MEP/FP Coordination - Bldg A - L1	40d	40d	03-Jun-25	29-Jul-25
MEP/FP-150	MEP/FP Coordination - Bldg B - L3	15d	15d	16-Jul-25	05-Aug-25
MEP/FP-120	MEP/FP Coordination - Bldg B,C, D, E - L2	30d	30d	30-Jul-25	10-Sep-25
MEP/FP-170	MEP/FP Coordination - Bldg B,C, D, E - L1 + Mezz	50d	50d	13-Aug-25	23-Oct-25
PRE-OP MEETINGS					
A186340	Pre-Op Meeting - Concrete	0d	0d	16-Jan-25 A	
A186360	Pre-Op Meeting - Geo-Thermal	0d	0d	27-Feb-25*	
A186350	Pre-Op Meeting - Steel	0d	0d	12-May-25	
CONSTRUCTION					
Enabling: Softball Field, Lower Parking Lot and Site Access Road					
Temporary/Permanent Student and Staff Parking Lot West of Existing School					
A8250	Mobilize	1d	0d	08-Jul-24 A	08-Jul-24 A
A8280	Install Temp Fence - Parking Lot	3d	0d	08-Jul-24 A	12-Jul-24 A
A8260	Layout - Parking Lot	1d	0d	09-Jul-24 A	10-Jul-24 A
A8270	Install Erosion Control - Parking Lot	3d	0d	17-Jul-24 A	19-Jul-24 A
A8300	Strip Existing Surfaces - Parking Lot	2d	0d	22-Jul-24 A	26-Jul-24 A
A8290	Demo Existing Backstop & Structures - Parking Lot	2d	0d	25-Jul-24 A	26-Jul-24 A
A8890	Excavate for Structures - Parking Lot	15d	0d	05-Aug-24 A	26-Aug-24 A
A8950	Install Water Retention System - Parking Lot	7d	0d	16-Aug-24 A	27-Aug-24 A
A9230	Make Connections - Parking Lot	7d	0d	21-Aug-24 A	27-Aug-24 A
A8310	Rough Grade / Fill - Parking Lot	3d	0d	22-Aug-24 A	27-Aug-24 A
A9750	Install Temp Lighting - Parking Lot	3d	0d	27-Aug-24 A	27-Aug-24 A
A9740	Remove Temp Fencing - Parking Lot	3d	0d	27-Aug-24 A	30-Aug-24 A
A8320	Install Loam & Seed - Parking Lot	2d	0d	27-Aug-24 A	30-Aug-24 A
A9720	Paving - Parking Lot	1d	0d	01-Sep-24 A	01-Sep-24 A
A9730	Striping - Parking Lot	1d	0d	02-Sep-24 A	02-Sep-24 A
A9920	Install Water Quality Units - Parking Lot (during school break)	6d	6d	18-Apr-25	23-Apr-25
Softball Field					
A8510	Subgrade for In-Field - Softball	2d	0d	17-Sep-24 A	18-Sep-24 A
A8570	Excavate & Set Sonotubes for Backstop Footings - Softball	2d	0d	03-Oct-24 A	08-Oct-24 A
A8590	FRP Backstop Footings - Softball	2d	0d	04-Oct-24 A	11-Oct-24 A
A8580	Install Vertical Posts for Backstop - Softball	3d	0d	21-Oct-24 A	22-Oct-24 A
A8530	Install Backstop - Softball	3d	0d	22-Oct-24 A	22-Oct-24 A
A8640	Install Softball Netting System	7d	0d	19-Nov-24 A	26-Nov-24 A
A8550	Landscape Touch-Up to Existing Field - Softball	1d	0d	20-Dec-24 A	20-Dec-24 A
Water Main					
A9760	Layout - Water Main	1d	0d	23-Jul-24 A	23-Jul-24 A
A9770	Excavate in Street - Water Main	1d	0d	24-Jul-24 A	24-Jul-24 A
A9780	Install Pipe & Tees - Water Main	1d	0d	26-Jul-24 A	26-Jul-24 A
A9800	Connect to Existing - Water Main	1d	0d	26-Jul-24 A	26-Jul-24 A
A9790	Continue Pipe Down Tri-County Drive - Water Main	2d	0d	29-Jul-24 A	20-Aug-24 A
A9815	Backfill - Water Main	1d	0d	21-Aug-24 A	21-Aug-24 A
A9810	Test - Water Main	1d	0d	22-Aug-24 A	22-Aug-24 A
A9820	Paving - Water Main	1d	0d	01-Sep-24 A	01-Sep-24 A
Shift Existing East Road					
A8370	Make Safe Existing Electric (in conflict with road)	2d	0d	29-Jul-24 A	29-Jul-24 A
A8380	Strip & Remove Existing Landscaping & Sidewalk	2d	0d	01-Aug-24 A	06-Aug-24 A
A8360	Install School Access Roadway & Temp Sidewalk	3d	0d	27-Aug-24 A	01-Sep-24 A
A8520	Additional Time - Construction Roadway & Temp Sidewalk Per CR004	10d	0d	01-Sep-24 A	01-Sep-24 A

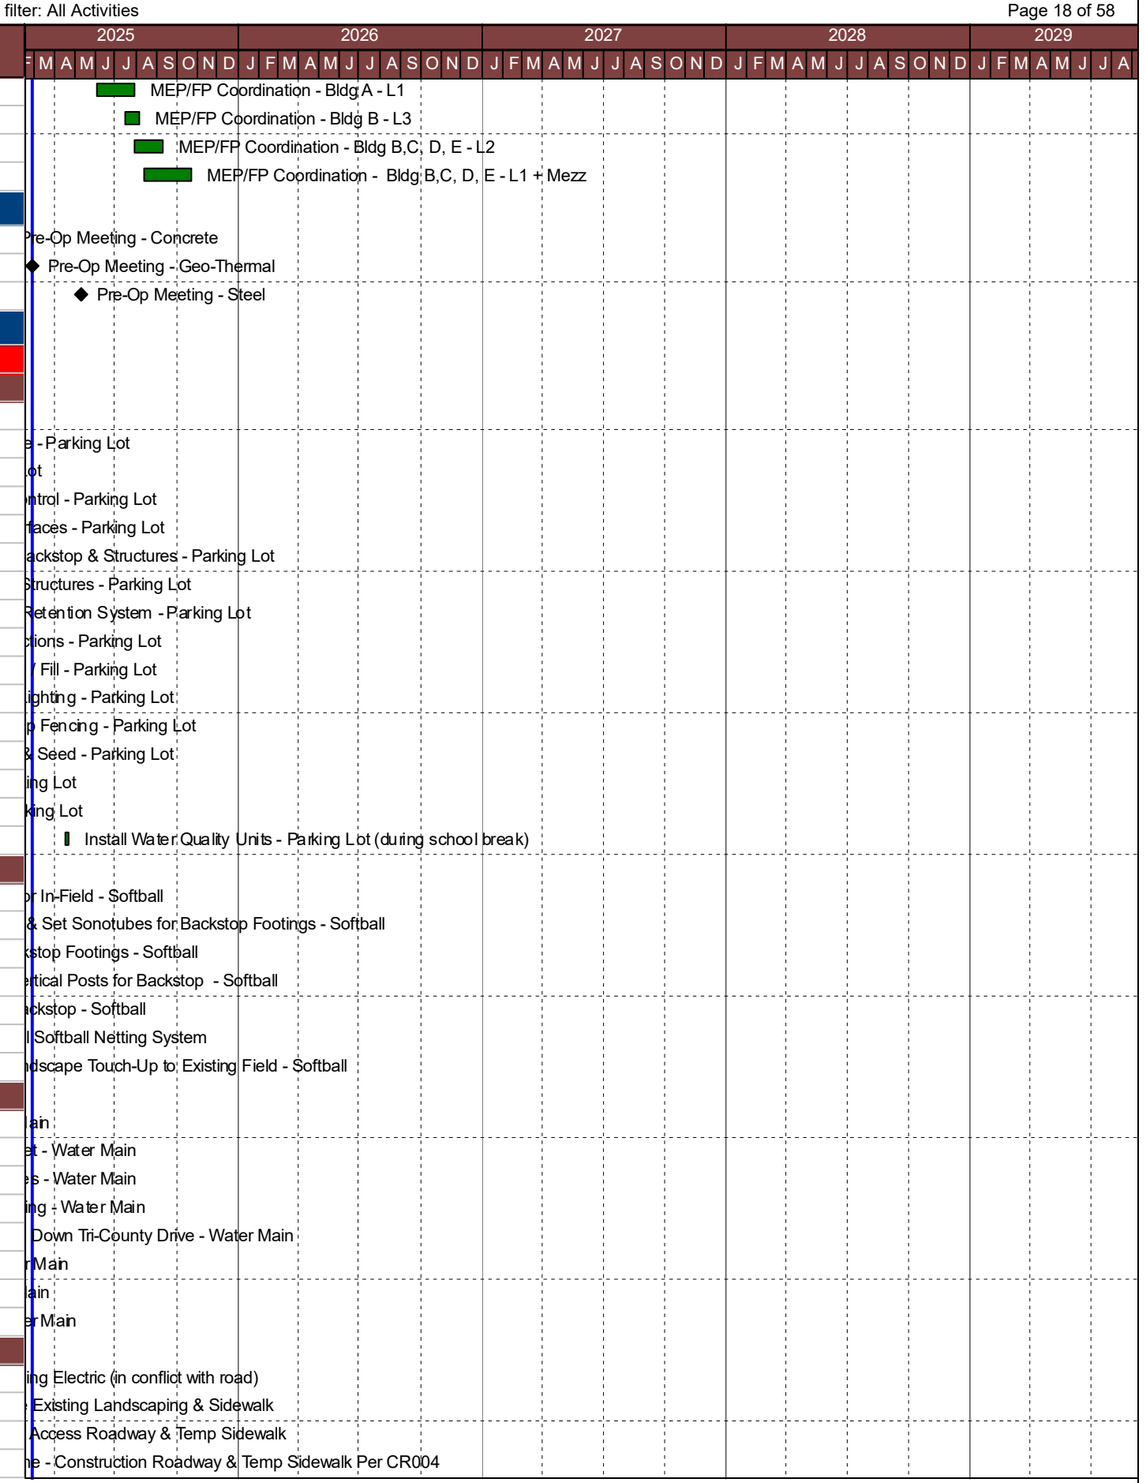

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
Temporary Roadway from Tri-County Drive up to Jobsite					
A8230	Tree Clearing for Access Road	5d	0d	27-Aug-24 A	03-Sep-24 A
A8220	Erosion Control	2d	0d	03-Sep-24 A	09-Sep-24 A
A8540	Erosion Control Inspection by ConComm	1d	0d	03-Sep-24 A	11-Sep-24 A
A8420	Test Pits	1d	0d	12-Sep-24 A	12-Sep-24 A
A8560	Stumping for Access Road	3d	0d	12-Sep-24 A	16-Sep-24 A
A8600	Blasting & Rock Drilling	10d	0d	23-Sep-24 A	07-Oct-24 A
A8880	Hammer Ledge Near Existing Gas Line	5d	0d	08-Oct-24 A	01-Nov-24 A
A8340	Excavate & Install Utilities	20d	0d	08-Oct-24 A	17-Dec-24 A
A8240	Cut / Fill for Roadway	2d	0d	29-Nov-24 A	18-Dec-24 A
A8350	Install Binder	1d	0d	20-Dec-24 A	20-Dec-24 A
A8330	Install Jersey Barriers & Fence	7d	0d	02-Jan-25 A	10-Jan-25 A
A8500	Install Construction Gate	5d	0d	15-Jan-25 A	28-Jan-25 A
A8490	Install Wheel Cleaning Area	2d	2d	13-Mar-25*	14-Mar-25
Early Site / Utility					
A8390	Wetlands Protection & Temp Fencing	5d	0d	16-Aug-24 A	16-Aug-24 A
A8400	Flag Wetlands (by Owner)	0d	0d		16-Aug-24 A
A8470	Install Temp Signage	2d	0d	29-Aug-24 A	30-Aug-24 A
A9250	Stumping	5d	0d	12-Sep-24 A	16-Sep-24 A
A8410	Strip Existing & Export Top Soil & Asphalt	24d	0d	16-Sep-24 A	18-Oct-24 A
A8440	Site Filling to Rough Grade	30d	0d	18-Sep-24 A	15-Nov-24 A
A9240	Strip Balance of Asphalt	2d	0d	07-Oct-24 A	30-Oct-24 A
A8800	Blasting for Utilities	18d	0d	07-Oct-24 A	05-Dec-24 A
A8450	Install Utilities Around Building	23d	12d	28-Oct-24 A	14-Mar-25
A8460	Pave Temp Road Around Perimeter of Building	1d	1d	01-Apr-25*	01-Apr-25
Phase 1: Building Footprint					
A7860	PV Field Removed (by Owner)	0d	0d	13-Aug-24 A	
A7690	Excavate for Building Cut	13d	0d	23-Oct-24 A	03-Dec-24 A
A7880	Fill Building Pad to 12" Below Slab	17d	0d	23-Oct-24 A	03-Dec-24 A
Phase 2: Building					
Structure & Shell					
Foundations / Waterproofing					
A2090	Excavate for Footings & Foundations - Building A - East	10d	17d	02-Jan-25 A	21-Mar-25
A25900	Excavate for Footings & Foundations - Building A - West	10d	17d	06-Jan-25 A	21-Mar-25
A25910	Excavate for Footings & Foundations - Building B	10d	22d	27-Jan-25 A	28-Mar-25
A8090	FRP Foundations Footings / Walls - Building A - East	15d	17d	03-Feb-25 A	21-Mar-25
A8100	FRP Foundations Footings / Walls - Building A - West	15d	17d	03-Feb-25 A	21-Mar-25
A8200	First Rebar Delivery - Bldg A (footings)	0d	0d	05-Feb-25 A	
A7970	FRP Perimeter Footings / Walls - Building B	25d	23d	25-Feb-25 A	31-Mar-25
A25920	Excavate for Footings & Foundations - Building C	10d	10d	28-Feb-25	13-Mar-25
A192600	FRP Masonry Support Footings / Walls - Building C	40d	40d	05-Mar-25	30-Apr-25
A192590	FRP Spread Footings - Building C	15d	15d	24-Mar-25	11-Apr-25
A7990	FRP Masonry Support Footings / Walls - Building B	5d	5d	25-Mar-25	31-Mar-25
A8430	Install Below Grade Damproofing - Building A	5d	5d	31-Mar-25	04-Apr-25
A23850	Waterproof Elevator Pit - Building A	5d	5d	31-Mar-25	04-Apr-25
A25930	Excavate for Footings & Foundations - Building D	10d	10d	01-Apr-25	14-Apr-25
A7980	FRP Spread Footings - Building B	10d	10d	01-Apr-25	14-Apr-25
A23800	Backfill Foundations - Building A	5d	5d	07-Apr-25	11-Apr-25
A23760	Install Below Grade Damproofing - Building B	3d	3d	08-Apr-25	10-Apr-25
A23810	Backfill Foundations - Building B	3d	3d	11-Apr-25	15-Apr-25

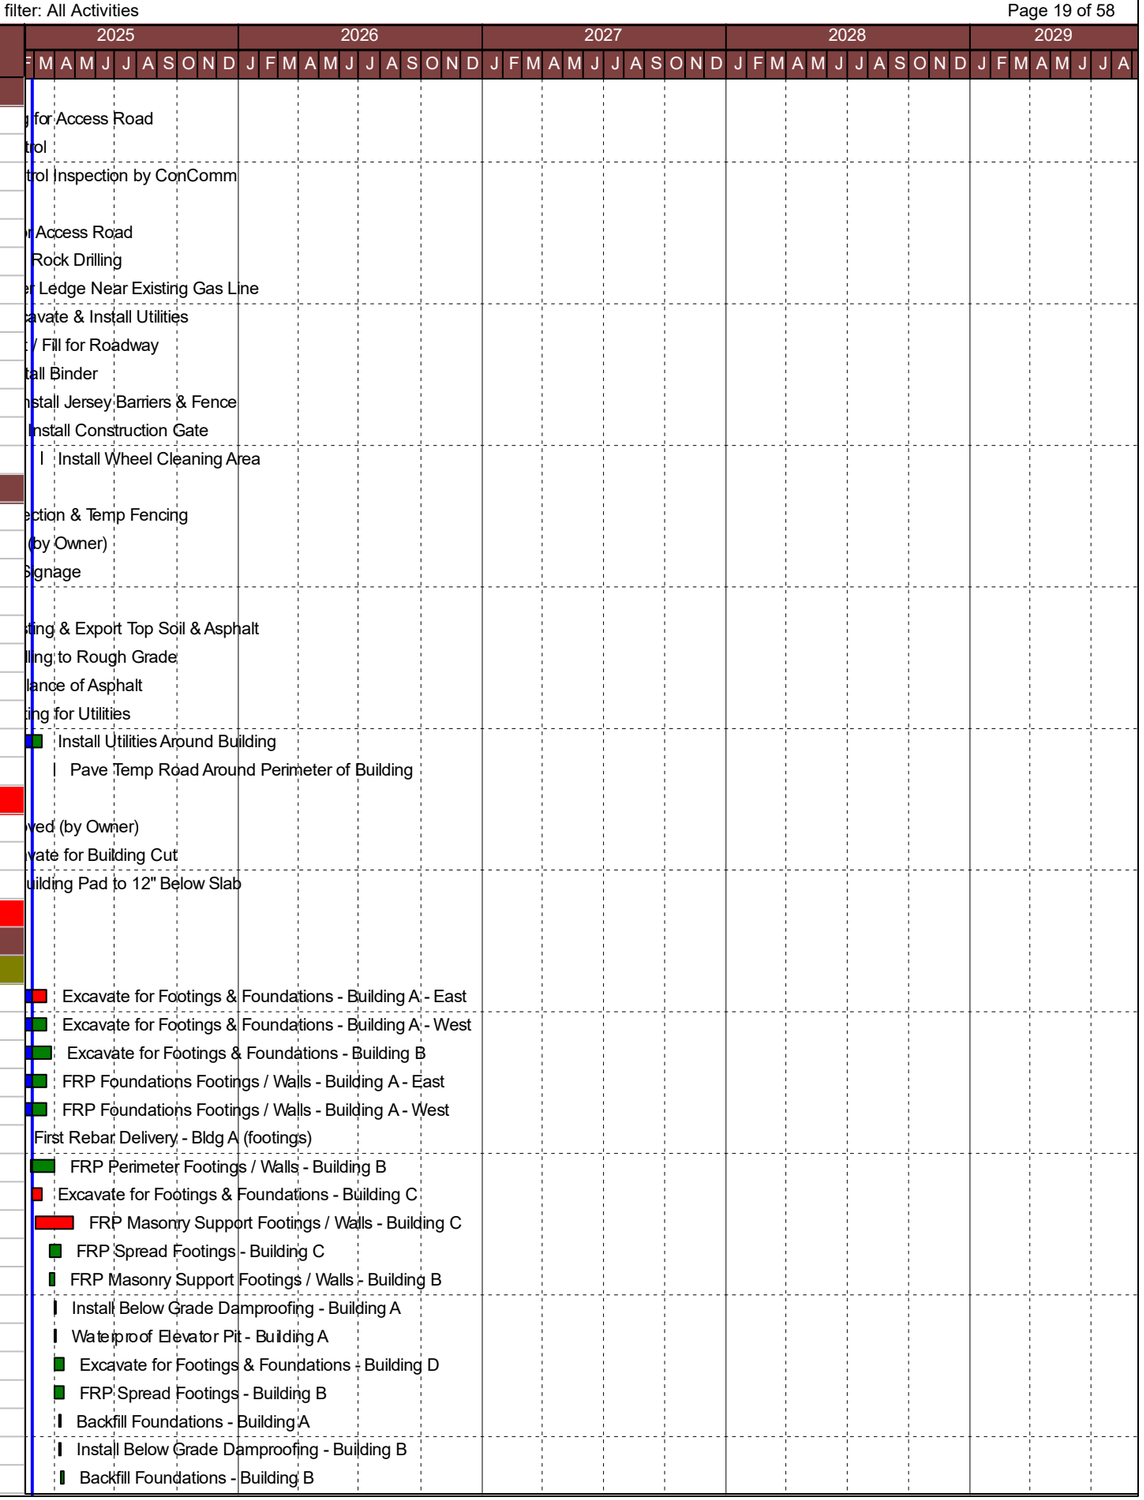

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A8120	FRP Perimeter Footings / Walls - Building D	25d	25d	15-Apr-25	20-May-25
A25940	Excavate for Footings & Foundations - Building E	10d	10d	16-Apr-25	30-Apr-25
A8110	FRP Perimeter Footings / Walls - Building C	25d	25d	16-Apr-25	21-May-25
A192620	FRP Masonry Support Footings / Walls - Building D	15d	15d	30-Apr-25	20-May-25
A192640	FRP Masonry Support Footings / Walls - Building E	30d	30d	01-May-25	12-Jun-25
A192610	FRP Spread Footings - Building D	10d	10d	21-May-25	04-Jun-25
A23860	Waterproof Elevator Pit - Building D	5d	5d	29-May-25	04-Jun-25
A23770	Install Below Grade Damproofing - Building C	5d	5d	30-May-25	05-Jun-25
A23820	Backfill Foundations - Building C	5d	5d	06-Jun-25	12-Jun-25
A23780	Install Below Grade Damproofing - Building D	3d	3d	12-Jun-25	16-Jun-25
A192630	FRP Spread Footings / Walls - Building E	10d	10d	13-Jun-25	26-Jun-25
A8130	FRP Perimeter Footings / Walls - Building E	20d	20d	13-Jun-25	11-Jul-25
A23830	Backfill Foundations - Building D	3d	3d	17-Jun-25	19-Jun-25
A23790	Install Below Grade Damproofing - Building E	5d	5d	21-Jul-25	25-Jul-25
A23840	Backfill Foundations - Building E	5d	5d	28-Jul-25	01-Aug-25
Steel / Fireproofing					
A188900	Install Structural CMU Interior Walls to Support Plank - Bldg A East	5d	5d	16-Apr-25	23-Apr-25
A188920	Install Structural CMU Interior Walls to Support Plank - Bldg C	10d	10d	24-Apr-25	07-May-25
A188910	Install Structural CMU Interior Walls to Support Plank - Bldg B	5d	5d	08-May-25	14-May-25
A8190	First Steel Delivery - Bldg A	0d	0d	22-May-25	
A8150	Erect Steel / Deck & Detail - Building A - West	30d	30d	22-May-25	03-Jul-25
A8140	Erect Steel / Deck & Detail - Building A - East	30d	30d	27-May-25	08-Jul-25
A8210	Install Mezz Precast Plank - Building A - East	3d	3d	28-May-25	30-May-25
A188930	Install Structural CMU Interior Walls to Support Plank - Bldg E	10d	10d	30-May-25	12-Jun-25
A9160	Install Mezz Precast Plank - Building B	2d	2d	02-Jun-25	03-Jun-25
A9170	Install Mezz Precast Plank - Building C	5d	5d	02-Jun-25	06-Jun-25
A9190	Install Mezz Precast Plank - Building E	5d	5d	13-Jun-25	19-Jun-25
A188940	Install Structural CMU Interior Walls to Support Plank - Bldg D	10d	10d	13-Jun-25	26-Jun-25
A7960	Erect Steel / Deck & Detail - Building B	30d	30d	13-Jun-25	25-Jul-25
A9180	Install Mezz Precast Plank - Building D	2d	2d	27-Jun-25	30-Jun-25
A8170	Erect Steel / Deck & Detail - Building D	20d	20d	08-Jul-25	04-Aug-25
A8160	Erect Steel / Deck & Detail - Building C	30d	30d	14-Jul-25	22-Aug-25
A8180	Erect Steel / Deck & Detail - Building E	23d	23d	04-Aug-25	04-Sep-25
Slabs / Underslab					
A3020	Install UG MEPs - Building A - West	10d	10d	07-Jul-25	18-Jul-25
A1950	FRP SOD - Bldg A - East - 2nd Fl	12d	12d	09-Jul-25	24-Jul-25
A8910	FRP SOD - Bldg A - West - 2nd Fl (including Monumental Stair)	12d	12d	09-Jul-25	24-Jul-25
A3010	Install UG MEPs - Building A - East	15d	15d	09-Jul-25	29-Jul-25
A9030	Install UG MEPs - Building B	10d	10d	21-Jul-25	01-Aug-25
A24260	Install Topping Slab @ Mezz - Bldg A - East	3d	3d	25-Jul-25	29-Jul-25
A8940	FRP SOD - Roof Pads - Bldg A	5d	5d	25-Jul-25	31-Jul-25
A8920	FRP SOD - Bldg A - West - 3rd Fl	12d	12d	25-Jul-25	11-Aug-25
A1970	FRP SOD - Bldg B - 2nd Fl	12d	12d	28-Jul-25	12-Aug-25
A9040	Install UG MEPs - Building C	10d	10d	04-Aug-25	15-Aug-25
A1960	FRP SOD - Bldg B - 3rd Fl	12d	12d	12-Aug-25	27-Aug-25
A24270	Install Topping Slab @ Mezz - Bldg B	3d	3d	13-Aug-25	15-Aug-25
A1920	Form, Reinforce, Place Slab on Decks	36d	36d	13-Aug-25	02-Oct-25
A8930	FRP SOG - Bldg A - West	12d	12d	15-Aug-25	02-Sep-25
A9050	Install UG MEPs - Building D	10d	10d	18-Aug-25	29-Aug-25
A8900	FRP SOG - Bldg A - East	12d	12d	22-Aug-25	09-Sep-25

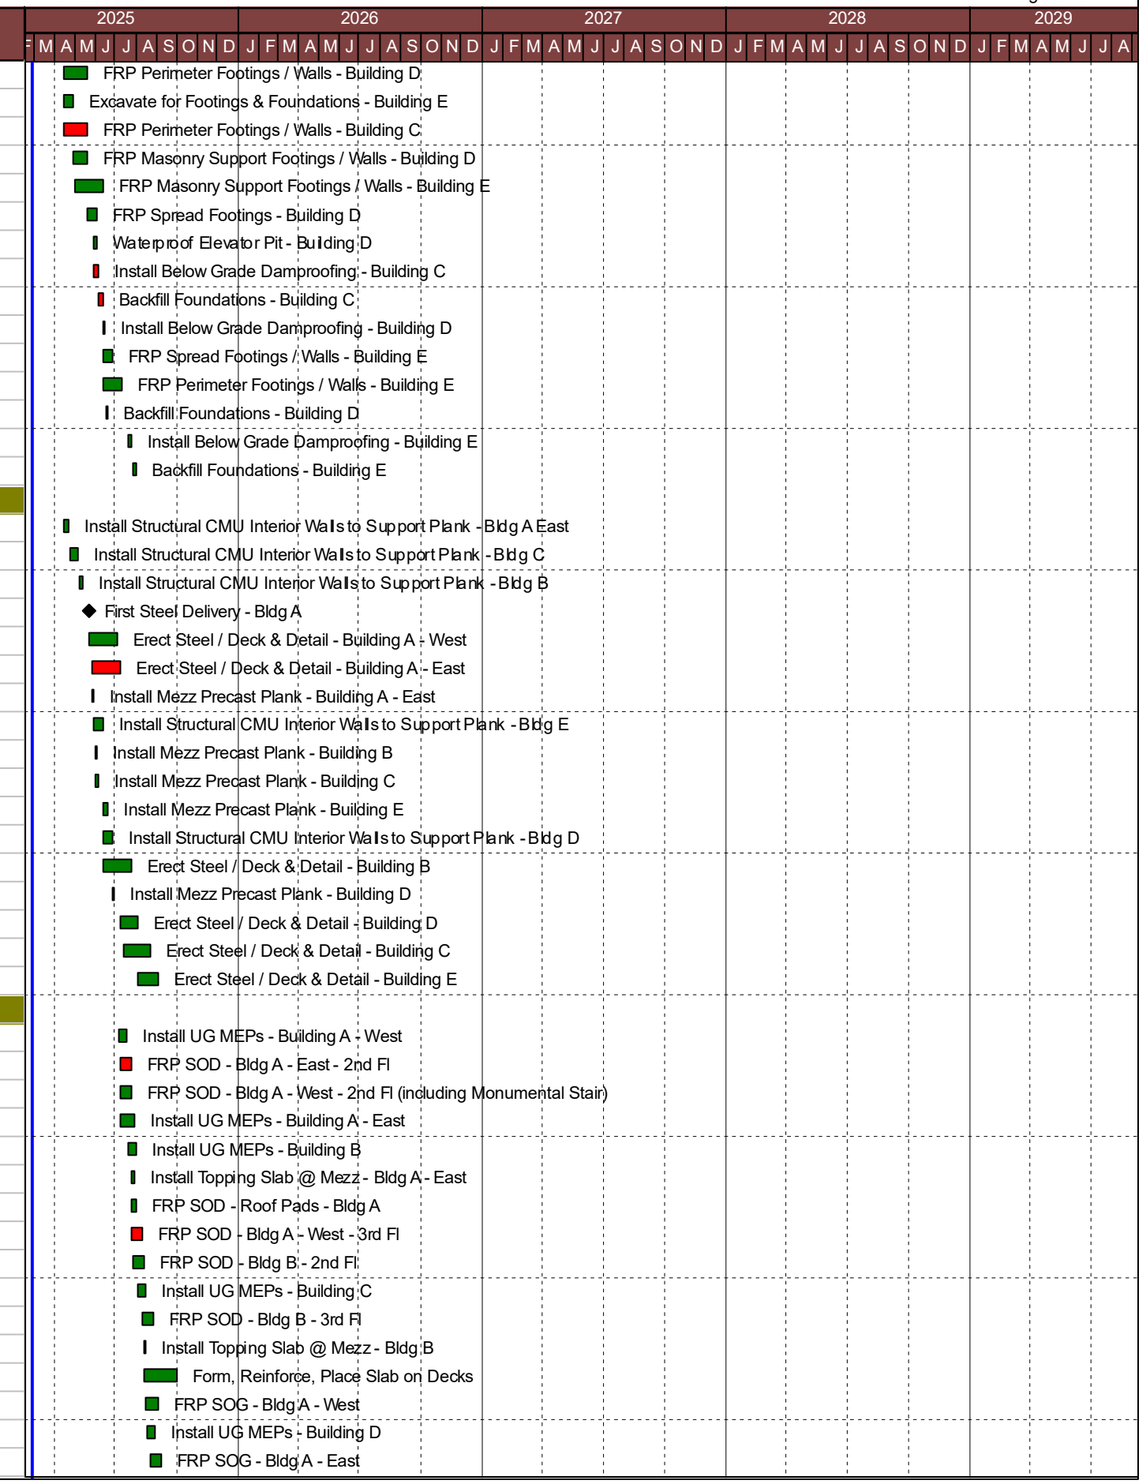

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A9560	FRP SOD - Roof Pads - Bldgs B &C	5d	5d	25-Aug-25	29-Aug-25
A8960	FRP SOD - Bldg C - 2nd Fl	12d	12d	25-Aug-25	10-Sep-25
A8990	FRP SOG - Bldg B	12d	12d	29-Aug-25	16-Sep-25
A9060	Install UG MEPs - Building E	10d	10d	02-Sep-25	15-Sep-25
A9570	FRP SOD - Roof Pads - Bldg D&E	5d	5d	05-Sep-25	11-Sep-25
A8980	FRP SOD - Bldg E - 2nd Fl	12d	12d	05-Sep-25	22-Sep-25
A24280	Install Topping Slab @ Mezz - Bldg C	5d	5d	11-Sep-25	17-Sep-25
A8970	FRP SOD - Bldg D - 2nd Fl	12d	12d	12-Sep-25	29-Sep-25
A9000	FRP SOG - Bldg C	12d	12d	19-Sep-25	06-Oct-25
A24300	Install Topping Slab @ Mezz - Bldg E	5d	5d	23-Sep-25	29-Sep-25
A24290	Install Topping Slab @ Mezz - Bldg D	3d	3d	30-Sep-25	02-Oct-25
A9020	FRP SOG - Bldg E	12d	12d	03-Oct-25	21-Oct-25
A3040	Form, Reinforce, Place Slab on Grade	31d	31d	03-Oct-25	18-Nov-25
A9010	FRP SOG - Bldg D	12d	12d	10-Oct-25	28-Oct-25
Roofing					
A7850	Install & Connect Rooftop Equipment	30d	30d	17-Feb-26	30-Mar-26
Building A					
A9300	Roof Blocking 1st Layer - Bldg A - West	8d	8d	07-Jul-25	16-Jul-25
A9260	Roof Blocking 1st Layer - Bldg A - East	8d	8d	09-Jul-25	18-Jul-25
A192460	Install Perimeter AVB (waterproofer & roofer) - Bldg A - West	5d	5d	15-Jul-25	21-Jul-25
A9710	Install Perimeter AVB (waterproofer & roofer) - Bldg A - East	5d	5d	17-Jul-25	23-Jul-25
A192470	Roof Blocking 2nd Layer - Bldg A - West	5d	5d	18-Jul-25	24-Jul-25
A10130	Roof Blocking 2nd Layer - Bldg A - East	5d	5d	22-Jul-25	28-Jul-25
A9310	Roof AVB - Bldg A - West	12d	12d	25-Jul-25	11-Aug-25
A9270	Roof AVB - Bldg A - East	12d	12d	29-Jul-25	13-Aug-25
A9580	Equipment Roof Curbs - Bldg A - West	5d	5d	13-Aug-25	19-Aug-25
A9590	Equipment Roof Curbs - Bldg A - East	5d	5d	13-Aug-25	19-Aug-25
A9280	Roofing - Bldg A - East	20d	20d	14-Aug-25	11-Sep-25
A9320	Roofing - Bldg A - West	20d	20d	20-Aug-25	17-Sep-25
A9510	Cut-in & Flash Roof Penetrations - Bldg A - East	5d	5d	12-Sep-25	18-Sep-25
A9290	Edge Metal - Bldg A - East	20d	20d	22-Jan-26	19-Feb-26
A9640	Set Roof Top Equipment - Bldg A - West	5d	5d	13-Feb-26	20-Feb-26
A9650	Set Roof Top Equipment - Bldg A - East	5d	5d	13-Feb-26	20-Feb-26
A9330	Edge Metal - Bldg A - West	20d	20d	20-Feb-26	19-Mar-26
A11310	Install Safety Rails - Bldg A - West	1d	1d	23-Feb-26	23-Feb-26
A9500	Cut-in & Flash Roof Penetrations - Bldg A - West	5d	5d	20-Mar-26	26-Mar-26
Building B					
A9340	Roof Blocking 1st Layer - Bldg B	5d	5d	28-Jul-25	01-Aug-25
A11330	Install Roof Screen - Bldg B	10d	10d	28-Jul-25	08-Aug-25
A192480	Install Perimeter AVB (waterproofer & roofer) - Bldg B	5d	5d	31-Jul-25	06-Aug-25
A192490	Roof Blocking 2nd Layer - Bldg B	5d	5d	05-Aug-25	11-Aug-25
A9350	Roof AVB - Bldg B	10d	10d	12-Aug-25	25-Aug-25
A9600	Equipment Roof Curbs - Bldg B	5d	5d	02-Sep-25	08-Sep-25
A9360	Roofing - Bldg B	20d	20d	18-Sep-25	16-Oct-25
A9520	Cut-in & Flash Roof Penetrations - Bldg B	5d	5d	17-Oct-25	23-Oct-25
A9660	Set Roof Top Equipment - Bldg B	5d	5d	13-Feb-26	20-Feb-26
A11320	Install Safety Rails - Bldg B	1d	1d	23-Feb-26	23-Feb-26
A9370	Edge Metal - Bldg B	15d	15d	25-Jun-26	15-Jul-26
Building C					
A11340	Install Roof Screen - Bldg C	5d	5d	25-Aug-25	29-Aug-25

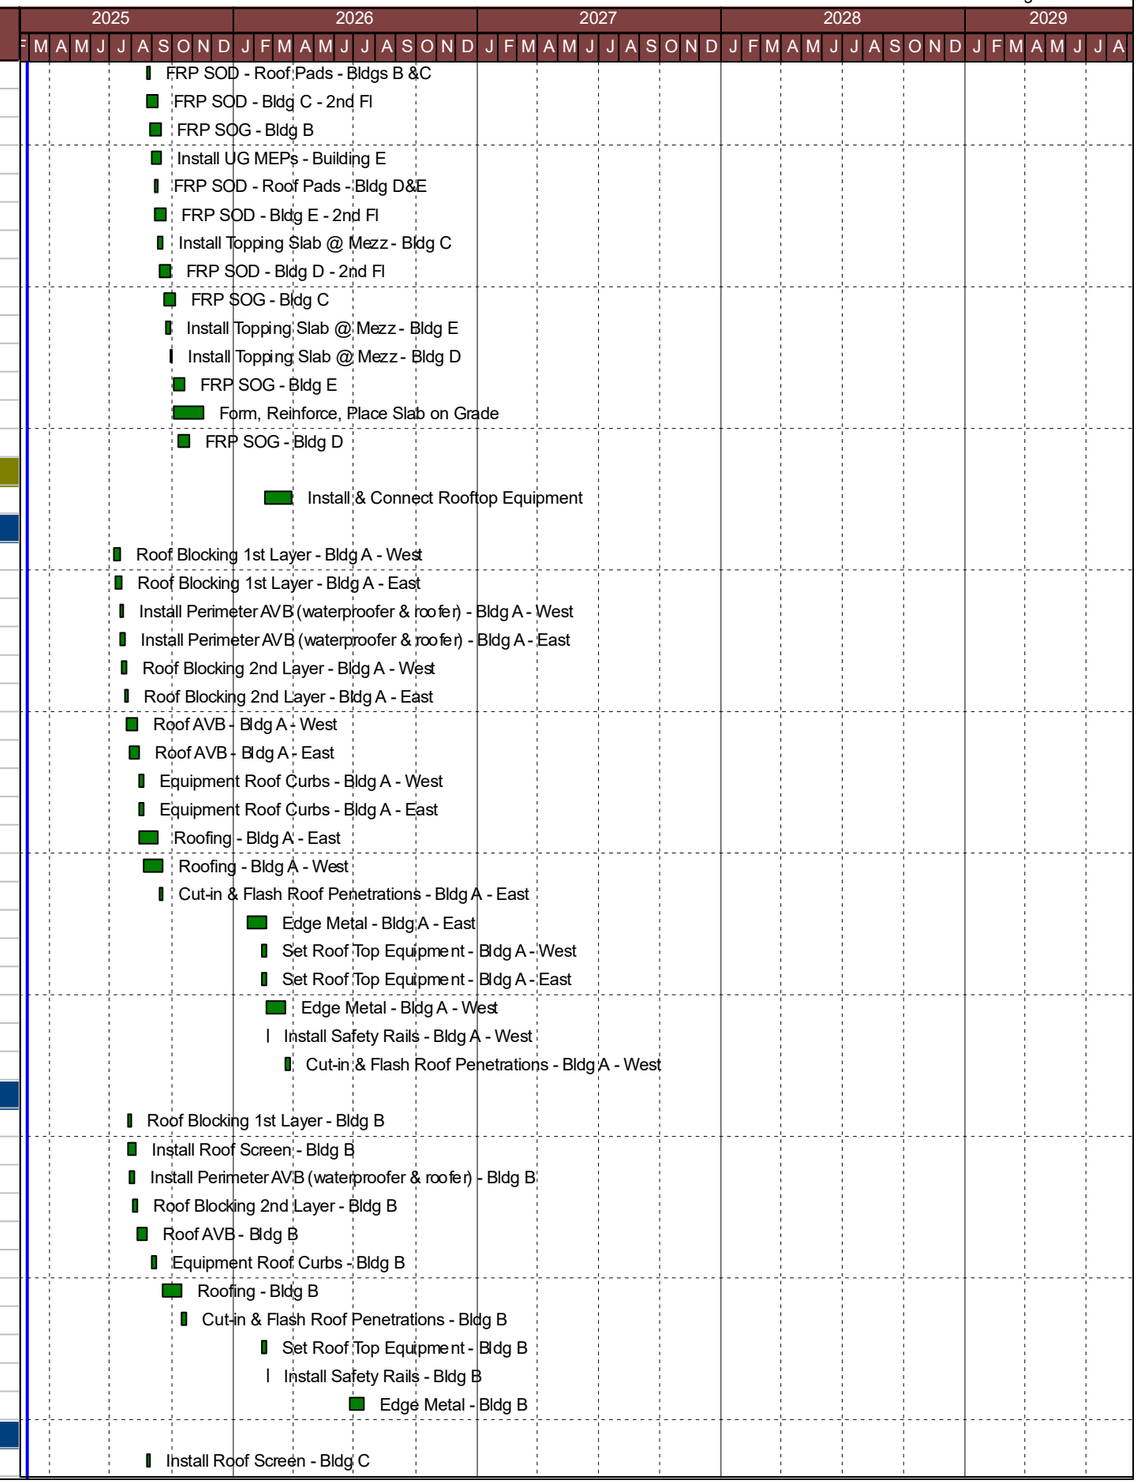

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A9380	Roof Blocking 1st Layer - Bldg C	8d	8d	25-Aug-25	04-Sep-25
A9610	Equipment Roof Curbs - Bldg C	5d	5d	02-Sep-25	08-Sep-25
A192500	Install Perimeter AVB (waterproofer & roofer) - Bldg C	5d	5d	03-Sep-25	09-Sep-25
A192510	Roof Blocking 2nd Layer - Bldg C	5d	5d	08-Sep-25	12-Sep-25
A9390	Roof AVB - Bldg C	16d	16d	15-Sep-25	06-Oct-25
A9400	Roofing - Bldg C	20d	20d	07-Oct-25	04-Nov-25
A9530	Cut-in & Flash Roof Penetrations - Bldg C	5d	5d	05-Nov-25	12-Nov-25
A9410	Edge Metal - Bldg C	20d	20d	05-Nov-25	04-Dec-25
A9670	Set Roof Top Equipment - Bldg C	5d	5d	13-Feb-26	20-Feb-26
Building D					
A9420	Roof Blocking 1st Layer - Bldg D	5d	5d	05-Aug-25	11-Aug-25
A192520	Install Perimeter AVB (waterproofer & roofer) - Bldg D	5d	5d	08-Aug-25	14-Aug-25
A192530	Roof Blocking 2nd Layer - Bldg D	5d	5d	13-Aug-25	19-Aug-25
A9430	Roof AVB - Bldg D	10d	10d	26-Aug-25	09-Sep-25
A9620	Equipment Roof Curbs - Bldg D	5d	5d	12-Sep-25	18-Sep-25
A9440	Roofing - Bldg D	10d	10d	17-Oct-25	30-Oct-25
A9540	Cut-in & Flash Roof Penetrations - Bldg D	5d	5d	31-Oct-25	06-Nov-25
A9680	Set Roof Top Equipment - Bldg D	5d	5d	13-Feb-26	20-Feb-26
A9450	Edge Metal - Bldg D	15d	15d	27-Mar-26	16-Apr-26
Building E					
A11350	Install Roof Screen - Bldg E	5d	5d	05-Sep-25	11-Sep-25
A9460	Roof Blocking 1st Layer - Bldg E	8d	8d	05-Sep-25	16-Sep-25
A9630	Equipment Roof Curbs - Bldg E	5d	5d	12-Sep-25	18-Sep-25
A192540	Install Perimeter AVB (waterproofer & roofer) - Bldg E	5d	5d	15-Sep-25	19-Sep-25
A192550	Roof Blocking 2nd Layer - Bldg E	5d	5d	18-Sep-25	24-Sep-25
A9470	Roof AVB - Bldg E	12d	12d	07-Oct-25	23-Oct-25
A9480	Roofing - Bldg E	20d	20d	05-Nov-25	04-Dec-25
A9550	Cut-in & Flash Roof Penetrations - Bldg E	5d	5d	05-Dec-25	11-Dec-25
A9490	Edge Metal - Bldg E	20d	20d	05-Dec-25	05-Jan-26
A9690	Set Roof Top Equipment - Bldg E	5d	5d	13-Feb-26	20-Feb-26
Spray Fireproofing					
A9900	Spray Fireproofing - Perimeter Struct & Slab Edge - Bldg A North	5d	5d	16-Jul-25	22-Jul-25
A10000	Spray Fireproofing - Perimeter Struct & Slab Edge - Bldg A West	5d	5d	16-Jul-25	22-Jul-25
A10010	Spray Fireproofing - Perimeter Struct & Slab Edge - Bldg A East	5d	5d	23-Jul-25	29-Jul-25
A10080	Spray Fireproofing - Perimeter Struct & Slab Edge - Bldg C East	5d	5d	25-Aug-25	29-Aug-25
A10070	Spray Fireproofing - Perimeter Struct & Slab Edge - Bldg E East	5d	5d	02-Sep-25	08-Sep-25
A9840	Spray Fireproofing - Bldg A - West - 3rd Fl PH	5d	5d	03-Sep-25	09-Sep-25
A10060	Spray Fireproofing - Perimeter Struct & Slab Edge - Bldg E South	5d	5d	09-Sep-25	15-Sep-25
A9990	Spray Fireproofing - Bldg A - West - 2nd Fl (inc roof deck)	7d	7d	10-Sep-25	18-Sep-25
A24990	Intumescent Paint - Bldg A - 2nd Fl	15d	15d	10-Sep-25	30-Sep-25
A10050	Spray Fireproofing - Perimeter Struct & Slab Edge - Bldg D South	5d	5d	16-Sep-25	22-Sep-25
A9860	Spray Fireproofing - Bldg B - 3rd Fl (inc roof deck)	6d	6d	16-Sep-25	23-Sep-25
A9830	Spray Fireproofing - Bldg A - East - 2nd Fl (inc roof deck)	5d	5d	19-Sep-25	25-Sep-25
A10040	Spray Fireproofing - Perimeter Struct & Slab Edge - Bldg D West	5d	5d	23-Sep-25	29-Sep-25
A9940	Spray Fireproofing - Bldg A - West - 1st Fl	5d	5d	26-Sep-25	02-Oct-25
A10030	Spray Fireproofing - Perimeter Struct & Slab Edge - Bldg B West	5d	5d	30-Sep-25	06-Oct-25
A25000	Intumescent Paint - Bldg A - 1st Fl	15d	15d	01-Oct-25	22-Oct-25
A9930	Spray Fireproofing - Bldg A - East - 1st Fl	5d	5d	03-Oct-25	09-Oct-25
A10020	Spray Fireproofing - Perimeter Struct & Slab Edge - Courtyard	5d	5d	07-Oct-25	14-Oct-25
A9850	Spray Fireproofing - Bldg B - 2nd Fl	5d	5d	10-Oct-25	17-Oct-25

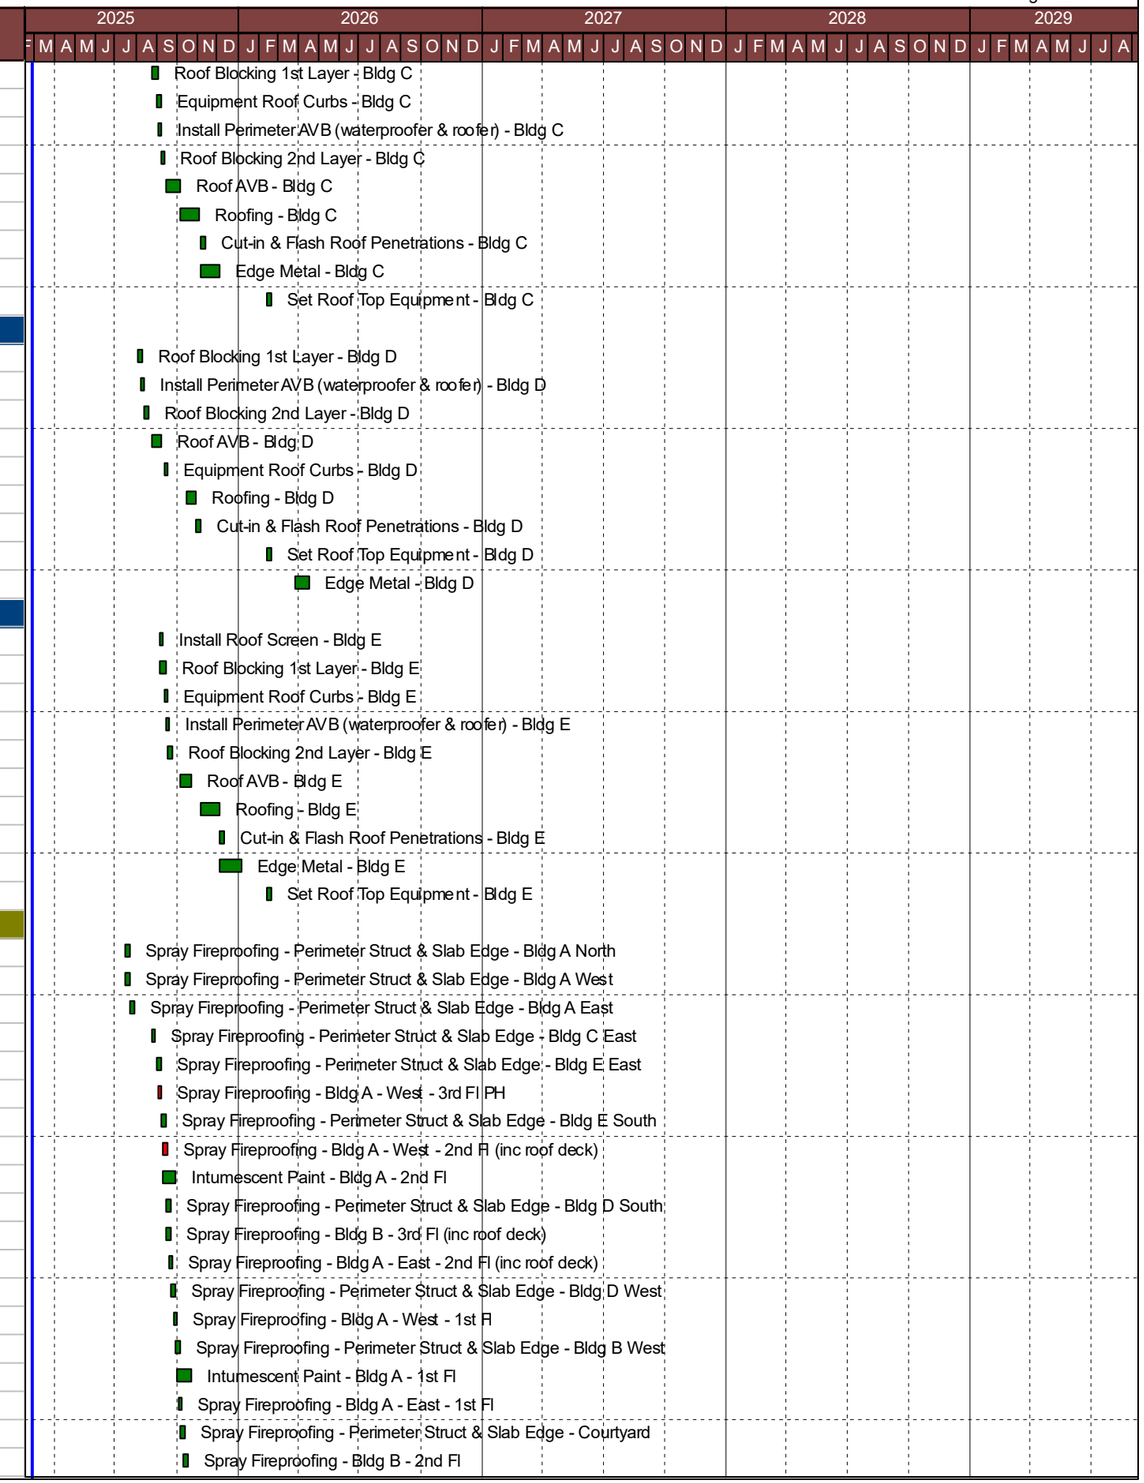

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A9950	Spray Fireproofing - Bldg B - 1st Fl	5d	5d	20-Oct-25	24-Oct-25
A9870	Spray Fireproofing - Bldg C - 2nd Fl (inc roof deck)	6d	6d	27-Oct-25	03-Nov-25
A9960	Spray Fireproofing - Bldg C - 1st Fl	6d	6d	04-Nov-25	12-Nov-25
A9880	Spray Fireproofing - Bldg D - 2nd Fl (inc roof deck)	3d	3d	13-Nov-25	17-Nov-25
A9970	Spray Fireproofing - Bldg D - 1st Fl	3d	3d	18-Nov-25	20-Nov-25
A9890	Spray Fireproofing - Bldg E - 2nd Fl (inc roof deck)	4d	4d	21-Nov-25	26-Nov-25
A9980	Spray Fireproofing - Bldg E - 1st Fl	3d	3d	28-Nov-25	02-Dec-25
Facade					
A6910	Install Facade - Courtyard	75d	75d	19-Sep-25	08-Jan-26
A1940	Install Facade - North Facade	90d	90d	03-Dec-25	13-Apr-26
A4300	Install Facade - East & West Facade	125d	125d	17-Feb-26	12-Aug-26
A4310	Install Facade - South Facade	90d	90d	11-May-26	15-Sep-26
Building A					
North					
A10160	Frame & Sheath Exterior Walls - Bldg A - North	10d	10d	23-Jul-25	05-Aug-25
A10170	AVB Exterior Walls - Bldg A - North	5d	5d	06-Aug-25	12-Aug-25
A10940	Install Precast Panels - Bldg A - North	2d	2d	13-Aug-25	14-Aug-25
A9210	CMU Veneer - Bldg A - North	6d	6d	15-Aug-25	22-Aug-25
A10190	Storefront - Bldg A - North	10d	10d	16-Oct-25	29-Oct-25
A10180	Curtainwall - Bldg A - North	15d	15d	16-Oct-25	05-Nov-25
A10200	Metal Panel - Bldg A - North	25d	25d	15-Dec-25	21-Jan-26
A10520	Joint Sealants - Bldg A - North	5d	5d	22-Jan-26	28-Jan-26
West					
A9910	Frame & Sheath Exterior Walls - Bldg A - West	10d	10d	23-Jul-25	05-Aug-25
A10090	AVB Exterior Walls - Bldg A - West	5d	5d	06-Aug-25	12-Aug-25
A10110	Storefront - Bldg A - West	6d	6d	16-Oct-25	23-Oct-25
A10100	Curtainwall - Bldg A - West	15d	15d	16-Oct-25	05-Nov-25
A10120	Metal Panel - Bldg A - West	20d	20d	22-Jan-26	19-Feb-26
A10860	Joint Sealants - Bldg A - West	5d	5d	20-Feb-26	26-Feb-26
East					
A10210	CMU Backup Walls - Bldg A - East	4d	4d	30-Jul-25	04-Aug-25
A10220	AVB Exterior Walls - Bldg A - East	5d	5d	05-Aug-25	11-Aug-25
A10260	Install Precast Panels - Bldg A - East	4d	4d	15-Aug-25	20-Aug-25
A9220	CMU Veneer - Bldg A - East	5d	5d	21-Aug-25	27-Aug-25
A10240	Storefront - Bldg A - East	6d	6d	21-Aug-25	28-Aug-25
A10230	Curtainwall - Bldg A - East	15d	15d	21-Aug-25	11-Sep-25
A10870	Joint Sealants - Bldg A - East	5d	5d	24-Nov-25	01-Dec-25
Building B					
West					
A10270	Frame & Sheath Exterior Walls - Bldg B - West	15d	15d	07-Oct-25	28-Oct-25
A10280	AVB Exterior Walls - Bldg B - West	10d	10d	29-Oct-25	12-Nov-25
A10330	Granite Base - Bldg B - West	3d	3d	13-Nov-25	17-Nov-25
A10300	Storefront Windows - Bldg B - West	10d	10d	18-Nov-25	02-Dec-25
A10290	Curtainwall - Bldg B - West	100d	100d	18-Nov-25	13-Apr-26
A10320	Flat Lock Metal Panel - Bldg B - West	30d	30d	14-Apr-26	27-May-26
A10310	ACM Metal Panel - Bldg B - West	20d	20d	28-May-26	24-Jun-26
A10880	Joint Sealants - Bldg B - West	5d	5d	25-Jun-26	01-Jul-26
Building C					
East					
A10340	Install Precast Panels - Bldg C - East	6d	6d	11-Sep-25	18-Sep-25

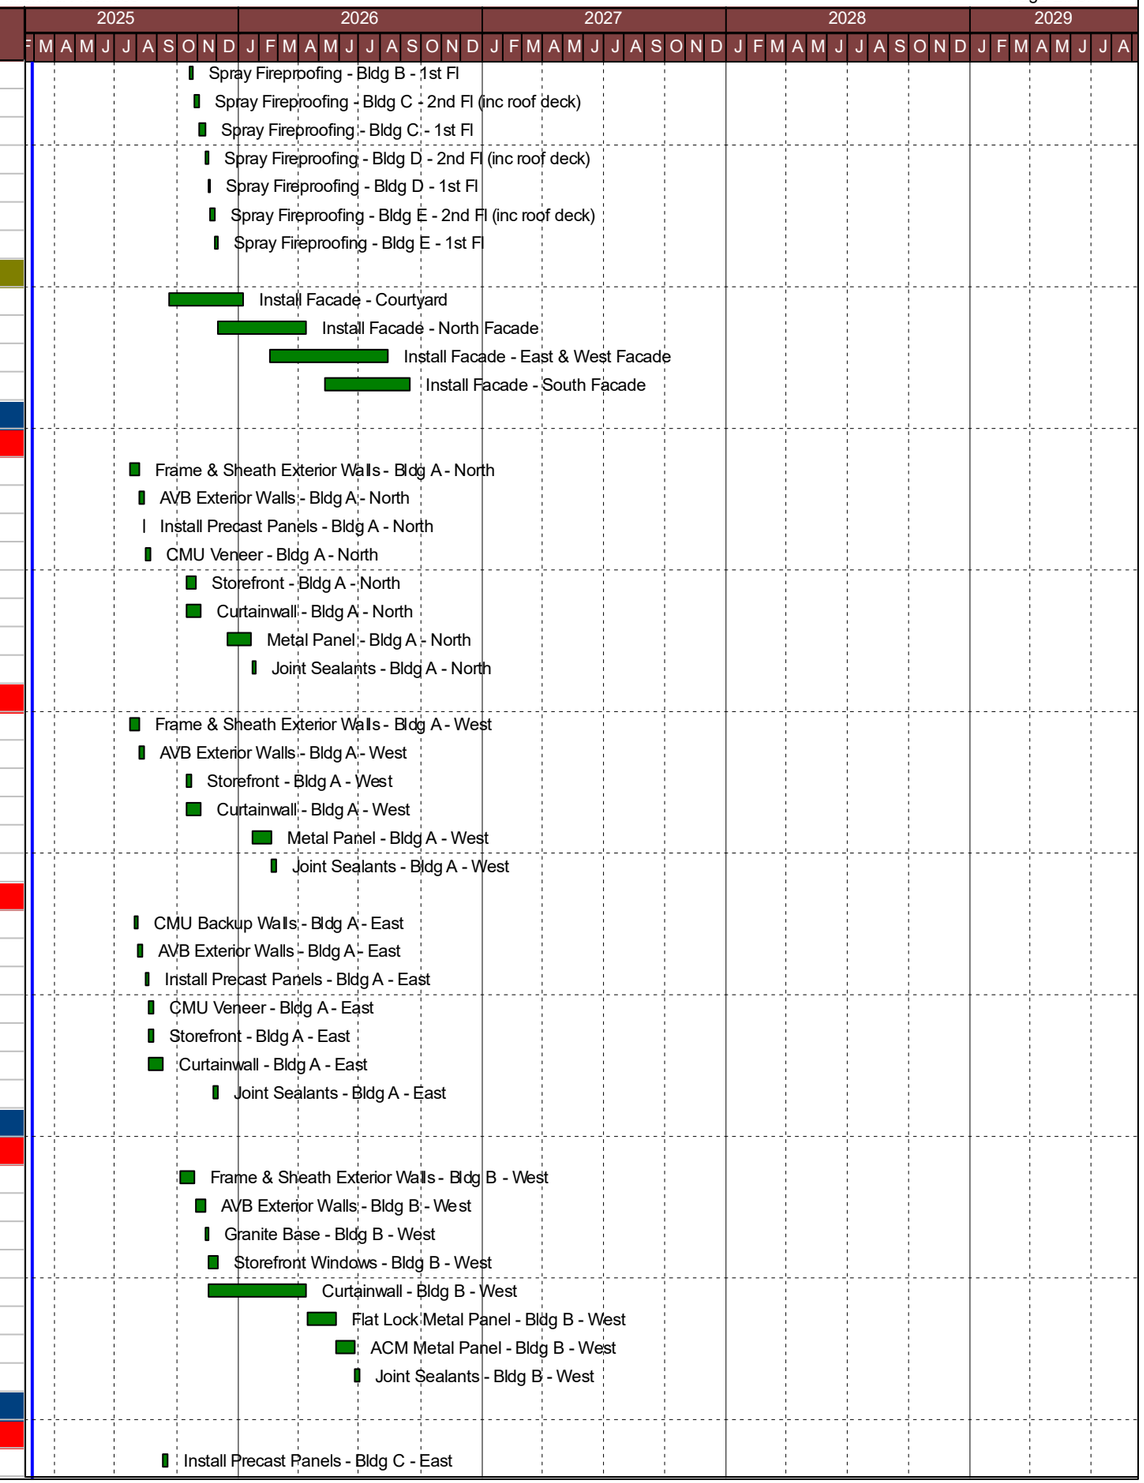

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A10350	Curtainwall - Bldg C - East	15d	15d	19-Sep-25	09-Oct-25
A10360	Storefront - Bldg C - East	24d	24d	19-Sep-25	23-Oct-25
A10890	Joint Sealants - Bldg C - East	5d	5d	24-Oct-25	30-Oct-25
A10370	Overhead Doors - Bldg C - East	12d	12d	13-Nov-25	01-Dec-25
Building D					
West					
A10460	Frame & Sheath Exterior Walls - Bldg D - West	10d	10d	23-Sep-25	06-Oct-25
A10480	AVB Exterior Walls - Bldg D - West	5d	5d	07-Oct-25	14-Oct-25
A10470	Install Precast Panels - Bldg D - West	2d	2d	08-Oct-25	09-Oct-25
A10490	Curtainwall - Bldg D- West	10d	10d	10-Oct-25	24-Oct-25
A10500	Storefront - Bldg D- West	3d	3d	15-Oct-25	17-Oct-25
A10510	ACM Metal Panel - Bldg D - West	10d	10d	20-Feb-26	05-Mar-26
A10900	Joint Sealants - Bldg D - South	5d	5d	06-Mar-26	12-Mar-26
South					
A10380	CMU Backup Walls - Bldg D - South	4d	4d	23-Sep-25	26-Sep-25
A10450	Frame & Sheath Exterior Walls - Bldg D - South	10d	10d	23-Sep-25	06-Oct-25
A10400	Install Precast Panels - Bldg D - South	3d	3d	03-Oct-25	07-Oct-25
A10390	AVB Exterior Walls - Bldg D - South	5d	5d	07-Oct-25	14-Oct-25
A10410	Curtainwall - Bldg D - South	15d	15d	08-Oct-25	29-Oct-25
A10430	CMU Veneer - Bldg D - South	4d	4d	15-Oct-25	20-Oct-25
A10420	Storefront - Bldg D - South	6d	6d	15-Oct-25	22-Oct-25
A10440	ACM Metal Panel - Bldg D - South	15d	15d	06-Mar-26	26-Mar-26
A10910	Joint Sealants - Bldg D - South	5d	5d	27-Mar-26	02-Apr-26
Building E					
East					
A10830	Install Precast Panels - Bldg E - East	3d	3d	23-Sep-25	25-Sep-25
A10840	Storefront - Bldg E - East	10d	10d	26-Sep-25	09-Oct-25
A10920	Joint Sealants - Bldg E - East	3d	3d	10-Oct-25	15-Oct-25
A10850	Overhead Doors - Bldg E - East	4d	4d	13-Nov-25	18-Nov-25
South					
A10800	Install Precast Panels - Bldg E - South	5d	5d	26-Sep-25	02-Oct-25
A10810	Storefront - Bldg E - South	15d	15d	03-Oct-25	24-Oct-25
A10930	Joint Sealants - Bldg E - South	5d	5d	27-Oct-25	31-Oct-25
A10820	Overhead Doors - Bldg E - South	12d	12d	13-Nov-25	01-Dec-25
Courtyard					
Courtyard - North [A - South]					
A11050	Frame & Sheath Exterior Walls - Courtyard - North	3d	3d	15-Oct-25	17-Oct-25
A11070	AVB Exterior Walls - Courtyard - North	2d	2d	20-Oct-25	21-Oct-25
A11080	Granite Base - Courtyard - North	1d	1d	22-Oct-25	22-Oct-25
A11090	Storefront - Courtyard - North	2d	2d	23-Oct-25	24-Oct-25
A11060	Curtainwall - Courtyard - North	8d	8d	23-Oct-25	03-Nov-25
A11100	ACM Metal Panel - Courtyard - North	10d	10d	25-Jun-26	08-Jul-26
A11110	Joint Sealants - Courtyard - North	3d	3d	09-Jul-26	13-Jul-26
Courtyard - East [C - West]					
A11120	Frame & Sheath Exterior Walls - Courtyard - East	10d	10d	20-Oct-25	31-Oct-25
A11130	AVB Exterior Walls - Courtyard - East	5d	5d	03-Nov-25	07-Nov-25
A11140	Granite Base - Courtyard - East	3d	3d	10-Nov-25	13-Nov-25
A11150	Storefront - Courtyard - East	11d	11d	14-Nov-25	01-Dec-25
A11160	ACM Metal Panel - Courtyard - East	20d	20d	09-Jul-26	05-Aug-26
A11170	Joint Sealants - Courtyard - East	5d	5d	06-Aug-26	12-Aug-26

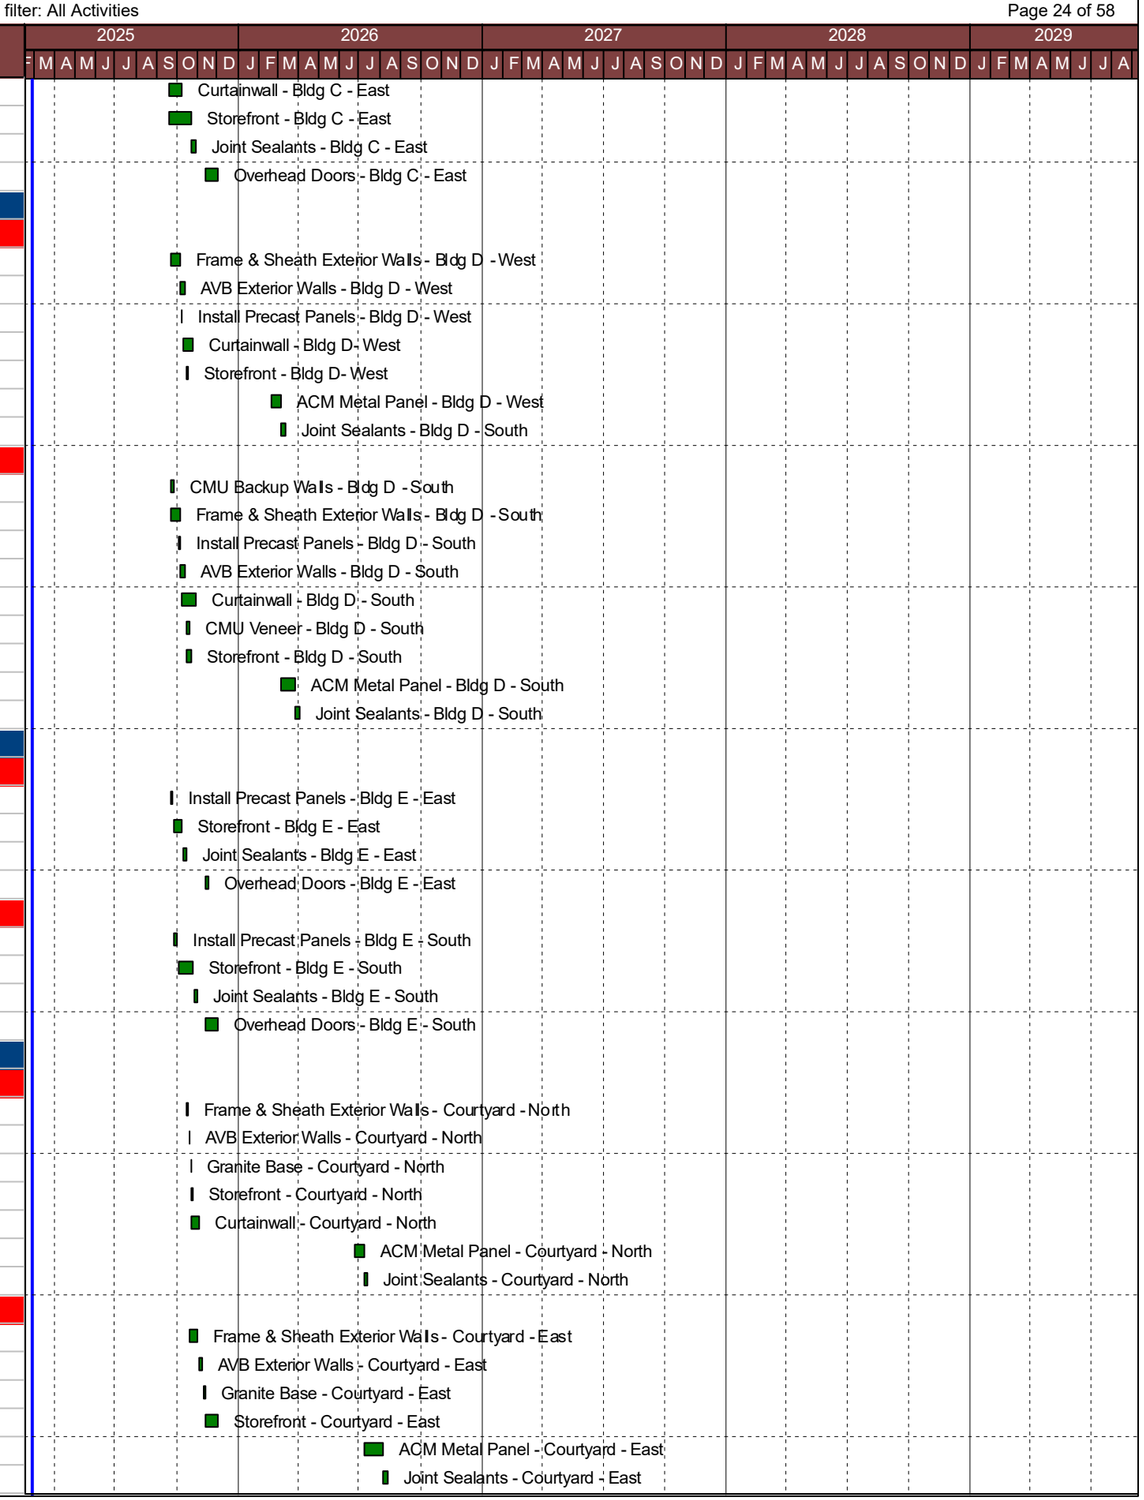

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
Courtyard - South [B - North]					
A11180	Frame & Sheath Exterior Walls - Courtyard - East	5d	5d	03-Nov-25	07-Nov-25
A11200	AVB Exterior Walls - Courtyard - South	2d	2d	10-Nov-25	12-Nov-25
A11210	Granite Base - Courtyard - South	2d	2d	13-Nov-25	14-Nov-25
A11190	Curtainwall - Courtyard - South	8d	8d	17-Nov-25	26-Nov-25
A11220	ACM Metal Panel - Courtyard - South	4d	4d	06-Aug-26	11-Aug-26
A11230	Joint Sealants - Courtyard - South	4d	4d	12-Aug-26	17-Aug-26
Courtyard - West [B - East]					
A11240	Frame & Sheath Exterior Walls - Courtyard - East	15d	15d	10-Nov-25	02-Dec-25
A11250	AVB Exterior Walls - Courtyard - East	7d	7d	03-Dec-25	11-Dec-25
A11260	Granite Base - Courtyard - East	3d	3d	12-Dec-25	16-Dec-25
A11300	HM Door - Courtyard - East	1d	1d	17-Dec-25	17-Dec-25
A11270	Storefront - Courtyard - East	14d	14d	17-Dec-25	07-Jan-26
A11280	ACM Metal Panel - Courtyard - East	25d	25d	12-Aug-26	16-Sep-26
A11290	Joint Sealants - Courtyard - East	7d	7d	17-Sep-26	25-Sep-26
Interior Construction					
A2120	Rough MEP / FP Risers	80d	80d	30-Jul-25	21-Nov-25
Building A					
3rd Floor					
A23600	Layout & Install Wall Clips - A-3	10d	10d	19-Aug-25	02-Sep-25
A23060	Punchlist - A-3	5d	5d	28-Sep-26	02-Oct-26
A23420	Final Clean - A-3	1d	1d	05-Oct-26	05-Oct-26
Electric / Mechanical / IDF Room - A300/A301/A303					
A22920	Frame Early Walls / One-Side Board - Elec/Mech - A300/A301/A305	3d	3d	10-Sep-25	12-Sep-25
A22970	Install OH Plumbing Rough - Elec/Mech - A300/A301/A305	3d	3d	15-Sep-25	17-Sep-25
A22960	Install OH Electrical Rough - Elec/Mech - A300/A301/A305	15d	15d	18-Sep-25	08-Oct-25
A22950	Install OH FP Rough - Elec/Mech - A300/A301/A305	5d	5d	02-Oct-25	08-Oct-25
A22940	Install OH Mechanical Pipe Rough - Elec/Mech - A300/A301/A305	15d	15d	09-Oct-25	30-Oct-25
A22930	OH Duct Rough - Elec/Mech - A300/A301/A305	15d	15d	17-Oct-25	06-Nov-25
A22980	FRP Housekeeping Pads - Elec/Mech - A300/A301/A305	5d	5d	07-Nov-25	14-Nov-25
A22990	Set Electrical Equipment - Elec/Mech - A300/A301/A305	5d	5d	17-Nov-25	21-Nov-25
A23000	Install Panels - Elec/Mech - A300/A301/A305	15d	15d	17-Nov-25	08-Dec-25
A23010	Pull Wires / Feeders to Panels / Equipment - Elec/Mech - A300/A301/A305	10d	10d	09-Dec-25	22-Dec-25
A23070	Set Air & Connect Handling Equip- Elec/Mech - A300/A301/A305	15d	15d	13-Feb-26	06-Mar-26
A23020	Install Doors & Hardware - Elec/Mech - A300/A301/A305	2d	2d	09-Mar-26	10-Mar-26
A23030	Final Paint - Elec/Mech - A300/A301/A305	2d	2d	09-Mar-26	10-Mar-26
A23040	Construction Clean - Elec/Mech - A300/A301/A305	2d	2d	11-Mar-26	12-Mar-26
A189030	Punchlist - Elec/Mech - A300/A301/A305	5d	5d	13-Mar-26	19-Mar-26
Mechanical Penthouse - A305					
A23080	Frame Early Walls / One-Side Board - Mech Rm - A305	3d	3d	15-Sep-25	17-Sep-25
A23150	Paint Ceiling - Mech Rm - A305	3d	3d	18-Sep-25	22-Sep-25
A23110	Install OH Plumbing Rough - Mech Rm - A305	3d	3d	23-Sep-25	25-Sep-25
A23130	Install OH Electrical Rough - Mech Rm - A305	15d	15d	26-Sep-25	17-Oct-25
A23120	Install OH FP Rough - Mech Rm - A305	5d	5d	10-Oct-25	17-Oct-25
A23100	Install OH Mechanical Pipe Rough - Mech Rm - A305	15d	15d	20-Oct-25	07-Nov-25
A23090	OH Duct Rough - Mech Rm - A305	15d	15d	27-Oct-25	17-Nov-25
A23140	FRP Housekeeping Pads - Mech Rm - A305	5d	5d	18-Nov-25	24-Nov-25
A23230	Set Air & Connect Handling Equip- Mech Rm - A305	15d	15d	20-Feb-26	12-Mar-26
A23180	Install Doors & Hardware - Mech Rm - A305	2d	2d	13-Mar-26	16-Mar-26
A23190	Final Paint - Mech Rm - A305	2d	2d	13-Mar-26	16-Mar-26

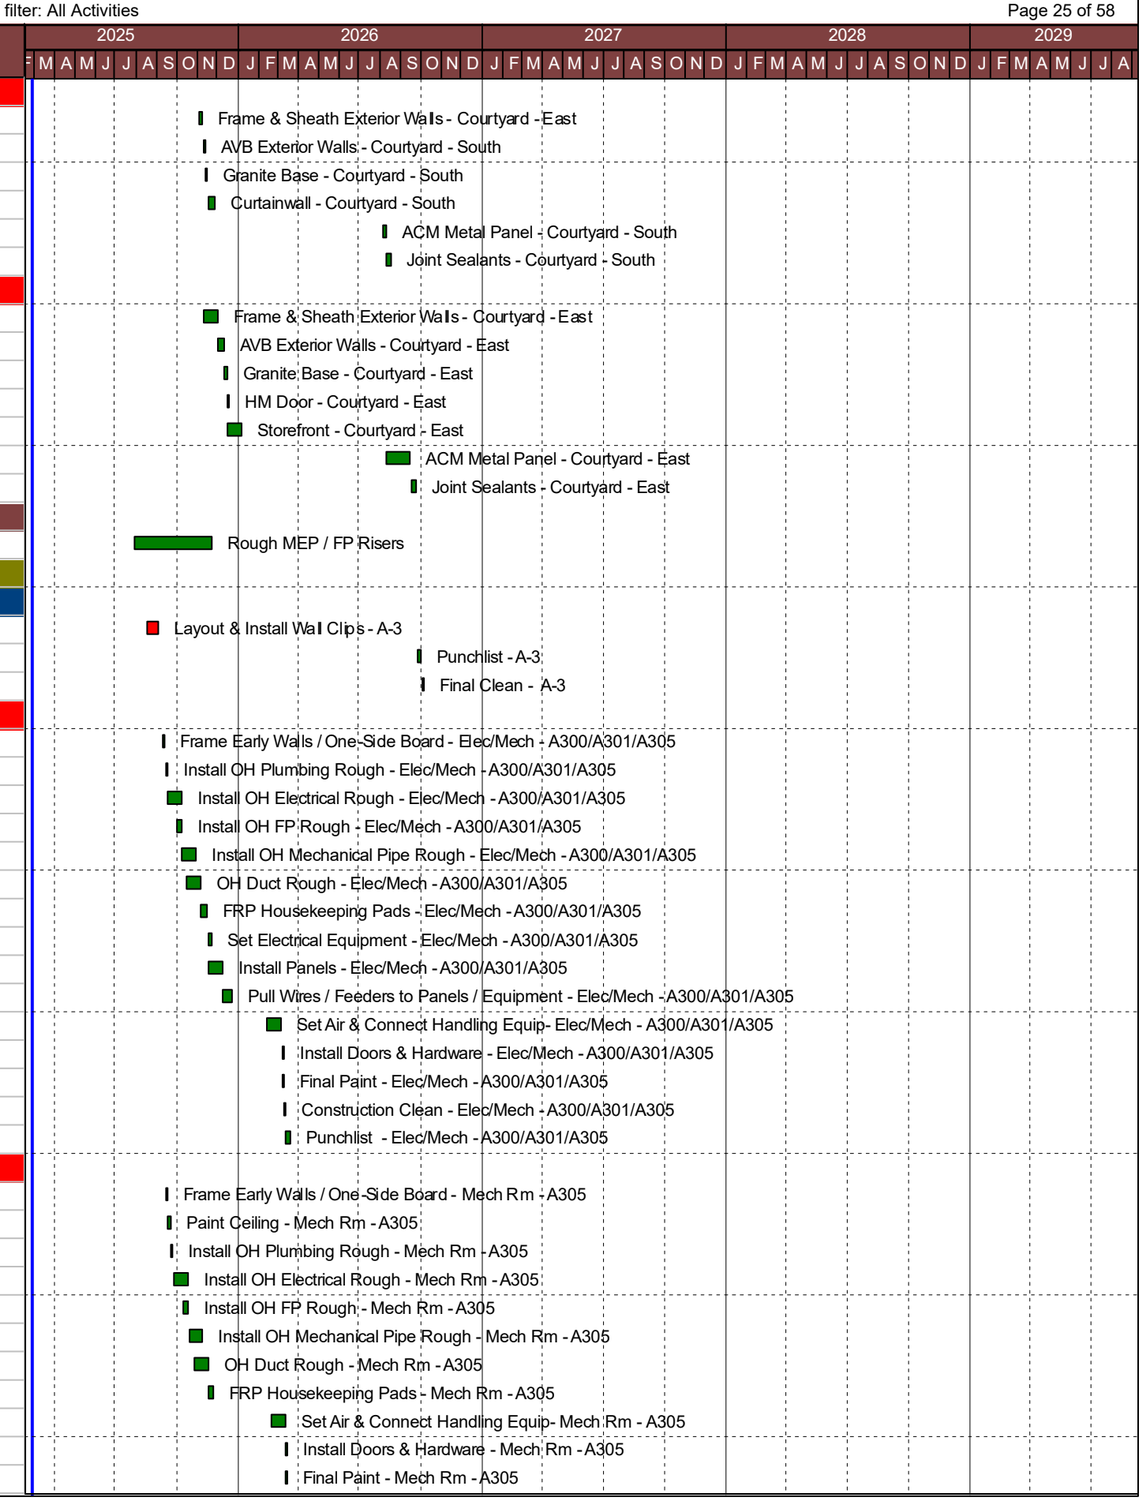

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A23200	Construction Clean - Mech Rm - A305	2d	2d	17-Mar-26	18-Mar-26
A189040	Punchlist - Mech Rm - A305	5d	5d	19-Mar-26	25-Mar-26
Dept Offices					
A23240	Frame Walls - Dept Office - A-3	2d	2d	18-Sep-25	19-Sep-25
A23300	OH Duct Rough - Dept Office - A-3	2d	2d	22-Sep-25	23-Sep-25
A23270	Install In-Wall & OH Electrical Rough - Dept Office - A-3	2d	2d	24-Sep-25	25-Sep-25
A23260	Install OH FP Rough - Dept Office - A-3	1d	1d	26-Sep-25	26-Sep-25
A23280	Inspections - Dept Office - A-3	5d	5d	29-Sep-25	03-Oct-25
A23310	Insulate / Drywall / Tape & Sands Walls - Dept Office - A-3	4d	4d	06-Oct-25	09-Oct-25
A23320	Prime, First Coat - Dept Office - A-3	1d	1d	10-Oct-25	10-Oct-25
A23330	Install ACT Grid - Dept Office - A-3	2d	2d	14-Oct-25	15-Oct-25
A23340	Install Finishes in Ceiling Grid - Dept Office - A-3	2d	2d	16-Oct-25	17-Oct-25
A23350	Above Ceiling Inspections - Dept Office - A-3	5d	5d	20-Oct-25	24-Oct-25
A23360	Install Ceiling Tiles - Dept Office - A-3	1d	1d	17-Sep-26	17-Sep-26
A23370	Install Flooring - Dept Office - A-3	3d	3d	18-Sep-26	22-Sep-26
A23380	Final Painting - Dept Office - A-3	1d	1d	23-Sep-26	23-Sep-26
A23390	Install Floor Base - Dept Office - A-3	1d	1d	24-Sep-26	24-Sep-26
A23400	Construction Clean - Dept Office - A-3	1d	1d	25-Sep-26	25-Sep-26
2nd Floor					
A25660	Install Control - A-2	2d	2d	01-Aug-25	04-Aug-25
A23610	Layout & Install Wall Clips - A-2	10d	10d	05-Aug-25	18-Aug-25
A23430	Install Hangers - A-2	5d	5d	19-Sep-25	25-Sep-25
A23440	Patch Spray Fireproofing - A-2	3d	3d	26-Sep-25	30-Sep-25
A24490	OH Duct Rough - A-2	25d	25d	01-Oct-25	05-Nov-25
A24520	OH HVAC Piping Rough - A-2	25d	25d	01-Oct-25	05-Nov-25
A24410	Install Door Frames - A-2	5d	5d	16-Oct-25	22-Oct-25
A24390	Frame & Top Off Walls - A-2	10d	10d	16-Oct-25	29-Oct-25
A24530	OH Plumbing Rough - A-2	20d	20d	16-Oct-25	13-Nov-25
A24510	OH Elect / Fire Alarm Rough - A-2	20d	20d	23-Oct-25	20-Nov-25
A24430	In-Wall HVAC Piping Rough - A-2	5d	5d	30-Oct-25	05-Nov-25
A24460	OH Sprinkler Rough - A-2	15d	15d	30-Oct-25	20-Nov-25
A24420	In-Wall Elect Rough - A-2	20d	20d	30-Oct-25	28-Nov-25
A24440	In-Wall Plumbing Rough - A-2	20d	20d	30-Oct-25	28-Nov-25
A192320	OH AV / Telcom / Low Voltage Rough - A-2	20d	20d	21-Nov-25	19-Dec-25
A24500	In-Wall Plumbing & Elect Inspection - A-2	10d	10d	01-Dec-25	12-Dec-25
A24540	Insulate Plumbing & Mech Piping - A-2	5d	5d	15-Dec-25	19-Dec-25
A24550	In-Wall Building Inspection - A-2	5d	5d	22-Dec-25	29-Dec-25
A24560	Insulate / Drywall / Tape & Sands Walls - A-2	20d	20d	30-Dec-25	28-Jan-26
A24620	Prime & First Coat Paint Walls & Ceilings - A-2	15d	15d	29-Jan-26	19-Feb-26
A24690	Install ACT Grid - A-2	9d	9d	20-Feb-26	04-Mar-26
A24770	Install Wall & Floor Tile @ Bathooms - A-2	10d	10d	20-Feb-26	05-Mar-26
A24700	Install OH MEP Drops & Lights Into Grid - A-2	10d	10d	05-Mar-26	18-Mar-26
A24750	Install Wall Tile @ Hallways- A-2	10d	10d	05-Mar-26	18-Mar-26
A24870	Install Plumbing Fixtures - A-2	3d	3d	06-Mar-26	10-Mar-26
A24880	Install Toilet Partitions - A-2	5d	5d	11-Mar-26	17-Mar-26
A24890	Install Toilet Accessories - A-2	2d	2d	18-Mar-26	19-Mar-26
A24720	OH Inspections - A-2	5d	5d	19-Mar-26	25-Mar-26
A24740	Install Ceiling Tiles - A-2	6d	6d	26-Mar-26	02-Apr-26
A24900	Install Casework - A-2	3d	3d	03-Apr-26	07-Apr-26
A24780	MEP Wall Finishes - A-2	5d	5d	03-Apr-26	09-Apr-26

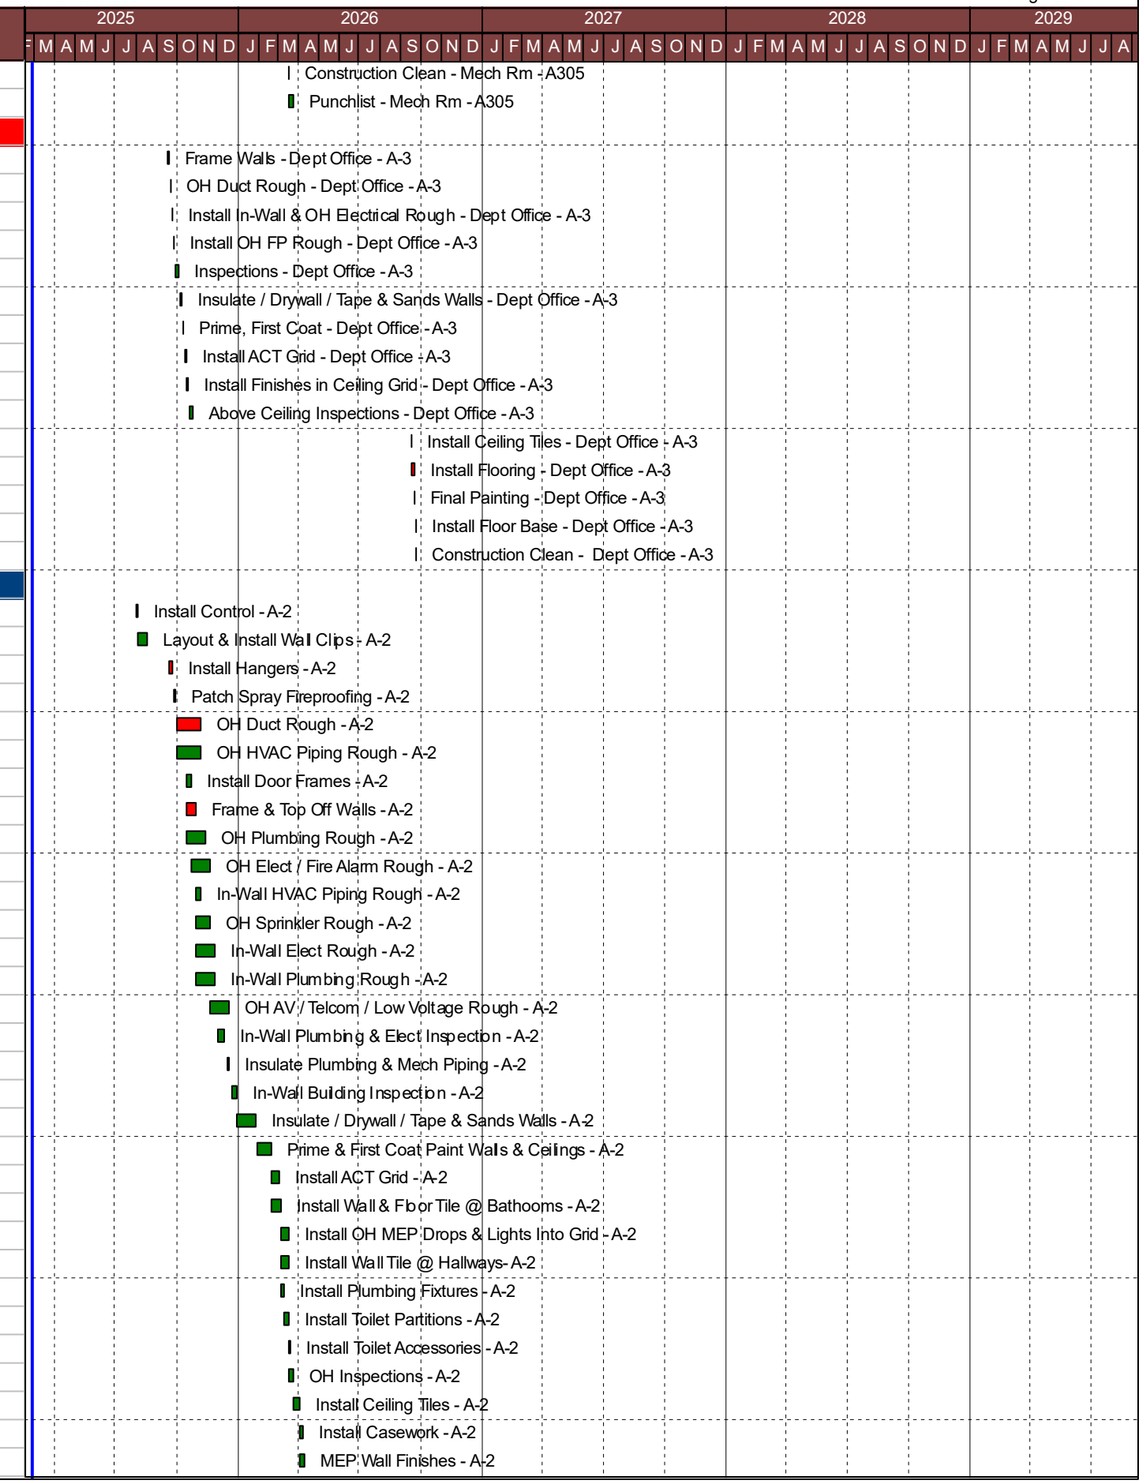

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A24710	Install Carpet - A-2	4d	4d	08-Apr-26	13-Apr-26
A24930	Install Floor Tile @ Serving Area - A-2	6d	6d	08-Apr-26	15-Apr-26
A24860	Install Rubber Tile - A-2	10d	10d	08-Apr-26	22-Apr-26
A24680	Final Painting - A-2	4d	4d	10-Apr-26	15-Apr-26
A24910	Install Food Service Equipment - A-2	2d	2d	16-Apr-26	17-Apr-26
A24920	Install Specialties - A-2	2d	2d	16-Apr-26	17-Apr-26
A24730	Install Doors & Hardware - A-2	2d	2d	23-Apr-26	24-Apr-26
A24760	Construction Clean - A-2	2d	2d	27-Apr-26	28-Apr-26
A24790	Punchlist - A-2	10d	10d	20-Oct-26	02-Nov-26
A24800	Final Cleaning - A-2	2d	2d	03-Nov-26	04-Nov-26
Library / Learning Commons					
A24810	Prime Paint Walls/ Exposed Deck/ Exposed MEPs - A-2 - Library / Learning Commons	5d	5d	29-Jan-26	04-Feb-26
A24940	Install Ceiling Clouds - A-2 - Library / Learning Commons	30d	30d	05-Feb-26	19-Mar-26
A24950	Install HVAC Finishes in Ceiling Clouds - A-2 - Library / Learning Commons	30d	30d	05-Feb-26	19-Mar-26
A24960	Install Electrical / AV Finishes in Ceiling Clouds - A-2 - Library / Learning Commons	30d	30d	05-Feb-26	19-Mar-26
A24970	Install Sprinkler Finishes in Ceiling Clouds - A-2 - Library / Learning Commons	30d	30d	05-Feb-26	19-Mar-26
A25010	Install Glass Storefronts - A-2 - Library / Learning Commons	8d	8d	20-Mar-26	31-Mar-26
A24980	Install Folding Glass Partition - A-2 - Library / Learning Commons	5d	5d	01-Apr-26	07-Apr-26
A25020	Install Millwork / Casework - A-2 - Library / Learning Commons	5d	5d	08-Apr-26	14-Apr-26
A25100	Install Large Format Porcelain Sheet @ North Elevation - A-2 - Library / Learning Commons	6d	6d	15-Apr-26	23-Apr-26
A25030	Install MEP Wall Finishes - A-2 - Library / Learning Commons	2d	2d	24-Apr-26	27-Apr-26
A25110	Install Green Wall - A-2 - Library / Learning Commons	5d	5d	24-Apr-26	30-Apr-26
A25040	Install Flooring - A-2 - Library / Learning Commons	8d	8d	01-May-26	12-May-26
A25050	Final Painting - A-2 - Library / Learning Commons	3d	3d	13-May-26	15-May-26
A25060	Install Doors & Hardware - A-2 - Library / Learning Commons	3d	3d	18-May-26	20-May-26
A25070	Construction Clean - A-2 - Library / Learning Commons	2d	2d	21-May-26	22-May-26
Bathrooms					
A189760	In-Wall Plumbing Rough - A-2 BR	5d	5d	04-Nov-25	10-Nov-25
A189770	In-Wall HVAC Piping Rough - A-2 BR	2d	2d	06-Nov-25	07-Nov-25
A189780	In-Wall Elect Rough - A-2 BR	2d	2d	01-Dec-25	02-Dec-25
A189790	In-Wall Elect & Plumbing Inspection - A-2 BR	5d	5d	03-Dec-25	09-Dec-25
A189800	Insulate Plumbing & Mech Piping - A-2 BR	2d	2d	10-Dec-25	11-Dec-25
A189810	In-Wall Building Inspection - A-2 BR	5d	5d	12-Dec-25	18-Dec-25
A189820	Frame Hard Ceilings - A-2 BR	2d	2d	19-Dec-25	22-Dec-25
A189830	Install OH MEP Drops & Lights Into Hard Ceilings - A-2 BR	2d	2d	23-Dec-25	24-Dec-25
A189840	OH Inspections - A-2 BR	5d	5d	26-Dec-25	02-Jan-26
A189850	Insulate / Drywall / Tape & Sands Walls & Ceilings - A-2 BR	5d	5d	05-Jan-26	09-Jan-26
A189860	Prime & First Coat Paint Walls & Ceilings - A-2 BR	1d	1d	12-Jan-26	12-Jan-26
A189870	Install Wall & Floor Tile @ Bathooms - A-2 BR	10d	10d	13-Jan-26	27-Jan-26
A189880	MEP Wall Finishes - A-2 BR	1d	1d	28-Jan-26	28-Jan-26
A189890	Final Painting - A-2 BR	4d	4d	29-Jan-26	03-Feb-26
A189900	Install Plumbing Fixtures - A-2 BR	5d	5d	04-Feb-26	10-Feb-26
A189910	Install Toilet Partitions - A-2 BR	3d	3d	11-Feb-26	13-Feb-26
A189920	Install Toilet Accessories - A-2 BR	2d	2d	17-Feb-26	18-Feb-26
A189930	Install Specialties - A-2 BR	2d	2d	17-Feb-26	18-Feb-26
A189940	Install Doors & Hardware - A-2 BR	1d	1d	19-Feb-26	19-Feb-26
A189950	Construction Clean - A-2 BR	2d	2d	20-Feb-26	23-Feb-26
1st Floor					
A25670	Install Control - A-1	2d	2d	10-Sep-25	11-Sep-25
A25240	Layout & Install Wall Clips - A-1	10d	10d	12-Sep-25	25-Sep-25

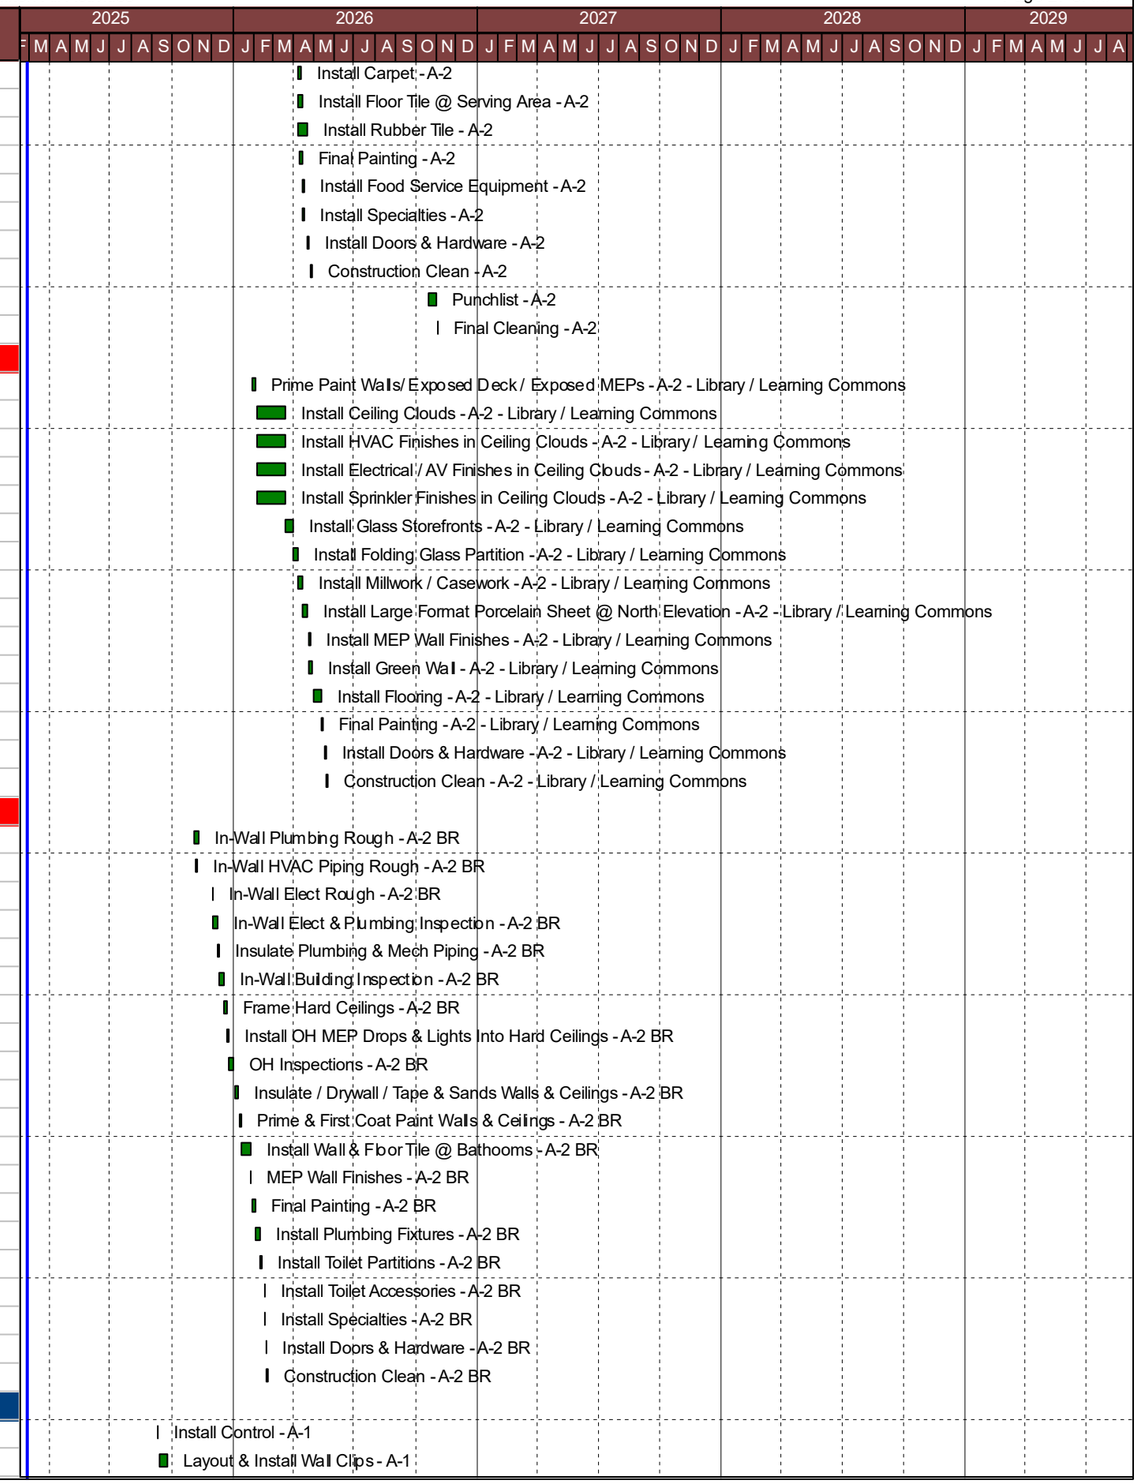

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A9100	CMU Interior Walls / Door Frames - Bldg A - East	20d	20d	25-Sep-25	23-Oct-25
A25250	Install Hangers - A-1	5d	5d	10-Oct-25	17-Oct-25
A25260	Patch Spray Fireproofing - A-1	3d	3d	20-Oct-25	22-Oct-25
A25270	OH Duct Rough - A-1	25d	25d	23-Oct-25	28-Nov-25
A25280	OH HVAC Piping Rough - A-1	25d	25d	23-Oct-25	28-Nov-25
A25300	OH Plumbing Rough - A-1	20d	20d	06-Nov-25	05-Dec-25
A25310	Install Door Frames - A-1	5d	5d	14-Nov-25	20-Nov-25
A25290	Frame & Top Off Walls - A-1	10d	10d	14-Nov-25	28-Nov-25
A25320	OH Elect / Fire Alarm Rough - A-1	20d	20d	14-Nov-25	12-Dec-25
A25330	OH Sprinkler Rough - A-1	15d	15d	21-Nov-25	12-Dec-25
A25350	In-Wall HVAC Piping Rough - A-1	5d	5d	01-Dec-25	05-Dec-25
A25340	In-Wall Elect Rough - A-1	25d	25d	01-Dec-25	06-Jan-26
A25360	In-Wall Plumbing Rough - A-1	25d	25d	01-Dec-25	06-Jan-26
A192330	OH AV / Telcom / Low Voltage Rough - A-1	20d	20d	15-Dec-25	13-Jan-26
A25370	In-Wall Plumbing & Elect Inspection - A-1	10d	10d	07-Jan-26	21-Jan-26
A25380	Insulate Plumbing & Mech Piping - A-1	10d	10d	22-Jan-26	04-Feb-26
A25390	In-Wall Building Inspection - A-1	5d	5d	05-Feb-26	11-Feb-26
A25400	Insulate / Drywall / Tape & Sands Walls - A-1	20d	20d	12-Feb-26	12-Mar-26
A25440	Prime & First Coat Paint Walls & Ceilings - A-1	15d	15d	13-Mar-26	02-Apr-26
Administration					
A25450	Install ACT Grid - A-1 - Administration	9d	9d	03-Apr-26	15-Apr-26
A25460	Install Wall & Floor Tile @ Bathooms - A-1 - Administration	10d	10d	03-Apr-26	16-Apr-26
A25470	Install OH MEP Drops & Lights Into Grid - A-1 - Administration	10d	10d	16-Apr-26	30-Apr-26
A25480	Install Wall Tile @ Hallways / Commons - A-1 - Administration	10d	10d	16-Apr-26	30-Apr-26
A25510	OH Inspections - A-1 - Administration	5d	5d	01-May-26	07-May-26
A25540	Install Ceiling Tiles - A-1 - Administration	6d	6d	08-May-26	15-May-26
A25490	Install Plumbing Fixtures - A-1 - Administration	3d	3d	18-May-26	20-May-26
A25570	Install Casework - A-1 - Administration	3d	3d	18-May-26	20-May-26
A25530	MEP Wall Finishes - A-1 - Administration	5d	5d	18-May-26	22-May-26
A25560	Install Rubber Tile - A-1 - Administration	10d	10d	18-May-26	01-Jun-26
A25590	Install Carpet - A-1 - Administration	4d	4d	21-May-26	27-May-26
A25500	Install Toilet Partitions - A-1 - Administration	5d	5d	21-May-26	28-May-26
A25520	Install Toilet Accessories - A-1 - Administration	2d	2d	29-May-26	01-Jun-26
A25550	Final Painting - A-1 - Administration	4d	4d	02-Jun-26	05-Jun-26
A25620	Install Doors & Hardware - A-1 - Administration	2d	2d	08-Jun-26	09-Jun-26
A25580	Install Specialties - A-1 - Administration	2d	2d	08-Jun-26	09-Jun-26
A25630	Construction Clean - A-1 - Administration	2d	2d	10-Jun-26	11-Jun-26
A25640	Punchlist - A-1 - Administration	10d	10d	03-Aug-26	14-Aug-26
A25650	Final Cleaning - A-1 - Administration	2d	2d	26-Jan-27	27-Jan-27
Student Commons (1st & 2nd Floor)					
A25170	Install Monumental Stair Structure - A-1 - Student Commons	10d	10d	03-Oct-25	17-Oct-25
A25830	Field Measure for Precast Terrazzo - A-1 - Student Commons	1d	1d	20-Oct-25	20-Oct-25
A25130	Install Clouds - A-2 - Student Commons	30d	30d	22-Dec-25	04-Feb-26
A25140	Install HVAC Finishes in Ceiling Clouds - A-2 - Student Commons	30d	30d	30-Dec-25	11-Feb-26
A25150	Install Electrical / AV Finishes in Ceiling Clouds - A-2 - Student Commons	30d	30d	30-Dec-25	11-Feb-26
A25160	Install Sprinkler Finishes in Ceiling Clouds - A-2 - Student Commons	30d	30d	30-Dec-25	11-Feb-26
A25690	Frame Hard Ceilings - A-1 - Student Commons	5d	5d	05-Feb-26	11-Feb-26
A25700	Install OH MEP Drops & Lights Into Hard Ceilings - A-1	5d	5d	12-Feb-26	19-Feb-26
A25710	Drywall / Tape & Sands Ceiling / Soffit - A-1 - Student Commons	20d	20d	20-Feb-26	19-Mar-26
A25600	Install Terrazzo Flooring (Rough) - A-1 - Student Commons	15d	15d	20-Mar-26	09-Apr-26

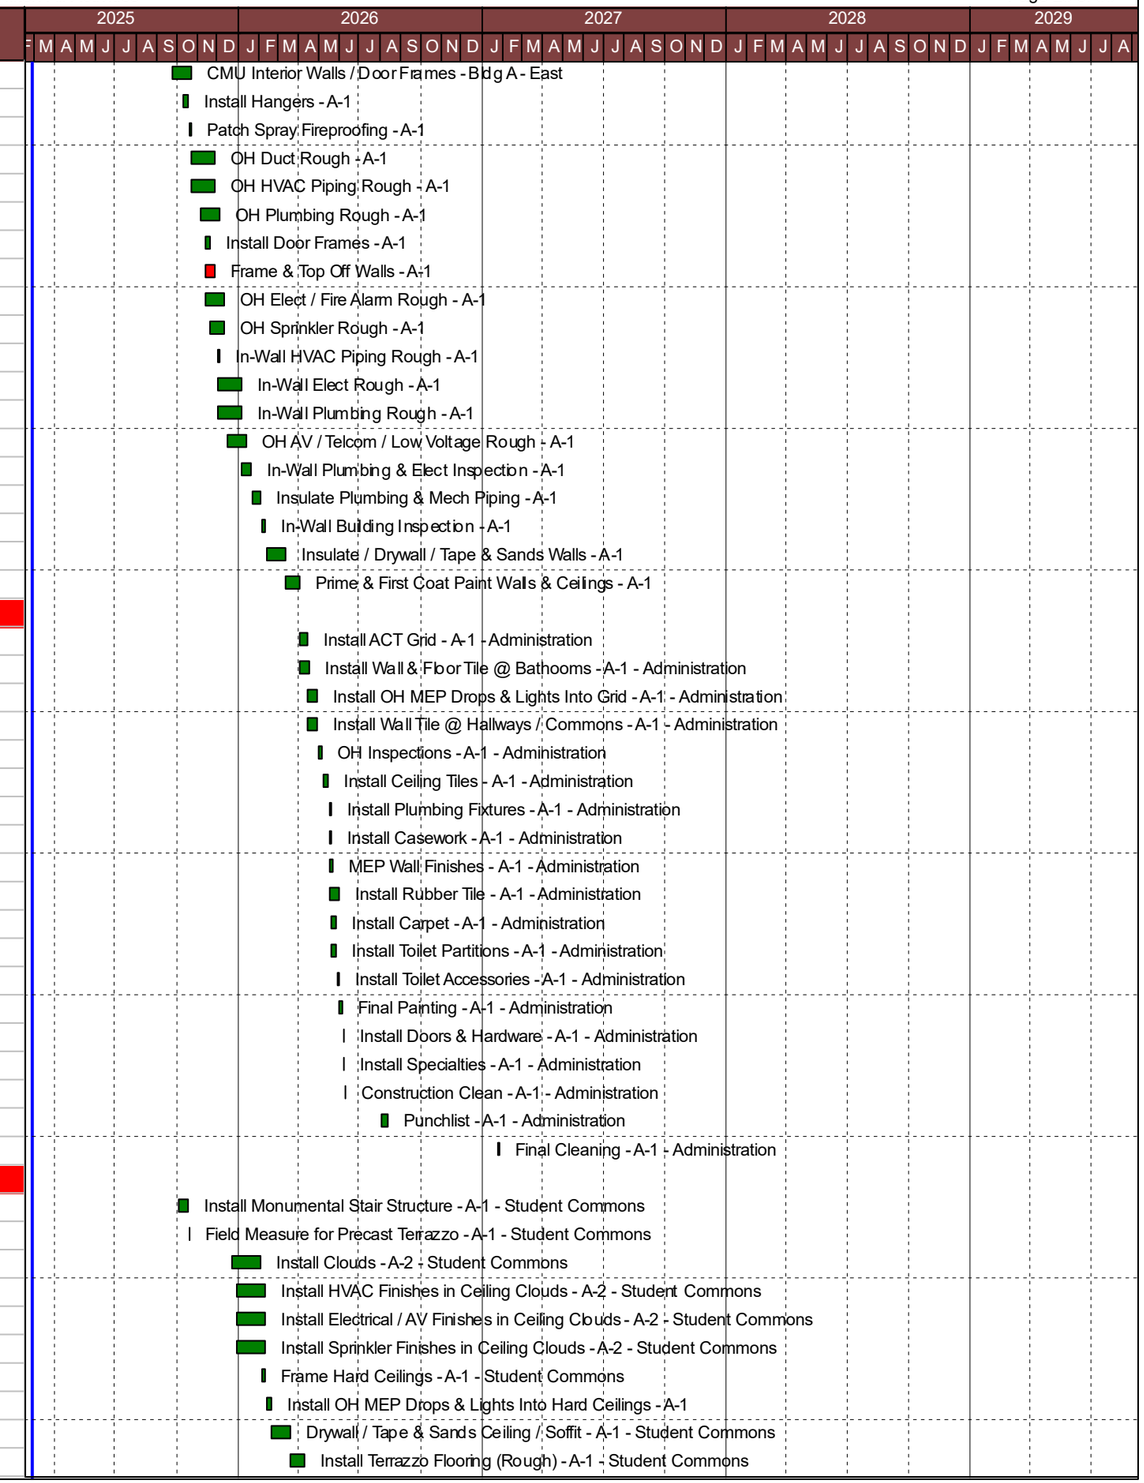

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A25210	Install Display Cases - A-1 - Student Commons	2d	2d	10-Apr-26	13-Apr-26
A25680	Install Display Cases - A-2 - Student Commons	2d	2d	10-Apr-26	13-Apr-26
A25180	Install Glass Railing - Students Commons	15d	15d	10-Apr-26	01-May-26
A25720	Prime & First Coat Paint Walls & Ceilings - A-1 - Student Commons	15d	15d	10-Apr-26	01-May-26
A25730	Install ACT Grid - A-1 - Student Commons	4d	4d	04-May-26	07-May-26
A25120	Install Rubber Tile Flooring - A-2 - Student Commons	7d	7d	04-May-26	12-May-26
A25740	Install OH MEP Drops & Lights Into Grid - A-1 - Student Commons	10d	10d	08-May-26	21-May-26
A25750	OH Inspections - A-1 - Student Commons	5d	5d	22-May-26	29-May-26
A25760	Install Ceiling Tiles - A-1 - Student Commons	6d	6d	01-Jun-26	08-Jun-26
A25810	Install Column Covers / Green Wall - A-1 - Student Commons	10d	10d	09-Jun-26	22-Jun-26
A25800	Polish Terrazzo Flooring - A-1 - Student Commons	5d	5d	23-Jun-26	29-Jun-26
A25820	Install Precast Terrazzo Treads & Riser - A-1 - Student Commons	15d	15d	30-Jun-26	20-Jul-26
A25770	Construction Clean - A-1 - Student Commons	2d	2d	21-Jul-26	22-Jul-26
Lockers / Fitness / Music					
A49600	Install Sound Isolator Ceiling - Music	5d	5d	10-Oct-25	17-Oct-25
A49570	Prime / Paint Walls - Lockers / Fitness / Music	15d	15d	14-Jan-26	04-Feb-26
A49590	Frame Hard Ceilings - Lockers / Fitness / Music	6d	6d	05-Feb-26	12-Feb-26
A49580	Install ACT Grid - Lockers / Fitness / Music	7d	7d	05-Feb-26	13-Feb-26
A49610	Install MEP Drops - Lockers / Fitness / Music	5d	5d	17-Feb-26	23-Feb-26
A49620	Install Locker Bases - Lockers	3d	3d	24-Feb-26	26-Feb-26
A49630	OH MEP Inspection - Lockers / Fitness / Music	5d	5d	24-Feb-26	02-Mar-26
A49640	Install Ceiling Tiles - Lockers / Fitness / Music	3d	3d	03-Mar-26	05-Mar-26
A49650	Board / Tape / Sand Ceilings - Lockers / Fitness / Music	5d	5d	03-Mar-26	09-Mar-26
A49660	Install Acoustic Wall Panels - Music	3d	3d	10-Mar-26	12-Mar-26
A49710	Prime / Paint Ceilings & Final Paint Walls - Lockers / Fitness / Music	15d	15d	10-Mar-26	30-Mar-26
A49700	Install Shower Bases - Lockers	3d	3d	31-Mar-26	02-Apr-26
A49770	Install Linoleum Flooring - Music	5d	5d	31-Mar-26	06-Apr-26
A49810	Install Rubber Athletic Flooring - Fitness	5d	5d	31-Mar-26	06-Apr-26
A49690	Install Tile Lockers	10d	10d	03-Apr-26	16-Apr-26
A49760	Install Prefab Sound Isolation Room - Music	3d	3d	07-Apr-26	09-Apr-26
A49820	Install Mirrors - Fitness	3d	3d	07-Apr-26	09-Apr-26
A49830	Install Fitness Equipment - Fitness	4d	4d	07-Apr-26	10-Apr-26
A49680	Epoxy Flooring - Lockers	8d	8d	17-Apr-26	29-Apr-26
A189170	Install Rubber Flooring - Hallway	5d	5d	30-Apr-26	06-May-26
A49720	Install Plumbing Fixtures - Lockers	13d	13d	30-Apr-26	18-May-26
A49670	Install Lockers / Benches - Lockers	15d	15d	30-Apr-26	20-May-26
A49840	Install Custom Display Cases - Hallway	5d	5d	07-May-26	13-May-26
A49730	Install Toilet Partitions / Shower Stalls - Lockers	10d	10d	19-May-26	02-Jun-26
A49740	Install Toilet Accessories - Lockers	3d	3d	03-Jun-26	05-Jun-26
A189180	Install Doors & Hardware - Lockers / Fitness / Music	7d	7d	03-Jun-26	11-Jun-26
A189190	Final Painting - Lockers / Fitness / Music	10d	10d	12-Jun-26	25-Jun-26
A49780	Construction Clean - Lockers / Fitness / Music	2d	2d	26-Jun-26	29-Jun-26
Kitchen / Servery					
A49850	Install Sound Isolator Ceiling - Kitchen / Servery	5d	5d	10-Oct-25	17-Oct-25
A49870	Install Hood - Kitchen	3d	3d	15-Dec-25	17-Dec-25
A49880	Install Final Connections to Hoods - Kitchen / Servery	3d	3d	18-Dec-25	22-Dec-25
A49960	Install Wall Tile - Servery	3d	3d	03-Apr-26	07-Apr-26
A49930	Install FRP Walls - Kitchen	5d	5d	03-Apr-26	09-Apr-26
A49860	Install Walk-In Cooler / Walk-In Freeze - Kitchen / Servery	3d	3d	10-Apr-26	14-Apr-26
A49890	Install ACT Grid - Kitchen / Servery	4d	4d	15-Apr-26	21-Apr-26

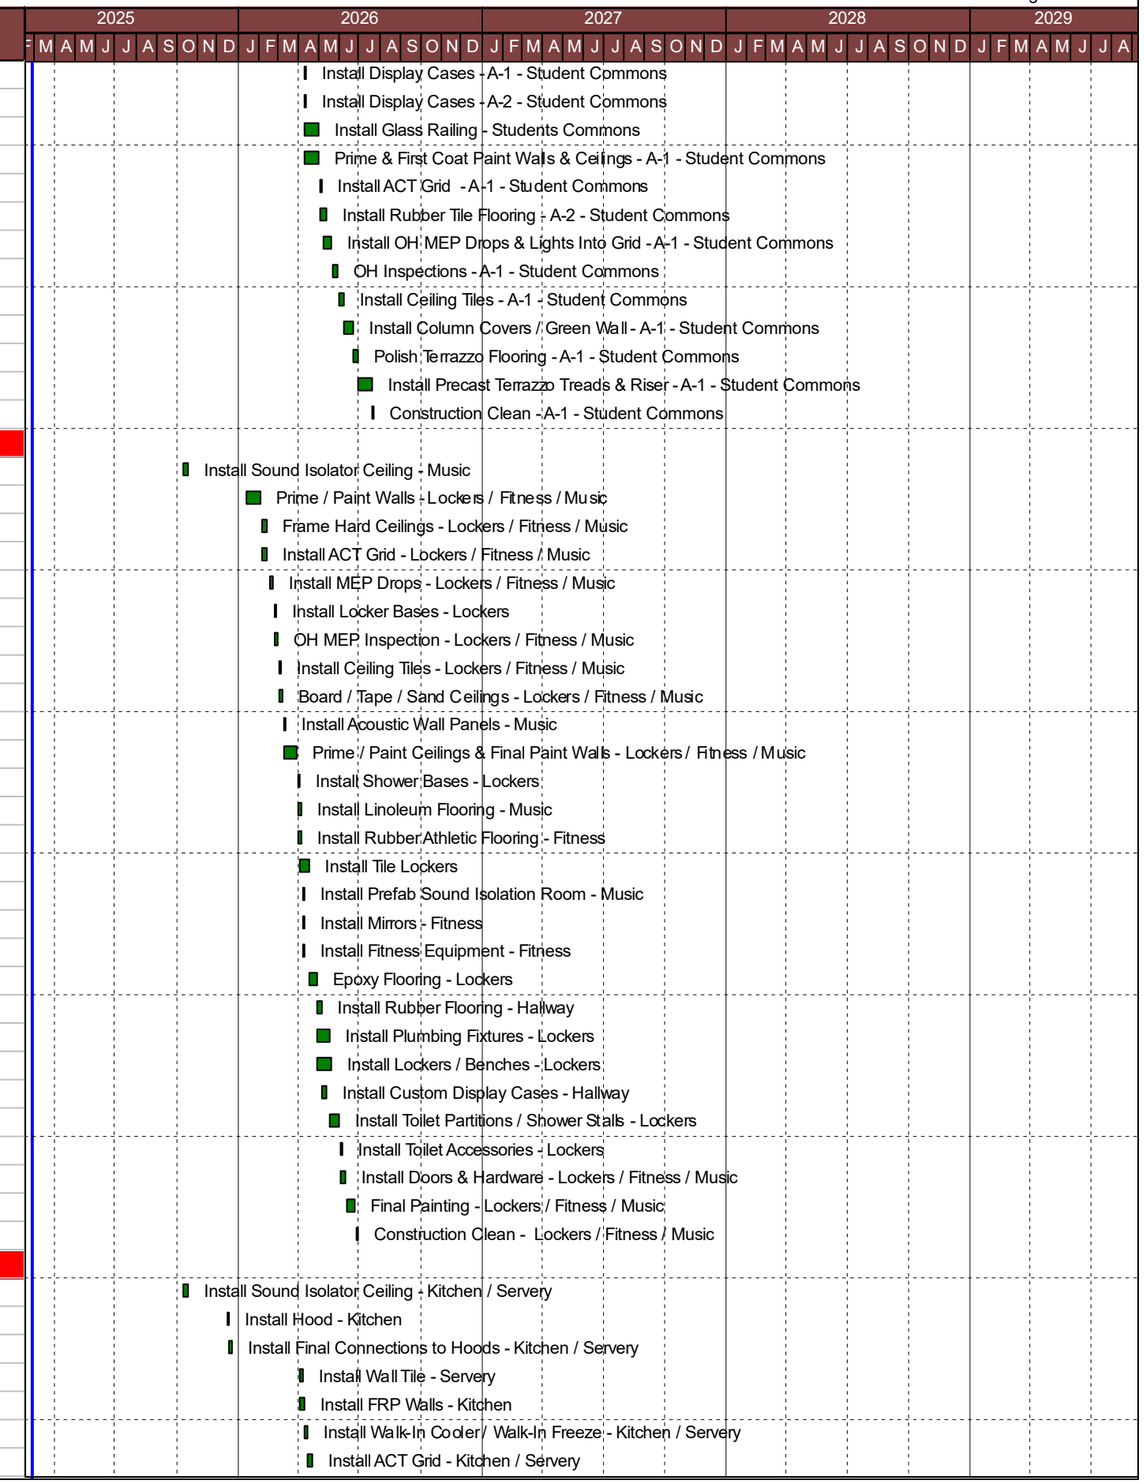

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A50040	Install Ansul System - Kitchen	2d	2d	22-Apr-26	23-Apr-26
A49900	Install MEP Drops - Kitchen / Servery	5d	5d	22-Apr-26	28-Apr-26
A49910	OH MEP Inspection - Kitchen / Servery	5d	5d	29-Apr-26	05-May-26
A49920	Install Ceiling Tiles - Kitchen / Servery	3d	3d	06-May-26	08-May-26
A50060	Install MEP Finishes - Kitchen / Servery	3d	3d	11-May-26	13-May-26
A49940	Install Epoxy Flooring - Kitchen	5d	5d	11-May-26	15-May-26
A50030	Final Painting - Kitchen / Servery	5d	5d	18-May-26	22-May-26
A49950	Install Terrazzo - Servery	5d	5d	23-Jun-26	29-Jun-26
A49970	Install Food Service Equipment - Kitchen / Servery	5d	5d	30-Jun-26	06-Jul-26
A50020	Connections to Food Service Equipment - Kitchen / Servery	10d	10d	07-Jul-26	20-Jul-26
A49980	Construction Clean - A-1 - Kitchen / Servery	2d	2d	21-Jul-26	22-Jul-26
A50010	Food Service Equipment Start-up - Kitchen / Servery	5d	5d	23-Jul-26	29-Jul-26
A50050	Test Ansul System with Fire Dept - Kitchen	2d	2d	30-Jul-26	31-Jul-26
Fire Pump Room / Water Service Room - A161/A162					
A50080	Paint Exposed Decks - FP/Water Service Rooms	2d	2d	10-Oct-25	14-Oct-25
A50070	FRP Equip Pads - FP/Water Service Rooms	3d	3d	15-Oct-25	17-Oct-25
A50090	Set Fire Pump / Equip - FP/Water Service Rooms	5d	5d	20-Oct-25	24-Oct-25
A50100	MEP Rough - FP/Water Service Rooms	20d	20d	27-Oct-25	24-Nov-25
Main Electric Room - A186					
A21330	Set CMU Walls - Main Electric Room - A186	10d	10d	03-Oct-25	17-Oct-25
A21350	FRP Housekeeping Pads - Main Electric Room - A186	5d	5d	20-Oct-25	24-Oct-25
A21440	In-Wall Electric Rough - Main Electric Room - A186	10d	10d	20-Oct-25	31-Oct-25
A21340	Prime / First Coat Walls - Main Electric Room - A186	2d	2d	03-Nov-25	04-Nov-25
A21360	Set Main Switchgear - Main Electric Room - A186	30d	30d	22-Jun-26	31-Jul-26
A21370	Install Sub-Panels - Main Electric Room - A186	15d	15d	13-Jul-26	31-Jul-26
A21450	Install Temp Door - Main Electric Room - A186	2d	2d	30-Jul-26	31-Jul-26
A21380	Pull Wires / Feeders to Panels / Gear - Main Electric Room - A186	10d	10d	03-Aug-26	14-Aug-26
A21390	Install OH Electric Rough (for Lighting / Power) - Main Electric Room - A186	10d	10d	17-Aug-26	28-Aug-26
A22730	National Grid Liven Transformers	22d	22d	17-Aug-26	16-Sep-26
A21400	Install Doors & Hardware - Main Electric Room - A186	2d	2d	31-Aug-26	01-Sep-26
A21410	Final Paint - Main Electric Room - A186	2d	2d	17-Sep-26	18-Sep-26
A21430	Construction Clean - Main Electric Room - A186	2d	2d	21-Sep-26	22-Sep-26
A21420	Seal Floor - Main Electric Room - A186	3d	3d	23-Sep-26	25-Sep-26
A189050	Punchlist - Main Electric Room - A186	10d	10d	23-Sep-26	06-Oct-26
Main Mechanical Room - A187					
A22880	Set CMU Walls - Main Mechanical Room - A187	5d	5d	07-Oct-25	14-Oct-25
A22890	In-Wall Elect Rough - Main Mechanical Room - A187	5d	5d	09-Oct-25	16-Oct-25
A22900	In-Wall Plumbing - Main Mechanical Room - A187	5d	5d	09-Oct-25	16-Oct-25
A15720	FRP Housekeeping Pads - Main Mechanical Room - A187	5d	5d	15-Oct-25	21-Oct-25
A15700	Prime / 1st Coat Walls - Main Mechanical Room - A187	3d	3d	17-Oct-25	21-Oct-25
A15620	Install OH Mechanical Pipe Rough - Main Mechanical Room - A187	30d	30d	22-Oct-25	04-Dec-25
A15600	OH Duct Rough - Main Mechanical Room - A187	10d	10d	20-Nov-25	04-Dec-25
A15610	Install OH Plumbing Rough - Main Mechanical Room - A187	20d	20d	28-Nov-25	26-Dec-25
A15640	Install OH Electrical Rough - Main Mechanical Room - A187	15d	15d	05-Dec-25	26-Dec-25
A16180	Build-Out Controls / Control Panel - Main Mechanical Room - A187	110d	110d	05-Dec-25	14-May-26
A15670	Install OH FP Rough - Main Mechanical Room - A187	5d	5d	29-Dec-25	05-Jan-26
A15730	Set Equipment - Main Mechanical Room - A187	30d	30d	06-Jan-26	18-Feb-26
A16020	Connect Plumbing to Equipment - Main Mechanical Room - A187	10d	10d	19-Feb-26	04-Mar-26
A15770	Install Flues & Intakes - Main Mechanical Room - A187	15d	15d	19-Feb-26	11-Mar-26
A15940	Install Mechanical Branch Lines - Main Mechanical Room - A187	44d	44d	19-Feb-26	22-Apr-26

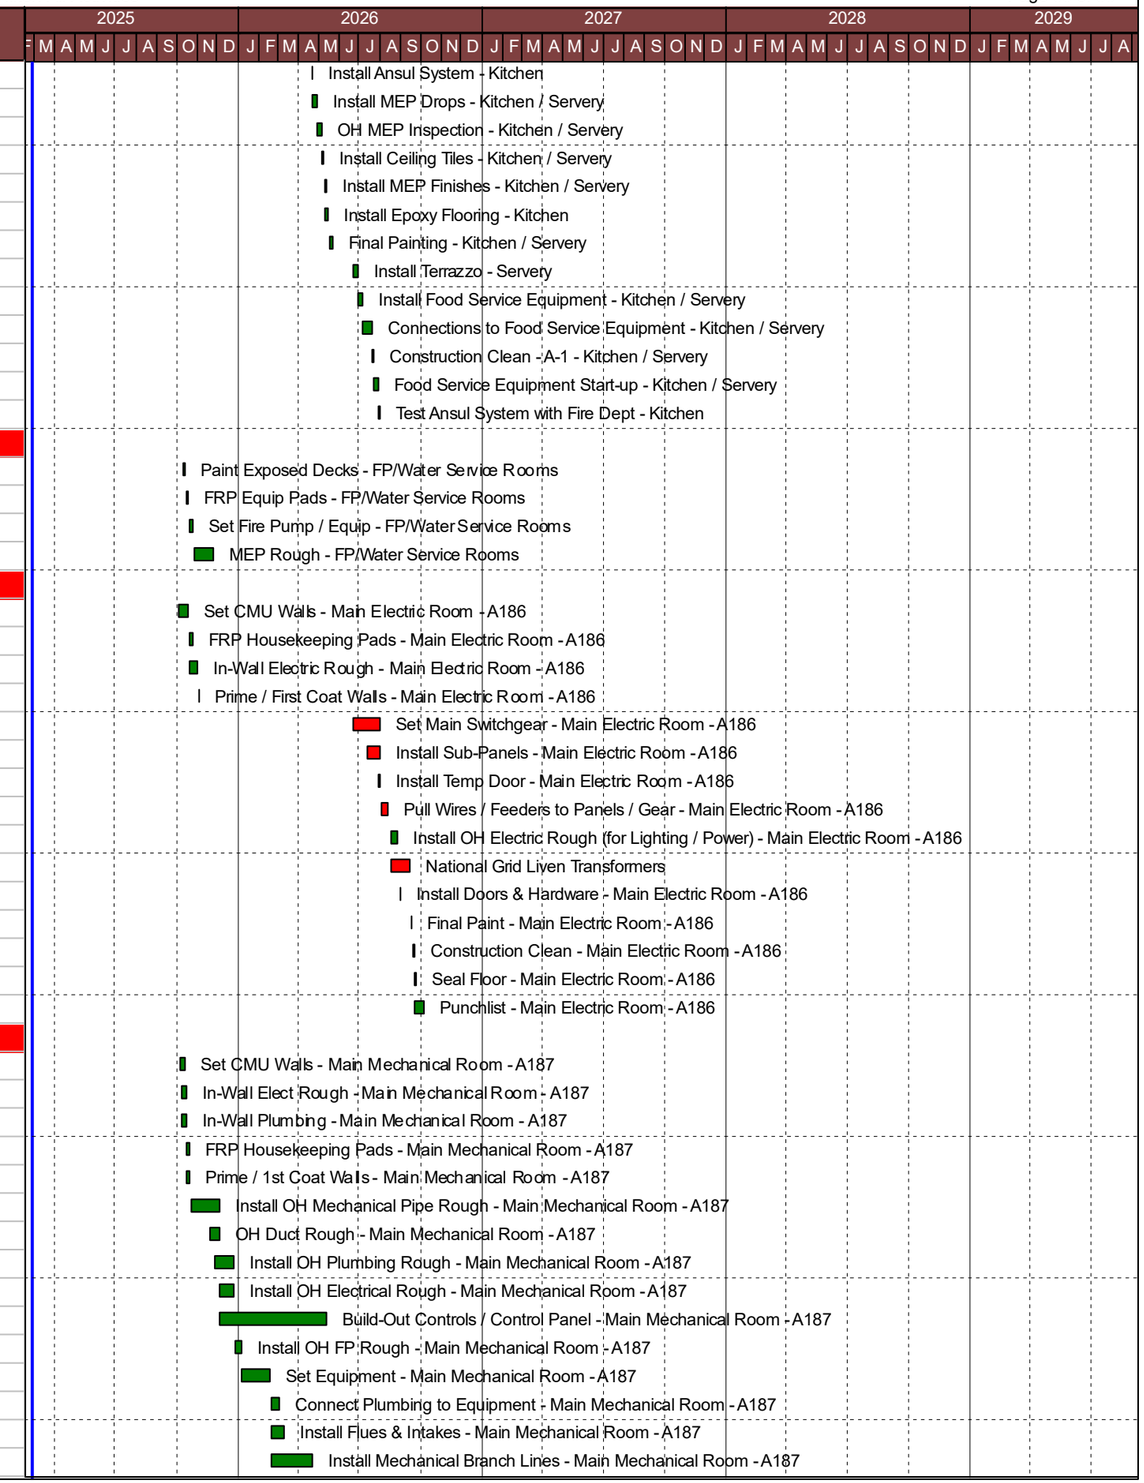

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A16170	Final Electrical Connections - Main Mechanical Room - A187	10d	10d	04-Mar-26	17-Mar-26
A20890	Install Epoxy Flooring - Main Mechanical Room - A187	5d	5d	19-Mar-26	25-Mar-26
A16030	VFD Start-up - Main Mechanical Room - A187	1d	1d	23-Apr-26	23-Apr-26
A16040	Boiler Start-up - Main Mechanical Room - A187	1d	1d	23-Apr-26	23-Apr-26
A16880	Install Fire Alarm - Main Mechanical Room - A187	5d	5d	08-May-26	14-May-26
A17750	Install Doors & Hardware - Main Mechanical Room - A187	1d	1d	15-May-26	15-May-26
A20180	Construction Clean - Main Mechanical Room - A187	2d	2d	18-May-26	19-May-26
A189060	Punchlist - Main Mechanical Room - A187	10d	10d	20-May-26	03-Jun-26
Bathrooms					
A189970	In-Wall HVAC Piping Rough - A-1 BR	2d	2d	08-Dec-25	09-Dec-25
A189980	In-Wall Elect Rough - A-1 BR	2d	2d	10-Dec-25	11-Dec-25
A189960	In-Wall Plumbing Rough - A-1 BR	5d	5d	15-Dec-25	19-Dec-25
A189990	In-Wall Elect & Plumbing Inspection - A-1 BR	5d	5d	22-Dec-25	29-Dec-25
A190000	Insulate Plumbing & Mech Piping - A-1 BR	2d	2d	30-Dec-25	31-Dec-25
A190010	In-Wall Building Inspection - A-1 BR	5d	5d	02-Jan-26	08-Jan-26
A190020	Frame Hard Ceilings - A-1 BR	2d	2d	09-Jan-26	12-Jan-26
A190030	Install OH MEP Drops & Lights Into Hard Ceilings - A-1 BR	2d	2d	13-Jan-26	14-Jan-26
A190040	OH Inspections - A-1 BR	5d	5d	15-Jan-26	22-Jan-26
A190050	Insulate / Drywall / Tape & Sands Walls & Ceilings - A-1 BR	5d	5d	23-Jan-26	29-Jan-26
A190060	Prime & First Coat Paint Walls & Ceilings - A-1 BR	1d	1d	30-Jan-26	30-Jan-26
A190070	Install Wall & Floor Tile @ Bathooms - A-1 BR	10d	10d	02-Feb-26	13-Feb-26
A190080	MEP Wall Finishes - A-1 BR	1d	1d	17-Feb-26	17-Feb-26
A190090	Final Painting - A-1 BR	4d	4d	18-Feb-26	23-Feb-26
A190100	Install Plumbing Fixtures - A-1 BR	5d	5d	24-Feb-26	02-Mar-26
A190110	Install Toilet Partitions - A-1 BR	3d	3d	03-Mar-26	05-Mar-26
A190120	Install Toilet Accessories - A-1 BR	2d	2d	06-Mar-26	09-Mar-26
A190130	Install Specialties - A-1 BR	2d	2d	06-Mar-26	09-Mar-26
A190140	Install Doors & Hardware - A-1 BR	1d	1d	10-Mar-26	10-Mar-26
A190150	Construction Clean - A-1 BR	2d	2d	11-Mar-26	12-Mar-26
Auditorium					
A11360	Frame & Top Off Walls - Auditorium	10d	10d	10-Sep-25	23-Sep-25
A11580	Install Door Frames - Auditorium	1d	1d	23-Sep-25	23-Sep-25
A11590	Install Fabric Wrapped Acoustic Panels - Auditorium	5d	5d	23-Sep-25	29-Sep-25
A11430	In-Wall HVAC Piping Rough - Auditorium	10d	10d	24-Sep-25	07-Oct-25
A11420	In-Wall Elect Rough - Auditorium	20d	20d	24-Sep-25	22-Oct-25
A11530	Install MEP & Ceiling Support Hangers (no more than 1' long) - Auditorium	5d	5d	03-Oct-25	09-Oct-25
A11470	In-Wall Plumbing & Elect Inspection - Auditorium	5d	5d	23-Oct-25	29-Oct-25
A11480	Insulate Plumbing & Mech Piping - Auditorium	5d	5d	30-Oct-25	05-Nov-25
A11460	In-Wall Building Inspection - Auditorium	5d	5d	06-Nov-25	13-Nov-25
A11490	Insulate / Drywall / Tape & Sands Walls - Auditorium	20d	20d	14-Nov-25	12-Dec-25
A11630	Install Overhead Door - Auditorium	2d	2d	15-Dec-25	16-Dec-25
A189200	Paint Structure- Auditorium	3d	3d	17-Dec-25	19-Dec-25
A11520	K-13 - Auditorium	5d	5d	22-Dec-25	29-Dec-25
A11510	Prime, First Coat & Paint Above Ceiling Walls - Auditorium	5d	5d	30-Dec-25	06-Jan-26
A11400	OH Sprinkler Rough - Auditorium	10d	10d	30-Dec-25	13-Jan-26
A11560	Prime & First Coat Paint Walls - Auditorium	15d	15d	30-Dec-25	21-Jan-26
A11500	Stage Curtain Rigging & Supports - Auditorium	5d	5d	14-Jan-26	21-Jan-26
A11370	OH Duct Rough - Auditorium	25d	25d	22-Jan-26	26-Feb-26
A11390	OH HVAC Piping Rough - Auditorium	10d	10d	12-Feb-26	26-Feb-26
A11410	OH Plumbing Rough - Auditorium	10d	10d	20-Feb-26	05-Mar-26

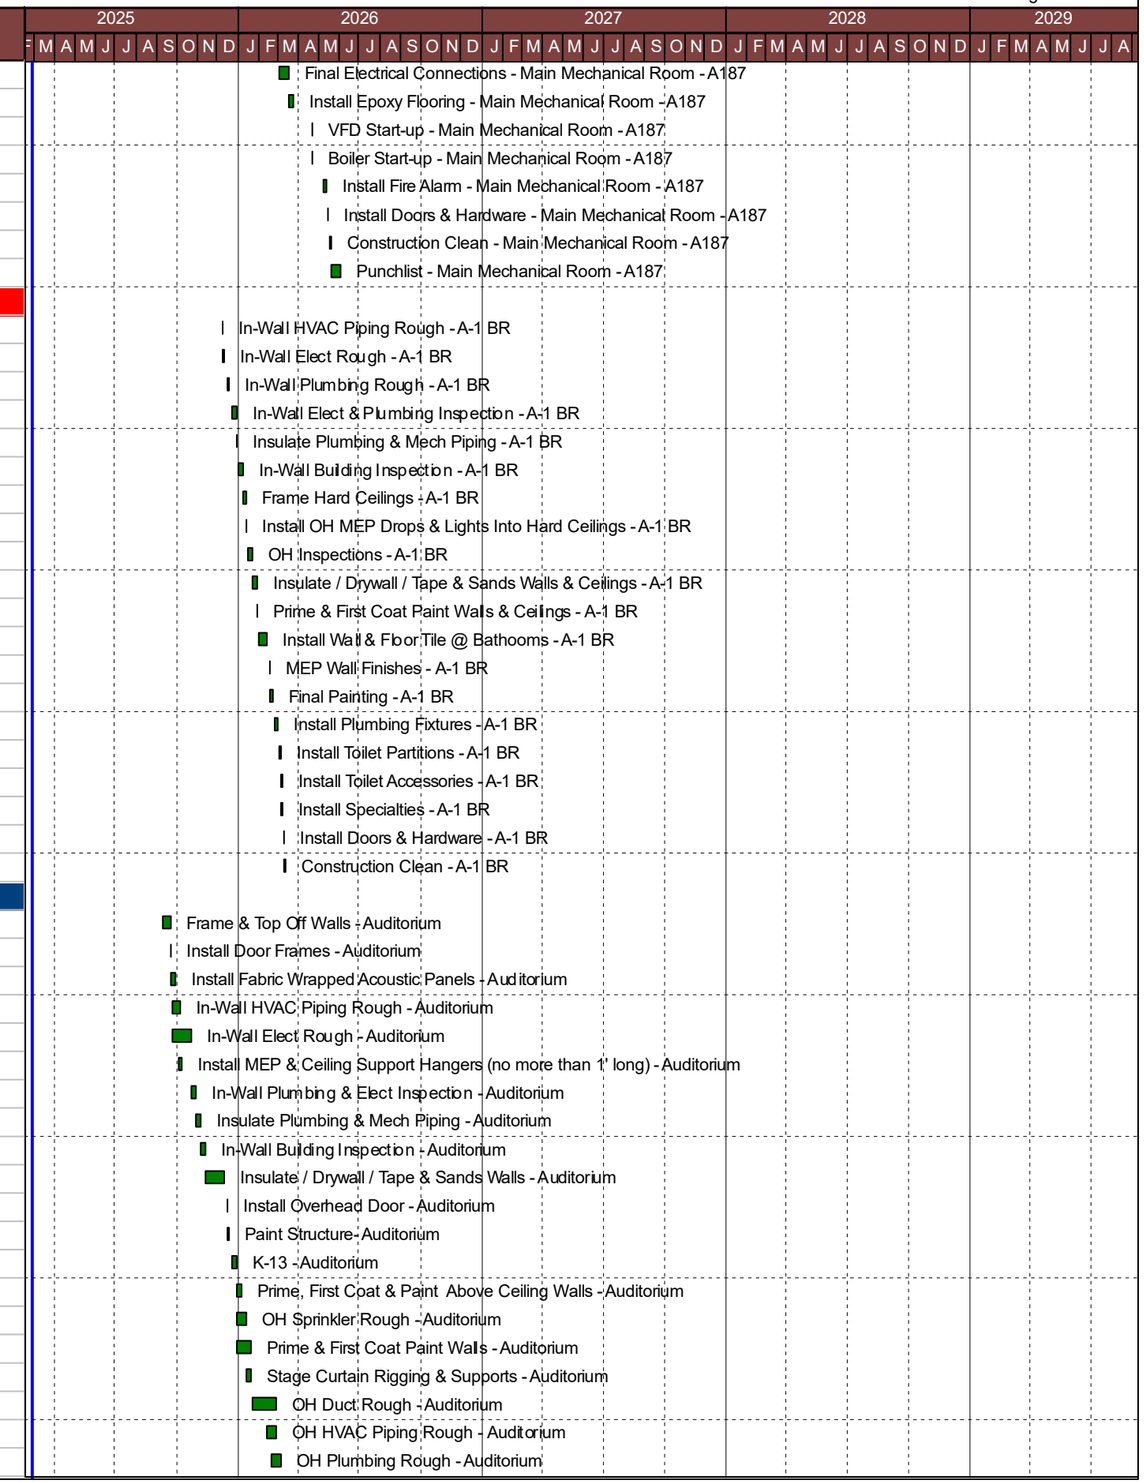

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A11380	OH Elect / Fire Alarm Rough - Auditorium	25d	25d	27-Feb-26	02-Apr-26
A192340	OH AV / Telcom / Low Voltage Rough - Auditorium	25d	25d	03-Apr-26	08-May-26
A11720	Install Grid at Mezzanine Ceilings - Auditorium	4d	4d	11-May-26	14-May-26
A11450	Install Theatrical Pipe Grid - Auditorium	5d	5d	11-May-26	15-May-26
A11730	MEP Finishes at Mezzanine Ceilings - Auditorium	2d	2d	15-May-26	18-May-26
A11550	Install Light Fixtures - Auditorium	5d	5d	18-May-26	22-May-26
A11750	Metal Fin Ceiling at Mezzanine - Auditorium	3d	3d	19-May-26	21-May-26
A11570	Install Mezzanine Glass Railing Systems - Auditorium	3d	3d	22-May-26	27-May-26
A11740	MEP Finishes at Main Ceiling - Auditorium	5d	5d	26-May-26	01-Jun-26
A11760	Install Flooring at Mezzanine - Auditorium	3d	3d	28-May-26	01-Jun-26
A11610	Install Sheet Vinyl Flooring - Auditorium	4d	4d	02-Jun-26	05-Jun-26
A11770	Install Seating at Mezzanines - Auditorium	4d	4d	02-Jun-26	05-Jun-26
A11540	Install Ceiling Clouds - Auditorium	6d	6d	02-Jun-26	09-Jun-26
A25890	Install Wood Flooring - Auditorium	10d	10d	08-Jun-26	19-Jun-26
A11660	Air & Water Balancing - Auditorium	3d	3d	22-Jun-26	24-Jun-26
A11620	Install Telescoping Bleachers - Auditorium	10d	10d	25-Jun-26	08-Jul-26
A11690	Install Electrical / AV Finishes (Control Booth) - Auditorium	10d	10d	25-Jun-26	08-Jul-26
A11600	Final Painting - Auditorium	3d	3d	09-Jul-26	13-Jul-26
A11670	Install Doors & Hardware - Auditorium	2d	2d	14-Jul-26	15-Jul-26
A11710	Construction Clean - Auditorium	2d	2d	16-Jul-26	17-Jul-26
A11640	Install Draperies - Auditorium	3d	3d	20-Jul-26	22-Jul-26
A11650	Install Theatrical Lighting - Auditorium	5d	5d	23-Jul-26	29-Jul-26
A11700	Punchlist - Auditorium	10d	10d	05-Oct-26	19-Oct-26
A11680	Final Cleaning - Auditorium	2d	2d	05-Nov-26	06-Nov-26
Gymnasium					
A11790	CMU Interior Wall - Gym	15d	15d	15-Aug-25	05-Sep-25
A11860	OH Sprinkler Rough - Gym	8d	8d	08-Sep-25	17-Sep-25
A189110	OH Duct Rough - Gym	20d	20d	15-Sep-25	10-Oct-25
A11810	In-Wall Elect - Gym	15d	15d	17-Sep-25	07-Oct-25
A11820	In-Wall Plumbing - Gym	15d	15d	17-Sep-25	07-Oct-25
A11830	In-Wall HVAC - Gym	15d	15d	17-Sep-25	07-Oct-25
A11800	Install Door Frames in CMU - Gym	2d	2d	25-Sep-25	26-Sep-25
A11780	Frame Walls - Gym	6d	6d	29-Sep-25	06-Oct-25
A189120	OH HVAC Piping Rough - Gym	10d	10d	06-Oct-25	20-Oct-25
A11840	In-Wall Inspections - Gym	5d	5d	08-Oct-25	15-Oct-25
A12030	Overhead MEP Insulation - Gym	5d	5d	08-Oct-25	15-Oct-25
A189100	OH Plumbing Rough - Gym	20d	20d	14-Oct-25	10-Nov-25
A11850	Insulate / Drywall / Tape & Sands Walls - Gym	20d	20d	16-Oct-25	13-Nov-25
A189090	OH Elect / Fire Alarm Rough - Gym	20d	20d	06-Nov-25	05-Dec-25
A192350	OH AV / Telcom / Low Voltage Rough - Gym	20d	20d	08-Dec-25	06-Jan-26
A11870	Install Supports for Basketball Hoops & Gym Equipment - Gym	4d	4d	12-Dec-25	17-Dec-25
A11880	Overhead Painting - Gym	6d	6d	07-Jan-26	14-Jan-26
A11890	Prime / First Coat Walls - Gym	4d	4d	15-Jan-26	21-Jan-26
A11920	Plumbing Finishes - Gym	2d	2d	22-Jan-26	23-Jan-26
A11900	HVAC Finishes - Gym	5d	5d	22-Jan-26	28-Jan-26
A11910	Electrical Finishes - Gym	7d	7d	26-Jan-26	03-Feb-26
A11930	Sprinkler Finishes - Gym	3d	3d	29-Jan-26	02-Feb-26
A11940	Final Paint Walls - Gym	15d	15d	04-Feb-26	25-Feb-26
A11950	Install Acoustic Wall Panels - Gym	8d	8d	26-Feb-26	09-Mar-26
A11960	Install Basketball Hoops - Gym	6d	6d	10-Mar-26	17-Mar-26

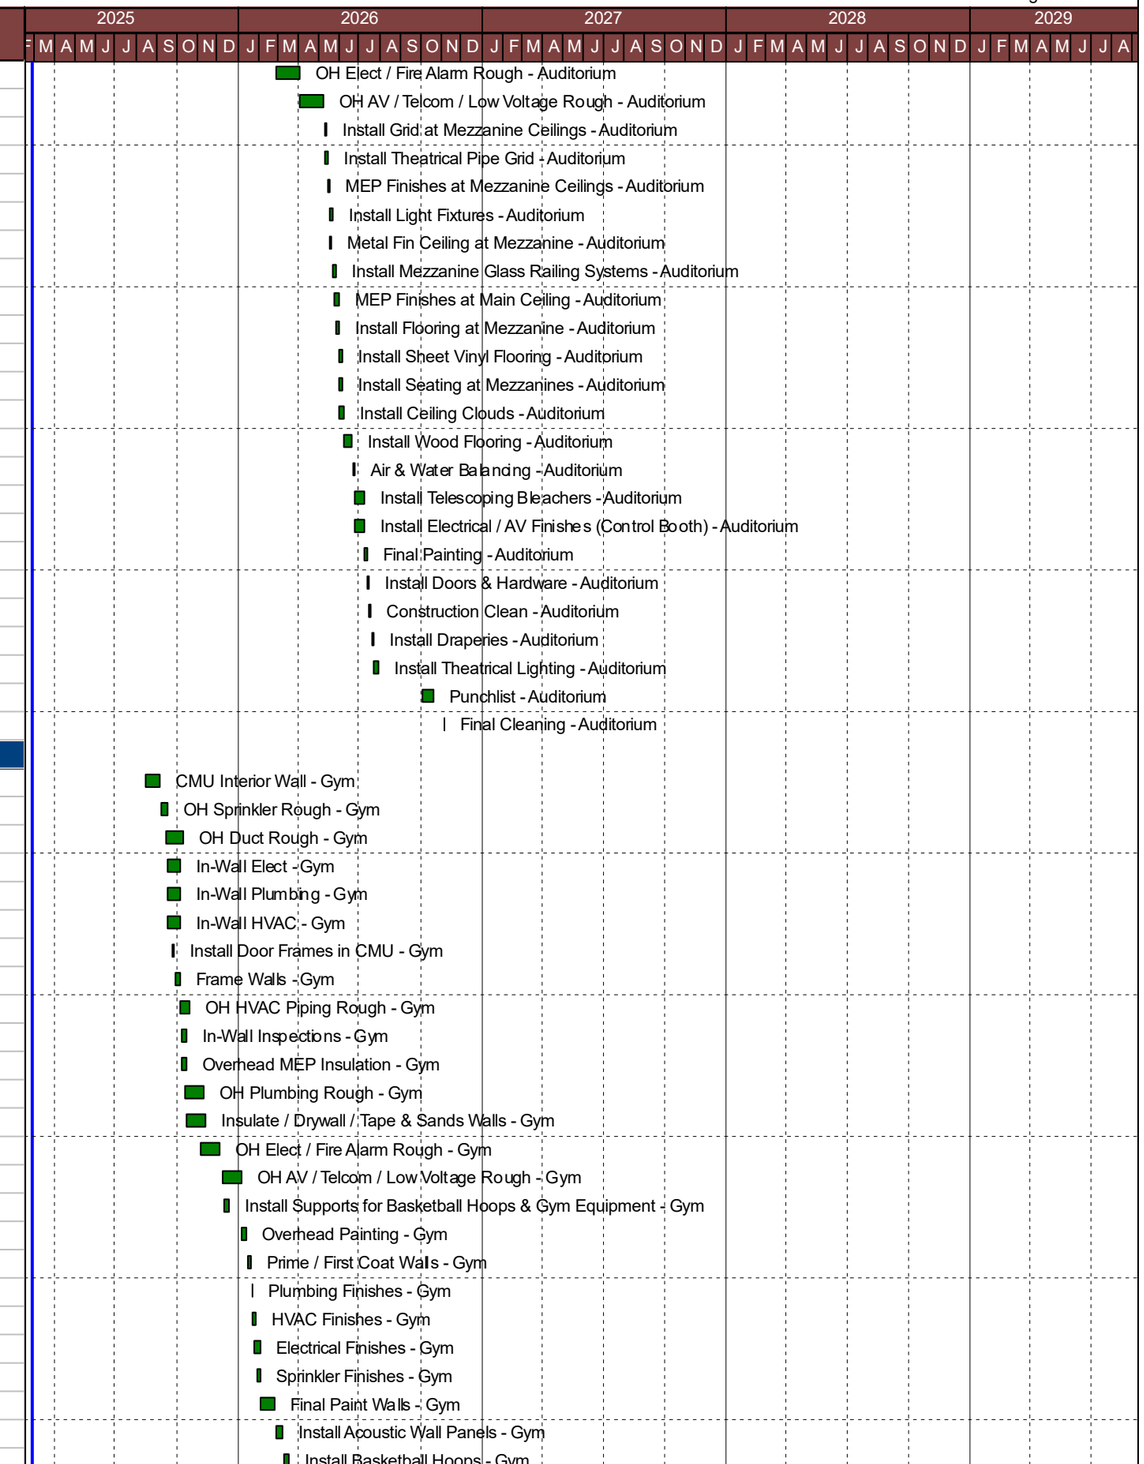

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A11970	Install Divider Curtains - Gym	2d	2d	18-Mar-26	19-Mar-26
A11980	Install Scoreboard - Gym	2d	2d	20-Mar-26	23-Mar-26
A11990	Install Wood Athletic Flooring & Striping - Gym	25d	25d	16-Oct-26	20-Nov-26
A12020	Install Doors - Gym	2d	2d	23-Nov-26	24-Nov-26
A12000	Install Bleachers - Gym	25d	25d	23-Nov-26	29-Dec-26
A12010	Install Walls Pads - Gym	3d	3d	30-Dec-26	04-Jan-27
A12040	Construction Clean - Gym	2d	2d	05-Jan-27	06-Jan-27
A12050	Punchlist - Gym	10d	10d	07-Jan-27	21-Jan-27
A12060	Final Clean - Gym	2d	2d	22-Jan-27	25-Jan-27
Building B					
3rd Floor					
A50110	Install Control - B-3	2d	2d	28-Aug-25	29-Aug-25
A50120	Layout & Install Wall Clips - B-3	10d	10d	02-Sep-25	15-Sep-25
A50130	Install Hangers - B-3	5d	5d	24-Sep-25	30-Sep-25
A50140	Patch Spray Fireproofing - B-3	3d	3d	01-Oct-25	03-Oct-25
A50150	OH Duct Rough - B-3	20d	20d	16-Oct-25	13-Nov-25
A50160	OH HVAC Piping Rough - B-3	20d	20d	16-Oct-25	13-Nov-25
A50180	OH Plumbing Rough - B-3	15d	15d	23-Oct-25	13-Nov-25
A50230	Install Door Frames - B-3	5d	5d	30-Oct-25	05-Nov-25
A50210	OH Sprinkler Rough - B-3	10d	10d	30-Oct-25	13-Nov-25
A50220	Frame & Top Off Walls - B-3	10d	10d	30-Oct-25	13-Nov-25
A50200	OH Elect / Fire Alarm Rough - B-3	15d	15d	30-Oct-25	20-Nov-25
A192360	OH AV / Telcom / Low Voltage Rough - B-3	15d	15d	21-Nov-25	12-Dec-25
A50260	Install Signage - B-3	2d	2d	02-Jun-26	03-Jun-26
A50540	Punchlist - B-3	10d	10d	22-Jan-27	04-Feb-27
A50550	Final Cleaning - B-3	2d	2d	05-Feb-27	08-Feb-27
Classrooms / Offices / Hallways (incl. CR-D300					
A50250	In-Wall HVAC Piping Rough - B-3 CR	5d	5d	14-Nov-25	20-Nov-25
A50240	In-Wall Elect Rough - B-3 CR	20d	20d	14-Nov-25	12-Dec-25
A50270	In-Wall Elect Inspection - B-3 CR	10d	10d	15-Dec-25	29-Dec-25
A50280	Insulate Mech Piping - B-3 CR	5d	5d	30-Dec-25	06-Jan-26
A50290	In-Wall Building Inspection - B-3 CR	5d	5d	07-Jan-26	13-Jan-26
A50300	Insulate / Drywall / Tape & Sands Walls - B-3 CR	25d	25d	14-Jan-26	19-Feb-26
A50340	Prime & First Coat Paint Walls & Ceilings - B-3 CR	15d	15d	20-Feb-26	12-Mar-26
A54790	Install VBC-12 Ceiling - B-3 CR	10d	10d	13-Mar-26	26-Mar-26
A50350	Install ACT Grid - B-3 CR	11d	11d	13-Mar-26	27-Mar-26
A50370	Install OH MEP Drops Into Grid - B-3 CR	5d	5d	30-Mar-26	03-Apr-26
A50570	Install OH Lights Into Grid - B-3 CR	5d	5d	30-Mar-26	03-Apr-26
A50380	Install Wall Tile @ Hallways- B-3 CR	10d	10d	30-Mar-26	10-Apr-26
A50410	OH Inspections - B-3 CR	5d	5d	06-Apr-26	10-Apr-26
A50440	Install Ceiling Tiles - B-3 CR	6d	6d	13-Apr-26	21-Apr-26
A50470	Install Casework - B-3 CR	3d	3d	22-Apr-26	24-Apr-26
A50430	MEP Wall Finishes - B-3 CR	5d	5d	22-Apr-26	28-Apr-26
A50490	Install Carpet - B-3 CR	5d	5d	27-Apr-26	01-May-26
A50560	Install Linoleum Flooring - B-3 CR	15d	15d	27-Apr-26	15-May-26
A50450	Final Painting - B-3 CR	4d	4d	29-Apr-26	04-May-26
A50480	Install Specialties - B-3 CR	2d	2d	05-May-26	06-May-26
A54800	Install Plumbing Finishes - B-3 CR	2d	2d	05-May-26	06-May-26
A189130	Install Lockers - B-3 CR	3d	3d	05-May-26	07-May-26
A50460	Install Rubber Tile - B-3 CR	10d	10d	18-May-26	01-Jun-26

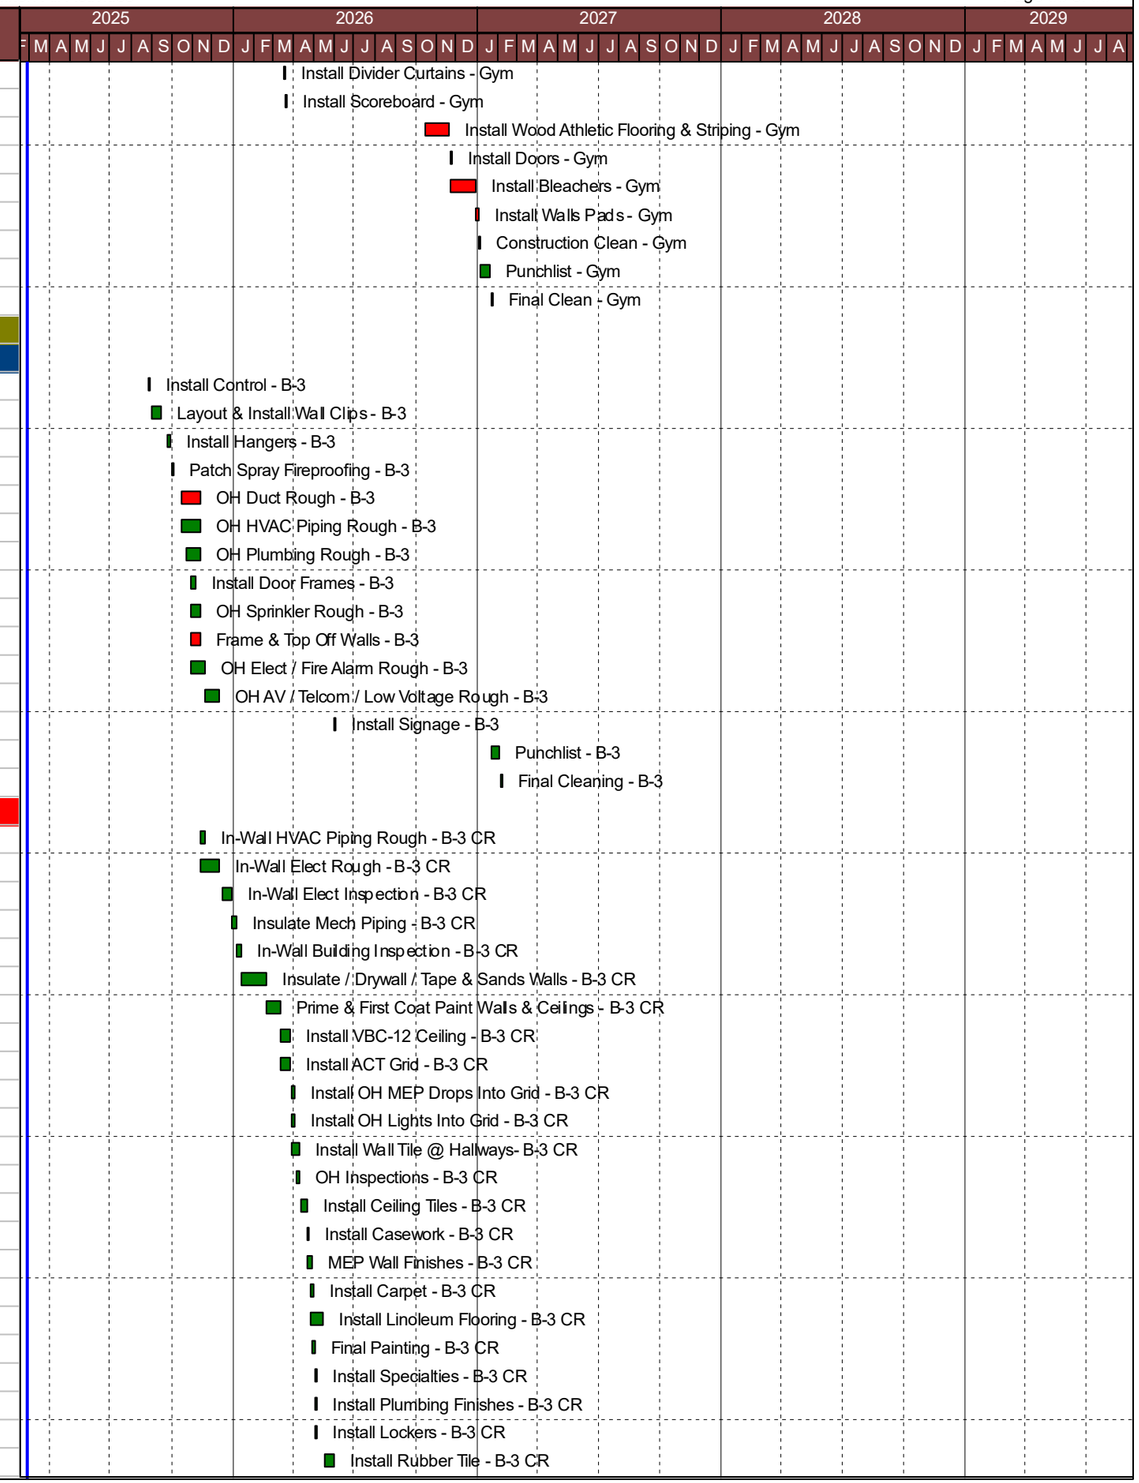

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A50520	Install Doors & Hardware - B-3 CR	2d	2d	02-Jun-26	03-Jun-26
A54810	Install Appliances - B-3 CR	4d	4d	02-Jun-26	05-Jun-26
A50530	Construction Clean - B-3 CR	2d	2d	08-Jun-26	09-Jun-26
SCI Lab					
A50840	In-Wall Plumbing Rough - B-3 SciLab	5d	5d	14-Nov-25	20-Nov-25
A50610	In-Wall HVAC Piping Rough - B-3 SciLab	2d	2d	21-Nov-25	24-Nov-25
A50600	In-Wall Elect Rough - B-3 SciLab	2d	2d	15-Dec-25	16-Dec-25
A50620	In-Wall Elect & Plumbing Inspection - B-3 SciLab	5d	5d	22-Dec-25	29-Dec-25
A50630	Insulate Plumbing & Mech Piping - B-3 SciLab	2d	2d	30-Dec-25	31-Dec-25
A50640	In-Wall Building Inspection - B-3 SciLab	5d	5d	02-Jan-26	08-Jan-26
A50650	Insulate / Drywall / Tape & Sands Walls - B-3 SciLab	6d	6d	20-Jan-26	27-Jan-26
A50660	Prime & First Coat Paint Walls & Ceilings - B-3 SciLab	1d	1d	28-Jan-26	28-Jan-26
A50670	Install ACT Grid - B-3 SciLab	3d	3d	29-Jan-26	02-Feb-26
A50680	Install OH MEP Drops Into Grid - B-3 SciLab	1d	1d	03-Feb-26	03-Feb-26
A50690	Install OH Lights Into Grid - B-3 SciLab	1d	1d	03-Feb-26	03-Feb-26
A50710	OH Inspections - B-3 SciLab	5d	5d	04-Feb-26	10-Feb-26
A50720	Install Ceiling Tiles - B-3 SciLab	1d	1d	11-Feb-26	11-Feb-26
A50730	MEP Wall Finishes - B-3 SciLab	2d	2d	12-Feb-26	13-Feb-26
A50760	Install Sheet Vinyl Flooring - B-3 SciLab	4d	4d	12-Feb-26	18-Feb-26
A50740	Final Painting - B-3 SciLab	1d	1d	17-Feb-26	17-Feb-26
A50780	Install Specialties - B-3 SciLab	2d	2d	18-Feb-26	19-Feb-26
A50750	Install Casework - B-3 SciLab	3d	3d	08-Apr-26	10-Apr-26
A50800	Install Doors & Hardware - B-3 SciLab	1d	1d	13-Apr-26	13-Apr-26
A54090	Install Appliances - B-3 SciLab	2d	2d	13-Apr-26	14-Apr-26
A54100	Install Fume Hoods - B-3 SciLab	2d	2d	13-Apr-26	14-Apr-26
A54020	Plumbing Finish - B-3 SciLab	3d	3d	13-Apr-26	15-Apr-26
A50810	Construction Clean - B-3 SciLab	1d	1d	16-Apr-26	16-Apr-26
Bathrooms					
A50890	In-Wall Plumbing Rough - B-3 BR	5d	5d	19-Nov-25	25-Nov-25
A50880	In-Wall HVAC Piping Rough - B-3 BR	2d	2d	25-Nov-25	26-Nov-25
A50870	In-Wall Elect Rough - B-3 BR	2d	2d	17-Dec-25	18-Dec-25
A50900	In-Wall Elect & Plumbing Inspection - B-3 BR	5d	5d	22-Dec-25	29-Dec-25
A50910	Insulate Plumbing & Mech Piping - B-3 BR	2d	2d	30-Dec-25	31-Dec-25
A50920	In-Wall Building Inspection - B-3 BR	5d	5d	02-Jan-26	08-Jan-26
A50940	Frame Hard Ceilings - B-3 BR	2d	2d	09-Jan-26	12-Jan-26
A50950	Install OH MEP Drops & Lights Into Hard Ceilings - B-3 BR	2d	2d	13-Jan-26	14-Jan-26
A51040	OH Inspections - B-3 BR	5d	5d	15-Jan-26	22-Jan-26
A50960	Insulate / Drywall / Tape & Sands Walls & Ceilings - B-3 BR	5d	5d	23-Jan-26	29-Jan-26
A50970	Prime & First Coat Paint Walls & Ceilings - B-3 BR	1d	1d	30-Jan-26	30-Jan-26
A50990	Install Wall & Floor Tile @ Bathooms - B-3 BR	10d	10d	02-Feb-26	13-Feb-26
A51060	MEP Wall Finishes - B-3 BR	1d	1d	17-Feb-26	17-Feb-26
A51080	Final Painting - B-3 BR	4d	4d	18-Feb-26	23-Feb-26
A51020	Install Plumbing Fixtures - B-3 BR	5d	5d	24-Feb-26	02-Mar-26
A51030	Install Toilet Partitions - B-3 BR	3d	3d	03-Mar-26	05-Mar-26
A51050	Install Toilet Accessories - B-3 BR	2d	2d	06-Mar-26	09-Mar-26
A51110	Install Specialties - B-3 BR	2d	2d	06-Mar-26	09-Mar-26
A51150	Install Doors & Hardware - B-3 BR	1d	1d	10-Mar-26	10-Mar-26
A51160	Construction Clean - B-3 BR	2d	2d	11-Mar-26	12-Mar-26
IDF / Elec - B318/B317					
A51230	Frame Walls - Elec Rm B318/B317	9d	9d	24-Sep-25	06-Oct-25

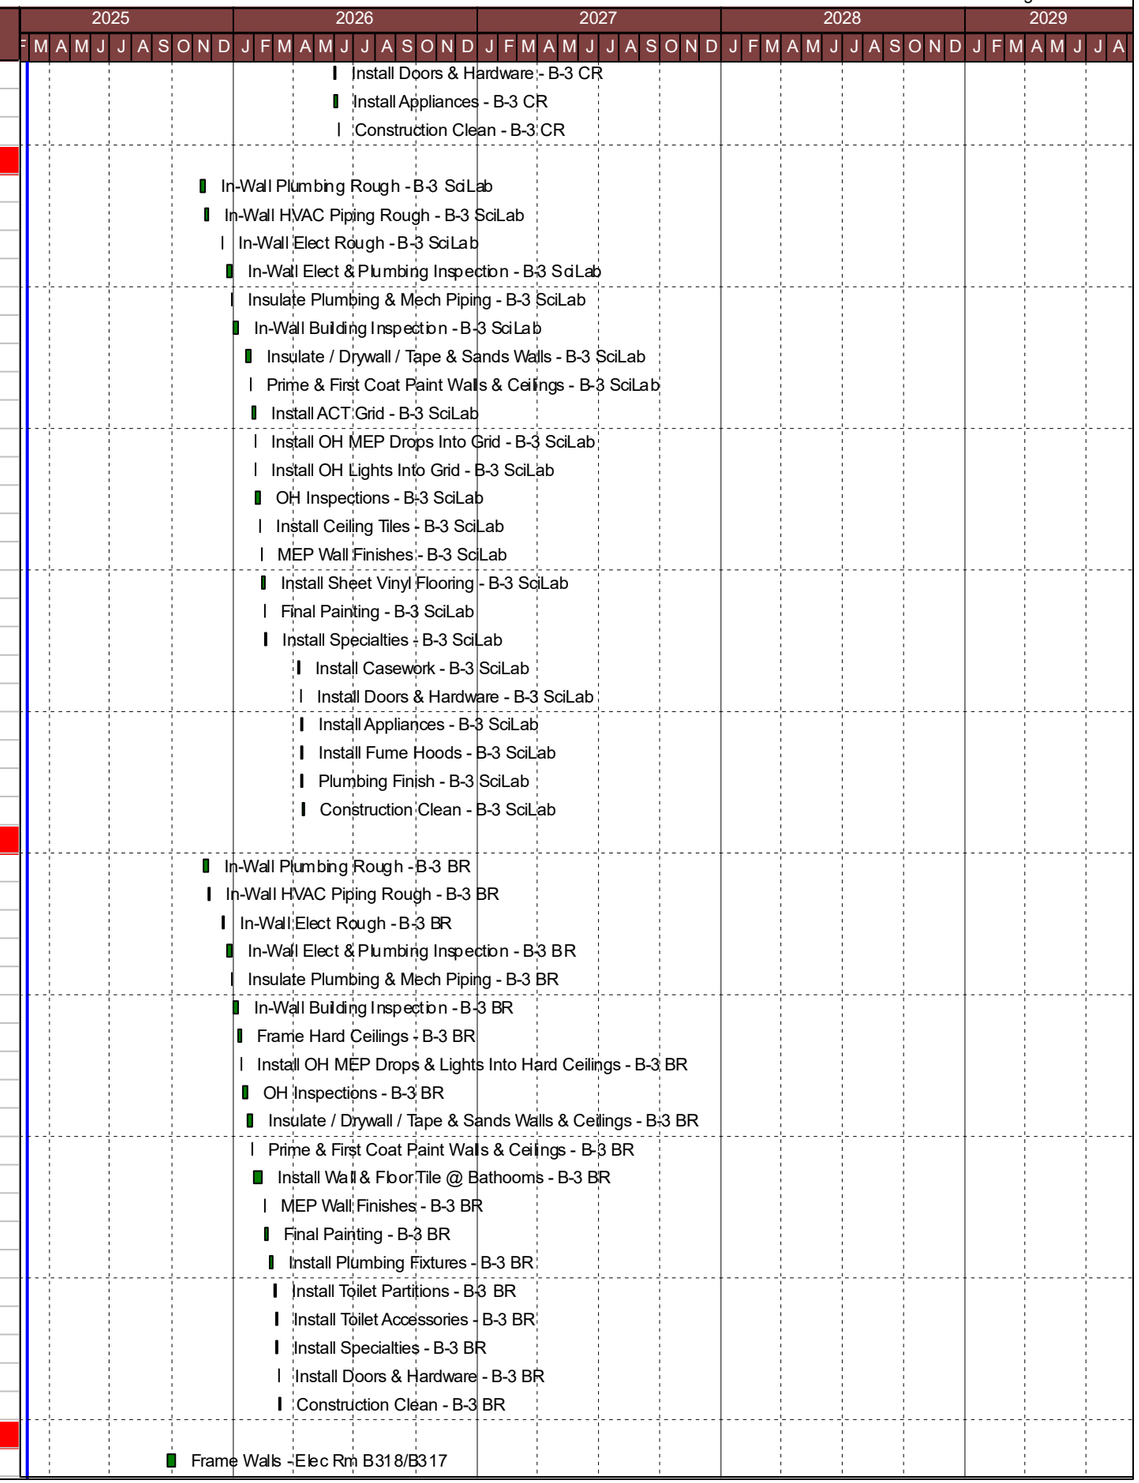

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A51240	Board / Tape / Sand Walls - Elec Rm B318/B317	5d	5d	07-Oct-25	14-Oct-25
A51250	Install Plywood on Walls - Elec Rm B318/B317	2d	2d	15-Oct-25	16-Oct-25
A51260	Paint Walls - Elec Rm B318/B317	1d	1d	17-Oct-25	17-Oct-25
A51300	FRP Equip Pads - Elec Rm B318/B317	2d	2d	20-Oct-25	21-Oct-25
A51270	Set Panel Tubs,Transformers & Interconnecting Conduits - Elec Rm B318/B317	8d	8d	22-Oct-25	31-Oct-25
A51290	Install & Fitout Low Voltage Racks - Elec Rm B318/B317	5d	5d	03-Nov-25	07-Nov-25
A51280	Install Panel Interiors & Balance of Conduits - Elec Rm B318/B317	6d	6d	10-Nov-25	18-Nov-25
2nd Floor					
A52410	Install Control - B-2	2d	2d	13-Aug-25	14-Aug-25
A23640	Layout & Install Wall Clips - B-2	10d	10d	20-Aug-25	03-Sep-25
A52430	Install Hangers - B-2	5d	5d	20-Oct-25	24-Oct-25
A52440	Patch Spray Fireproofing - B-2	3d	3d	27-Oct-25	29-Oct-25
A52450	OH Duct Rough - B-2	20d	20d	06-Nov-25	05-Dec-25
A52460	OH HVAC Piping Rough - B-2	20d	20d	06-Nov-25	05-Dec-25
A52490	OH Plumbing Rough - B-2	15d	15d	14-Nov-25	05-Dec-25
A52510	OH Sprinkler Rough - B-2	10d	10d	21-Nov-25	05-Dec-25
A52500	OH Elect / Fire Alarm Rough - B-2	15d	15d	21-Nov-25	12-Dec-25
A52480	Install Door Frames - B-2	5d	5d	01-Dec-25	05-Dec-25
A52470	Frame & Top Off Walls - B-2	10d	10d	01-Dec-25	12-Dec-25
A192370	OH AV / Telcom / Low Voltage Rough - B-2	15d	15d	15-Dec-25	06-Jan-26
A52520	Install Signage - B-2	2d	2d	20-Aug-26	21-Aug-26
A51930	Punchlist - B-2	10d	10d	26-Aug-26	09-Sep-26
A51940	Final Cleaning - B-2	2d	2d	09-Feb-27	10-Feb-27
Classrooms / Offices / Hallways					
A51720	In-Wall HVAC Piping Rough - B-2 CR	5d	5d	15-Dec-25	19-Dec-25
A51710	In-Wall Elect Rough - B-2 CR	20d	20d	15-Dec-25	13-Jan-26
A51730	In-Wall Elect Inspection - B-2 CR	10d	10d	14-Jan-26	28-Jan-26
A51740	Insulate Mech Piping - B-2 CR	5d	5d	29-Jan-26	04-Feb-26
A51750	In-Wall Building Inspection - B-2 CR	5d	5d	05-Feb-26	11-Feb-26
A51760	Insulate / Drywall / Tape & Sands Walls - B-2 CR	25d	25d	12-Feb-26	19-Mar-26
A51770	Prime & First Coat Paint Walls & Ceilings - B-2 CR	15d	15d	20-Mar-26	09-Apr-26
A54760	Install VBC-12 Ceiling - B-2 CR	10d	10d	10-Apr-26	24-Apr-26
A51780	Install ACT Grid - B-2 CR	11d	11d	10-Apr-26	27-Apr-26
A51790	Install OH MEP Drops Into Grid - B-2 CR	5d	5d	28-Apr-26	04-May-26
A51800	Install OH Lights Into Grid - B-2 CR	5d	5d	28-Apr-26	04-May-26
A51810	Install Wall Tile @ Hallways- B-2 CR	10d	10d	28-Apr-26	11-May-26
A51820	OH Inspections - B-2 CR	5d	5d	05-May-26	11-May-26
A51830	Install Ceiling Tiles - B-2 CR	6d	6d	12-May-26	19-May-26
A51860	Install Casework - B-2 CR	3d	3d	20-May-26	22-May-26
A51840	MEP Wall Finishes - B-2 CR	5d	5d	20-May-26	27-May-26
A51880	Install Carpet - B-2 CR	5d	5d	26-May-26	01-Jun-26
A51870	Install Linoleum Flooring - B-2 CR	15d	15d	26-May-26	15-Jun-26
A51850	Final Painting - B-2 CR	4d	4d	28-May-26	02-Jun-26
A51890	Install Specialties - B-2 CR	2d	2d	03-Jun-26	04-Jun-26
A54770	Install Plumbing Finishes - B-2 CR	2d	2d	03-Jun-26	04-Jun-26
A189140	Install Lockers - B-2 CR	3d	3d	03-Jun-26	05-Jun-26
A51900	Install Rubber Tile - B-2 CR	10d	10d	16-Jun-26	29-Jun-26
A51910	Install Doors & Hardware - B-2 CR	2d	2d	30-Jun-26	01-Jul-26
A54780	Install Appliances - B-2 CR	4d	4d	30-Jun-26	03-Jul-26
A51920	Construction Clean - B-2 CR	2d	2d	24-Aug-26	25-Aug-26

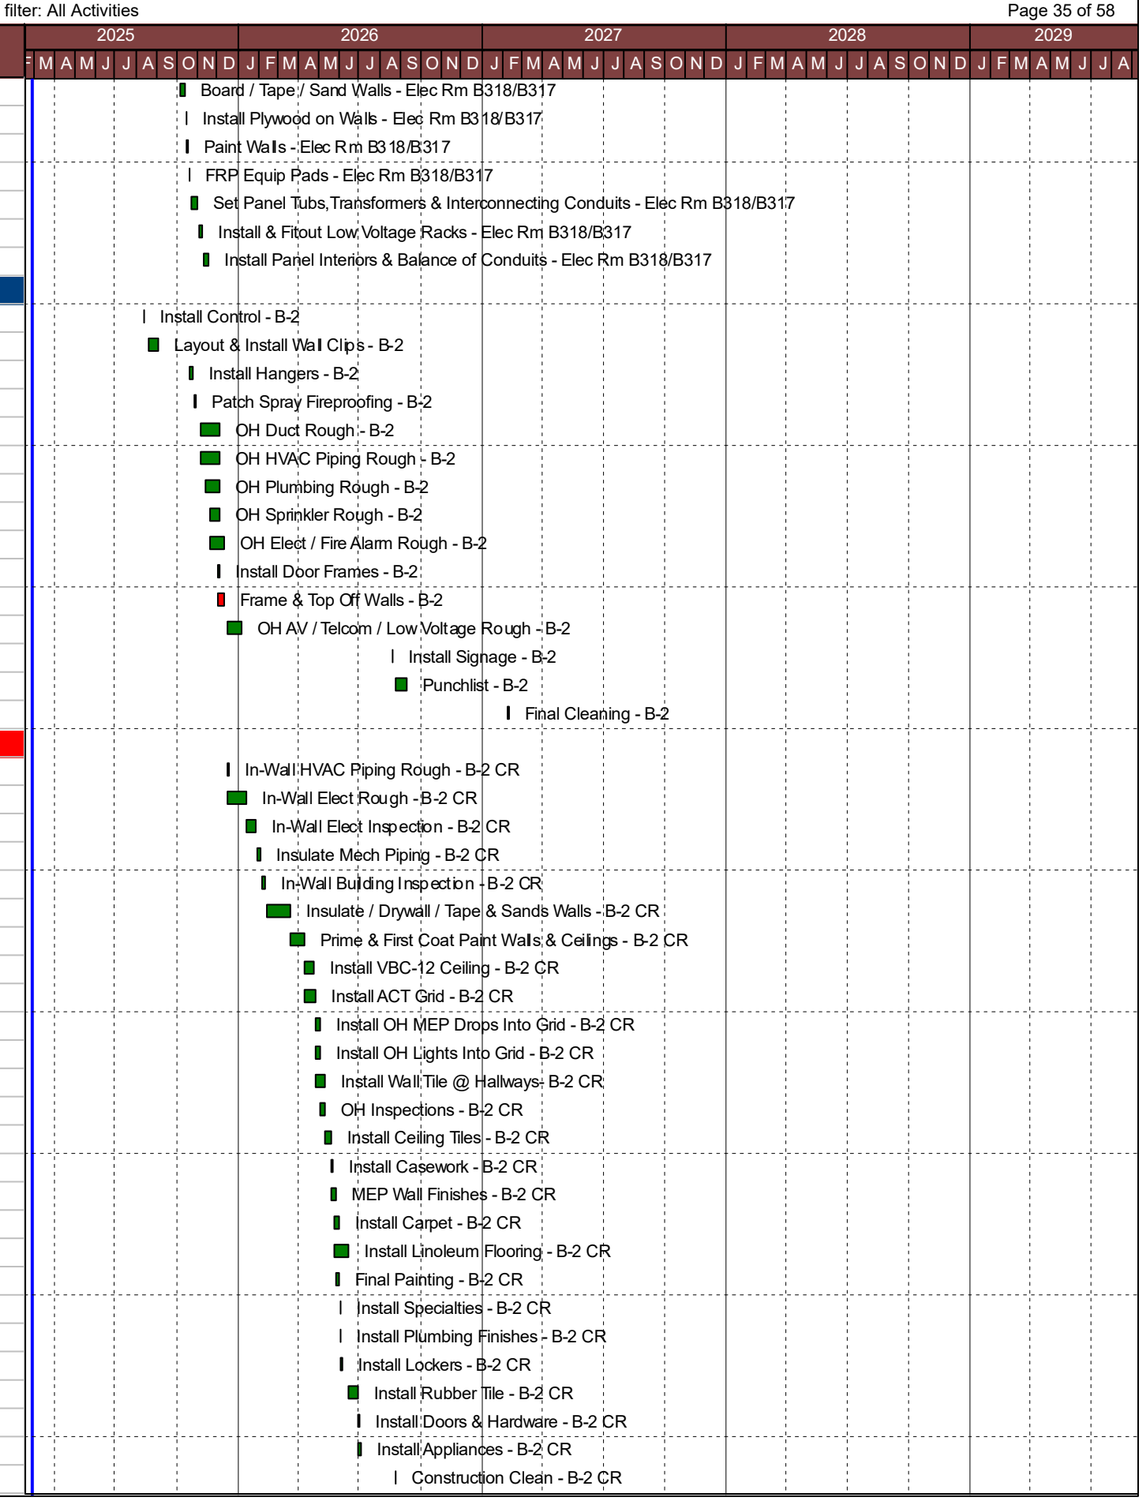

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
SCI Labs					
A51970	In-Wall Plumbing Rough - B-2 SciLab	5d	5d	15-Dec-25	19-Dec-25
A51960	In-Wall HVAC Piping Rough - B-2 SciLab	2d	2d	22-Dec-25	23-Dec-25
A51950	In-Wall Elect Rough - B-2 SciLab	2d	2d	14-Jan-26	15-Jan-26
A51980	In-Wall Elect & Plumbing Inspection - B-2 SciLab	5d	5d	22-Jan-26	28-Jan-26
A51990	Insulate Plumbing & Mech Piping - B-2 SciLab	2d	2d	29-Jan-26	30-Jan-26
A52000	In-Wall Building Inspection - B-2 SciLab	5d	5d	02-Feb-26	06-Feb-26
A52010	Insulate / Drywall / Tape & Sands Walls - B-2 SciLab	6d	6d	18-Feb-26	25-Feb-26
A52020	Prime & First Coat Paint Walls & Ceilings - B-2 SciLab	1d	1d	26-Feb-26	26-Feb-26
A52030	Install ACT Grid - B-2 SciLab	3d	3d	27-Feb-26	03-Mar-26
A52070	Install OH MEP Drops Into Grid - B-2 SciLab	1d	1d	04-Mar-26	04-Mar-26
A52080	Install OH Lights Into Grid - B-2 SciLab	1d	1d	04-Mar-26	04-Mar-26
A52090	OH Inspections - B-2 SciLab	5d	5d	05-Mar-26	11-Mar-26
A52100	Install Ceiling Tiles - B-2 SciLab	1d	1d	12-Mar-26	12-Mar-26
A52040	MEP Wall Finishes - B-2 SciLab	2d	2d	13-Mar-26	16-Mar-26
A52120	Install Sheet Vinyl Flooring - B-2 SciLab	4d	4d	13-Mar-26	18-Mar-26
A52050	Final Painting - B-2 SciLab	1d	1d	17-Mar-26	17-Mar-26
A52060	Install Specialties - B-2 SciLab	2d	2d	18-Mar-26	19-Mar-26
A52110	Install Casework - B-2 SciLab	3d	3d	13-Apr-26	15-Apr-26
A52130	Install Doors & Hardware - B-2 SciLab	1d	1d	16-Apr-26	16-Apr-26
A54070	Install Appliances - B-2 SciLab	2d	2d	16-Apr-26	17-Apr-26
A54080	Install Fume Hoods - B-2 SciLab	2d	2d	16-Apr-26	17-Apr-26
A54030	Plumbing Finish - B-2 SciLab	3d	3d	16-Apr-26	21-Apr-26
A52140	Construction Clean - B-2 SciLab	1d	1d	22-Apr-26	22-Apr-26
Bathrooms					
A52190	In-Wall Plumbing Rough - B-2 BR	5d	5d	18-Dec-25	24-Dec-25
A52180	In-Wall HVAC Piping Rough - B-2 BR	2d	2d	24-Dec-25	26-Dec-25
A52170	In-Wall Elect Rough - B-2 BR	2d	2d	16-Jan-26	20-Jan-26
A52200	In-Wall Plumbing & Elect Inspection - B-2 BR	5d	5d	22-Jan-26	28-Jan-26
A52210	Insulate Plumbing & Mech Piping - B-2 BR	2d	2d	29-Jan-26	30-Jan-26
A52220	In-Wall Building Inspection - B-2 BR	5d	5d	02-Feb-26	06-Feb-26
A52240	Frame Hard Ceilings - B-2 BR	2d	2d	09-Feb-26	10-Feb-26
A52250	Install OH MEP Drops & Lights Into Hard Ceilings - B-2 BR	2d	2d	11-Feb-26	12-Feb-26
A52260	OH Inspections - B-2 BR	5d	5d	13-Feb-26	20-Feb-26
A52280	Insulate / Drywall / Tape & Sands Walls & Ceilings - B-2 BR	5d	5d	23-Feb-26	27-Feb-26
A52290	Prime & First Coat Paint Walls & Ceilings - B-2 BR	1d	1d	02-Mar-26	02-Mar-26
A52300	Install Wall & Floor Tile @ Bathooms - B-2 BR	10d	10d	03-Mar-26	16-Mar-26
A52320	MEP Wall Finishes - B-2 BR	1d	1d	17-Mar-26	17-Mar-26
A52340	Final Painting - B-2 BR	4d	4d	18-Mar-26	23-Mar-26
A52330	Install Plumbing Fixtures - B-2 BR	3d	3d	24-Mar-26	26-Mar-26
A52350	Install Toilet Partitions - B-2 BR	3d	3d	27-Mar-26	31-Mar-26
A52370	Install Toilet Accessories - B-2 BR	2d	2d	01-Apr-26	02-Apr-26
A52360	Install Specialties - B-2 BR	2d	2d	01-Apr-26	02-Apr-26
A52310	Install Doors & Hardware - B-2 BR	1d	1d	03-Apr-26	03-Apr-26
A52380	Construction Clean - B-2 BR	2d	2d	06-Apr-26	07-Apr-26
IDF / Elec - B214/B213					
A51310	Frame Walls - Elec Rm B214/B213	9d	9d	20-Oct-25	30-Oct-25
A51320	Board / Tape / Sand Walls - Elec Rm B214/B213	5d	5d	31-Oct-25	06-Nov-25
A51330	Install Plywood on Walls - Elec Rm B214/B213	2d	2d	07-Nov-25	10-Nov-25
A51340	Paint Walls - Elec Rm B214/B213	1d	1d	12-Nov-25	12-Nov-25

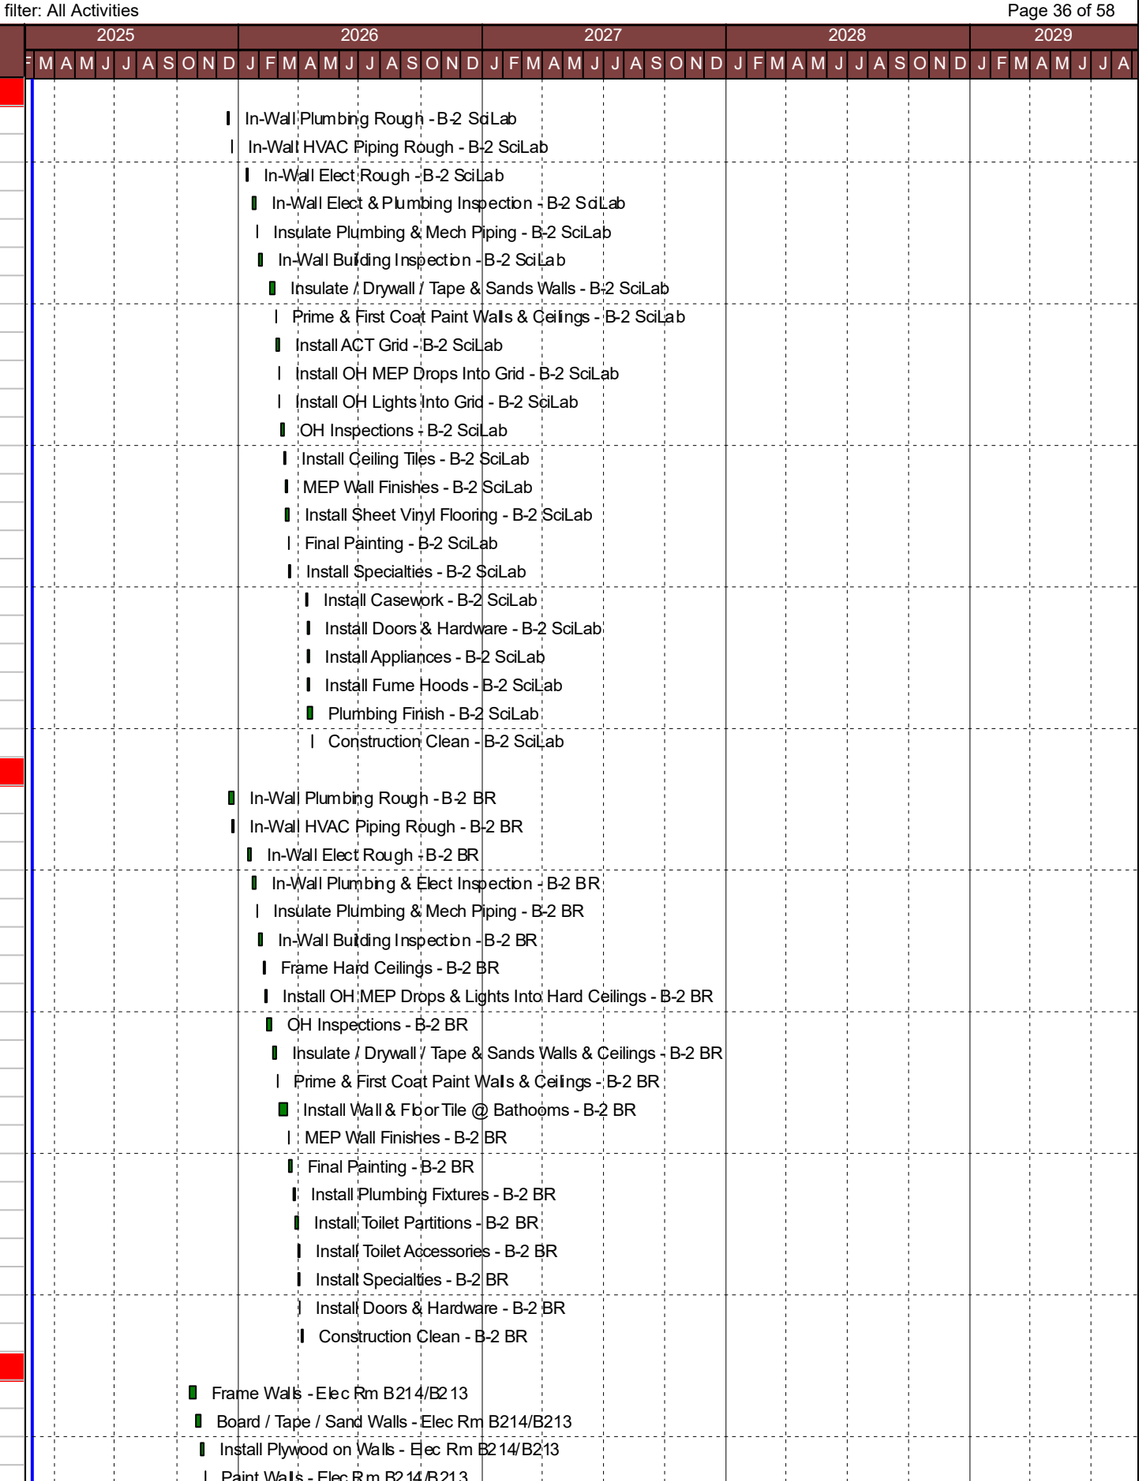

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A51350	FRP Equip Pads - Elec Rm B214/B213	2d	2d	13-Nov-25	14-Nov-25
A51360	Set Panel Tubs,Transformers & Interconnecting Conduits - Elec Rm B214/B213	8d	8d	17-Nov-25	26-Nov-25
A51370	Install & Fitout Low Voltage Racks - Elec Rm B214/B213	5d	5d	28-Nov-25	04-Dec-25
A51380	Install Panel Interiors & Balance of Conduits - Elec Rm B214/B213	6d	6d	05-Dec-25	12-Dec-25
Mezzanine					
Elec - M102					
A51630	Frame Walls - Elec Rm M102	9d	9d	20-Oct-25	30-Oct-25
A51640	Board / Tape / Sand Walls - Elec Rm M102	5d	5d	31-Oct-25	06-Nov-25
A51650	Install Plywood on Walls - Elec Rm M102	2d	2d	07-Nov-25	10-Nov-25
A51660	Paint Walls - Elec Rm M102	1d	1d	12-Nov-25	12-Nov-25
A51670	FRP Equip Pads - Elec Rm M102	2d	2d	13-Nov-25	14-Nov-25
A51680	Set Panel Tubs,Transformers & Interconnecting Conduits - Elec Rm M102	8d	8d	17-Nov-25	26-Nov-25
A51700	Install Panel Interiors & Balance of Conduits - Elec Rm M102	6d	6d	28-Nov-25	05-Dec-25
1st Floor					
A53000	Install Control - B-1	2d	2d	17-Sep-25	18-Sep-25
A52990	Layout & Install Wall Clips - B-1	10d	10d	19-Sep-25	02-Oct-25
A9110	CMU Interior Walls / Door Frames - B-1	5d	5d	24-Oct-25	30-Oct-25
A53010	Install Hangers - B-1	5d	5d	27-Oct-25	31-Oct-25
A53020	Patch Spray Fireproofing - B-1	3d	3d	03-Nov-25	05-Nov-25
A53030	OH Duct Rough - B-1	20d	20d	21-Nov-25	19-Dec-25
A53040	OH HVAC Piping Rough - B-1	20d	20d	21-Nov-25	19-Dec-25
A53070	OH Plumbing Rough - B-1	15d	15d	01-Dec-25	19-Dec-25
A53090	OH Sprinkler Rough - B-1	10d	10d	08-Dec-25	19-Dec-25
A53080	OH Elect / Fire Alarm Rough - B-1	15d	15d	08-Dec-25	29-Dec-25
A53060	Install Door Frames - B-1	5d	5d	15-Dec-25	19-Dec-25
A53050	Frame & Top Off Walls - B-1	10d	10d	15-Dec-25	29-Dec-25
A192380	OH AV / Telcom / Low Voltage Rough - B-1	15d	15d	30-Dec-25	21-Jan-26
A53100	Install Signage - B-1	2d	2d	25-Jun-26	26-Jun-26
A53330	Punchlist - B-1	10d	10d	10-Sep-26	23-Sep-26
A53340	Final Cleaning - B-1	2d	2d	11-Feb-27	12-Feb-27
Cosmetology					
A53120	In-Wall HVAC Piping Rough - B-1 Cosmo	5d	5d	30-Dec-25	06-Jan-26
A53110	In-Wall Elect Rough - B-1 Cosmo	20d	20d	30-Dec-25	28-Jan-26
A53830	In-Wall Plumbing Rough - B-1 Cosmo	20d	20d	30-Dec-25	28-Jan-26
A53850	Frame Hard Ceilings @ Bathrooms - B-1 Cosmo	2d	2d	22-Jan-26	23-Jan-26
A53870	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - B-1 Cosmo	2d	2d	26-Jan-26	27-Jan-26
A53860	Drywall / Tape & Sands Ceiling @ Bathrooms - B-1 Cosmo	4d	4d	28-Jan-26	02-Feb-26
A53130	In-Wall Elect & Plumb Inspection - B-1 Cosmo	10d	10d	29-Jan-26	11-Feb-26
A53140	Insulate Mech Piping - B-1 Cosmo	5d	5d	12-Feb-26	19-Feb-26
A53150	In-Wall Building Inspection - B-1 Cosmo	5d	5d	20-Feb-26	26-Feb-26
A53160	Insulate / Drywall / Tape & Sands Walls - B-1 Cosmo	20d	20d	27-Feb-26	26-Mar-26
A53170	Prime & First Coat Paint Walls & Ceilings - B-1 Cosmo	5d	5d	27-Mar-26	02-Apr-26
A53180	Install ACT Grid - B-1 Cosmo	3d	3d	03-Apr-26	07-Apr-26
A53200	Install OH Lights Into Grid - B-1 Cosmo	2d	2d	08-Apr-26	09-Apr-26
A53190	Install OH MEP Drops Into Grid - B-1 Cosmo	5d	5d	08-Apr-26	14-Apr-26
A53220	OH Inspections - B-1 Cosmo	5d	5d	15-Apr-26	22-Apr-26
A53230	Install Ceiling Tiles - B-1 Cosmo	6d	6d	23-Apr-26	30-Apr-26
A53240	MEP Wall Finishes - B-1 Cosmo	5d	5d	01-May-26	07-May-26
A53890	Install Storefront - B-1 Cosmo	5d	5d	01-May-26	07-May-26
A53300	Install Tile @ Bathroom - B-1 Cosmo	10d	10d	01-May-26	14-May-26

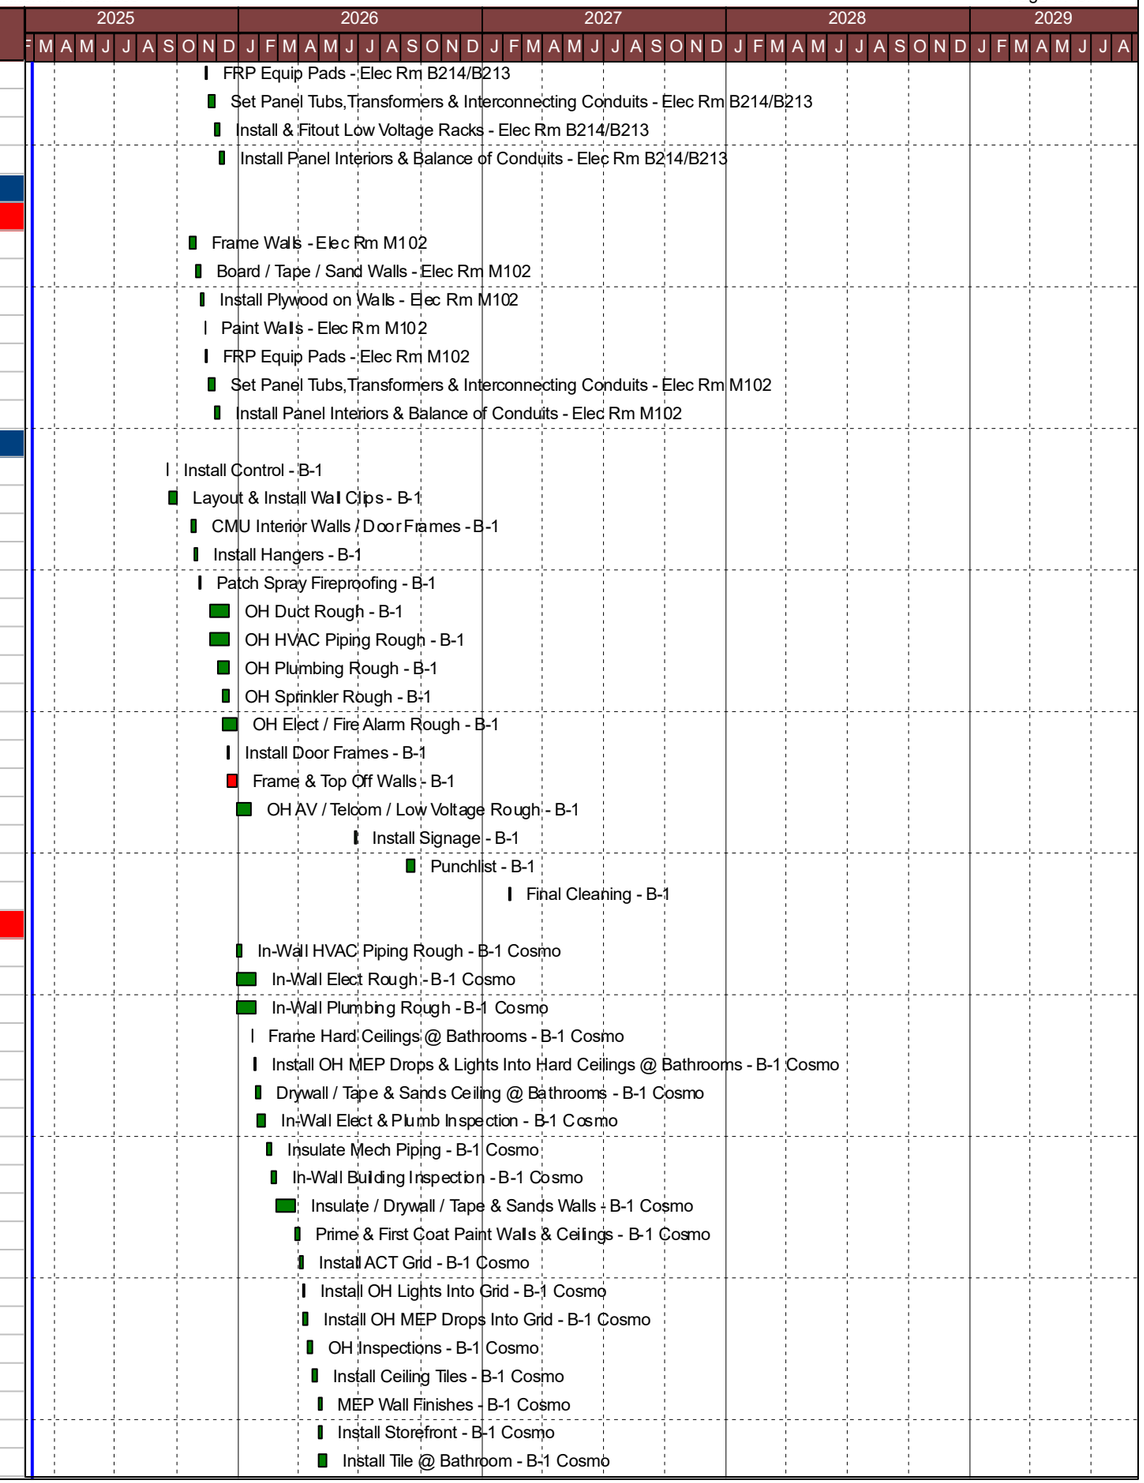

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A53270	Install Sheet Vinyl Flooring - B-1 Cosmo	10d	10d	08-May-26	21-May-26
A53250	Final Painting - B-1 Cosmo	4d	4d	22-May-26	28-May-26
A53310	Install Doors & Hardware - B-1 Cosmo	4d	4d	29-May-26	03-Jun-26
A53290	Install Specialties / Lockers - B-1 Cosmo	5d	5d	29-May-26	04-Jun-26
A53840	Install Plumbing Finish - B-1 Cosmo	10d	10d	29-May-26	11-Jun-26
A53880	Install & Connect Specialty Equipment - B-1 Cosmo	10d	10d	29-May-26	11-Jun-26
A53260	Install Casework - B-1 Cosmo	5d	5d	11-Jun-26	17-Jun-26
A53320	Construction Clean - B-1 Cosmo	2d	2d	24-Aug-26	25-Aug-26
Early Education					
A53360	In-Wall HVAC Piping Rough - B-1 Early Ed	5d	5d	05-Jan-26	09-Jan-26
A53350	In-Wall Elect Rough - B-1 Early Ed	20d	20d	05-Jan-26	02-Feb-26
A53930	Frame Hard Ceilings @ Bathrooms - B-1 Early Ed	2d	2d	22-Jan-26	23-Jan-26
A53450	Paint OH MEPs & Exposed Structure - B-1 Early Ed	2d	2d	22-Jan-26	23-Jan-26
A53940	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - B-1 Early Ed	2d	2d	26-Jan-26	27-Jan-26
A53950	Drywall / Tape & Sands Ceiling @ Bathrooms - B-1 Early Ed	4d	4d	28-Jan-26	02-Feb-26
A53370	In-Wall Elect Inspection - B-1 Early Ed	10d	10d	03-Feb-26	17-Feb-26
A53380	Insulate Mech Piping - B-1 Early Ed	5d	5d	18-Feb-26	24-Feb-26
A53390	In-Wall Building Inspection - B-1 Early Ed	5d	5d	25-Feb-26	03-Mar-26
A53400	Insulate / Drywall / Tape & Sands Walls - B-1 Early Ed	20d	20d	04-Mar-26	31-Mar-26
A53410	Prime & First Coat Paint Walls & Ceilings - B-1 Early Ed	5d	5d	01-Apr-26	07-Apr-26
A53420	Install ACT Grid - B-1 Early Ed	4d	4d	08-Apr-26	13-Apr-26
A53440	Install OH Lights Into Grid - B-1 Early Ed	2d	2d	14-Apr-26	15-Apr-26
A53430	Install OH MEP Drops Into Grid - B-1 Early Ed	5d	5d	14-Apr-26	21-Apr-26
A53960	Install Metal Panel Ceiling - B-1 Early Ed	9d	9d	14-Apr-26	27-Apr-26
A53460	OH Inspections - B-1 Early Ed	5d	5d	22-Apr-26	28-Apr-26
A53470	Install Ceiling Tiles - B-1 Early Ed	6d	6d	29-Apr-26	06-May-26
A53480	MEP Wall Finishes - B-1 Early Ed	5d	5d	07-May-26	13-May-26
A53490	Final Painting - B-1 Early Ed	4d	4d	14-May-26	19-May-26
A53530	Install Specialties - B-1 Early Ed	2d	2d	20-May-26	21-May-26
A53910	Install Plumbing Finish - B-1 Early Ed	5d	5d	20-May-26	27-May-26
A53500	Install Casework / Cubbies - B-1 Early Ed	5d	5d	29-May-26	04-Jun-26
A53510	Install Linoleum Flooring - B-1 Early Ed	4d	4d	05-Jun-26	10-Jun-26
A53540	Install Tile @ Bathroom - B-1 Early Ed	10d	10d	11-Jun-26	24-Jun-26
A53920	Install Appliances - B-1 Early Ed	2d	2d	25-Jun-26	26-Jun-26
A53550	Install Doors & Hardware - B-1 Early Ed	4d	4d	25-Jun-26	30-Jun-26
A53900	Install Specialties / Lockers - B-1 Early Ed	4d	4d	25-Jun-26	30-Jun-26
A53560	Construction Clean - B-1 Early Ed	2d	2d	24-Aug-26	25-Aug-26
Administration Office					
A53600	In-Wall HVAC Piping Rough - B-1 Admin	5d	5d	08-Jan-26	14-Jan-26
A53590	In-Wall Elect Rough - B-1 Admin	20d	20d	08-Jan-26	05-Feb-26
A53970	Frame Hard Ceilings @ Bathrooms - B-1 Admin	3d	3d	22-Jan-26	26-Jan-26
A53980	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - B-1 Admin	3d	3d	27-Jan-26	29-Jan-26
A53990	Drywall / Tape & Sands Ceiling @ Bathrooms - B-1 Admin	5d	5d	30-Jan-26	05-Feb-26
A53610	In-Wall Elect Inspection - B-1 Admin	10d	10d	06-Feb-26	20-Feb-26
A53620	Insulate Mech Piping - B-1 Admin	5d	5d	23-Feb-26	27-Feb-26
A53630	In-Wall Building Inspection - B-1 Admin	5d	5d	02-Mar-26	06-Mar-26
A53640	Insulate / Drywall / Tape & Sands Walls - B-1 Admin	20d	20d	10-Mar-26	06-Apr-26
A53650	Prime & First Coat Paint Walls & Ceilings - B-1 Admin	5d	5d	07-Apr-26	13-Apr-26
A53660	Install ACT Grid - B-1 Admin	9d	9d	14-Apr-26	27-Apr-26
A53680	Install OH Lights Into Grid - B-1 Admin	3d	3d	28-Apr-26	30-Apr-26

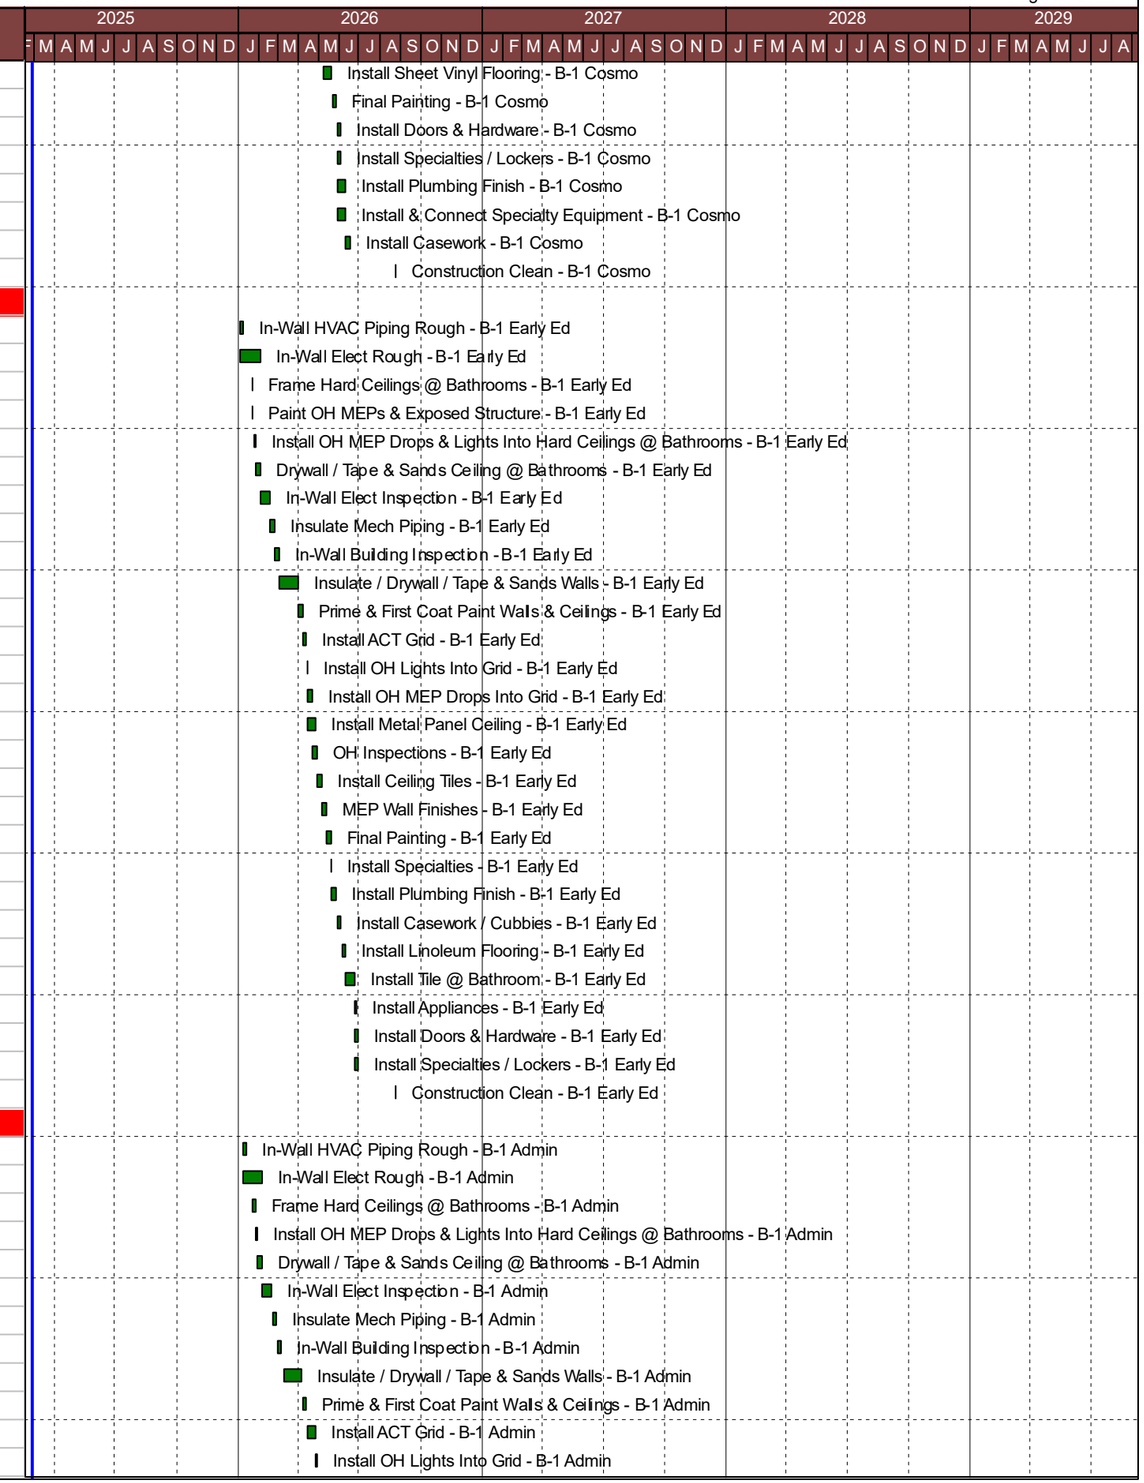

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A53670	Install OH MEP Drops Into Grid - B-1 Admin	5d	5d	28-Apr-26	04-May-26
A53690	Install Wall Tile @ Hallways- B-1 Admin	10d	10d	28-Apr-26	11-May-26
A53700	OH Inspections - B-1 Admin	5d	5d	05-May-26	11-May-26
A53710	Install Ceiling Tiles - B-1 Admin	6d	6d	12-May-26	19-May-26
A53720	MEP Wall Finishes - B-1 Admin	5d	5d	20-May-26	27-May-26
A54010	Install Tile @ Bathroom - B-1 Admin	10d	10d	20-May-26	03-Jun-26
A53730	Final Painting - B-1 Admin	4d	4d	28-May-26	02-Jun-26
A53770	Install Specialties - B-1 Admin	2d	2d	03-Jun-26	04-Jun-26
A54000	Install Plumbing Finish - B-1 Admin	5d	5d	03-Jun-26	09-Jun-26
A53740	Install Casework - B-1 Admin	4d	4d	05-Jun-26	10-Jun-26
A53760	Install Carpet - B-1 Admin	5d	5d	11-Jun-26	17-Jun-26
A53750	Install Linoleum Flooring - B-1 Admin	5d	5d	11-Jun-26	17-Jun-26
A53780	Install Rubber Tile - B-1 Admin	5d	5d	18-Jun-26	24-Jun-26
A53790	Install Doors & Hardware - B-1 Admin	6d	6d	25-Jun-26	02-Jul-26
A53800	Construction Clean - B-1 Admin	2d	2d	24-Aug-26	25-Aug-26
SCI Labs					
A52780	In-Wall HVAC Piping Rough - B-1 SciLab	2d	2d	15-Jan-26	16-Jan-26
A52790	In-Wall Plumbing Rough - B-1 SciLab	5d	5d	16-Jan-26	23-Jan-26
A52770	In-Wall Elect Rough - B-1 SciLab	2d	2d	06-Feb-26	09-Feb-26
A52800	In-Wall Elect & Plumbing Inspection - B-1 SciLab	5d	5d	10-Feb-26	17-Feb-26
A52810	Insulate Plumbing & Mech Piping - B-1 SciLab	2d	2d	18-Feb-26	19-Feb-26
A52820	In-Wall Building Inspection - B-1 SciLab	5d	5d	20-Feb-26	26-Feb-26
A52830	Insulate / Drywall / Tape & Sands Walls - B-1 SciLab	6d	6d	13-Mar-26	20-Mar-26
A52840	Prime & First Coat Paint Walls & Ceilings - B-1 SciLab	1d	1d	23-Mar-26	23-Mar-26
A52850	Install ACT Grid - B-1 SciLab	4d	4d	24-Mar-26	27-Mar-26
A52890	Install OH MEP Drops Into Grid - B-1 SciLab	1d	1d	30-Mar-26	30-Mar-26
A52900	Install OH Lights Into Grid - B-1 SciLab	1d	1d	30-Mar-26	30-Mar-26
A52910	OH Inspections - B-1 SciLab	5d	5d	31-Mar-26	06-Apr-26
A52920	Install Ceiling Tiles - B-1 SciLab	1d	1d	07-Apr-26	07-Apr-26
A52860	MEP Wall Finishes - B-1 SciLab	2d	2d	08-Apr-26	09-Apr-26
A52940	Install Sheet Vinyl Flooring - B-1 SciLab	4d	4d	08-Apr-26	13-Apr-26
A52870	Final Painting - B-1 SciLab	1d	1d	10-Apr-26	10-Apr-26
A52880	Install Specialties - B-1 SciLab	2d	2d	13-Apr-26	14-Apr-26
A52930	Install Casework - B-1 SciLab	3d	3d	26-May-26	28-May-26
A54060	Install Fume Hoods - B-1 SciLab	2d	2d	29-May-26	01-Jun-26
A54050	Install Appliances - B-1 SciLab	2d	2d	02-Jun-26	03-Jun-26
A54040	Install Plumbing Finish - B-1 SciLab	3d	3d	04-Jun-26	08-Jun-26
A52950	Install Doors & Hardware - B-1 SciLab	1d	1d	09-Jun-26	09-Jun-26
A52960	Construction Clean - B-1 SciLab	1d	1d	10-Jun-26	10-Jun-26
Bathrooms					
A52540	In-Wall HVAC Piping Rough - B-1 BR	2d	2d	20-Jan-26	21-Jan-26
A52550	In-Wall Plumbing Rough - B-1 BR	5d	5d	22-Jan-26	28-Jan-26
A52530	In-Wall Elect Rough - B-1 BR	2d	2d	10-Feb-26	11-Feb-26
A52560	In-Wall Plumbing & Elect Inspection - B-1 BR	5d	5d	12-Feb-26	19-Feb-26
A52570	Insulate Plumbing & Mech Piping - B-1 BR	2d	2d	20-Feb-26	23-Feb-26
A52580	In-Wall Building Inspection - B-1 BR	5d	5d	24-Feb-26	02-Mar-26
A52600	Frame Hard Ceilings - B-1 BR	2d	2d	03-Mar-26	04-Mar-26
A52610	Install OH MEP Drops & Lights Into Hard Ceilings - B-1 BR	2d	2d	05-Mar-26	06-Mar-26
A52620	OH Inspections - B-1 BR	5d	5d	09-Mar-26	13-Mar-26
A52640	Insulate / Drywall / Tape & Sands Walls & Ceilings - B-1 BR	5d	5d	16-Mar-26	20-Mar-26

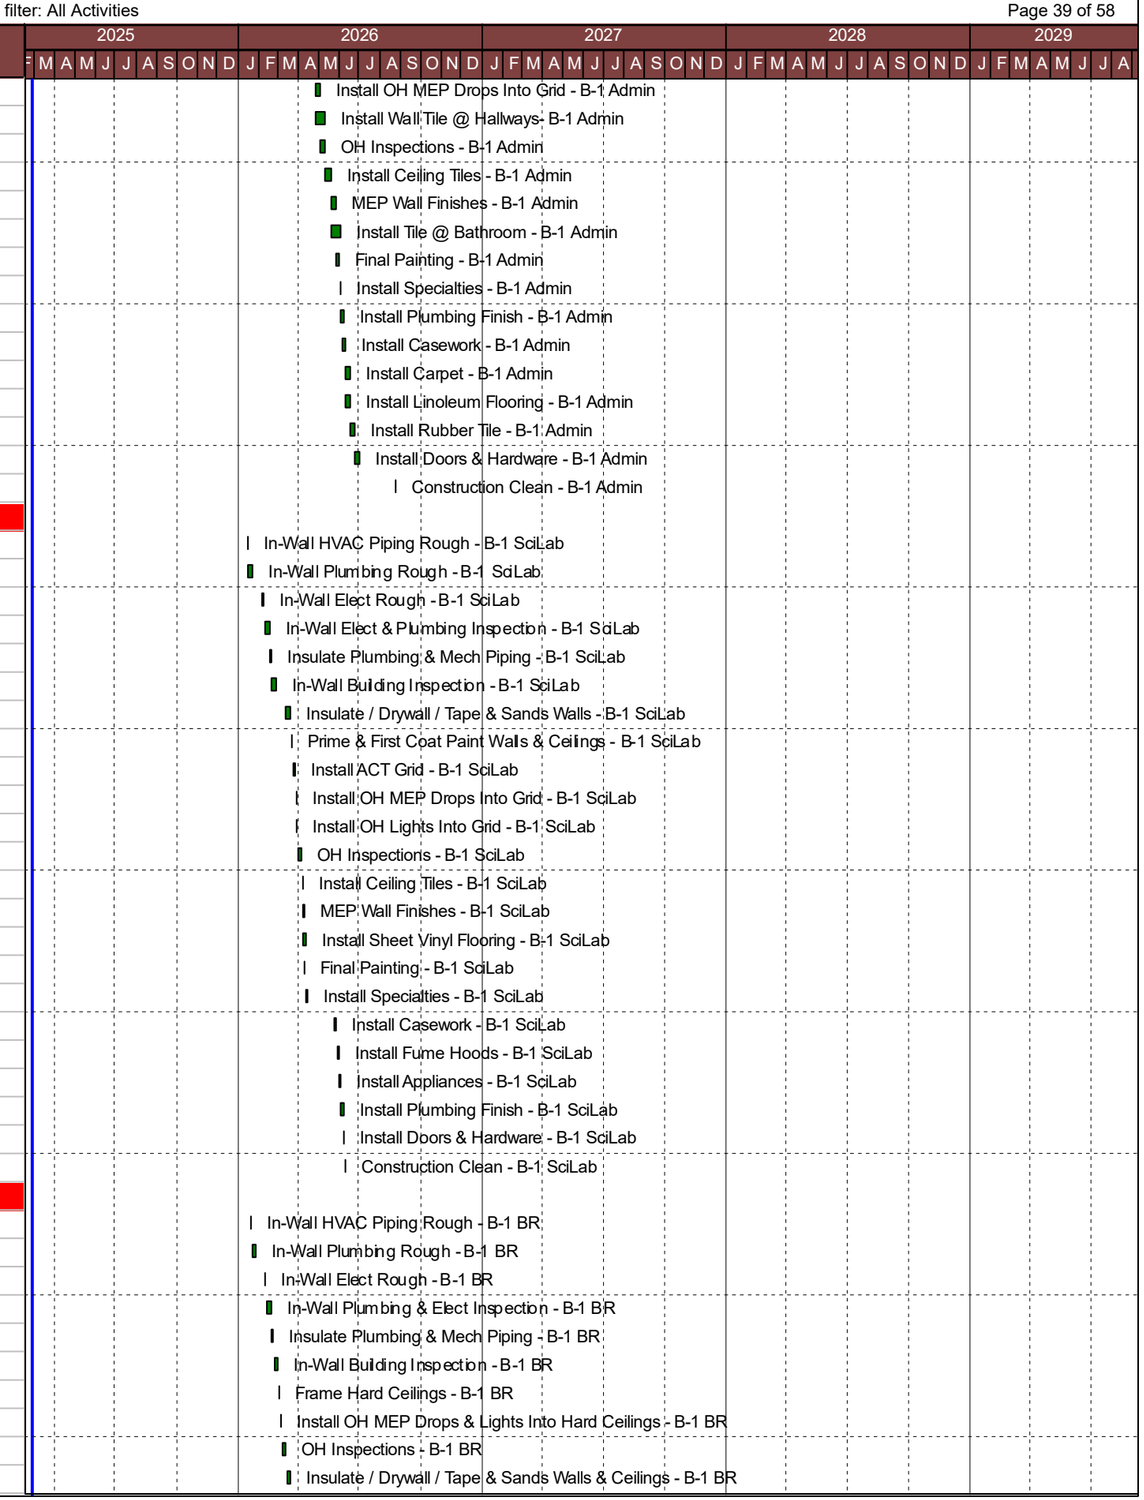

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A52650	Prime & First Coat Paint Walls & Ceilings - B-1 BR	1d	1d	23-Mar-26	23-Mar-26
A52660	Install Wall & Floor Tile @ Bathooms - B-1 BR	10d	10d	24-Mar-26	06-Apr-26
A52680	MEP Wall Finishes - B-1 BR	1d	1d	07-Apr-26	07-Apr-26
A52700	Final Painting - B-1 BR	4d	4d	08-Apr-26	13-Apr-26
A52690	Install Plumbing Fixtures - B-1 BR	3d	3d	14-Apr-26	16-Apr-26
A52710	Install Toilet Partitions - B-1 BR	3d	3d	17-Apr-26	22-Apr-26
A52730	Install Toilet Accessories - B-1 BR	2d	2d	23-Apr-26	24-Apr-26
A52720	Install Specialties - B-1 BR	2d	2d	23-Apr-26	24-Apr-26
A52670	Install Doors & Hardware - B-1 BR	1d	1d	27-Apr-26	27-Apr-26
A52740	Construction Clean - B-1 BR	2d	2d	28-Apr-26	29-Apr-26
IDF - B128					
A51390	Frame Walls - IDF B128	9d	9d	27-Oct-25	06-Nov-25
A51400	Board / Tape / Sand Walls - IDF B128	5d	5d	07-Nov-25	14-Nov-25
A51410	Install Plywood on Walls - IDF B128	2d	2d	17-Nov-25	18-Nov-25
A51420	Paint Walls - IDF B128	1d	1d	19-Nov-25	19-Nov-25
A51430	FRP Equip Pads - IDF B128	2d	2d	20-Nov-25	21-Nov-25
A51440	Set Panel Tubs,Transformers & Interconnecting Conduits - IDF B128	8d	8d	24-Nov-25	04-Dec-25
A51450	Install & Fitout Low Voltage Racks - IDF B128	5d	5d	05-Dec-25	11-Dec-25
Building C					
2nd Floor					
A54590	Install Control - C-2	2d	2d	11-Sep-25	12-Sep-25
A54600	Layout & Install Wall Clips - C-2	10d	10d	15-Sep-25	26-Sep-25
A54620	Install Hangers - C-2	10d	10d	04-Nov-25	18-Nov-25
A54630	Patch Spray Fireproofing - C-2	3d	3d	19-Nov-25	21-Nov-25
A54640	OH Duct Rough - C-2	20d	20d	08-Dec-25	06-Jan-26
A54650	OH HVAC Piping Rough - C-2	20d	20d	08-Dec-25	06-Jan-26
A54680	OH Plumbing Rough - C-2	15d	15d	15-Dec-25	06-Jan-26
A54700	OH Sprinkler Rough - C-2	10d	10d	22-Dec-25	06-Jan-26
A54690	OH Elect / Fire Alarm Rough - C-2	15d	15d	22-Dec-25	13-Jan-26
A54670	Install Door Frames - C-2	5d	5d	30-Dec-25	06-Jan-26
A54660	Frame & Top Off Walls - C-2	10d	10d	30-Dec-25	13-Jan-26
A192390	OH AV / Telcom / Low Voltage Rough - C-2	15d	15d	14-Jan-26	04-Feb-26
A54710	Install Signage - C-2	2d	2d	30-Jun-26	01-Jul-26
A55090	Punchlist - C-2	10d	10d	24-Sep-26	07-Oct-26
A55100	Final Cleaning - C-2	2d	2d	16-Feb-27	17-Feb-27
Dental					
A54840	In-Wall Plumbing Rough - C-2 Dental	20d	20d	07-Jan-26	04-Feb-26
A54830	In-Wall HVAC Piping Rough - C-2 Dental	5d	5d	14-Jan-26	21-Jan-26
A54850	Frame Hard Ceilings @ Bathrooms - C-2 Dental	2d	2d	05-Feb-26	06-Feb-26
A54820	In-Wall Elect Rough - C-2 Dental	20d	20d	05-Feb-26	05-Mar-26
A54860	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - C-2 Dental	2d	2d	09-Feb-26	10-Feb-26
A54870	Drywall / Tape & Sands Ceiling @ Bathrooms - C-2 Dental	4d	4d	11-Feb-26	17-Feb-26
A54880	In-Wall Elect & Plumb Inspection - C-2 Dental	10d	10d	06-Mar-26	19-Mar-26
A54890	Insulate Mech Piping - C-2 Dental	5d	5d	20-Mar-26	26-Mar-26
A54900	In-Wall Building Inspection - C-2 Dental	5d	5d	27-Mar-26	02-Apr-26
A54910	Insulate / Drywall / Tape & Sands Walls - C-2 Dental	10d	10d	03-Apr-26	16-Apr-26
A54920	Prime & First Coat Paint Walls & Ceilings - C-2 Dental	6d	6d	17-Apr-26	27-Apr-26
A54930	Install ACT Grid - C-2 Dental	5d	5d	28-Apr-26	04-May-26
A54960	Install OH Lights Into Grid - C-2 Dental	2d	2d	05-May-26	06-May-26
A54950	Install OH MEP Drops Into Grid - C-2 Dental	5d	5d	05-May-26	11-May-26

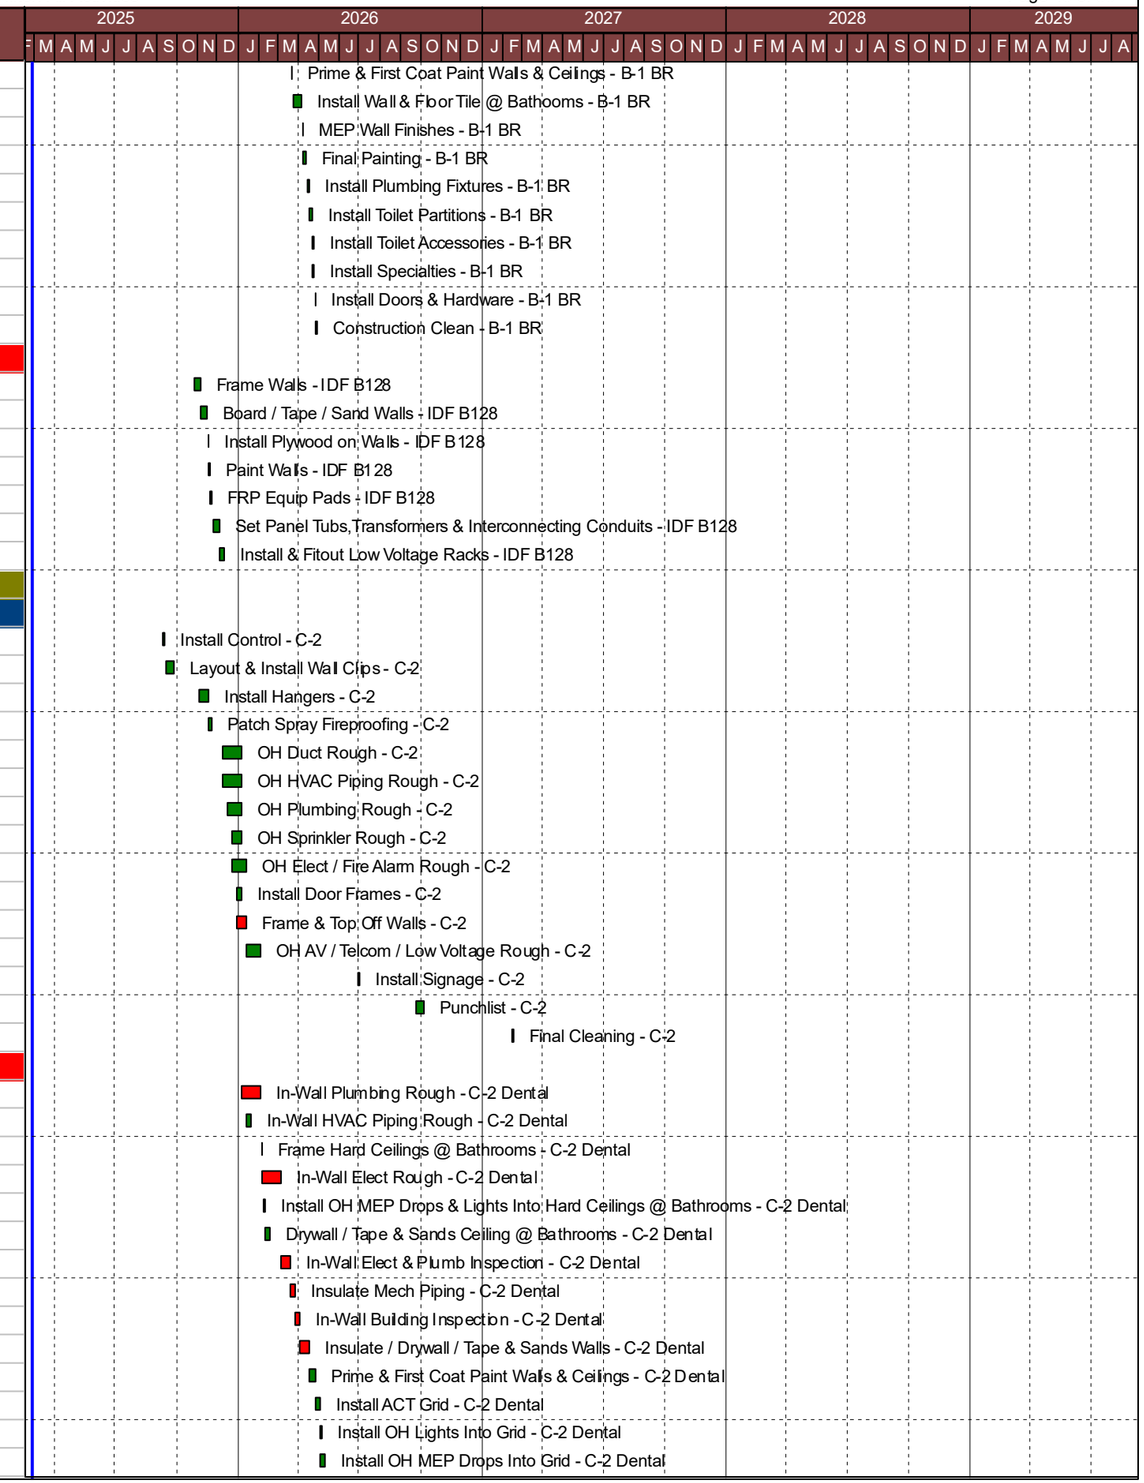

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A54970	OH Inspections - C-2 Dental	5d	5d	12-May-26	18-May-26
A54980	Install Ceiling Tiles - C-2 Dental	6d	6d	19-May-26	27-May-26
A54990	Install Tile @ Bathroom - C-2 Dental	5d	5d	28-May-26	03-Jun-26
A55010	Install Storefront - C-2 Dental	5d	5d	28-May-26	03-Jun-26
A54940	MEP Wall Finishes - C-2 Dental	5d	5d	04-Jun-26	10-Jun-26
A55020	Install Sheet Vinyl Flooring - C-2 Dental	7d	7d	04-Jun-26	12-Jun-26
A55030	Final Painting - C-2 Dental	4d	4d	15-Jun-26	18-Jun-26
A55000	Install Casework - C-2 Dental	5d	5d	18-Jun-26	24-Jun-26
A55040	Install Doors & Hardware - C-2 Dental	4d	4d	19-Jun-26	24-Jun-26
A55050	Install Specialties - C-2 Dental	5d	5d	19-Jun-26	25-Jun-26
A55070	Install & Connect Dental Equipment - C-2 Dental	10d	10d	19-Jun-26	02-Jul-26
A55060	Install Plumbing Finish - C-2 Dental	10d	10d	25-Jun-26	08-Jul-26
A55080	Construction Clean - C-2 Dental	2d	2d	24-Aug-26	25-Aug-26
Health Careers					
A55130	In-Wall Plumbing Rough - C-2 Health	20d	20d	14-Jan-26	11-Feb-26
A55120	In-Wall HVAC Piping Rough - C-2 Health	5d	5d	20-Jan-26	26-Jan-26
A55140	Frame Hard Ceilings @ Bathrooms - C-2 Health	2d	2d	05-Feb-26	06-Feb-26
A55150	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - C-2 Health	2d	2d	09-Feb-26	10-Feb-26
A55110	In-Wall Elect Rough - C-2 Health	20d	20d	10-Feb-26	10-Mar-26
A55160	Drywall / Tape & Sands Ceiling @ Bathrooms - C-2 Health	4d	4d	11-Feb-26	17-Feb-26
A55170	In-Wall Elect & Plumb Inspection - C-2 Health	10d	10d	11-Mar-26	24-Mar-26
A55180	Insulate Mech Piping - C-2 Health	5d	5d	25-Mar-26	31-Mar-26
A55190	In-Wall Building Inspection - C-2 Health	5d	5d	01-Apr-26	07-Apr-26
A55200	Insulate / Drywall / Tape & Sands Walls - C-2 Health	20d	20d	08-Apr-26	06-May-26
A55380	Install Blocking / Supports for Curtain Track - C-2 Health	2d	2d	17-Apr-26	21-Apr-26
A55210	Prime & First Coat Paint Walls & Ceilings - C-2 Health	6d	6d	07-May-26	14-May-26
A55220	Install ACT Grid - C-2 Health	5d	5d	15-May-26	21-May-26
A55250	Install OH Lights Into Grid - C-2 Health	2d	2d	22-May-26	26-May-26
A55700	Install Curtain Track - C-2 Health	2d	2d	22-May-26	26-May-26
A55240	Install OH MEP Drops Into Grid - C-2 Health	5d	5d	22-May-26	29-May-26
A55260	OH Inspections - C-2 Health	5d	5d	01-Jun-26	05-Jun-26
A55270	Install Ceiling Tiles - C-2 Health	6d	6d	08-Jun-26	15-Jun-26
A55280	Install Tile @ Bathroom - C-2 Health	5d	5d	16-Jun-26	22-Jun-26
A55300	Install Storefront - C-2 Health	5d	5d	16-Jun-26	22-Jun-26
A55230	MEP Wall Finishes - C-2 Health	5d	5d	23-Jun-26	29-Jun-26
A55290	Install Casework - C-2 Health	5d	5d	25-Jun-26	01-Jul-26
A55310	Install Sheet Vinyl - C-2 Health	7d	7d	30-Jun-26	08-Jul-26
A189340	Install Linoleum - C-2 Health	1d	1d	09-Jul-26	09-Jul-26
A55320	Final Painting - C-2 Health	4d	4d	10-Jul-26	15-Jul-26
A55340	Install Specialties - C-2 Health	5d	5d	16-Jul-26	22-Jul-26
A55350	Install Plumbing Finish - C-2 Health	10d	10d	16-Jul-26	29-Jul-26
A55360	Install & Connect Specialty Equipment - C-2 Health	10d	10d	16-Jul-26	29-Jul-26
A55330	Install Doors & Hardware - C-2 Health	4d	4d	23-Jul-26	28-Jul-26
A55370	Construction Clean - C-2 Health	2d	2d	24-Aug-26	25-Aug-26
Medical Assisting					
A55420	In-Wall Plumbing Rough - C-2 Med Assist	20d	20d	20-Jan-26	17-Feb-26
A55410	In-Wall HVAC Piping Rough - C-2 Med Assist	5d	5d	23-Jan-26	29-Jan-26
A55430	Frame Hard Ceilings @ Bathrooms - C-2 Med Assist	2d	2d	05-Feb-26	06-Feb-26
A55440	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - C-2 Med Assist	2d	2d	09-Feb-26	10-Feb-26
A55450	Drywall / Tape & Sands Ceiling @ Bathrooms - C-2 Med Assist	4d	4d	11-Feb-26	17-Feb-26

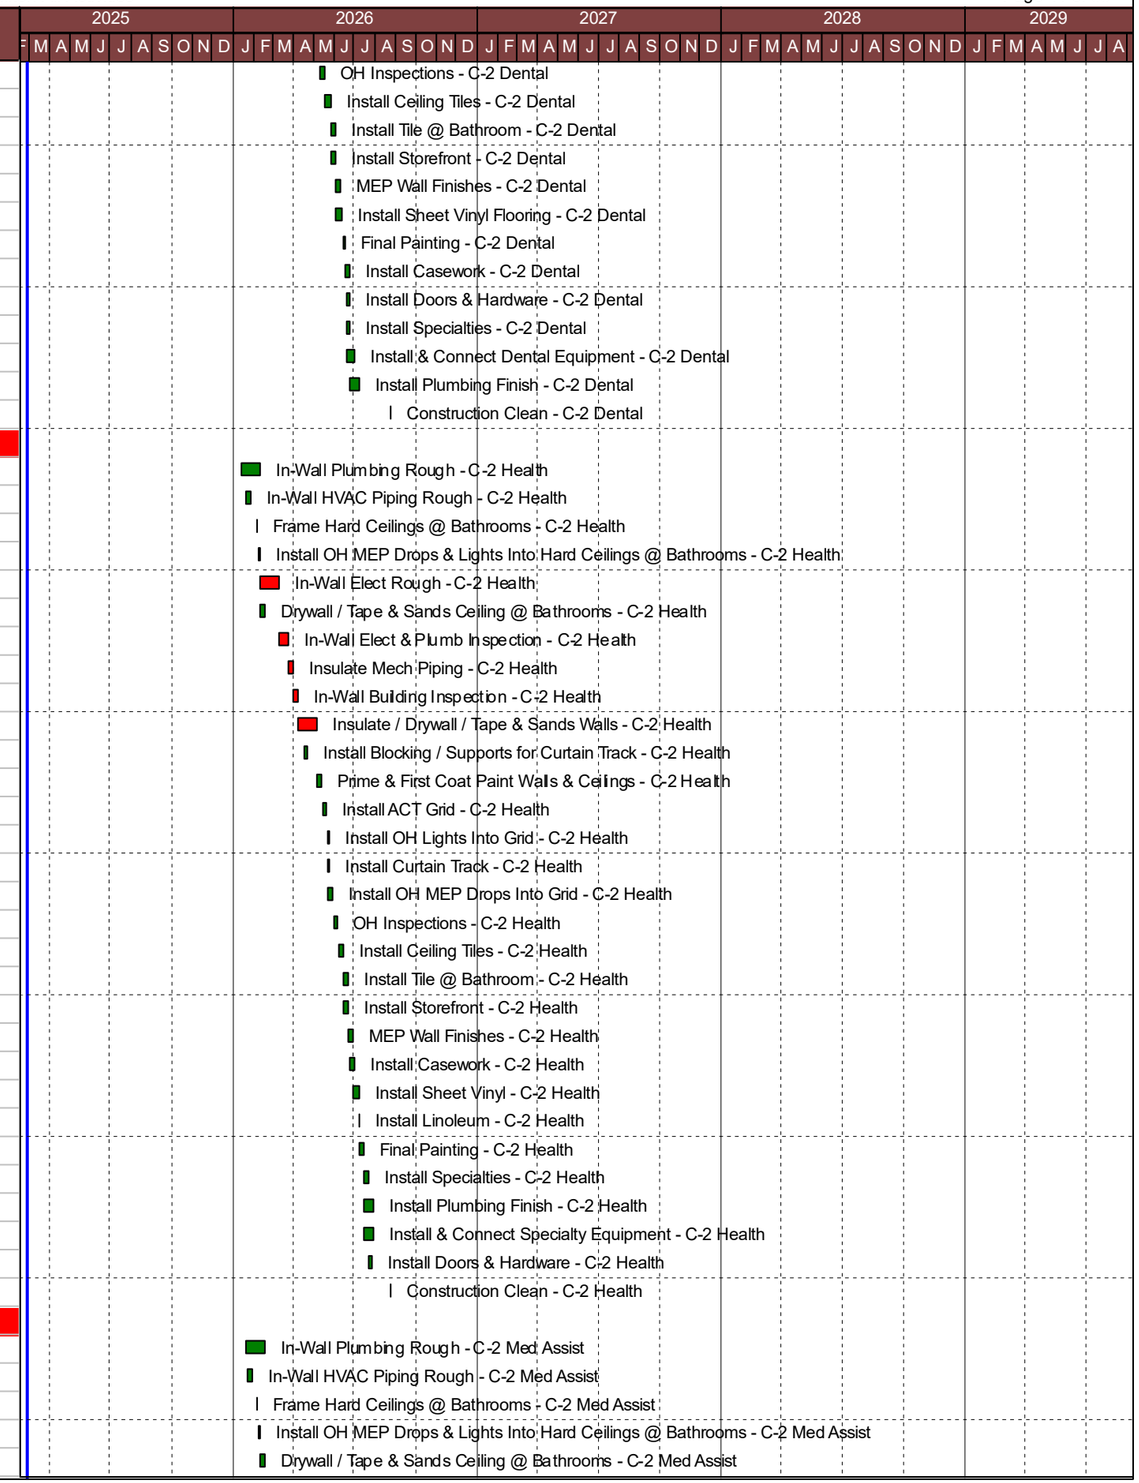

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A55400	In-Wall Elect Rough - C-2 Med Assist	20d	20d	13-Feb-26	13-Mar-26
A55460	In-Wall Elect & Plumb Inspection - C-2 Med Assist	10d	10d	16-Mar-26	27-Mar-26
A55470	Insulate Mech Piping - C-2 Med Assist	5d	5d	30-Mar-26	03-Apr-26
A55480	In-Wall Building Inspection - C-2 Med Assist	5d	5d	06-Apr-26	10-Apr-26
A55490	Insulate / Drywall / Tape & Sands Walls - C-2 Med Assist	20d	20d	13-Apr-26	11-May-26
A55500	Prime & First Coat Paint Walls & Ceilings - C-2 Med Assist	6d	6d	12-May-26	19-May-26
A189150	Install Blocking / Supports for Curtain Track - C-2 Med Assist	2d	2d	20-May-26	21-May-26
A55510	Install ACT Grid - C-2 Med Assist	5d	5d	22-May-26	29-May-26
A55540	Install OH Lights Into Grid - C-2 Med Assist	2d	2d	01-Jun-26	02-Jun-26
A189160	Install Curtain Track - C-2 Med Assist	2d	2d	01-Jun-26	02-Jun-26
A55530	Install OH MEP Drops Into Grid - C-2 Med Assist	5d	5d	01-Jun-26	05-Jun-26
A55550	OH Inspections - C-2 Med Assist	5d	5d	08-Jun-26	12-Jun-26
A55560	Install Ceiling Tiles - C-2 Med Assist	6d	6d	15-Jun-26	22-Jun-26
A55570	Install Tile @ Bathroom - C-2 Med Assist	5d	5d	23-Jun-26	29-Jun-26
A55520	MEP Wall Finishes - C-2 Med Assist	5d	5d	30-Jun-26	06-Jul-26
A55580	Install Casework - C-2 Med Assist	5d	5d	02-Jul-26	08-Jul-26
A55600	Install Sheet Vinyl Flooring - C-2 Med Assist	7d	7d	07-Jul-26	15-Jul-26
A55610	Final Painting - C-2 Med Assist	4d	4d	16-Jul-26	21-Jul-26
A55620	Install Doors & Hardware - C-2 Med Assist	4d	4d	22-Jul-26	27-Jul-26
A55630	Install Specialties - C-2 Med Assist	5d	5d	22-Jul-26	28-Jul-26
A55640	Install Plumbing Finish - C-2 Med Assist	10d	10d	22-Jul-26	04-Aug-26
A55650	Install & Connect Specialty Equipment - C-2 Med Assist	10d	10d	22-Jul-26	04-Aug-26
A55660	Construction Clean - C-2 Med Assist	2d	2d	24-Aug-26	25-Aug-26
Classrooms / Offices / Hallways					
A54120	In-Wall HVAC Piping Rough - C-2 CR	5d	5d	30-Jan-26	05-Feb-26
A54110	In-Wall Elect Rough - C-2 CR	20d	20d	19-Feb-26	18-Mar-26
A54130	In-Wall Elect Inspection - C-2 CR	10d	10d	19-Mar-26	01-Apr-26
A54140	Insulate Mech Piping - C-2 CR	5d	5d	02-Apr-26	08-Apr-26
A54150	In-Wall Building Inspection - C-2 CR	5d	5d	09-Apr-26	15-Apr-26
A54160	Insulate / Drywall / Tape & Sands Walls - C-2 CR	20d	20d	16-Apr-26	14-May-26
A54170	Prime & First Coat Paint Walls, Ceilings & Exposed MEPs - C-2 CR	6d	6d	15-May-26	22-May-26
A54210	Install Wall Tile @ Hallways- C-2 CR	10d	10d	26-May-26	08-Jun-26
A54180	Install ACT Grid - C-2 CR	8d	8d	09-Jun-26	18-Jun-26
A54190	Install OH MEP Drops Into Grid - C-2 CR	5d	5d	19-Jun-26	25-Jun-26
A54200	Install OH Lights Into Grid - C-2 CR	5d	5d	19-Jun-26	25-Jun-26
A54720	Install VBC-12 Ceiling - C-2 CR	10d	10d	19-Jun-26	02-Jul-26
A54220	OH Inspections - C-2 CR	5d	5d	26-Jun-26	02-Jul-26
A54230	Install Ceiling Tiles - C-2 CR	6d	6d	03-Jul-26	10-Jul-26
A54260	Install Casework - C-2 CR	3d	3d	13-Jul-26	15-Jul-26
A54240	MEP Wall Finishes - C-2 CR	5d	5d	13-Jul-26	17-Jul-26
A54270	Install Linoleum Flooring - C-2 CR	10d	10d	20-Jul-26	31-Jul-26
A189350	Install Rubber Tile Flooring - C-2 CR	5d	5d	03-Aug-26	07-Aug-26
A54280	Install Carpet - C-2 CR	2d	2d	10-Aug-26	11-Aug-26
A54250	Final Painting - C-2 CR	4d	4d	10-Aug-26	13-Aug-26
A54310	Install Doors & Hardware - C-2 CR	2d	2d	14-Aug-26	17-Aug-26
A54290	Install Specialties - C-2 CR	2d	2d	14-Aug-26	17-Aug-26
A54740	Install Plumbing Finishes - C-2 CR	2d	2d	14-Aug-26	17-Aug-26
A54750	Install Appliances - C-2 CR	4d	4d	14-Aug-26	19-Aug-26
A54730	Install Wall Graphics - C-2 CR	4d	4d	20-Aug-26	25-Aug-26
A54320	Construction Clean - C-2 CR	2d	2d	26-Aug-26	27-Aug-26

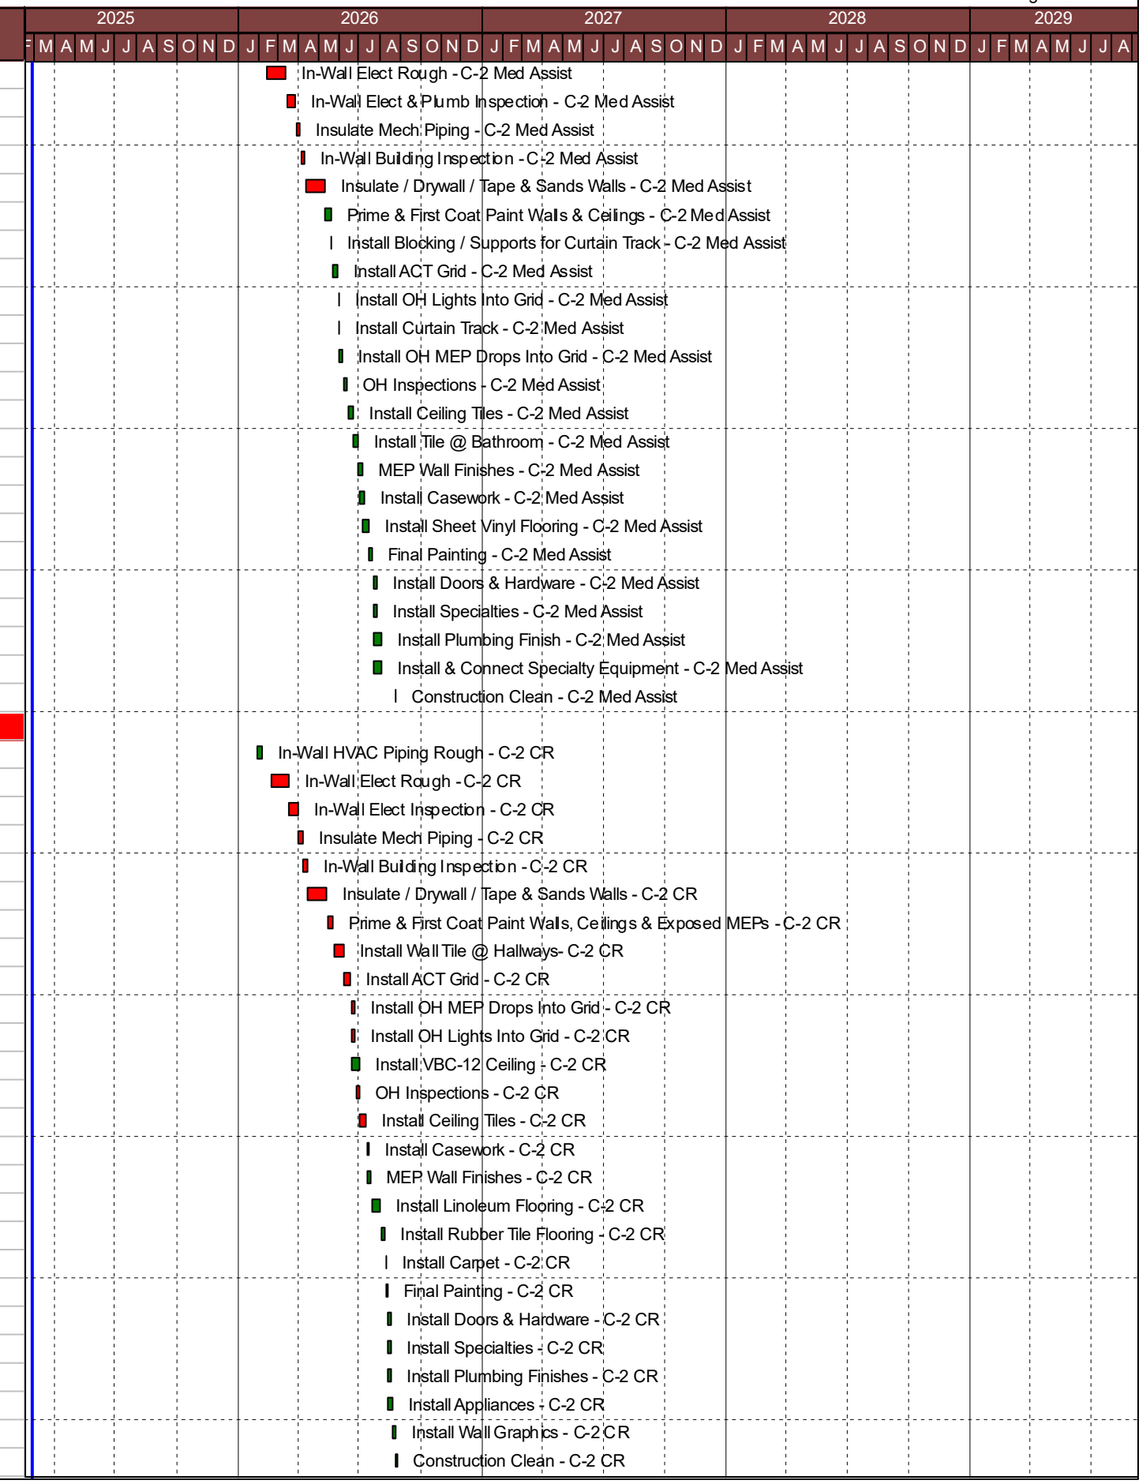

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
Bathrooms					
A54360	In-Wall HVAC Piping Rough - C-2 BR	2d	2d	06-Feb-26	09-Feb-26
A54370	In-Wall Plumbing Rough - C-2 BR	5d	5d	10-Feb-26	17-Feb-26
A54510	Frame Hard Ceilings - C-2 BR	2d	2d	20-Feb-26	23-Feb-26
A54520	Install OH MEP Drops & Lights Into Hard Ceilings - C-2 BR	2d	2d	24-Feb-26	25-Feb-26
A54480	OH Inspections - C-2 BR	5d	5d	26-Feb-26	04-Mar-26
A54350	In-Wall Elect Rough - C-2 BR	2d	2d	19-Mar-26	20-Mar-26
A54390	In-Wall Plumbing & Elect Inspection - C-2 BR	5d	5d	26-Mar-26	01-Apr-26
A54400	Insulate Plumbing & Mech Piping - C-2 BR	2d	2d	02-Apr-26	03-Apr-26
A54380	In-Wall Building Inspection - C-2 BR	5d	5d	06-Apr-26	10-Apr-26
A54410	Insulate / Drywall / Tape & Sands Walls & Ceilings - C-2 BR	5d	5d	13-Apr-26	17-Apr-26
A54420	Prime & First Coat Paint Walls & Ceilings - C-2 BR	1d	1d	21-Apr-26	21-Apr-26
A54500	Install Wall & Floor Tile @ Bathooms - C-2 BR	10d	10d	22-Apr-26	05-May-26
A54540	MEP Wall Finishes - C-2 BR	1d	1d	06-May-26	06-May-26
A54430	Final Painting - C-2 BR	2d	2d	07-May-26	08-May-26
A54550	Install Plumbing Fixtures - C-2 BR	3d	3d	11-May-26	13-May-26
A54560	Install Toilet Partitions - C-2 BR	3d	3d	14-May-26	18-May-26
A54570	Install Toilet Accessories - C-2 BR	2d	2d	19-May-26	20-May-26
A54580	Install Specialties - C-2 BR	2d	2d	19-May-26	20-May-26
A54440	Install Doors & Hardware - C-2 BR	1d	1d	21-May-26	21-May-26
A54470	Construction Clean - C-2 BR	2d	2d	02-Jul-26	03-Jul-26
IDF / Elect - C215/C216					
A51470	Frame Walls - Elec Rm C215/C216	9d	9d	04-Nov-25	17-Nov-25
A51480	Board / Tape / Sand Walls - Elec Rm C215/C216	5d	5d	18-Nov-25	24-Nov-25
A51490	Install Plywood on Walls - Elec Rm C215/C216	2d	2d	25-Nov-25	26-Nov-25
A51500	Paint Walls - Elec Rm C215/C216	1d	1d	28-Nov-25	28-Nov-25
A51510	FRP Equip Pads - Elec Rm C215/C216	2d	2d	01-Dec-25	02-Dec-25
A51520	Set Panel Tubs,Transformers & Interconnecting Conduits - Elec Rm C215/C216	8d	8d	03-Dec-25	12-Dec-25
A51530	Install & Fitout Low Voltage Racks - Elec Rm C215/C216	5d	5d	15-Dec-25	19-Dec-25
A51540	Install Panel Interiors & Balance of Conduits - Elec Rm C215/C216	6d	6d	22-Dec-25	30-Dec-25
1st Floor					
A55710	Install Control - C-1	2d	2d	07-Oct-25	08-Oct-25
A55720	Layout & Install Wall Clips - C-1	10d	10d	09-Oct-25	23-Oct-25
A9120	CMU Interior Walls / Door Frames - C-1	20d	20d	31-Oct-25	01-Dec-25
A6010	In-Wall MEP Rough - C-1	20d	20d	31-Oct-25	01-Dec-25
A55730	Install Hangers - C-1	5d	5d	13-Nov-25	19-Nov-25
A55740	Patch Spray Fireproofing - C-1	3d	3d	20-Nov-25	24-Nov-25
A55750	OH Duct Rough - C-1	20d	20d	22-Dec-25	21-Jan-26
A55760	OH HVAC Piping Rough - C-1	20d	20d	22-Dec-25	21-Jan-26
A55770	OH Plumbing Rough - C-1	15d	15d	30-Dec-25	21-Jan-26
A55810	OH Sprinkler Rough - C-1	10d	10d	07-Jan-26	21-Jan-26
A55800	OH Elect / Fire Alarm Rough - C-1	15d	15d	07-Jan-26	28-Jan-26
A55790	Install Door Frames - C-1	5d	5d	14-Jan-26	21-Jan-26
A55780	Frame & Top Off Walls - C-1	10d	10d	14-Jan-26	28-Jan-26
A192400	OH AV / Telcom / Low Voltage Rough - C-1	15d	15d	29-Jan-26	19-Feb-26
A55820	Install Signage - C-1	2d	2d	30-Jun-26	01-Jul-26
A6180	Punchlist - C-1	10d	10d	08-Oct-26	22-Oct-26
A56330	Final Cleaning - C-1	2d	2d	18-Feb-27	19-Feb-27
Plumbing Shop					
A6070	Install Sound Ceiling [Mezz] - C-1 - Plumbing Shop	10d	10d	20-Nov-25	04-Dec-25

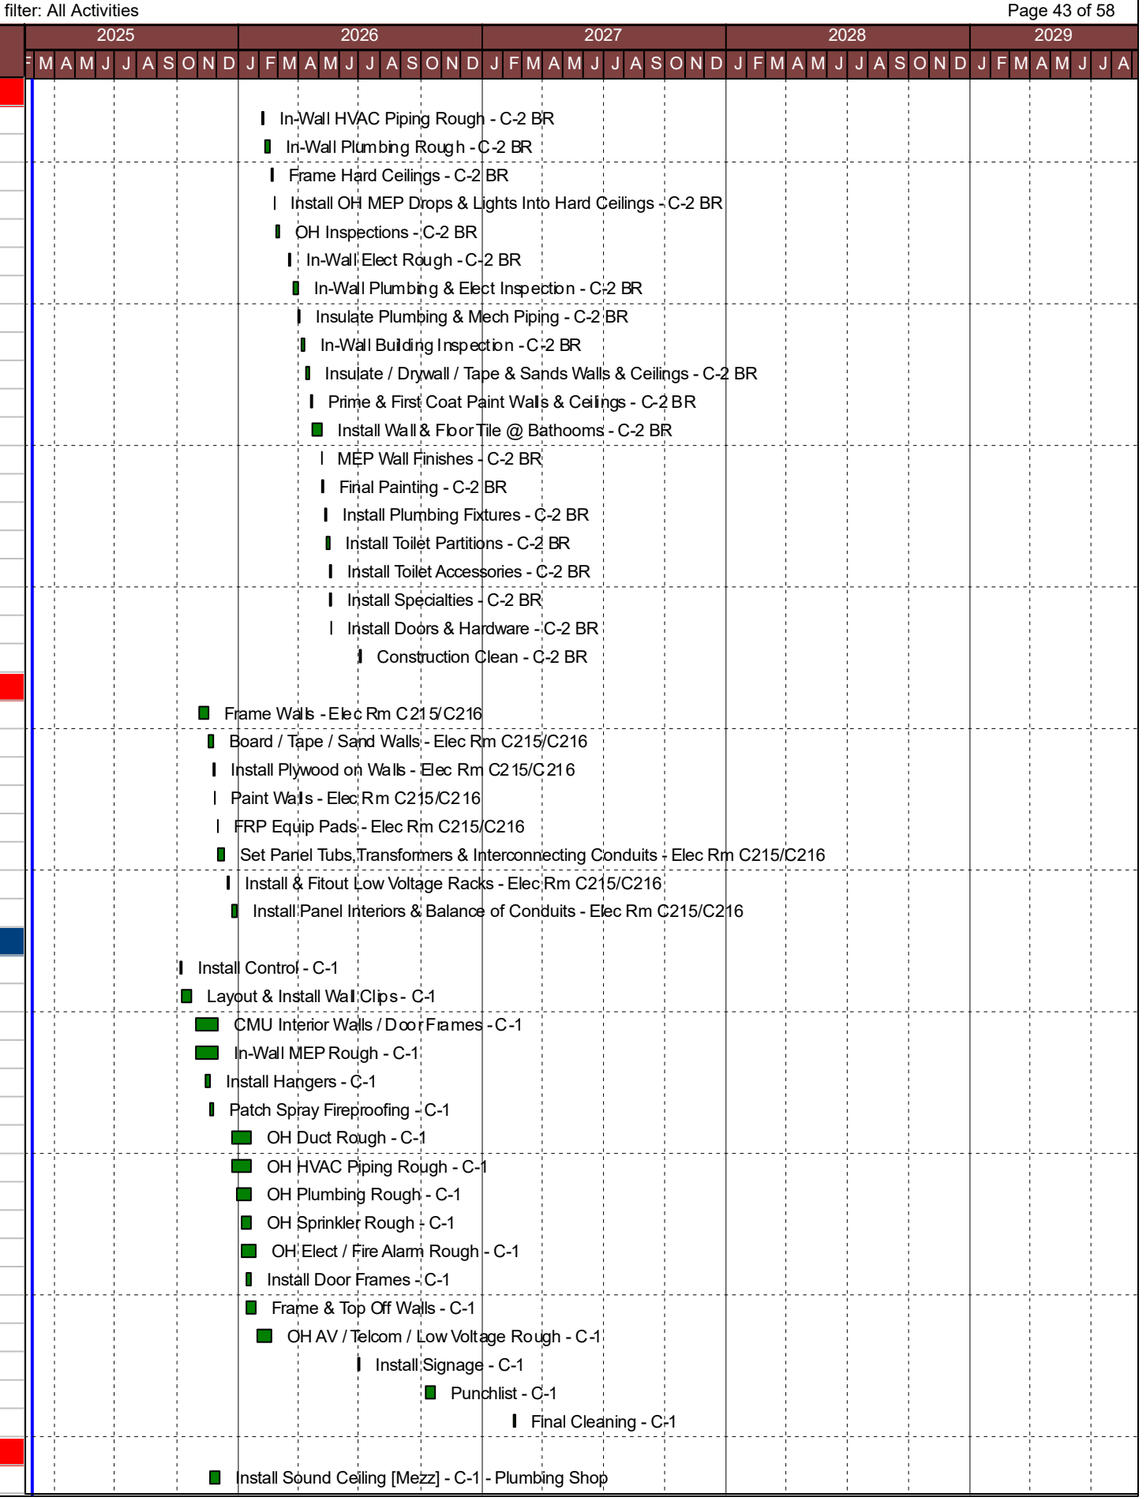

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A6020	Complete In-Wall MEP Inspection - C-1 - Plumbing Shop	5d	5d	02-Dec-25	08-Dec-25
A6190	HVAC Equip [Mezz] - C-1 - Plumbing Shop	5d	5d	05-Dec-25	11-Dec-25
A6200	Install Stair / Railings [Mezz] - C-1 - Plumbing Shop	4d	4d	12-Dec-25	17-Dec-25
A189370	Install ACT Grid - C-1 - Plumbing Shop	2d	2d	20-Feb-26	23-Feb-26
A185300	Drywall / Tape & Sands Ceiling @ Bathrooms - C-1 - Plumbing Shop	5d	5d	20-Feb-26	26-Feb-26
A189380	Install OH MEP Drops Into Grid - C-1 - Plumbing Shop	2d	2d	24-Feb-26	25-Feb-26
A189390	Install OH Lights Into Grid - C-1 - Plumbing Shop	2d	2d	24-Feb-26	25-Feb-26
A189400	OH Inspections - C-1 - Plumbing Shop	5d	5d	26-Feb-26	04-Mar-26
A6040	Paint Walls / Ceilings - C-1 - Plumbing Shop	5d	5d	03-Mar-26	09-Mar-26
A189410	Install Ceiling Tiles - C-1 - Plumbing Shop	1d	1d	05-Mar-26	05-Mar-26
A6100	Electrical Finishes - C-1 - Plumbing Shop	10d	10d	10-Mar-26	23-Mar-26
A6080	HVAC Finishes - C-1 - Plumbing Shop	3d	3d	17-Mar-26	19-Mar-26
A6150	Install Epoxy Flooring - C-1 - Plumbing Shop	7d	7d	24-Mar-26	01-Apr-26
A6210	Frame Workstation Cubbies - C-1 - Plumbing Shop	3d	3d	02-Apr-26	06-Apr-26
A185140	Install Casework - C-1 - Plumbing Shop	3d	3d	16-Jul-26	20-Jul-26
A56350	Install Linoleum Flooring - C-1 - Plumbing Shop	3d	3d	21-Jul-26	23-Jul-26
A56340	Install Wire Mesh Partitions - C-1 - Plumbing Shop	2d	2d	24-Jul-26	27-Jul-26
A6120	Install Lockers - C-1 - Plumbing Shop	4d	4d	29-Jul-26	03-Aug-26
A6110	Plumbing Finishes - C-1 - Plumbing Shop	15d	15d	04-Aug-26	24-Aug-26
A6130	Install Toilet Accessories / Specialties - C-1 - Plumbing Shop	1d	1d	25-Aug-26	25-Aug-26
A56360	Install Rubber Stair Treads - C-1 - Plumbing Shop	1d	1d	25-Aug-26	25-Aug-26
A6160	Install Specialty Equipment - C-1 - Plumbing Shop	5d	5d	25-Aug-26	31-Aug-26
A6220	Install Doors & Hardware - C-1 - Plumbing Shop	3d	3d	01-Sep-26	03-Sep-26
A189360	Construction Clean - C-1 - Plumbing Shop	1d	1d	04-Sep-26	04-Sep-26
HVAC Shop					
A185150	Install Sound Ceiling [Mezz] - C-1 - HVAC Shop	10d	10d	05-Dec-25	18-Dec-25
A185160	HVAC Equip [Mezz] - C-1 - HVAC Shop	5d	5d	19-Dec-25	26-Dec-25
A185170	Install Stair / Railings [Mezz] - C-1 - HVAC Shop	4d	4d	29-Dec-25	02-Jan-26
A173110	Install Flues - C-1 - HVAC Shop	20d	20d	22-Jan-26	19-Feb-26
A171280	FRP Locker Bases & Equip Pads - C-1 - HVAC Shop	4d	4d	20-Feb-26	25-Feb-26
A171090	OH Inspection - C-1 - HVAC Shop	5d	5d	20-Feb-26	26-Feb-26
A185310	Drywall / Tape & Sands Ceiling @ Bathrooms - C-1 - HVAC Shop	5d	5d	20-Feb-26	26-Feb-26
A189420	Install ACT Grid - C-1 - HVAC Shop	2d	2d	24-Feb-26	25-Feb-26
A189430	Install OH MEP Drops Into Grid - C-1 - HVAC Shop	2d	2d	26-Feb-26	27-Feb-26
A189460	Install OH Lights Into Grid - C-1 - HVAC Shop	2d	2d	26-Feb-26	27-Feb-26
A185270	Install ACT Ceiling - C-1 - HVAC Shop	3d	3d	26-Feb-26	02-Mar-26
A185380	FRP Condsensor Pad (exterior) - C-1 - HVAC Shop	3d	3d	27-Feb-26	03-Mar-26
A171110	Paint Walls & Ceiling - C-1 - HVAC Shop	5d	5d	27-Feb-26	05-Mar-26
A189440	OH Inspections - C-1 - HVAC Shop	5d	5d	02-Mar-26	06-Mar-26
A171160	Install Epoxy Flooring - C-1 - HVAC Shop	7d	7d	06-Mar-26	16-Mar-26
A189450	Install Ceiling Tiles - C-1 - HVAC Shop	1d	1d	09-Mar-26	09-Mar-26
A185180	Install Rubber Stair Treads - C-1 - HVAC Shop	1d	1d	17-Mar-26	17-Mar-26
A171290	Install Lockers - C-1 - HVAC Shop	2d	2d	17-Mar-26*	18-Mar-26
A171300	Frame / Sheath Workstation Cubbies & Training Wall- C-1 - HVAC Shop	5d	5d	17-Mar-26	23-Mar-26
A171150	Electrical Finishes - C-1 - HVAC Shop	10d	10d	17-Mar-26	30-Mar-26
A173100	Install Learning Equipment - C-1 - HVAC Shop	10d	10d	17-Mar-26	30-Mar-26
A171220	Install & Connect Specialty Equipment - C-1 - HVAC Shop	10d	10d	31-Mar-26	13-Apr-26
A171180	Install Casework - C-1 - HVAC Shop	3d	3d	21-Jul-26	23-Jul-26
A185280	Install Linoleum Flooring - C-1 - HVAC Shop	3d	3d	24-Jul-26	28-Jul-26
A171190	Plumbing Finishes - C-1 - HVAC Shop	5d	5d	24-Jul-26	30-Jul-26

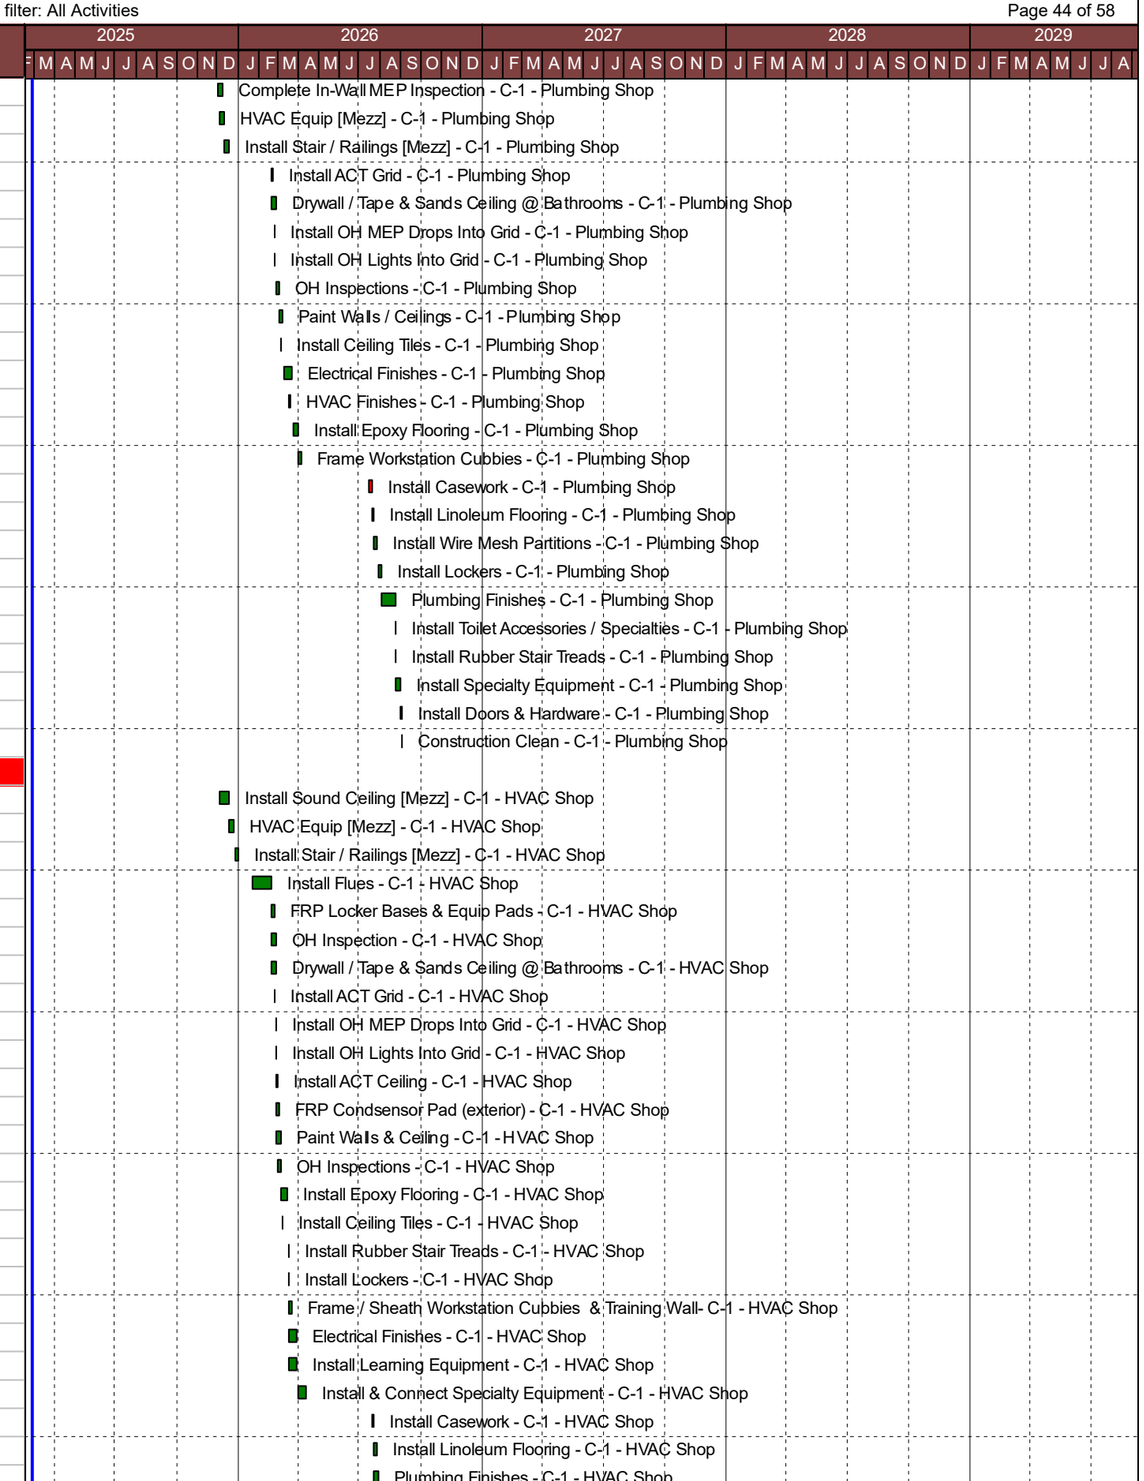

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A185290	Install Wire Mesh Partitions - C-1 - HVAC Shop	2d	2d	29-Jul-26	30-Jul-26
A171200	Install Toilet Accessories / Specialties - C-1 - HVAC Shop Bathrooms	1d	1d	31-Jul-26	31-Jul-26
A171210	Construction Clean - C-1 - HVAC Shop	1d	1d	03-Aug-26	03-Aug-26
Elec Shop					
A185190	Install Sound Ceiling [Mezz] - C-1 - Electrical Shop	10d	10d	19-Dec-25	05-Jan-26
A185200	HVAC Equip [Mezz] - C-1 - Electrical Shop	5d	5d	06-Jan-26	12-Jan-26
A185210	Install Stair / Railings [Mezz] - C-1 - Electrical Shop	4d	4d	13-Jan-26	16-Jan-26
A170880	OH Inspection - C-1 - Electrical Shop	5d	5d	20-Feb-26	26-Feb-26
A189470	Install ACT Grid - C-1 - Electrical Shop	2d	2d	26-Feb-26	27-Feb-26
A171260	FRP Locker Base - C-1 - Electrical Shop	2d	2d	27-Feb-26	02-Mar-26
A170870	Drywall / Tape & Sands Ceiling @ Bathrooms- C-1 - Electrical Shop	5d	5d	27-Feb-26	05-Mar-26
A189480	Install OH MEP Drops Into Grid - C-1 - Electrical Shop	2d	2d	02-Mar-26	03-Mar-26
A189510	Install OH Lights Into Grid - C-1 - Electrical Shop	2d	2d	02-Mar-26	03-Mar-26
A171270	Install Lockers - C-1 - Electrical Shop	2d	2d	03-Mar-26*	04-Mar-26
A189490	OH Inspections - C-1 - Electrical Shop	5d	5d	04-Mar-26	10-Mar-26
A185320	Drywall / Tape & Sands Ceiling @ Bathrooms - C-1 - Electrical Shop	4d	4d	05-Mar-26	10-Mar-26
A170900	Paint Walls / Ceilings - C-1 - Electrical Shop	5d	5d	06-Mar-26	12-Mar-26
A189500	Install Ceiling Tiles - C-1 - Electrical Shop	1d	1d	11-Mar-26	11-Mar-26
A170950	Install Epoxy Flooring - C-1 - Electrical Shop	7d	7d	13-Mar-26	23-Mar-26
A185220	Install Rubber Stair Treads - C-1 - Electrical Shop	1d	1d	24-Mar-26	24-Mar-26
A170920	Frame / Sheath Workstation Cubbies & Training Wall - C-1 - Electrical Shop	10d	10d	24-Mar-26	06-Apr-26
A171030	Install Wire Mesh Partitions - C-1 - Electrical Shop	3d	3d	03-Apr-26*	07-Apr-26
A170910	HVAC Finishes - C-1 - Electrical Shop	2d	2d	07-Apr-26	08-Apr-26
A170940	Electrical Finishes - C-1 - Electrical Shop	10d	10d	07-Apr-26	21-Apr-26
A170970	Install Casework - C-1 - Electrical Shop	3d	3d	24-Jul-26	28-Jul-26
A189720	Install Linoleum Flooring - C-1 - Electrical Shop	2d	2d	29-Jul-26	30-Jul-26
A170980	Plumbing Finishes - C-1 - Electrical Shop	5d	5d	31-Jul-26	06-Aug-26
A171010	Install & Connect Specialty Equipment - C-1 - Electrical Shop	10d	10d	31-Jul-26	13-Aug-26
A170990	Install Toilet Accessories / Specialties - C-1 - Electrical Shop Bathrooms	1d	1d	07-Aug-26	07-Aug-26
A171000	Construction Clean - C-1 - Electrical Shop	1d	1d	14-Aug-26	14-Aug-26
Carpentry Shop					
A185230	Install Sound Ceiling [Mezz] - C-1 - Carpentry Shop	10d	10d	06-Jan-26	20-Jan-26
A185240	HVAC Equip [Mezz] - C-1 - Carpentry Shop	5d	5d	21-Jan-26	27-Jan-26
A170600	Board / Tape / Sand - C-1 - Carpentry Shop	10d	10d	21-Jan-26	03-Feb-26
A171120	Install Dust Collector Duct - C-1 - Carpentry Shop	10d	10d	22-Jan-26	04-Feb-26
A185250	Install Stair / Railings [Mezz] - C-1 - Carpentry Shop	4d	4d	28-Jan-26	02-Feb-26
A185260	Install Rubber Stair Treads - C-1 - Carpentry Shop	1d	1d	03-Feb-26	03-Feb-26
A170700	Paint Walls / Ceilings - C-1 - Carpentry Shop	5d	5d	04-Feb-26	10-Feb-26
A170720	Electrical Finishes - C-1 - Carpentry Shop	12d	12d	06-Feb-26	24-Feb-26
A170710	HVAC Finishes - C-1 - Carpentry Shop	2d	2d	11-Feb-26	12-Feb-26
A170740	Install OH Door - C-1 - Carpentry Shop	2d	2d	11-Feb-26	12-Feb-26
A171130	FRP Pad for Dust Collector (exterior) - C-1 - Carpentry Shop	3d	3d	11-Feb-26	13-Feb-26
A171250	Install Locker Base - C-1 - Carpentry Shop	2d	2d	17-Feb-26*	18-Feb-26
A185360	Set Dust Collector (exterior) - C-1 - Carpentry Shop	3d	3d	17-Feb-26	19-Feb-26
A170730	Install Epoxy Flooring - C-1 - Carpentry Shop	15d	15d	25-Feb-26	17-Mar-26
A189520	Install ACT Grid - C-1 - Carpentry Shop	2d	2d	02-Mar-26	03-Mar-26
A189530	Install OH MEP Drops Into Grid - C-1 - Carpentry Shop	2d	2d	04-Mar-26	05-Mar-26
A189560	Install OH Lights Into Grid - C-1 - Carpentry Shop	2d	2d	04-Mar-26	05-Mar-26
A185330	Drywall / Tape & Sands Ceiling @ Bathrooms - C-1 - Carpentry Shop	4d	4d	05-Mar-26	10-Mar-26
A189540	OH Inspections - C-1 - Carpentry Shop	5d	5d	06-Mar-26	12-Mar-26

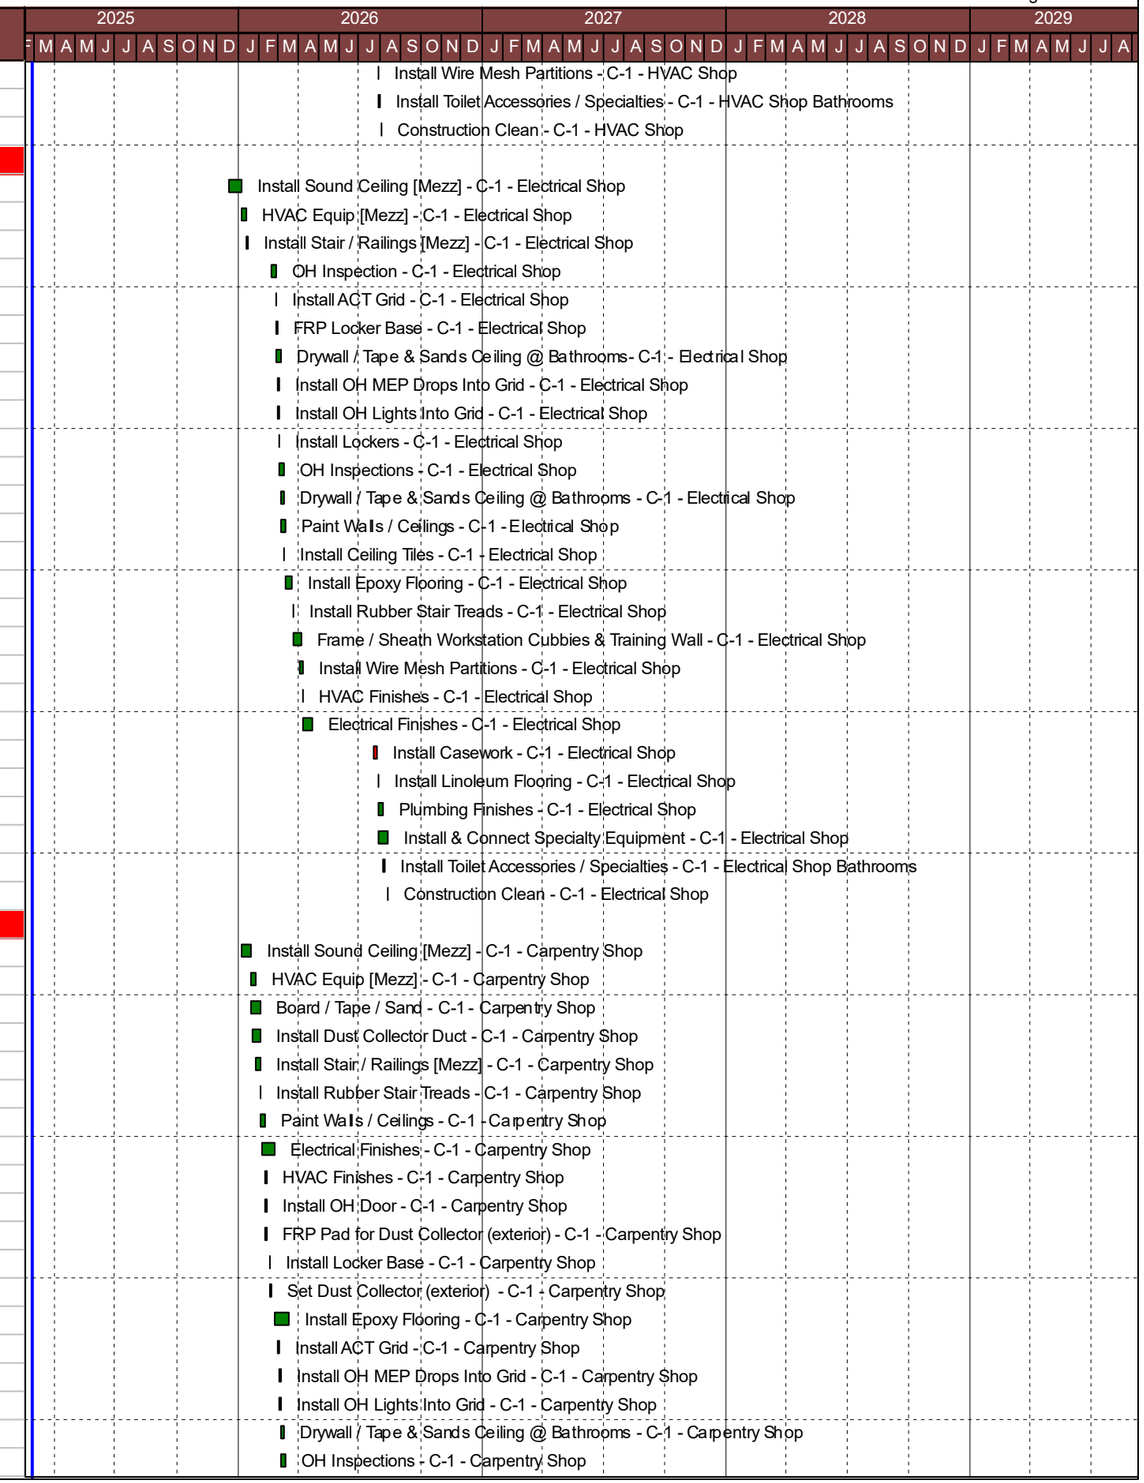

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A189550	Install Ceiling Tiles - C-1 - Carpentry Shop	1d	1d	13-Mar-26	13-Mar-26
A170750	Install Casework - C-1 - Carpentry Shop	3d	3d	29-Jul-26	31-Jul-26
A185370	Install Linoleum Flooring - C-1 - Carpentry Shop	2d	2d	03-Aug-26	04-Aug-26
A171240	Install Lockers - C-1 - Carpentry Shop	2d	2d	05-Aug-26*	06-Aug-26
A170760	Plumbing Finishes - C-1 - Carpentry Shop	5d	5d	05-Aug-26	11-Aug-26
A172060	Install Millwork - C-1 - Carpentry Shop	5d	5d	05-Aug-26	11-Aug-26
A170790	Install & Connect Specialty Equipment - C-1 - Carpentry Shop	10d	10d	05-Aug-26	18-Aug-26
A170770	Install Toilet Accessories / Specialties - C-1 - Carpentry Shop Bathrooms	1d	1d	12-Aug-26	12-Aug-26
A170820	Install Fin Tube Heating - C-1 - Carpentry Shop	5d	5d	12-Aug-26	18-Aug-26
A170780	Construction Clean - C-1 - Carpentry Shop	2d	2d	19-Aug-26*	20-Aug-26
Classroom					
A56080	In-Wall HVAC Piping Rough - C-1 CR	5d	5d	29-Jan-26	04-Feb-26
A56070	In-Wall Elect Rough - C-1 CR	20d	20d	29-Jan-26	26-Feb-26
A56090	In-Wall Elect Inspection - C-1 CR	10d	10d	27-Feb-26	12-Mar-26
A56100	Insulate Mech Piping - C-1 CR	5d	5d	13-Mar-26	19-Mar-26
A56110	In-Wall Building Inspection - C-1 CR	5d	5d	20-Mar-26	26-Mar-26
A56120	Insulate / Drywall / Tape & Sands Walls - C-1 CR	15d	15d	27-Mar-26	16-Apr-26
A56130	Prime & First Coat Paint Walls, Ceilings & Exposed MEPs - C-1 CR	4d	4d	17-Apr-26	23-Apr-26
A56140	Install ACT Grid - C-1 CR	4d	4d	24-Apr-26	29-Apr-26
A56160	Install OH MEP Drops Into Grid - C-1 CR	5d	5d	30-Apr-26	06-May-26
A56170	Install OH Lights Into Grid - C-1 CR	5d	5d	30-Apr-26	06-May-26
A56150	Install VBC-12 Ceiling - C-1 CR	10d	10d	30-Apr-26	13-May-26
A56190	OH Inspections - C-1 CR	5d	5d	07-May-26	13-May-26
A56180	Install Wall Tile @ Hallways- C-1 CR	10d	10d	07-May-26	20-May-26
A56200	Install Ceiling Tiles - C-1 CR	6d	6d	21-May-26	29-May-26
A56210	MEP Wall Finishes - C-1 CR	5d	5d	01-Jun-26	05-Jun-26
A56220	Final Painting - C-1 CR	4d	4d	08-Jun-26	11-Jun-26
A56260	Install Specialties - C-1 CR	2d	2d	12-Jun-26	15-Jun-26
A56270	Install Plumbing Finishes - C-1 CR	2d	2d	12-Jun-26	15-Jun-26
A56230	Install Casework - C-1 CR	3d	3d	03-Aug-26	05-Aug-26
A56240	Install Linoleum Flooring - C-1 CR	10d	10d	06-Aug-26	19-Aug-26
A189730	Install Rubber Tile Flooring - C-1 CR	5d	5d	20-Aug-26	26-Aug-26
A56250	Install Carpet - C-1 CR	2d	2d	27-Aug-26	28-Aug-26
A56300	Install Appliances - C-1 CR	4d	4d	27-Aug-26	01-Sep-26
A56280	Install Doors & Hardware - C-1 CR	2d	2d	31-Aug-26	01-Sep-26
A56290	Install Wall Graphics - C-1 CR	4d	4d	02-Sep-26	08-Sep-26
A56310	Construction Clean - C-1 CR	2d	2d	09-Sep-26	10-Sep-26
Bathrooms					
A55850	In-Wall Plumbing Rough - C-1 BR	5d	5d	29-Jan-26	04-Feb-26
A55840	In-Wall HVAC Piping Rough - C-1 BR	2d	2d	05-Feb-26	06-Feb-26
A55890	Frame Hard Ceilings - C-1 - BR	2d	2d	20-Feb-26	23-Feb-26
A55900	Install OH MEP Drops & Lights Into Hard Ceilings - C-1 - BR	2d	2d	24-Feb-26	25-Feb-26
A55920	OH Inspections - C-1 - BR	5d	5d	26-Feb-26	04-Mar-26
A55830	In-Wall Elect Rough - C-1 BR	2d	2d	27-Feb-26	02-Mar-26
A55860	In-Wall Plumbing & Elect Inspection - C-1 BR	5d	5d	06-Mar-26	12-Mar-26
A55870	Insulate Plumbing & Mech Piping - C-1 BR	2d	2d	13-Mar-26	16-Mar-26
A55880	In-Wall Building Inspection - C-1 BR	5d	5d	17-Mar-26	23-Mar-26
A55940	Insulate / Drywall / Tape & Sands Walls & Ceilings - C-1 BR	5d	5d	24-Mar-26	30-Mar-26
A55950	Prime & First Coat Paint Walls & Ceilings - C-1 BR	1d	1d	31-Mar-26	31-Mar-26
A55960	Install Wall & Floor Tile @ Bathooms - C-1 BR	10d	10d	01-Apr-26	14-Apr-26

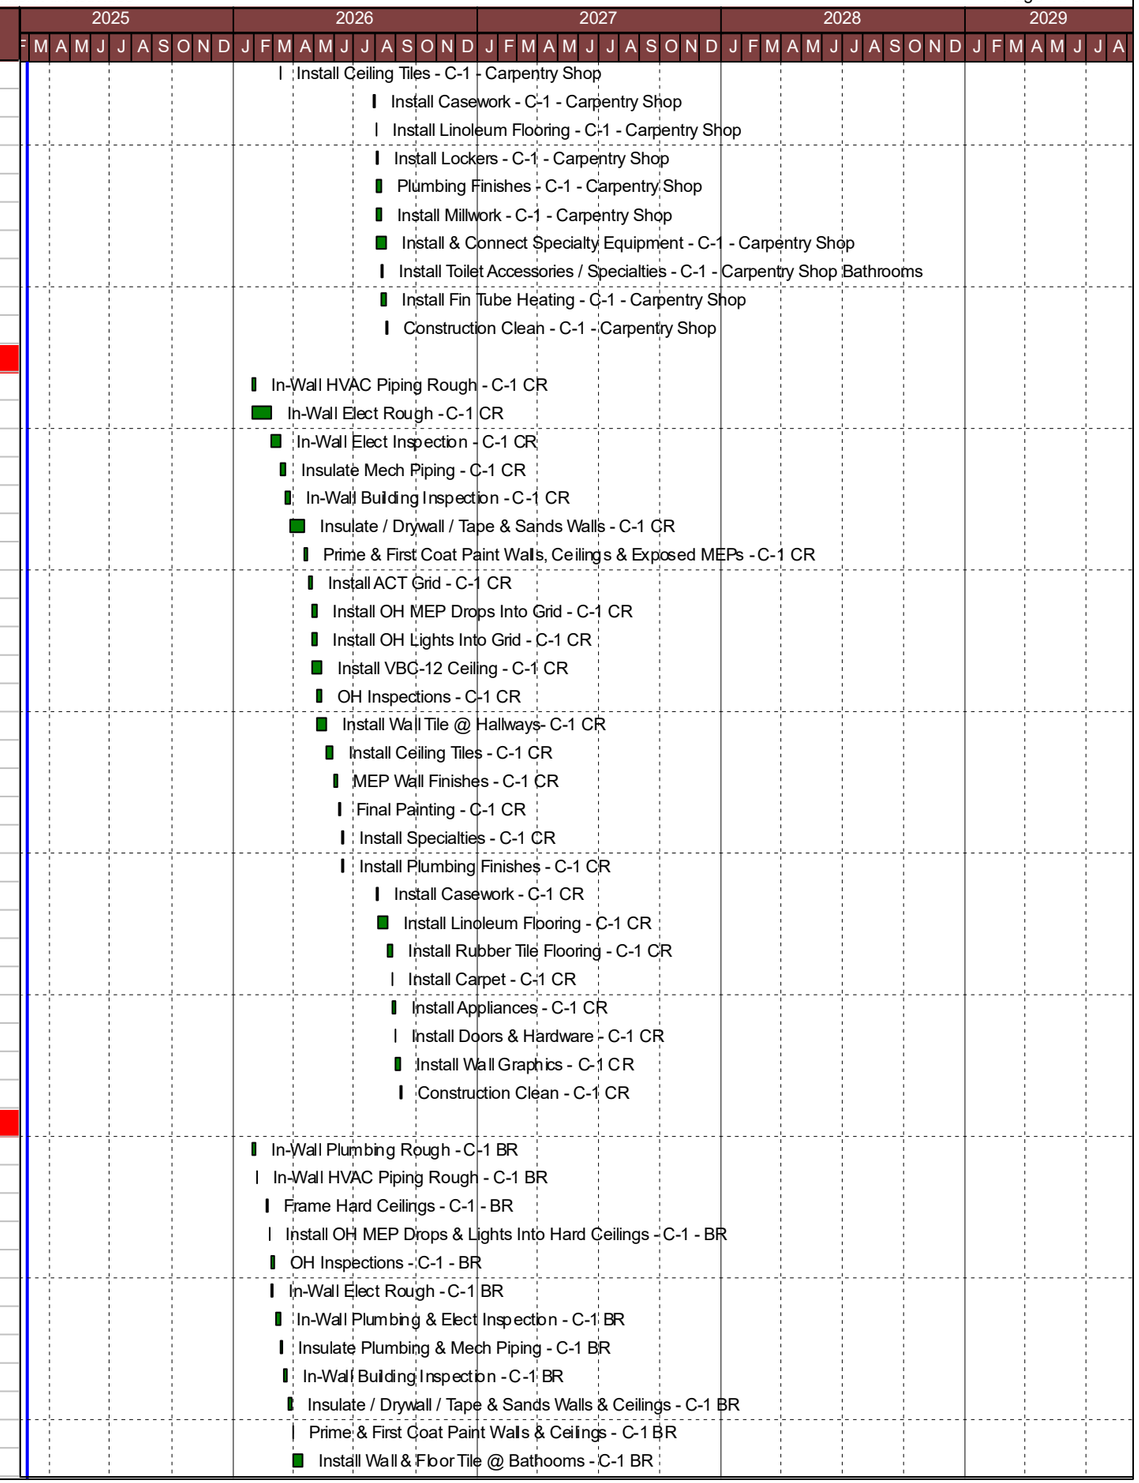

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A55980	MEP Wall Finishes - C-1 BR	1d	1d	15-Apr-26	15-Apr-26
A56000	Final Painting - C-1 BR	4d	4d	16-Apr-26	22-Apr-26
A55990	Install Plumbing Fixtures - C-1 BR	3d	3d	23-Apr-26	27-Apr-26
A56010	Install Toilet Partitions - C-1 BR	3d	3d	28-Apr-26	30-Apr-26
A56030	Install Toilet Accessories - C-1 BR	2d	2d	01-May-26	04-May-26
A56020	Install Specialties - C-1 BR	2d	2d	01-May-26	04-May-26
A55970	Install Doors & Hardware - C-1 BR	1d	1d	05-May-26	05-May-26
A56040	Construction Clean - C-1 BR	2d	2d	06-May-26	07-May-26
IDF / Elect - C116/C115					
A51550	Frame Walls - Elec Rm C116/C115	9d	9d	13-Nov-25	25-Nov-25
A51560	Board / Tape / Sand Walls - Elec Rm C116/C115	5d	5d	26-Nov-25	03-Dec-25
A51570	Install Plywood on Walls - Elec Rm C116/C115	2d	2d	04-Dec-25	05-Dec-25
A51580	Paint Walls - Elec Rm C116/C115	1d	1d	08-Dec-25	08-Dec-25
A51590	FRP Equip Pads - Elec Rm C116/C115	2d	2d	09-Dec-25	10-Dec-25
A51600	Set Panel Tubs,Transformers & Interconnecting Conduits - Elec Rm C116/C115	8d	8d	11-Dec-25	22-Dec-25
A51610	Install & Fitout Low Voltage Racks - Elec Rm C116/C115	5d	5d	23-Dec-25	30-Dec-25
A51620	Install Panel Interiors & Balance of Conduits - Elec Rm C116/C115	6d	6d	31-Dec-25	08-Jan-26
Building D					
A185950	Punchlist - D-2	10d	10d	23-Oct-26	05-Nov-26
A185960	Final Cleaning - D-2	2d	2d	22-Feb-27	23-Feb-27
2nd Floor					
A185390	Install Control - D-2	2d	2d	30-Sep-25	01-Oct-25
A185400	Layout & Install Wall Clips - D-2	10d	10d	02-Oct-25	16-Oct-25
A185430	Install Hangers - D-2	5d	5d	18-Nov-25	24-Nov-25
A185440	Patch Spray Fireproofing - D-2	3d	3d	25-Nov-25	28-Nov-25
A185450	OH Duct Rough - D-2	20d	20d	07-Jan-26	04-Feb-26
A185460	OH HVAC Piping Rough - D-2	20d	20d	07-Jan-26	04-Feb-26
A185490	OH Plumbing Rough - D-2	15d	15d	14-Jan-26	04-Feb-26
A185500	OH Sprinkler Rough - D-2	10d	10d	22-Jan-26	04-Feb-26
A185510	OH Elect / Fire Alarm Rough - D-2	15d	15d	22-Jan-26	11-Feb-26
A185470	Install Door Frames - D-2	5d	5d	29-Jan-26	04-Feb-26
A185480	Frame & Top Off Walls - D-2	10d	10d	29-Jan-26	11-Feb-26
A192410	OH AV / Telcom / Low Voltage Rough - D-2	15d	15d	12-Feb-26	05-Mar-26
A185420	In-Wall MEP Rough - D-2	20d	20d	12-Feb-26	12-Mar-26
A185520	Install Signage - D-2	2d	2d	05-Jun-26	08-Jun-26
Legal & Protective Services					
A185670	In-Wall HVAC Piping Rough - D-2 Legal	5d	5d	12-Feb-26	19-Feb-26
A185680	In-Wall Elect Rough - D-2 Legal	20d	20d	12-Feb-26	12-Mar-26
A185700	Frame Hard Ceilings @ Bathrooms - D-2 Legal	2d	2d	06-Mar-26	09-Mar-26
A185720	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - D-2 Legal	2d	2d	10-Mar-26	11-Mar-26
A185690	In-Wall Elect Inspection - D-2 Legal	10d	10d	13-Mar-26	26-Mar-26
A185730	Insulate Mech Piping - D-2 Legal	5d	5d	27-Mar-26	02-Apr-26
A185750	In-Wall Building Inspection - D-2 Legal	5d	5d	03-Apr-26	09-Apr-26
A185760	Insulate / Drywall / Tape & Sands Walls & Ceilings - D-2 Legal	10d	10d	10-Apr-26	24-Apr-26
A185710	Paint OH MEPs & Exposed Structure - D-2 Legal	2d	2d	27-Apr-26	28-Apr-26
A185770	Prime & First Coat Paint Walls & Ceilings - D-2 Legal	4d	4d	27-Apr-26	30-Apr-26
A185790	Install ACT Grid - D-2 Legal	3d	3d	01-May-26	05-May-26
A185810	Install OH Lights Into Grid - D-2 Legal	2d	2d	06-May-26	07-May-26
A185800	Spray Acoustic Insulation - D-2 Legal	3d	3d	06-May-26	08-May-26
A185830	Install OH MEP Drops Into Grid - D-2 Legal	5d	5d	06-May-26	12-May-26

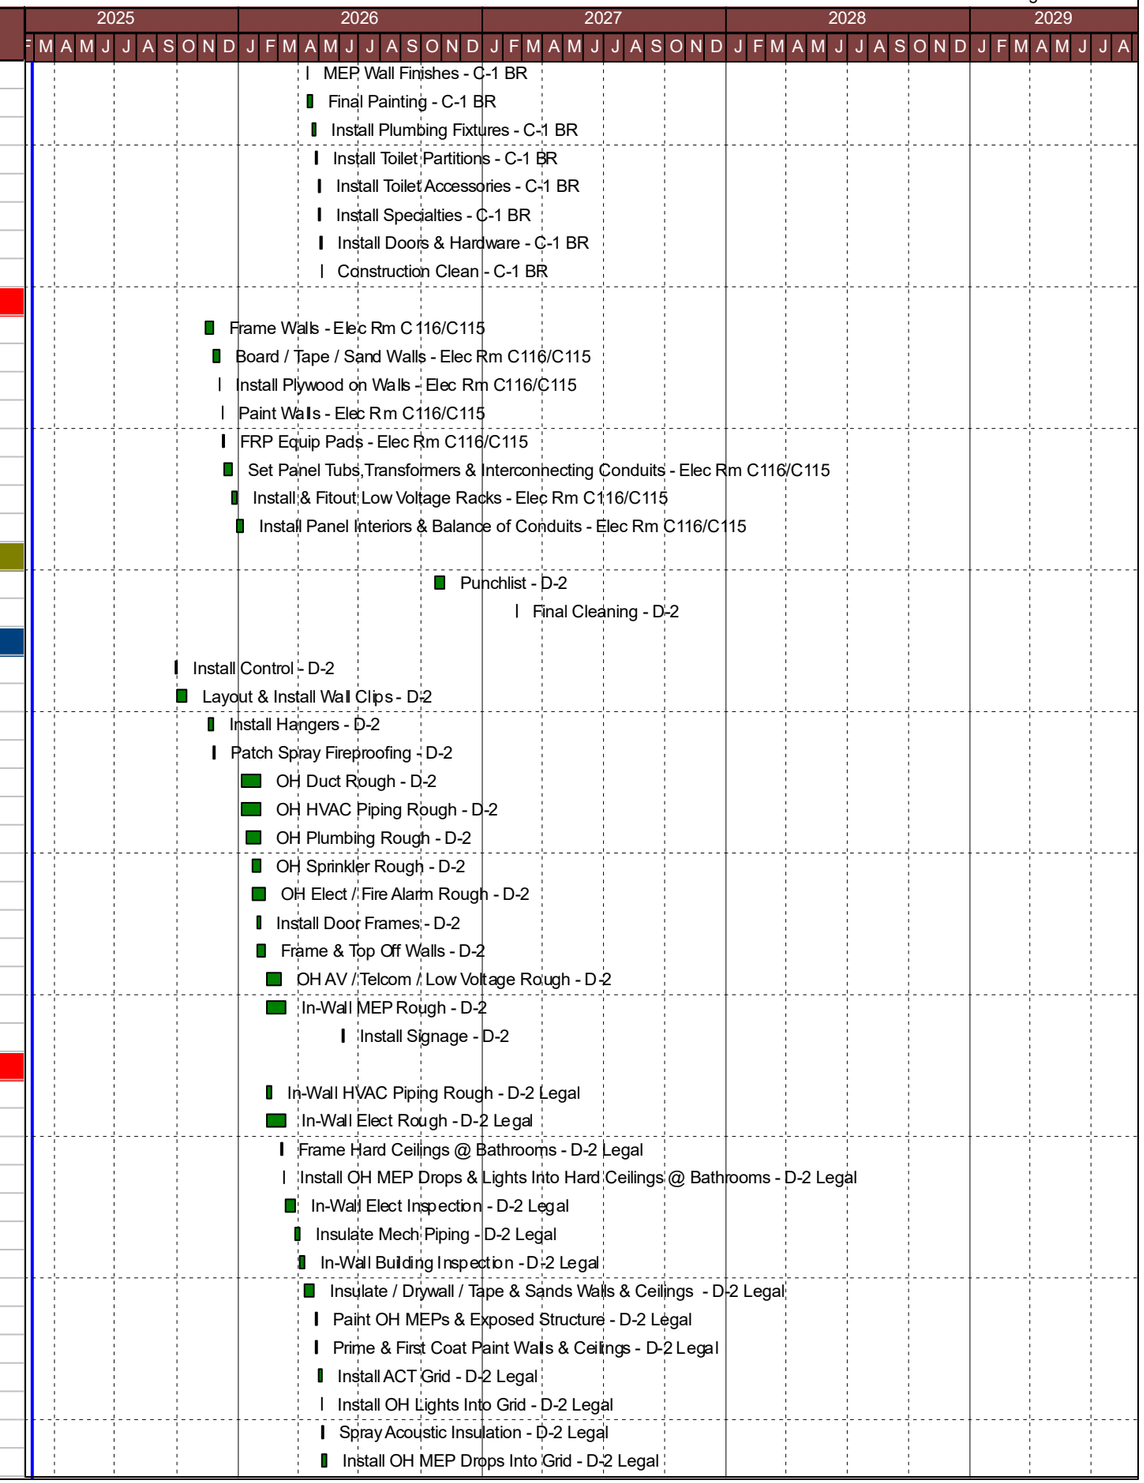

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A185860	OH Inspections - D-2 Legal	5d	5d	13-May-26	19-May-26
A185870	Install Ceiling Tiles - D-2 Legal	6d	6d	20-May-26	28-May-26
A185900	Install Tile @ Bathroom - D-2 Legal	5d	5d	29-May-26	04-Jun-26
A185780	MEP Wall Finishes - D-2 Legal	5d	5d	29-May-26	04-Jun-26
A185820	Final Painting - D-2 Legal	4d	4d	05-Jun-26	10-Jun-26
A185850	Install Plumbing Finish - D-2 Legal	5d	5d	11-Jun-26	17-Jun-26
A185890	Install Casework / Cubbies - D-2 Legal	5d	5d	06-Aug-26	12-Aug-26
A185880	Install Linoleum Flooring - D-2 Legal	4d	4d	13-Aug-26	18-Aug-26
A185910	Install Wire Mesh Partitions- D-2 Legal	2d	2d	19-Aug-26	20-Aug-26
A185930	Install Specialties / Lockers - D-2 Legal	4d	4d	19-Aug-26	24-Aug-26
A185920	Install Doors & Hardware - D-2 Legal	4d	4d	25-Aug-26	28-Aug-26
A185940	Construction Clean - D-2 Legal	2d	2d	31-Aug-26	01-Sep-26
Mechanical					
A185970	Frame Early Walls / One-Side Board - Mech Rm - D200	3d	3d	18-Nov-25	20-Nov-25
A185980	Paint Ceiling - Mech Rm - D200	3d	3d	21-Nov-25	25-Nov-25
A185990	Install OH FP Rough - Mech Rm - D200	5d	5d	26-Nov-25	03-Dec-25
A186000	Install OH Electrical Rough - Mech Rm - D200	5d	5d	26-Nov-25	03-Dec-25
A186010	Install OH Plumbing Rough - Mech Rm - D200	3d	3d	04-Dec-25	08-Dec-25
A186020	Install OH Mechanical Pipe Rough - Mech Rm - D200	15d	15d	09-Dec-25	30-Dec-25
A186030	OH Duct Rough - Mech Rm - D200	15d	15d	16-Dec-25	07-Jan-26
A186040	FRP Housekeeping Pads - Mech Rm - D200	5d	5d	08-Jan-26	14-Jan-26
A186050	Set Air & Connect Handling Equip- Mech Rm - D200	15d	15d	13-Mar-26	02-Apr-26
A186060	Install Doors & Hardware - Mech Rm - D200	2d	2d	03-Apr-26	06-Apr-26
A186070	Final Paint - Mech Rm - D200	2d	2d	03-Apr-26	06-Apr-26
A186080	Construction Clean - Mech Rm - D200	2d	2d	07-Apr-26	08-Apr-26
A189070	Punchlist - Mech Rm - D200	10d	10d	09-Apr-26	23-Apr-26
Mezzanine					
A186120	Frame Walls - Cont Ed - D-M	2d	2d	11-Mar-26	12-Mar-26
A186130	OH Duct Rough - Cont Ed - D-M	2d	2d	13-Mar-26	16-Mar-26
A186140	Install In-Wall & OH Electrical Rough - Cont Ed - D-M	2d	2d	17-Mar-26	18-Mar-26
A186150	Install OH FP Rough - Cont Ed - D-M	1d	1d	19-Mar-26	19-Mar-26
A186160	In-Wall Inspections - Cont Ed - D-M	5d	5d	19-Mar-26	25-Mar-26
A186290	Paint OH MEPs & Exposed Structure - Cont Ed - D-M	2d	2d	20-Mar-26	23-Mar-26
A186300	Spray Acoustic Insulation - Cont Ed - D-M	3d	3d	24-Mar-26	26-Mar-26
A186170	Insulate / Drywall / Tape & Sands Walls - Cont Ed - D-M	4d	4d	05-May-26	08-May-26
A186180	Prime, First Coat - Cont Ed - D-M	1d	1d	11-May-26	11-May-26
A186190	Install ACT Grid - Cont Ed - D-M	2d	2d	12-May-26	13-May-26
A186200	Install Finishes in Ceiling Grid - Cont Ed - D-M	2d	2d	14-May-26	15-May-26
A186210	Above Ceiling Inspections - Cont Ed - D-M	5d	5d	18-May-26	22-May-26
A186220	Install Ceiling Tiles - Cont Ed - D-M	1d	1d	26-May-26	26-May-26
A186330	Install Storefront - Cont Ed - D-M	2d	2d	27-May-26	28-May-26
A186320	Install Casework - Cont Ed - D-M	2d	2d	27-Aug-26	28-Aug-26
A186230	Install Linoleum Flooring - Cont Ed - D-M	3d	3d	31-Aug-26	02-Sep-26
A186310	Install Carpet Tile Flooring - Cont Ed - D-M	3d	3d	03-Sep-26	08-Sep-26
A186240	Final Painting - Cont Ed - D-M	1d	1d	09-Sep-26	09-Sep-26
A186250	Install Floor Base - Cont Ed - D-M	1d	1d	10-Sep-26	10-Sep-26
A186260	Construction Clean - Cont Ed - D-M	1d	1d	11-Sep-26	11-Sep-26
1st Floor					
A185530	Install Control - D-1	2d	2d	29-Oct-25	30-Oct-25
A185540	Layout & Install Wall Clips - D-1	10d	10d	31-Oct-25	14-Nov-25

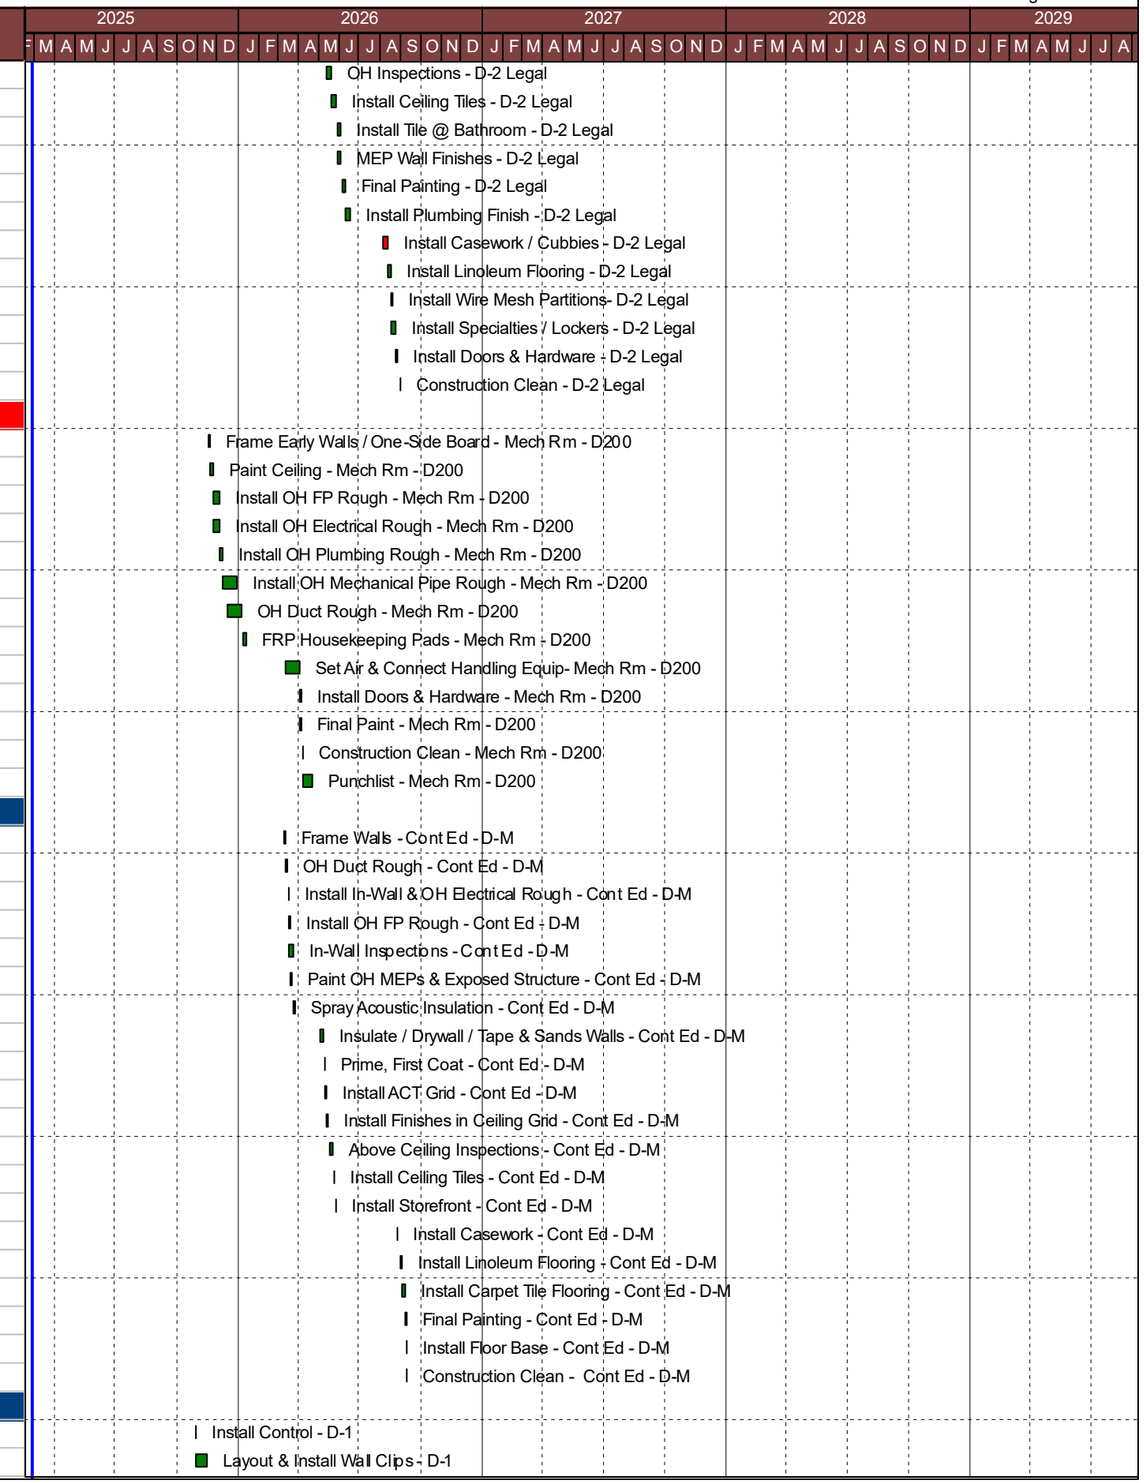

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A185570	Install Hangers - D-1	5d	5d	21-Nov-25	28-Nov-25
A185580	Patch Spray Fireproofing - D-1	3d	3d	01-Dec-25	03-Dec-25
A185640	OH Sprinkler Rough - D-1	10d	10d	01-Dec-25	12-Dec-25
A185650	OH Elect / Fire Alarm Rough - D-1	15d	15d	05-Feb-26	26-Feb-26
A185630	OH Plumbing Rough - D-1	15d	15d	05-Feb-26	26-Feb-26
A185590	OH Duct Rough - D-1	20d	20d	05-Feb-26	05-Mar-26
A185600	OH HVAC Piping Rough - D-1	20d	20d	05-Feb-26	05-Mar-26
A185610	Install Door Frames - D-1	5d	5d	27-Feb-26	05-Mar-26
A185620	Frame & Top Off Walls - D-1	10d	10d	27-Feb-26	12-Mar-26
A192420	OH AV / Telcom / Low Voltage Rough - D-1	15d	15d	27-Feb-26	19-Mar-26
A185560	In-Wall MEP Rough - D-1	20d	20d	13-Mar-26	09-Apr-26
A185660	Install Signage - D-1	2d	2d	21-Aug-26	24-Aug-26
A186920	Punchlist - D-1	10d	10d	06-Nov-26	20-Nov-26
A186930	Final Cleaning - D-1	2d	2d	24-Feb-27	25-Feb-27
Culinary / Restaurant					
A187180	In-Wall Plumbing Rough - D-1 - Culinary / Resturant	2d	2d	13-Mar-26	16-Mar-26
A187160	In-Wall Elect Rough - D-1 - Culinary / Resturant	20d	20d	13-Mar-26	09-Apr-26
A187190	Frame Hard Ceilings @ Bathrooms - D-1 - Culinary / Resturant	2d	2d	20-Mar-26	23-Mar-26
A186950	Install Hood - Culinary Kitchen	3d	3d	20-Mar-26	24-Mar-26
A187320	Prime Paint Walls/ Exposed Deck / Exposed MEPs - Resturant	5d	5d	20-Mar-26	26-Mar-26
A187170	In-Wall HVAC Piping Rough - D-1 - Culinary / Resturant	5d	5d	23-Mar-26	27-Mar-26
A187200	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - D-1 - Culinary / Resturant	2d	2d	24-Mar-26	25-Mar-26
A186960	Install Final Connections to Hoods - D-1 - Culinary / Resturant	3d	3d	25-Mar-26	27-Mar-26
A187210	Drywall / Tape & Sands Ceiling @ Bathrooms - D-1 - Culinary / Resturant	4d	4d	26-Mar-26	31-Mar-26
A187330	Install Ceiling Clouds - Resturant	30d	30d	27-Mar-26	08-May-26
A187340	Install HVAC Finishes in Ceiling Clouds - Resturant	30d	30d	27-Mar-26	08-May-26
A187350	Install Electrical / AV Finishes in Ceiling Clouds - Resturant	30d	30d	27-Mar-26	08-May-26
A187360	Install Sprinkler Finishes in Ceiling Clouds - Resturant	30d	30d	27-Mar-26	08-May-26
A187220	In-Wall Elect & Plumb Inspection - D-1 - Culinary / Resturant	10d	10d	10-Apr-26	24-Apr-26
A187230	Insulate Mech Piping - D-1 - Culinary / Resturant	5d	5d	27-Apr-26	01-May-26
A187240	In-Wall Building Inspection - D-1 - Culinary / Resturant	5d	5d	04-May-26	08-May-26
A187250	Insulate / Drywall / Tape & Sands Walls - D-1 - Culinary / Resturant	20d	20d	11-May-26	08-Jun-26
A187260	Prime & First Coat Paint Walls & Ceilings - D-1 - Culinary / Resturant	4d	4d	09-Jun-26	12-Jun-26
A186980	Install Wall Tile - Resturant	3d	3d	15-Jun-26	17-Jun-26
A186970	Install FRP Walls - Culinary Kitchen	5d	5d	15-Jun-26	19-Jun-26
A186990	Install Walk-In Cooler / Walk-In Freeze - D-1 - Culinary / Resturant	3d	3d	22-Jun-26	24-Jun-26
A187000	Install Ceiling Grid - D-1 - Culinary / Resturant	4d	4d	25-Jun-26	30-Jun-26
A187270	Install ACT Grid - D-1 - Culinary / Resturant	5d	5d	25-Jun-26	01-Jul-26
A187030	Install Ansul System - Culinary Kitchen	2d	2d	01-Jul-26	02-Jul-26
A187300	Install OH Lights Into Grid - D-1 - Culinary / Resturant	2d	2d	02-Jul-26	03-Jul-26
A187290	Install OH MEP Drops Into Grid - D-1 - Culinary / Resturant	5d	5d	02-Jul-26	08-Jul-26
A187310	OH Inspections - D-1 - Culinary / Resturant	5d	5d	09-Jul-26	15-Jul-26
A187050	Install Ceiling Tiles - D-1 - Culinary / Resturant	3d	3d	16-Jul-26	20-Jul-26
A187060	Install Epoxy Flooring - Culinary Kitchen	5d	5d	21-Jul-26	27-Jul-26
A187070	Final Painting - D-1 - Culinary / Resturant	5d	5d	28-Jul-26	03-Aug-26
A187080	Install Terrazzo - Resturant	5d	5d	04-Aug-26	10-Aug-26
A187090	Install Food Service Equipment - D-1 - Culinary / Resturant	5d	5d	11-Aug-26	17-Aug-26
A187370	Install Metal Plank & Glass Wall Finishes - Resturant	15d	15d	11-Aug-26	31-Aug-26
A187110	Connections to Food Service Equipment - D-1 - Culinary / Resturant	10d	10d	18-Aug-26	31-Aug-26
A187280	MEP Wall Finishes - D-1 - Culinary / Resturant	5d	5d	01-Sep-26	08-Sep-26

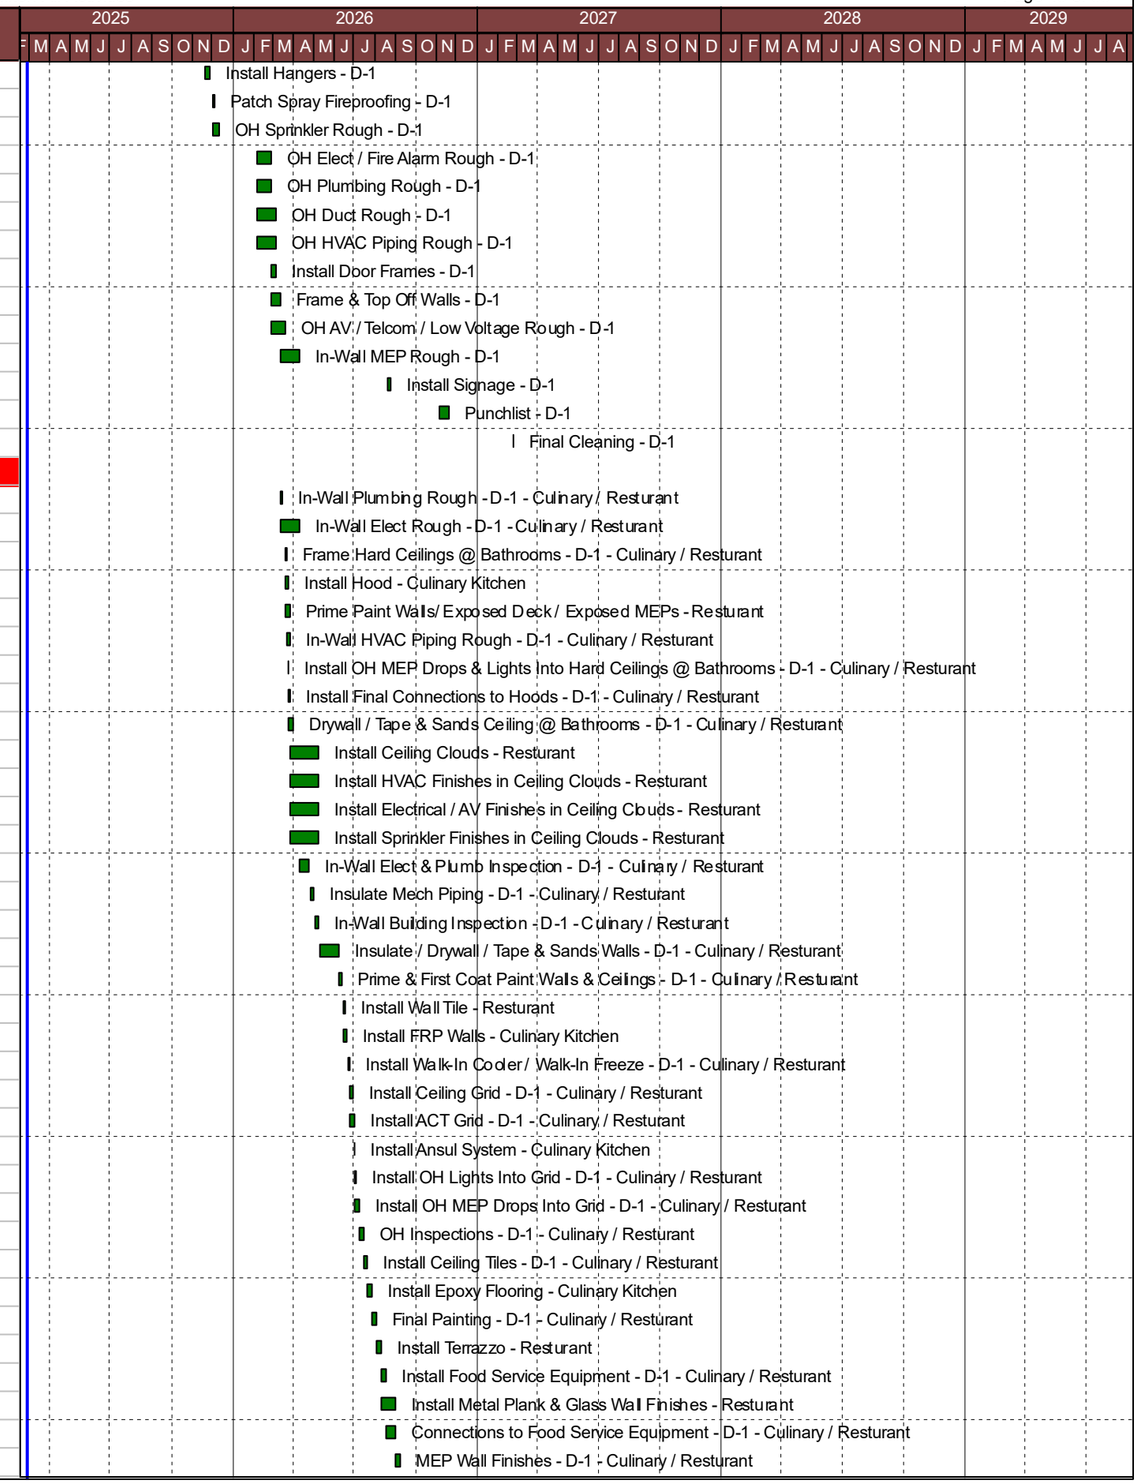

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A190190	Install Doors & Hardware - D-1 - Culinary / Resturant	4d	4d	09-Sep-26	14-Sep-26
A187100	Construction Clean - D-1 - Culinary / Resturant	2d	2d	15-Sep-26	16-Sep-26
A187120	Food Service Equipment Start-up - D-1 - Culinary / Resturant	5d	5d	17-Sep-26	23-Sep-26
A187130	Test Ansul System with Fire Dept - Culinary Kitchen	2d	2d	24-Sep-26	25-Sep-26
Post Grad Nursing					
A186670	In-Wall HVAC Piping Rough - D-1 PG Nursing	5d	5d	13-Mar-26	19-Mar-26
A186700	Frame Hard Ceilings @ Bathrooms - D-1 PG Nursing	2d	2d	20-Mar-26	23-Mar-26
A186720	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - D-1 PG Nursing	2d	2d	24-Mar-26	25-Mar-26
A186730	Drywall / Tape & Sands Ceiling @ Bathrooms - D-1 PG Nursing	4d	4d	26-Mar-26	31-Mar-26
A186660	In-Wall Elect Rough - D-1 PG Nursing	20d	20d	10-Apr-26	08-May-26
A186680	In-Wall Plumbing Rough - D-1 PG Nursing	20d	20d	10-Apr-26	08-May-26
A186690	In-Wall Elect & Plumb Inspection - D-1 PG Nursing	10d	10d	11-May-26	22-May-26
A186710	Insulate Mech Piping - D-1 PG Nursing	5d	5d	26-May-26	01-Jun-26
A186740	In-Wall Building Inspection - D-1 PG Nursing	5d	5d	02-Jun-26	08-Jun-26
A186750	Insulate / Drywall / Tape & Sands Walls - D-1 PG Nursing	20d	20d	09-Jun-26	06-Jul-26
A186760	Prime & First Coat Paint Walls & Ceilings - D-1 PG Nursing	6d	6d	07-Jul-26	14-Jul-26
A190160	Install Blocking / Supports for Curtain Track - D-1 PG Nursing	2d	2d	15-Jul-26	16-Jul-26
A186770	Install ACT Grid - D-1 PG Nursing	3d	3d	17-Jul-26	21-Jul-26
A186800	Install OH Lights Into Grid - D-1 PG Nursing	2d	2d	22-Jul-26	23-Jul-26
A186790	Install OH MEP Drops Into Grid - D-1 PG Nursing	5d	5d	22-Jul-26	28-Jul-26
A190170	Install Curtain Track - D-1 PG Nursing	2d	2d	29-Jul-26	30-Jul-26
A186810	OH Inspections - D-1 PG Nursing	5d	5d	31-Jul-26	06-Aug-26
A186820	Install Ceiling Tiles - D-1 PG Nursing	6d	6d	07-Aug-26	14-Aug-26
A186780	MEP Wall Finishes - D-1 PG Nursing	5d	5d	17-Aug-26	21-Aug-26
A186840	Install Casework - D-1 PG Nursing	5d	5d	31-Aug-26	04-Sep-26
A186850	Install Sheet Vinyl Flooring - D-1 PG Nursing	6d	6d	08-Sep-26	15-Sep-26
A190180	Install Tile @ Bathroom - D-1 PG Nursing	5d	5d	16-Sep-26	22-Sep-26
A186860	Final Painting - D-1 PG Nursing	4d	4d	23-Sep-26	28-Sep-26
A186890	Install Plumbing Finish - D-1 PG Nursing	10d	10d	29-Sep-26	13-Oct-26
A186900	Install & Connect Specialty Equipment - D-1 PG Nursing	10d	10d	29-Sep-26	13-Oct-26
A186880	Install Specialties - D-1 PG Nursing	5d	5d	06-Oct-26	13-Oct-26
A186870	Install Doors & Hardware - D-1 PG Nursing	4d	4d	14-Oct-26	19-Oct-26
A186910	Construction Clean - D-1 PG Nursing	2d	2d	20-Oct-26	21-Oct-26
Post Grad Cosmetology					
A186370	In-Wall Elect Rough - D-1 PG Cosmo	15d	15d	13-Mar-26	02-Apr-26
A186390	In-Wall Plumbing Rough - D-1 PG Cosmo	20d	20d	13-Mar-26	09-Apr-26
A186380	In-Wall HVAC Piping Rough - D-1 PG Cosmo	5d	5d	18-Mar-26	24-Mar-26
A186400	Frame Hard Ceilings @ Bathrooms - D-1 PG Cosmo	2d	2d	20-Mar-26	23-Mar-26
A186410	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - D-1 PG Cosmo	2d	2d	24-Mar-26	25-Mar-26
A186420	Drywall / Tape & Sands Ceiling @ Bathrooms - D-1 PG Cosmo	4d	4d	26-Mar-26	31-Mar-26
A186430	In-Wall Elect & Plumb Inspection - D-1 PG Cosmo	10d	10d	10-Apr-26	24-Apr-26
A186440	Insulate Mech Piping - D-1 PG Cosmo	5d	5d	27-Apr-26	01-May-26
A186450	In-Wall Building Inspection - D-1 PG Cosmo	5d	5d	04-May-26	08-May-26
A186460	Insulate / Drywall / Tape & Sands Walls - D-1 PG Cosmo	20d	20d	12-Jun-26	09-Jul-26
A186470	Prime & First Coat Paint Walls & Ceilings - D-1 PG Cosmo	6d	6d	10-Jul-26	17-Jul-26
A186480	Install ACT Grid - D-1 PG Cosmo	3d	3d	20-Jul-26	22-Jul-26
A186510	Install OH Lights Into Grid - D-1 PG Cosmo	2d	2d	23-Jul-26	24-Jul-26
A186500	Install OH MEP Drops Into Grid - D-1 PG Cosmo	5d	5d	23-Jul-26	29-Jul-26
A186520	OH Inspections - D-1 PG Cosmo	5d	5d	30-Jul-26	05-Aug-26
A186530	Install Ceiling Tiles - D-1 PG Cosmo	6d	6d	06-Aug-26	13-Aug-26

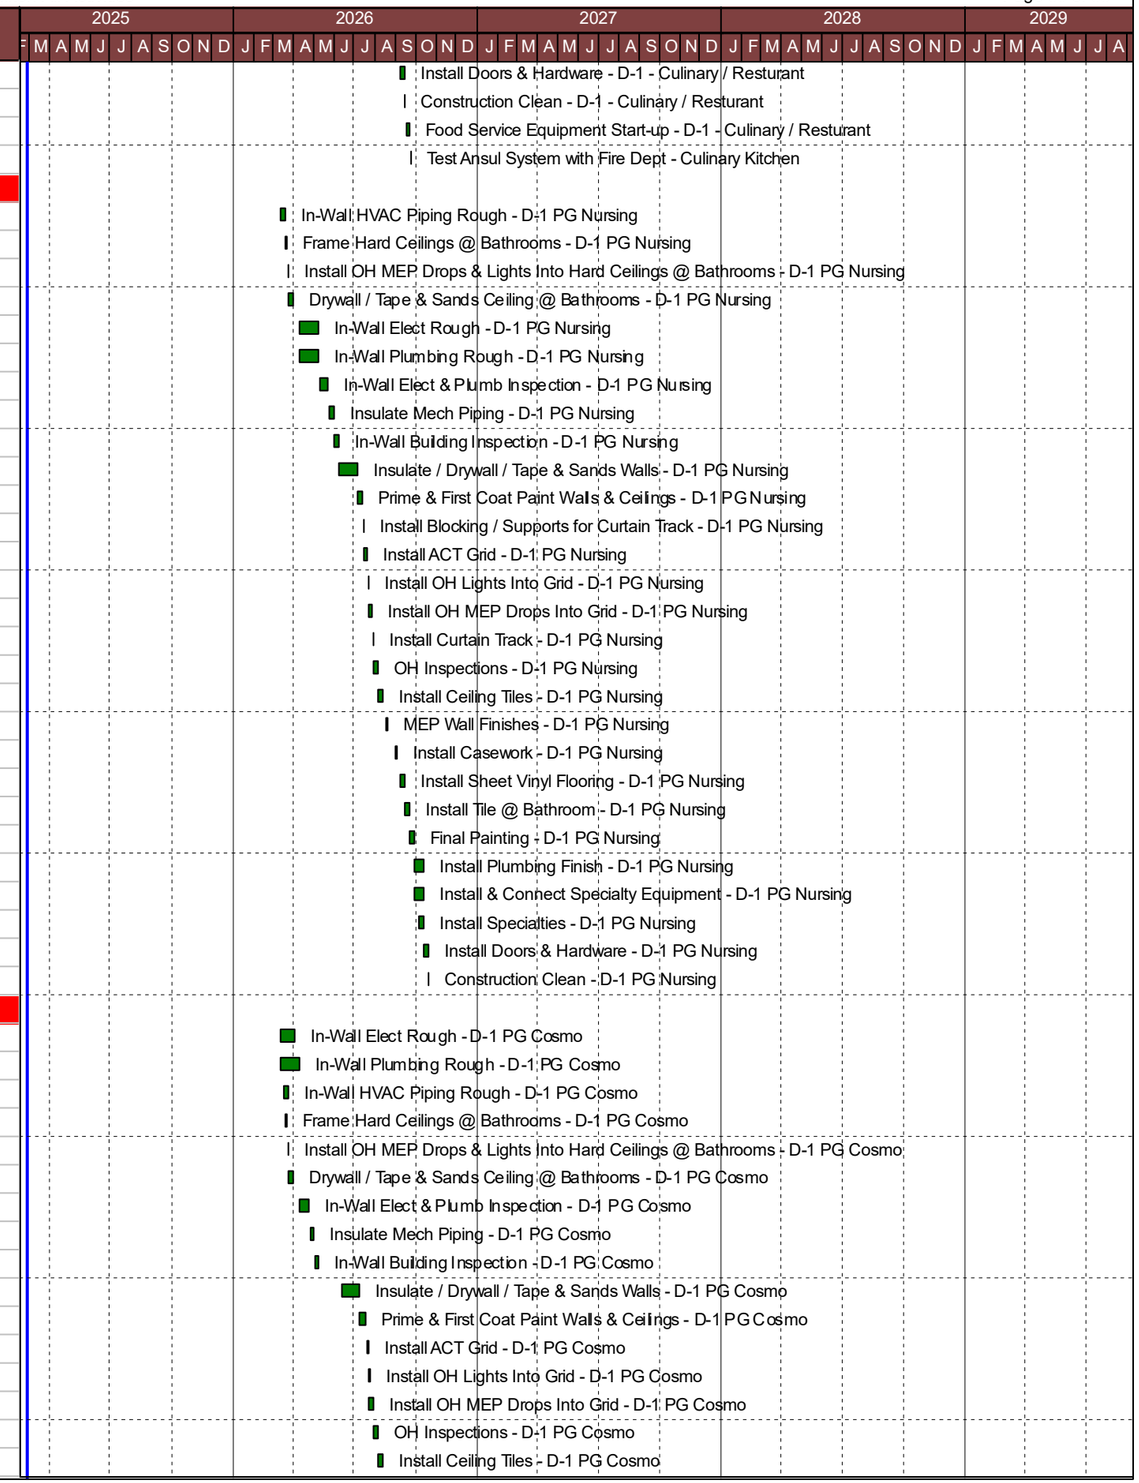

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A186540	Install Tile @ Bathroom - D-1 PG Cosmo	5d	5d	14-Aug-26	20-Aug-26
A186560	Install Storefront - D-1 PG Cosmo	5d	5d	14-Aug-26	20-Aug-26
A186490	MEP Wall Finishes - D-1 PG Cosmo	5d	5d	21-Aug-26	27-Aug-26
A186550	Install Casework - D-1 PG Cosmo	5d	5d	08-Sep-26	14-Sep-26
A186570	Install Sheet Vinyl Flooring - D-1 PG Cosmo	7d	7d	15-Sep-26	23-Sep-26
A186610	Install Plumbing Finish - D-1 PG Cosmo	10d	10d	24-Sep-26	07-Oct-26
A186580	Final Painting - D-1 PG Cosmo	4d	4d	08-Oct-26	14-Oct-26
A186600	Install Specialties / Lockers - D-1 PG Cosmo	5d	5d	15-Oct-26	21-Oct-26
A186620	Install & Connect Specialty Equipment - D-1 PG Cosmo	10d	10d	15-Oct-26	28-Oct-26
A186590	Install Doors & Hardware - D-1 PG Cosmo	4d	4d	23-Oct-26	28-Oct-26
A186630	Construction Clean - D-1 PG Cosmo	2d	2d	29-Oct-26	30-Oct-26
Building E					
2nd Floor					
A187380	Install Control - E-2	2d	2d	23-Sep-25	24-Sep-25
A187390	Layout & Install Wall Clips - E-2	10d	10d	25-Sep-25	08-Oct-25
A187400	Install Hangers - E-2	5d	5d	28-Nov-25	04-Dec-25
A187410	Patch Spray Fireproofing - E-2	3d	3d	05-Dec-25	09-Dec-25
A187420	OH Duct Rough - E-2	20d	20d	22-Jan-26	19-Feb-26
A187430	OH HVAC Piping Rough - E-2	20d	20d	22-Jan-26	19-Feb-26
A187440	OH Plumbing Rough - E-2	15d	15d	29-Jan-26	19-Feb-26
A187480	OH Sprinkler Rough - E-2	10d	10d	05-Feb-26	19-Feb-26
A187470	OH Elect / Fire Alarm Rough - E-2	15d	15d	05-Feb-26	26-Feb-26
A187460	Install Door Frames - E-2	5d	5d	12-Feb-26	19-Feb-26
A187450	Frame & Top Off Walls - E-2	10d	10d	12-Feb-26	26-Feb-26
A192430	OH AV / Telcom / Low Voltage Rough - E-2	15d	15d	27-Feb-26	19-Mar-26
A187490	In-Wall MEP Rough - E-2	20d	20d	27-Feb-26	26-Mar-26
A187500	Install Signage - E-2	2d	2d	22-Jul-26	23-Jul-26
A187790	Punchlist - E-2	10d	10d	23-Nov-26	07-Dec-26
A187800	Final Cleaning - E-2	2d	2d	26-Feb-27	01-Mar-27
Computer Information Systems					
A187520	In-Wall HVAC Piping Rough - E-2 CIS	5d	5d	27-Feb-26	05-Mar-26
A187510	In-Wall Elect Rough - E-2 CIS	20d	20d	27-Feb-26	26-Mar-26
A187550	Frame Hard Ceilings @ Bathrooms - E-2 CIS	2d	2d	20-Mar-26	23-Mar-26
A187560	Paint OH MEPs & Exposed Structure - E-2 CIS	2d	2d	20-Mar-26	23-Mar-26
A187580	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - E-2 CIS	2d	2d	24-Mar-26	25-Mar-26
A187590	Drywall / Tape & Sands Ceiling @ Bathrooms - E-2 CIS	4d	4d	26-Mar-26	31-Mar-26
A187530	In-Wall Elect Inspection - E-2 CIS	10d	10d	27-Mar-26	09-Apr-26
A187570	Insulate Mech Piping - E-2 CIS	5d	5d	10-Apr-26	16-Apr-26
A187620	In-Wall Building Inspection - E-2 CIS	5d	5d	17-Apr-26	24-Apr-26
A187640	Insulate / Drywall / Tape & Sands Walls - E-2 CIS	20d	20d	27-Apr-26	22-May-26
A187670	Prime & First Coat Paint Walls & Ceilings - E-2 CIS	6d	6d	26-May-26	02-Jun-26
A187540	Install ACT Grid - E-2 CIS	3d	3d	03-Jun-26	05-Jun-26
A187690	Spray Acoustic Insulation - E-2 CIS	3d	3d	03-Jun-26	05-Jun-26
A187610	Install OH Lights Into Grid - E-2 CIS	2d	2d	08-Jun-26	09-Jun-26
A187600	Install OH MEP Drops Into Grid - E-2 CIS	5d	5d	08-Jun-26	12-Jun-26
A187630	OH Inspections - E-2 CIS	5d	5d	15-Jun-26	19-Jun-26
A187650	Install Ceiling Tiles - E-2 CIS	6d	6d	22-Jun-26	29-Jun-26
A187700	Install Sheet Vinyl Flooring - E-2 CIS	4d	4d	30-Jun-26	03-Jul-26
A187680	MEP Wall Finishes - E-2 CIS	5d	5d	30-Jun-26	06-Jul-26
A187720	Install Tile @ Bathroom - E-2 CIS	5d	5d	06-Jul-26	10-Jul-26

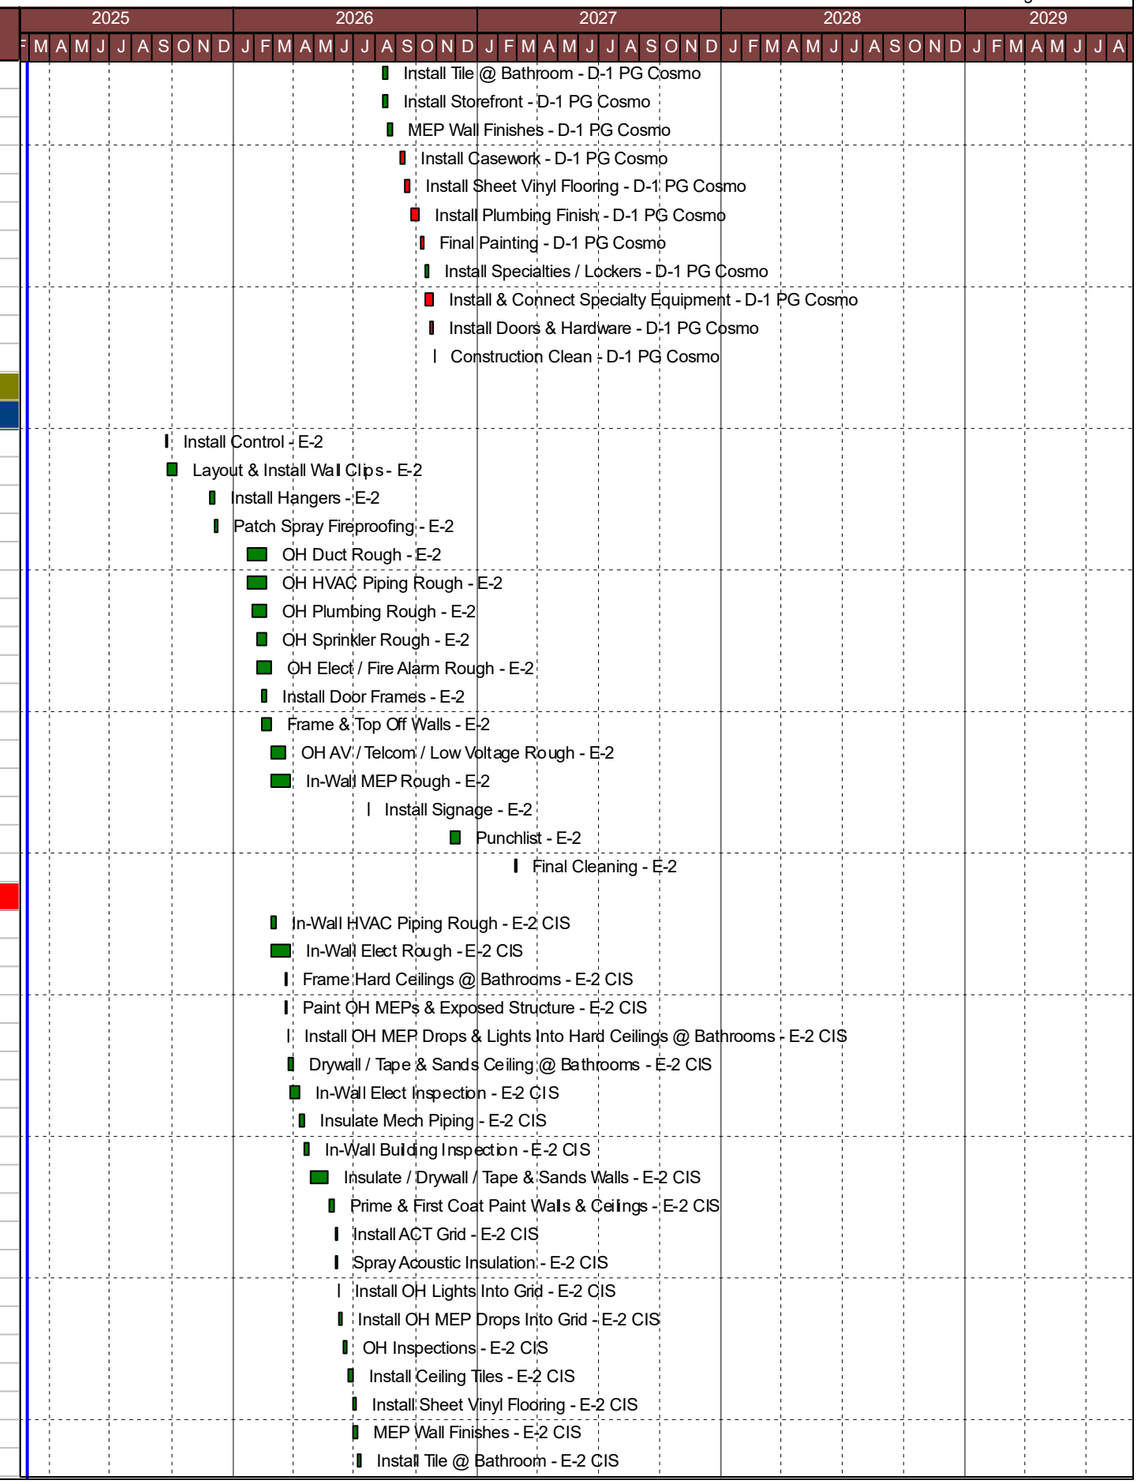

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A187710	Final Painting - E-2 CIS	4d	4d	07-Jul-26	10-Jul-26
A187760	Install Doors & Hardware - E-2 CIS	4d	4d	13-Jul-26	16-Jul-26
A187770	Install Specialties / Lockers - E-2 CIS	4d	4d	13-Jul-26	16-Jul-26
A187740	Install Plumbing Finish - E-2 CIS	5d	5d	13-Jul-26	17-Jul-26
A187660	Install Casework / Cubbies - E-2 CIS	5d	5d	13-Aug-26	19-Aug-26
A187780	Construction Clean - E-2 CIS	2d	2d	20-Aug-26	21-Aug-26
Graphic Communications					
A187820	In-Wall HVAC Piping Rough - E-2 Graphics Comm	5d	5d	04-Mar-26	10-Mar-26
A187810	In-Wall Elect Rough - E-2 Graphics Comm	20d	20d	04-Mar-26	31-Mar-26
A187850	Frame Hard Ceilings @ Bathrooms - E-2 Graphics Comm	2d	2d	20-Mar-26	23-Mar-26
A187860	Paint OH MEPs & Exposed Structure - E-2 Graphics Comm	2d	2d	20-Mar-26	23-Mar-26
A187880	Install OH MEP Drops & Lights Into Hard Ceilings @ Bathrooms - E-2 Graphics Comm	2d	2d	24-Mar-26	25-Mar-26
A187890	Drywall / Tape & Sands Ceiling @ Bathrooms - E-2 Graphics Comm	4d	4d	26-Mar-26	31-Mar-26
A187830	In-Wall Elect Inspection - E-2 Graphics Comm	5d	5d	01-Apr-26	07-Apr-26
A187870	Insulate Mech Piping - E-2 Graphics Comm	5d	5d	08-Apr-26	14-Apr-26
A187920	In-Wall Building Inspection - E-2 Graphics Comm	10d	10d	15-Apr-26	29-Apr-26
A187940	Insulate / Drywall / Tape & Sands Walls - E-2 Graphics Comm	20d	20d	30-Apr-26	28-May-26
A187970	Prime & First Coat Paint Walls & Ceilings - E-2 Graphics Comm	6d	6d	29-May-26	05-Jun-26
A187990	Spray Acoustic Insulation - E-2 Graphics Comm	3d	3d	08-Jun-26	10-Jun-26
A187840	Install ACT Grid - E-2 Graphics Comm	4d	4d	11-Jun-26	16-Jun-26
A187910	Install OH Lights Into Grid - E-2 Graphics Comm	2d	2d	17-Jun-26	18-Jun-26
A187900	Install OH MEP Drops Into Grid - E-2 Graphics Comm	5d	5d	17-Jun-26	23-Jun-26
A187930	OH Inspections - E-2 Graphics Comm	5d	5d	24-Jun-26	30-Jun-26
A187950	Install Ceiling Tiles - E-2 Graphics Comm	6d	6d	01-Jul-26	08-Jul-26
A188000	Install Sheet Vinyl Flooring - E-2 Graphics Comm	4d	4d	09-Jul-26	14-Jul-26
A188020	Install Tile @ Bathroom - E-2 Graphics Comm	5d	5d	15-Jul-26	21-Jul-26
A188070	Install Specialties / Lockers - E-2 Graphics Comm	4d	4d	22-Jul-26	27-Jul-26
A187980	MEP Wall Finishes - E-2 Graphics Comm	5d	5d	22-Jul-26	28-Jul-26
A188110	Install & Connect Specialties Equipment - E-2 Graphics Comm	5d	5d	28-Jul-26	03-Aug-26
A188010	Final Painting - E-2 Graphics Comm	4d	4d	29-Jul-26	03-Aug-26
A188060	Install Doors & Hardware - E-2 Graphics Comm	4d	4d	04-Aug-26	07-Aug-26
A188040	Install Plumbing Finish - E-2 Graphics Comm	5d	5d	04-Aug-26	10-Aug-26
A187960	Install Casework / Cubbies - E-2 Graphics Comm	5d	5d	20-Aug-26	26-Aug-26
A188080	Construction Clean - E-2 Graphics Comm	2d	2d	27-Aug-26	28-Aug-26
Mezzanine					
MDF Room - M110					
A188120	Set CMU Walls - MDF Rm M110	9d	9d	28-Nov-25	10-Dec-25
A188150	Paint Walls - MDF Rm M110	1d	1d	11-Dec-25	11-Dec-25
A188160	Overhead Finishes - MDF Rm M110	5d	5d	12-Dec-25	18-Dec-25
A188170	Set Racks & Other Equip - MDF Rm M110	5d	5d	19-Dec-25	26-Dec-25
A188180	Fitout Racks - MDF Rm M110	20d	20d	29-Dec-25	27-Jan-26
Elect - M111					
A22740	Set CMU Walls - Electric Room M111 - E-M	10d	10d	28-Nov-25	11-Dec-25
A22910	In-Wall Electric Rough - Electric Room M111 - E-M	10d	10d	02-Dec-25	15-Dec-25
A22760	FRP Housekeeping Pads - Electric Room M111 - E-M	5d	5d	12-Dec-25	18-Dec-25
A22750	Prime / First Coat Walls - Electric Room M111 - E-M	2d	2d	16-Dec-25	17-Dec-25
A22770	Set Main Switchgear - Electric Room M111 - E-M	30d	30d	22-Jun-26	31-Jul-26
A22780	Install Sub-Panels - Electric Room M111 - E-M	15d	15d	13-Jul-26	31-Jul-26
A22790	Pull Wires / Feeders to Panels / Gear - Electric Room M111 - E-M	10d	10d	03-Aug-26	14-Aug-26
A22800	Install OH Electric Rough (for Lighting / Power) - Electric Room M111 - E-M	10d	10d	03-Aug-26	14-Aug-26

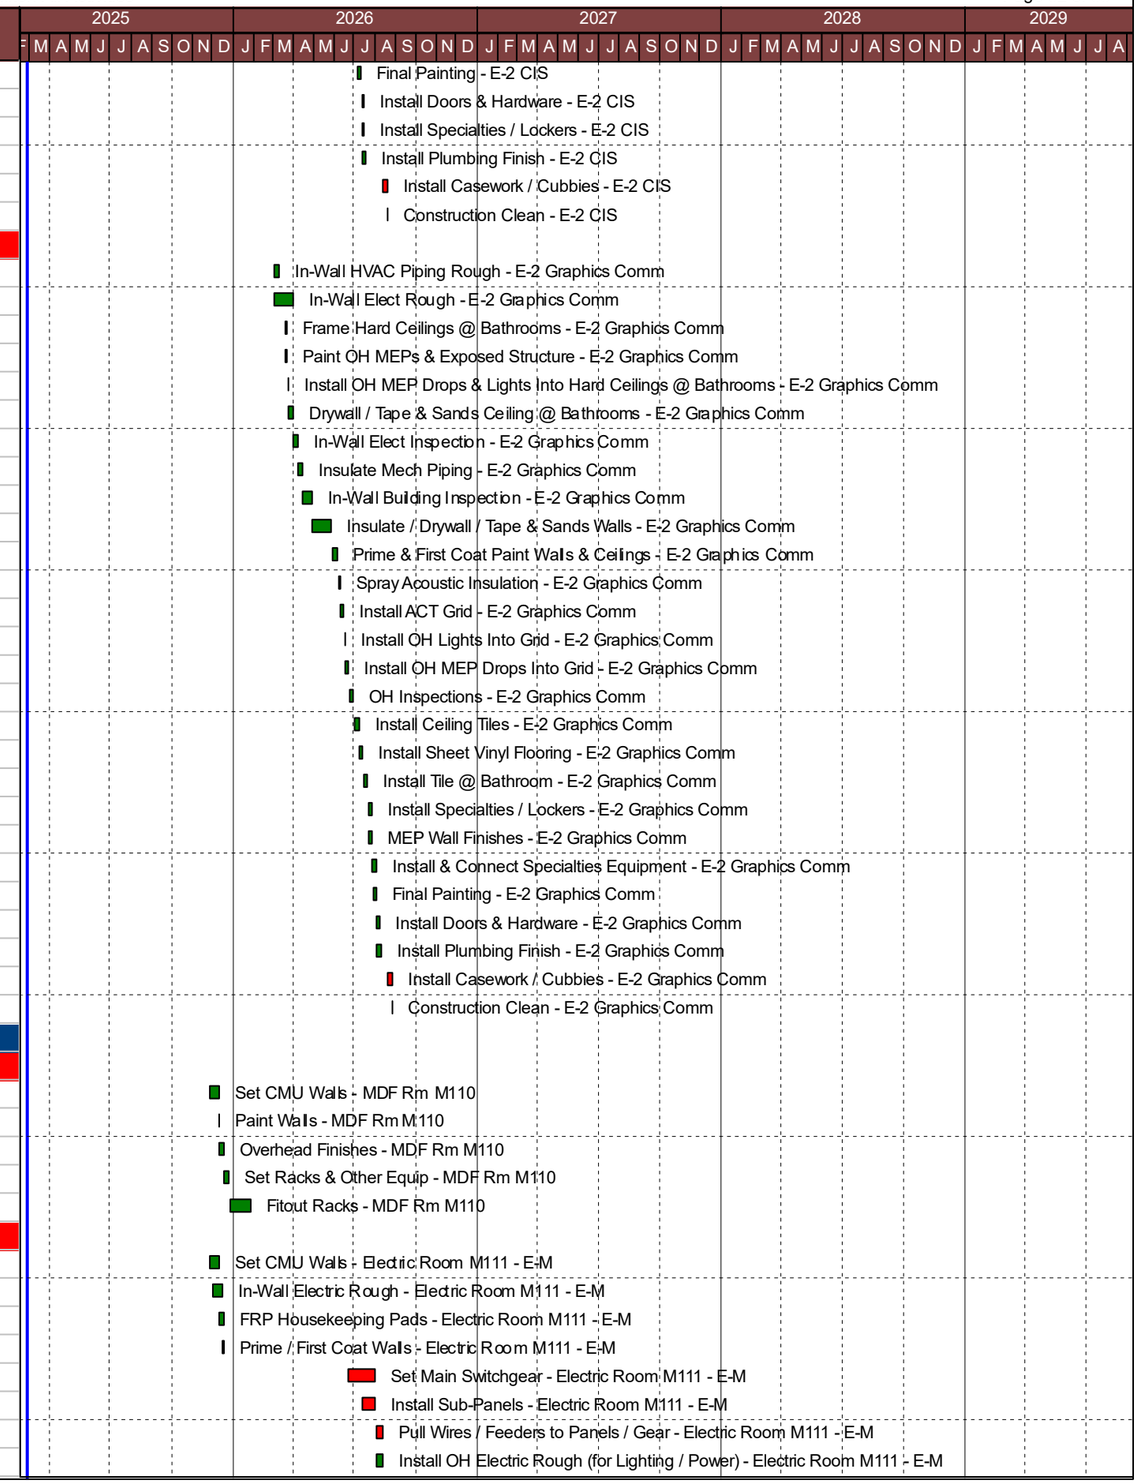

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A22810	Install Doors & Hardware - Electric Room M111 - E-M	2d	2d	17-Aug-26	18-Aug-26
A22820	National Grid Liven Transformers - Electric Room M111 - E-M	22d	22d	17-Aug-26	16-Sep-26
A22830	Final Paint - Electric Room M111 - E-M	2d	2d	17-Sep-26	18-Sep-26
A22840	Construction Clean - Electric Room M111 - E-M	2d	2d	21-Sep-26	22-Sep-26
A22850	Seal Floor - Electric Room M111 - E-M	3d	3d	21-Sep-26	23-Sep-26
A189080	Punchlist - Electric Room M111 - E-M	10d	10d	23-Sep-26	06-Oct-26
1st Floor					
A9140	CMU Interior Walls / Door Frames - Bldg E	15d	15d	02-Jul-25	23-Jul-25
A188640	Install Control - E-1	2d	2d	22-Oct-25	23-Oct-25
A23740	Layout & Install Wall Clips - E-1	10d	10d	29-Oct-25	12-Nov-25
A188660	Install Hangers - E-1	5d	5d	03-Dec-25	09-Dec-25
A188670	Patch Spray Fireproofing - E-1	3d	3d	10-Dec-25	12-Dec-25
A188680	OH Duct Rough - E-1	20d	20d	20-Feb-26	19-Mar-26
A188690	OH HVAC Piping Rough - E-1	20d	20d	20-Feb-26	19-Mar-26
A188700	OH Plumbing Rough - E-1	15d	15d	27-Feb-26	19-Mar-26
A188720	Install Door Frames - E-1	5d	5d	06-Mar-26	12-Mar-26
A188740	OH Sprinkler Rough - E-1	10d	10d	06-Mar-26	19-Mar-26
A188710	Frame & Top Off Walls - E-1	10d	10d	06-Mar-26	19-Mar-26
A188730	OH Elect / Fire Alarm Rough - E-1	15d	15d	06-Mar-26	26-Mar-26
A188750	In-Wall MEP Rough - E-1	20d	20d	20-Mar-26	16-Apr-26
A192440	OH AV / Telcom / Low Voltage Rough - E-1	15d	15d	27-Mar-26	16-Apr-26
A188760	Install Signage - E-1	2d	2d	30-Jul-26	31-Jul-26
A188400	Punchlist - E-1	10d	10d	08-Dec-26	21-Dec-26
A189020	Final Cleaning - E-1	2d	2d	02-Mar-27	03-Mar-27
Eng Tech Shop					
A188190	Install Sound Ceiling [Mezz] - E-1 - Eng Tech Shop	10d	10d	15-Dec-25	29-Dec-25
A188200	HVAC Equip [Mezz] - E-1 - Eng Tech Shop	5d	5d	30-Dec-25	06-Jan-26
A188210	Install Stair / Railings [Mezz] - E-1 - Eng Tech Shop	4d	4d	07-Jan-26	12-Jan-26
A189570	Install ACT Grid - E-1 - Eng Tech Shop	2d	2d	17-Apr-26	21-Apr-26
A188220	OH Inspection - E-1 - Eng Tech Shop	5d	5d	17-Apr-26	24-Apr-26
A189580	Install OH MEP Drops Into Grid - E-1 - Eng Tech Shop	2d	2d	22-Apr-26	23-Apr-26
A189610	Install OH Lights Into Grid - E-1 - Eng Tech Shop	2d	2d	22-Apr-26	23-Apr-26
A189590	OH Inspections - E-1 - Eng Tech Shop	5d	5d	24-Apr-26	30-Apr-26
A188230	Drywall / Tape & Sands Ceiling @ Bathrooms- E-1 - Eng Tech Shop	5d	5d	27-Apr-26	01-May-26
A189600	Install Ceiling Tiles - E-1 - Eng Tech Shop	1d	1d	01-May-26	01-May-26
A188340	Insulate / Drywall / Tape & Sands Walls - E-1 - Eng Tech Shop	20d	20d	09-Jun-26	06-Jul-26
A188280	Paint Walls / Ceilings - E-1 - Eng Tech Shop	5d	5d	07-Jul-26	13-Jul-26
A188290	Install Epoxy Flooring - E-1 - Eng Tech Shop	7d	7d	14-Jul-26	22-Jul-26
A191010	Install Resilient Carpet - E-1 - Eng Tech Shop	5d	5d	23-Jul-26	29-Jul-26
A188330	Install Casework - E-1 - Eng Tech Shop	3d	3d	15-Sep-26	17-Sep-26
A188880	Install Linoleum Flooring - E-1 - Eng Tech Shop	5d	5d	18-Sep-26	24-Sep-26
A188350	Install Rubber Stair Treads - E-1 - Eng Tech Shop	1d	1d	25-Sep-26	25-Sep-26
A188300	HVAC Finishes - E-1 - Eng Tech Shop	2d	2d	25-Sep-26	28-Sep-26
A188320	Plumbing Finishes - E-1 - Eng Tech Shop	5d	5d	25-Sep-26	01-Oct-26
A188310	Electrical Finishes - E-1 - Eng Tech Shop	10d	10d	25-Sep-26	08-Oct-26
A188360	Install Toilet Accessories / Specialties - E-1 - Eng Tech Shop Bathrooms	1d	1d	02-Oct-26	02-Oct-26
A188850	Install Doors & Hardware - E-1 - Eng Tech Shop	2d	2d	09-Oct-26	13-Oct-26
A188380	Install & Connect Specialty Equipment - E-1 - Eng Tech Shop	10d	10d	09-Oct-26	23-Oct-26
A188390	Construction Clean - E-1 - Eng Tech Shop	1d	1d	26-Oct-26	26-Oct-26
Metal Fab Shop					

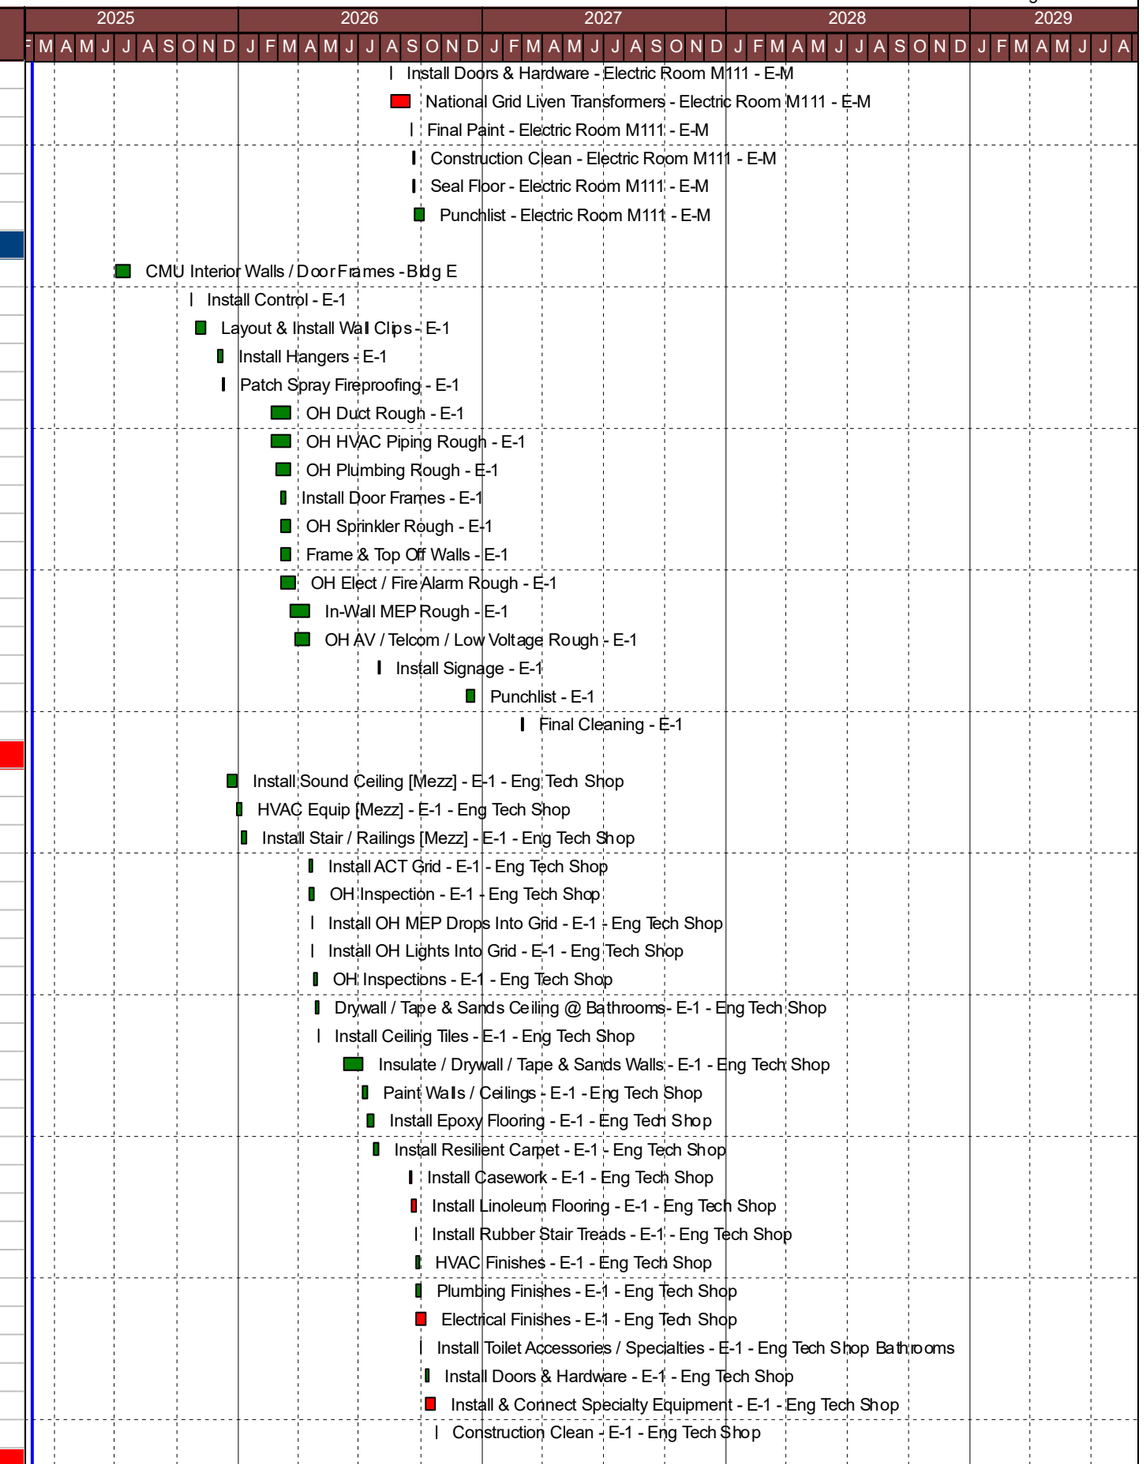

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A188410	Install Sound Ceiling [Mezz] - E-1 - Metal Fab Shop	10d	10d	30-Dec-25	13-Jan-26
A188420	HVAC Equip [Mezz] - E-1 - Metal Fab Shop	5d	5d	14-Jan-26	21-Jan-26
A188430	Install Stair / Railings [Mezz] - E-1 - Metal Fab Shop	4d	4d	22-Jan-26	27-Jan-26
A188440	OH Inspection - E-1 - Metal Fab Shop	5d	5d	17-Apr-26	24-Apr-26
A188460	FRP Locker Base - E-1 - Metal Fab Shop	2d	2d	27-Apr-26	28-Apr-26
A191020	Drywall / Tape & Sands Instructor Area- E-1 - Metal Fab Shop	10d	10d	05-Jun-26	18-Jun-26
A188450	Drywall / Tape & Sands Ceiling @ Bathrooms- E-1 - Metal Fab Shop	5d	5d	12-Jun-26	18-Jun-26
A188500	Paint Walls / Ceilings - E-1 - Metal Fab Shop	5d	5d	19-Jun-26	25-Jun-26
A189620	Install ACT Grid - E-1 - Metal Fab Shop	2d	2d	26-Jun-26	29-Jun-26
A189630	Install OH MEP Drops Into Grid - E-1 - Metal Fab Shop	2d	2d	30-Jun-26	01-Jul-26
A189660	Install OH Lights Into Grid - E-1 - Metal Fab Shop	2d	2d	30-Jun-26	01-Jul-26
A189640	OH Inspections - E-1 - Metal Fab Shop	5d	5d	02-Jul-26	08-Jul-26
A188510	Install Epoxy Flooring - E-1 - Metal Fab Shop	7d	7d	09-Jul-26	17-Jul-26
A189650	Install Ceiling Tiles - E-1 - Metal Fab Shop	1d	1d	20-Jul-26	20-Jul-26
A188830	Install Linoleum Flooring - E-1 - Metal Fab Shop	3d	3d	21-Jul-26	23-Jul-26
A188570	Install Rubber Stair Treads - E-1 - Metal Fab Shop	1d	1d	24-Jul-26	24-Jul-26
A188520	HVAC Finishes - E-1 - Metal Fab Shop	2d	2d	24-Jul-26	27-Jul-26
A188480	Install Lockers - E-1 - Metal Fab Shop	2d	2d	24-Jul-26	27-Jul-26
A188530	Electrical Finishes - E-1 - Metal Fab Shop	10d	10d	24-Jul-26	06-Aug-26
A188560	Frame / Sheath Workstation Cubbies & Training Wall - E-1 - Metal Fab Shop	10d	10d	24-Jul-26	06-Aug-26
A188860	Install Doors & Hardware - E-1 - Metal Fab Shop	2d	2d	07-Aug-26	10-Aug-26
A188600	Install & Connect Specialty Equipment - E-1 - Metal Fab Shop	10d	10d	07-Aug-26	20-Aug-26
A188840	Install & Connect Overhead Crane - E-1 - Metal Fab Shop	10d	10d	07-Aug-26	20-Aug-26
A188550	Install Casework - E-1 - Metal Fab Shop	3d	3d	18-Sep-26	22-Sep-26
A188540	Plumbing Finishes - E-1 - Metal Fab Shop	5d	5d	18-Sep-26	24-Sep-26
A188580	Install Toilet Accessories / Specialties - E-1 - Metal Fab Shop Bathrooms	1d	1d	25-Sep-26	25-Sep-26
A188610	Construction Clean - E-1 - Metal Fab Shop	1d	1d	28-Sep-26	28-Sep-26
Auto Tech Shop					
A188800	Install Sound Ceiling [Mezz] - E-1 - Auto Tech	10d	10d	14-Jan-26	28-Jan-26
A188810	HVAC Equip [Mezz] - E-1 - Auto Tech	5d	5d	29-Jan-26	04-Feb-26
A188820	Install Stair / Railings [Mezz] - E-1 - Auto Tech	4d	4d	05-Feb-26	10-Feb-26
A188770	Paint OH MEPs - E-1 - Auto Tech	11d	11d	17-Apr-26	04-May-26
A183510	Install K-13 Ceiling - E-1 - Auto Tech	5d	5d	05-May-26	11-May-26
A21480	Board / Tape / Sand - E-1 - Auto Tech	5d	5d	10-Jun-26	16-Jun-26
A21490	Prime / First Coat Walls - E-1 - Auto Tech	5d	5d	17-Jun-26	23-Jun-26
A189670	Install ACT Grid - E-1 - Auto Tech	2d	2d	30-Jun-26	01-Jul-26
A189680	Install OH MEP Drops Into Grid - E-1 - Auto Tech	2d	2d	02-Jul-26	03-Jul-26
A189710	Install OH Lights Into Grid - E-1 - Auto Tech	2d	2d	02-Jul-26	03-Jul-26
A189690	OH Inspections - E-1 - Auto Tech	5d	5d	06-Jul-26	10-Jul-26
A21510	Install Epoxy Flooring - Auto Tech	10d	10d	13-Jul-26	24-Jul-26
A189700	Install Ceiling Tiles - E-1 - Auto Tech	1d	1d	27-Jul-26	27-Jul-26
A188890	Install Linoleum Flooring - E-1 - Auto Tech	2d	2d	28-Jul-26	29-Jul-26
A21550	Install Lockers - E-1 - Auto Tech	2d	2d	30-Jul-26	31-Jul-26
A21560	Install Plumbing Fixtures - E-1 - Auto Tech	5d	5d	30-Jul-26	05-Aug-26
A21520	Install Auto Lifts & Equipment - E-1 - Auto Tech	10d	10d	30-Jul-26	12-Aug-26
A21500	MEP Drops to Equipment / Lighting - E-1 - Auto Tech	10d	10d	12-Aug-26	25-Aug-26
A21530	Final Connections to Equipment - E-1 - Auto Tech	10d	10d	12-Aug-26	25-Aug-26
A21590	Final Paint - E-1 - Auto Tech	5d	5d	26-Aug-26	01-Sep-26
A188870	Install Doors & Hardware - E-1 - Auto Tech	2d	2d	02-Sep-26	03-Sep-26
A21580	Construction Clean - E-1 - Auto Tech	1d	1d	04-Sep-26	04-Sep-26

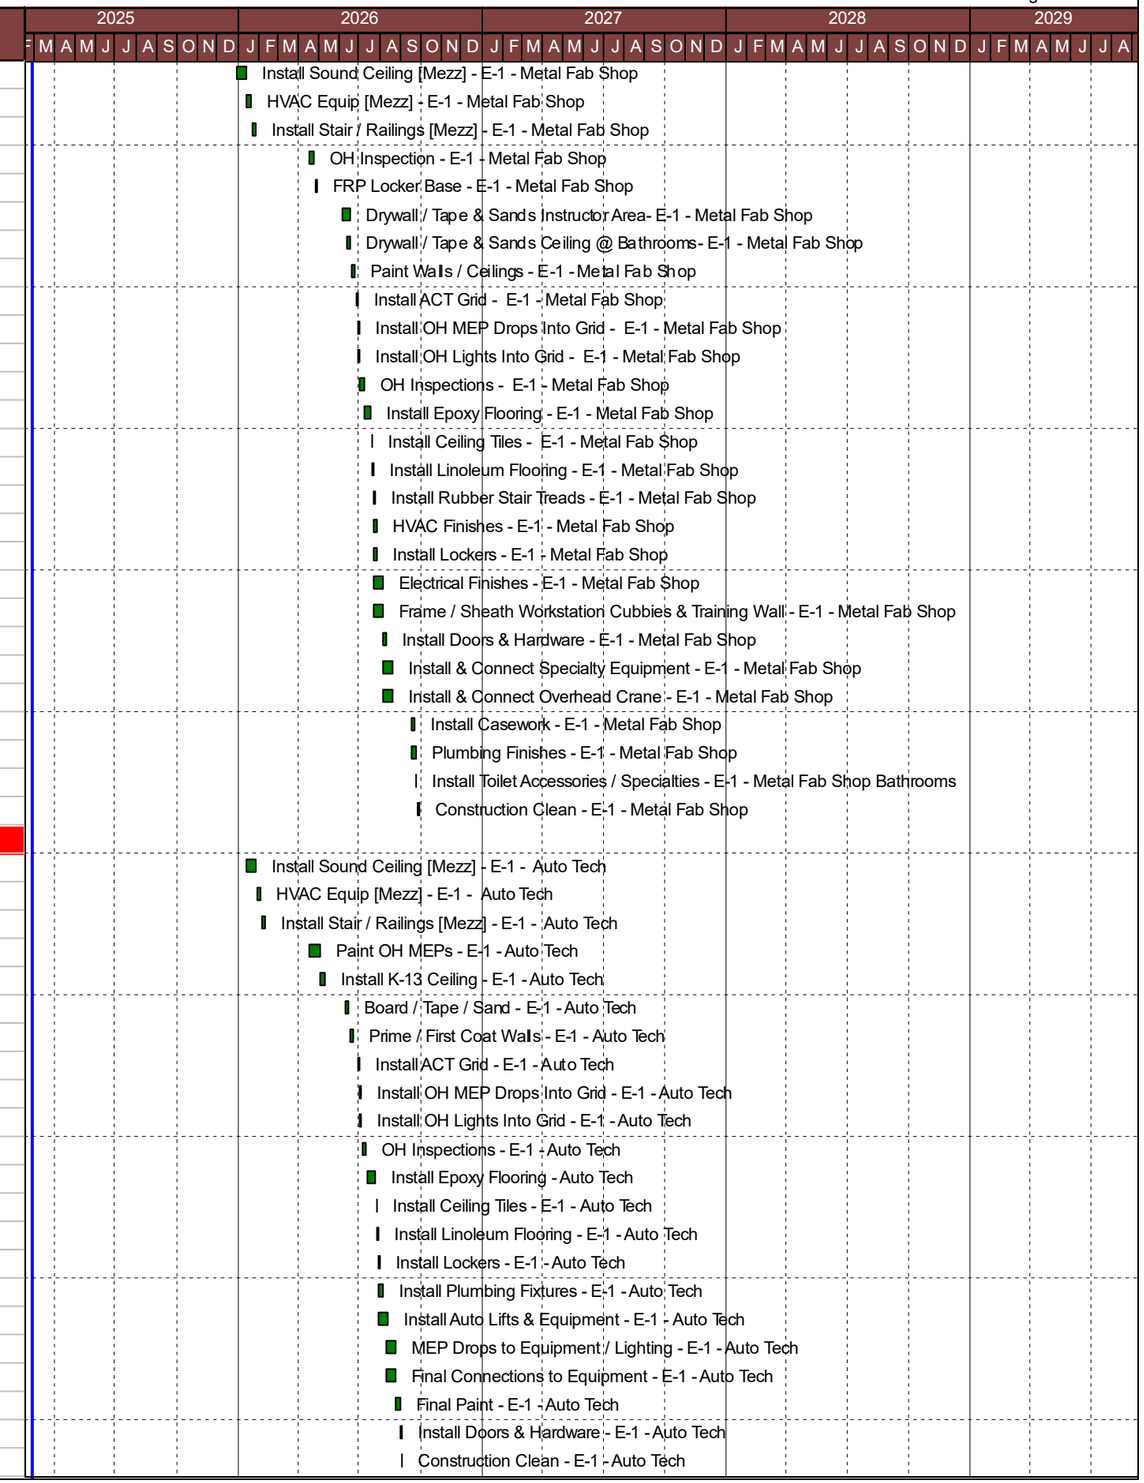

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
Vertical Circulation					
Elevators					
Elevator 1 - Bldg A					
A7870	Install CMU Shaft - Elevator 1 - Bldg A	15d	15d	02-Jul-25	23-Jul-25
A7890	Install Hoist Beam - Elevator 1 - Bldg A	3d	3d	24-Jul-25	28-Jul-25
A7840	Install Elevator 1 - Bldg A	30d	30d	14-Apr-26	27-May-26
Elevator 2 - Bldg D					
A23870	Install CMU Shaft - Elevator 2 - Bldg D	15d	15d	24-Jul-25	13-Aug-25
A23890	Install Hoist Beam - Elevator 2 - Bldg D	3d	3d	14-Aug-25	18-Aug-25
A23880	Install Elevator 2 - Bldg D	30d	30d	28-May-26	08-Jul-26
Generator					
A192580	FRP Pad for Generator	7d	7d	13-May-26	21-May-26
A192570	Set Generator	0d	0d	22-May-26	
Site Finishes - Around Building - Phase 1					
A192130	Complete Shallow Utilities	20d	20d	04-May-26	01-Jun-26
A192150	Install Bollard, Light Pole Bases, Misc Site Footings	15d	15d	02-Jun-26	22-Jun-26
A192160	Install UG Electric for Site Finishes	15d	15d	23-Jun-26	13-Jul-26
A192140	Subgrade	30d	30d	14-Jul-26	24-Aug-26
A192190	Install Balance of Site Binder	10d	10d	25-Aug-26	08-Sep-26
A192170	Install Curbing	20d	20d	09-Sep-26	06-Oct-26
A192180	FRP Concrete Sidewalks & Vehicular Concrete	50d	50d	07-Oct-26	18-Dec-26
A192200	Loam & Seed	20d	20d	05-Apr-27*	03-May-27
A192210	Install Trees & Shrubs	20d	20d	04-May-27	01-Jun-27
A192220	Final Paving & Striping	7d	7d	02-Jun-27	10-Jun-27
Site Finishes - Courtyard					
A192230	Install Shallow UG Utilities - Courtyard	15d	15d	28-Sep-26	19-Oct-26
A192240	Subgrade - Courtyard	10d	10d	20-Oct-26	02-Nov-26
A192250	Footing for Deck & Benches - Courtyard	15d	15d	03-Nov-26	24-Nov-26
A192270	Place Sidewalks - Courtyard	15d	15d	03-Nov-26	24-Nov-26
A192260	Install Deck - Courtyard	20d	20d	25-Nov-26	23-Dec-26
A192280	Loam - Courtyard	10d	10d	05-Apr-27*	16-Apr-27
A192310	Install Site Finishes - Courtyard	5d	5d	20-Apr-27	26-Apr-27
A192290	Trees / Shrubs - Courtyard	10d	10d	27-Apr-27	10-May-27
A192300	Seed Loam Areas - Courtyard	5d	5d	11-May-27	17-May-27
New Building Closeout					
A4170	Equipment Start Up	80d	80d	28-Sep-26	25-Jan-27
A4180	Testing & Balancing	80d	80d	07-Jan-27	03-May-27
A4200	Low Voltage Start-up / Programming / Testing	40d	40d	08-Mar-27	03-May-27
A4190	Final Inspections	50d	50d	04-May-27	14-Jul-27
Occupancy					
A1990	Owner Move-In	30d	30d	15-Jul-27	25-Aug-27
Phase 3: Geothermal Wells					
A10780	Strip Existing Football Field for Geothermal	15d	0d	06-Jan-25 A	17-Jan-25 A
A10730	Install Geothermal Wells (150 @ 600' - 2 Rigs, .75 well / rig / day)	100d	100d	20-Mar-25	11-Aug-25
A10740	Install Geothermal Vault	6d	6d	09-Jun-25	16-Jun-25
A10750	Install Lateral Mains from Vault to Building - Geothermal	43d	43d	17-Jun-25	15-Aug-25
A10250	Install Lateral Circuits - Geothermal	46d	46d	20-Jun-25	25-Aug-25
A10760	Install Manifold Inside Building - Geothermal	10d	10d	15-Sep-25	26-Sep-25
A10770	Testing - (Pressure Test, Fill, Flush, Glycol & DI) - Geothermal	15d	15d	29-Sep-25	20-Oct-25
Phase 3: Fields - Track / Soccer Field (Northwest)					

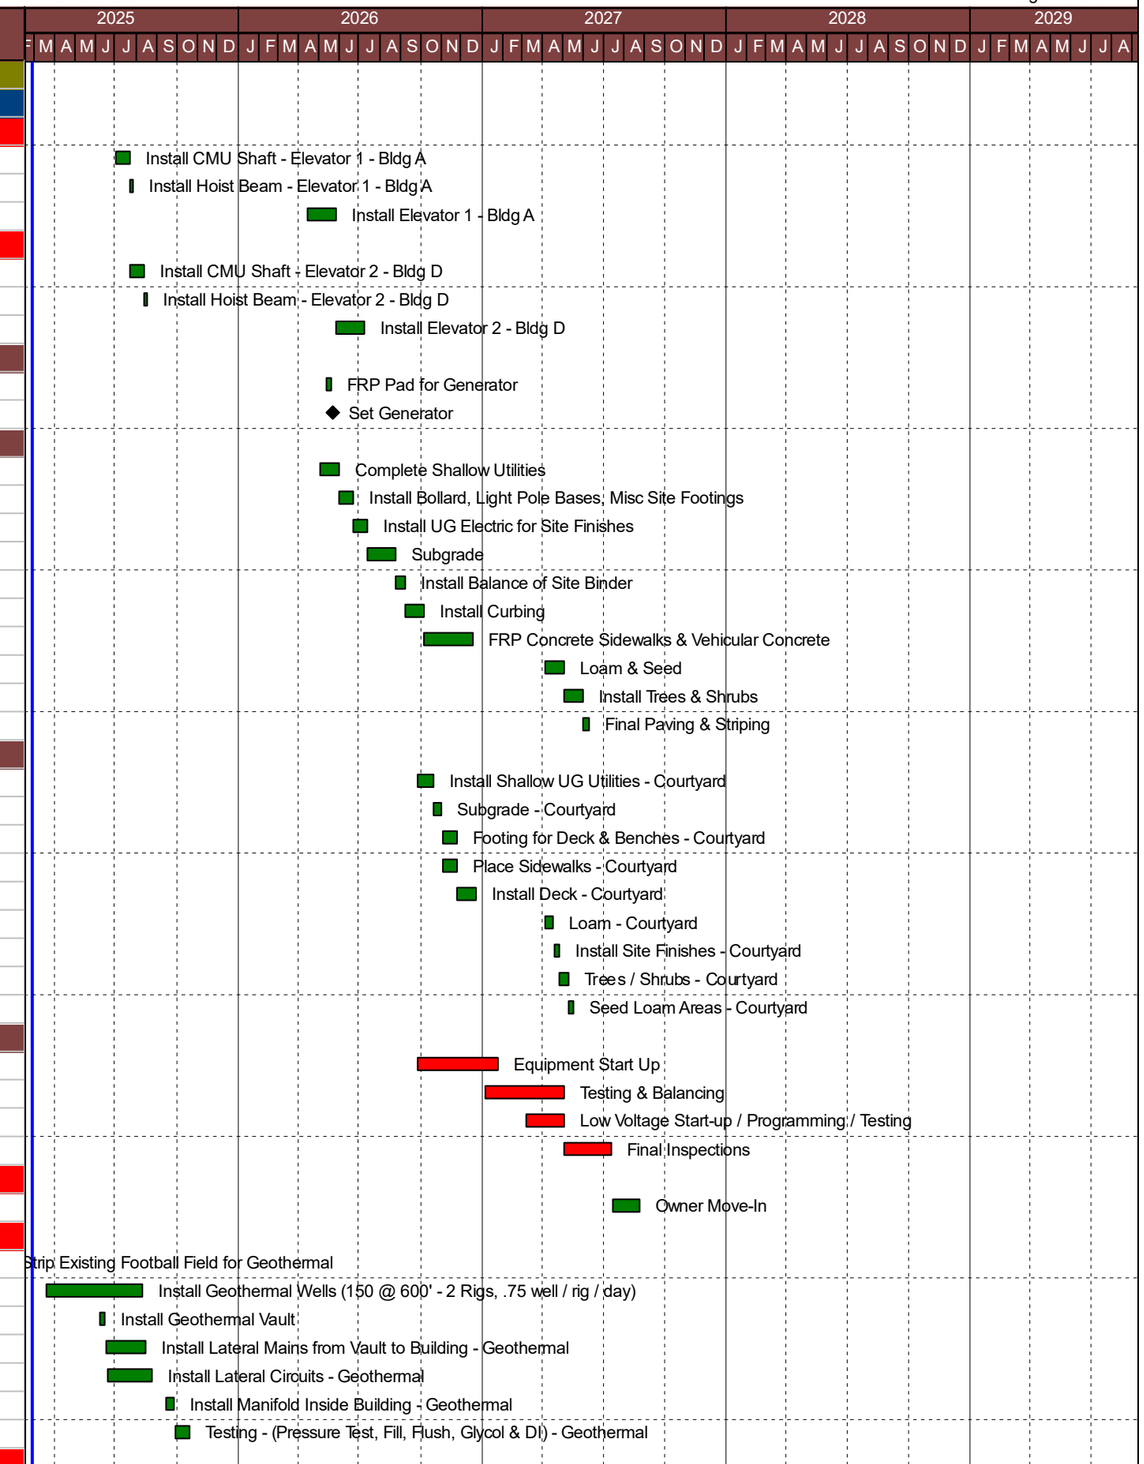

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A191050	Infill and Subgrade, Track / Soccer Field NW	10d	10d	26-Aug-25	09-Sep-25
A191080	Install Under-Field Drainage, Track / Soccer Field NW	20d	20d	26-Aug-25	23-Sep-25
A191870	Install Perimeter Trench Drain, Track / Soccer Field NW	20d	20d	26-Aug-25	23-Sep-25
A191920	Install Block Retaining Wall, Track / Soccer Field NW	5d	5d	10-Sep-25	16-Sep-25
A191960	Install Irrigation Piping, Track / Soccer Field NW	5d	5d	10-Sep-25	16-Sep-25
A191970	Install Irrigation Control Conduit and Scoreboard, Track / Soccer Field NW	10d	10d	10-Sep-25	23-Sep-25
A191900	Install Concrete Pad for Bleachers, Track / Soccer Field NW	5d	5d	17-Sep-25	23-Sep-25
A191930	Install & Rough Light Pole Footings, Track / Soccer Field NW	5d	5d	17-Sep-25	23-Sep-25
A191090	Binder Tracks, Track / Soccer Field NW	10d	10d	24-Sep-25	07-Oct-25
A191150	Install Filter Fabric and Flat Drain, Track / Soccer Field NW	11d	11d	24-Sep-25	08-Oct-25
A49990	Install Sand Base, Track / Soccer Field NW	11d	11d	01-Oct-25	16-Oct-25
A191190	Install Athletic Top Soil, Track / Soccer Field NW	10d	10d	08-Oct-25	22-Oct-25
A191880	Install Stone Dust at Long Jump & Shot Put Pits, Track / Soccer Field NW	2d	2d	09-Oct-25	10-Oct-25
A191210	Resilient Track Surfacing, Track / Soccer Field NW	10d	10d	16-Oct-25	29-Oct-25
A191220	Install Sod, Track / Soccer Field NW	5d	5d	23-Oct-25	29-Oct-25
A191910	Install Bleachers, Track / Soccer Field NW	4d	4d	30-Oct-25	04-Nov-25
A191940	Install Light Poles , Track / Soccer Field NW	4d	4d	30-Oct-25	04-Nov-25
A191890	Install Fence, Track / Soccer Field NW	5d	5d	30-Oct-25	05-Nov-25
A7680	Field Germination, Track / Soccer Field NW	130d	130d	30-Oct-25	08-May-26
A191950	Field Striping, Track / Soccer Field NW	2d	2d	11-May-26	12-May-26
A191230	Install Nets, Track / Soccer Field NW	3d	3d	13-May-26	15-May-26
Phase 4: Fields - Multi-Purpose (Northeast)					
A7460	School Ends	0d	0d	22-Jun-26*	
A7470	Set Up Temp Fence @ Future Softball Field	10d	10d	22-Jun-26	03-Jul-26
A7480	Rough Grade & Build Softball Field	50d	50d	06-Jul-26	14-Sep-26
Phase 5: Demolition					
A5920	School End	0d	0d	24-Jun-27*	
A4260	Demo & Abatement	120d	120d	24-Jun-27	15-Dec-27
Phase 5: Football / Baseball / Parking					
A7510	Install Remaining Infiltration Basins and Complete Site Drainage	5d	5d	24-Jun-27	30-Jun-27
A7490	Build Access Road to New Building	15d	15d	24-Jun-27	15-Jul-27
A7520	Complete Remaining Fields (Football, Baseball & Multipurpose)	245d	245d	23-Aug-27	10-Aug-28
Baseball					
A191250	Subgrade and Install Collector Drain, Baseball	18d	18d	21-Jun-27	15-Jul-27
A191290	Install Irrigation Piping, Baseball	5d	5d	16-Jul-27	22-Jul-27
A191300	Install Irrigation Control Conduit, Baseball	10d	10d	16-Jul-27	29-Jul-27
A191260	Prep. for Dugouts, Walkways, etc., Baseball	10d	10d	20-Jul-27	02-Aug-27
A50170	Install Filter Fabric and Flat Drain, Baseball	11d	11d	23-Jul-27	06-Aug-27
A191310	Install Sand Base, Baseball	11d	11d	23-Jul-27	06-Aug-27
A191270	F/R/P/S Concrete Dugouts, Baseball	5d	5d	03-Aug-27	09-Aug-27
A191320	Install Asphalt Walkways, Baseball	2d	2d	06-Aug-27	09-Aug-27
A50190	Install all Fence Posts, Baseball	10d	10d	10-Aug-27	23-Aug-27
A191370	Install Athletic Dirt at Infield and Warning Track, Baseball	12d	12d	11-Aug-27	26-Aug-27
A191340	Install Athletic Top Soil, Baseball	15d	15d	11-Aug-27	31-Aug-27
A50310	Install Dugouts, Baseball	1d	1d	16-Aug-27	16-Aug-27
A50320	Install Fence Fabric and Sports Netting, Baseball	12d	12d	17-Aug-27	01-Sep-27
A191350	Install Foundations for Bases, Benches, Field Markers, etc., Baseball	5d	5d	24-Aug-27	30-Aug-27
A50330	Install Batting Cages, Bleachers, Bullpens, Baseball	7d	7d	24-Aug-27	01-Sep-27
A191390	Install Stone Trench Drain, Baseball	5d	5d	27-Aug-27	02-Sep-27
A191400	Install Foul Poles, Baseball	1d	1d	01-Sep-27	01-Sep-27

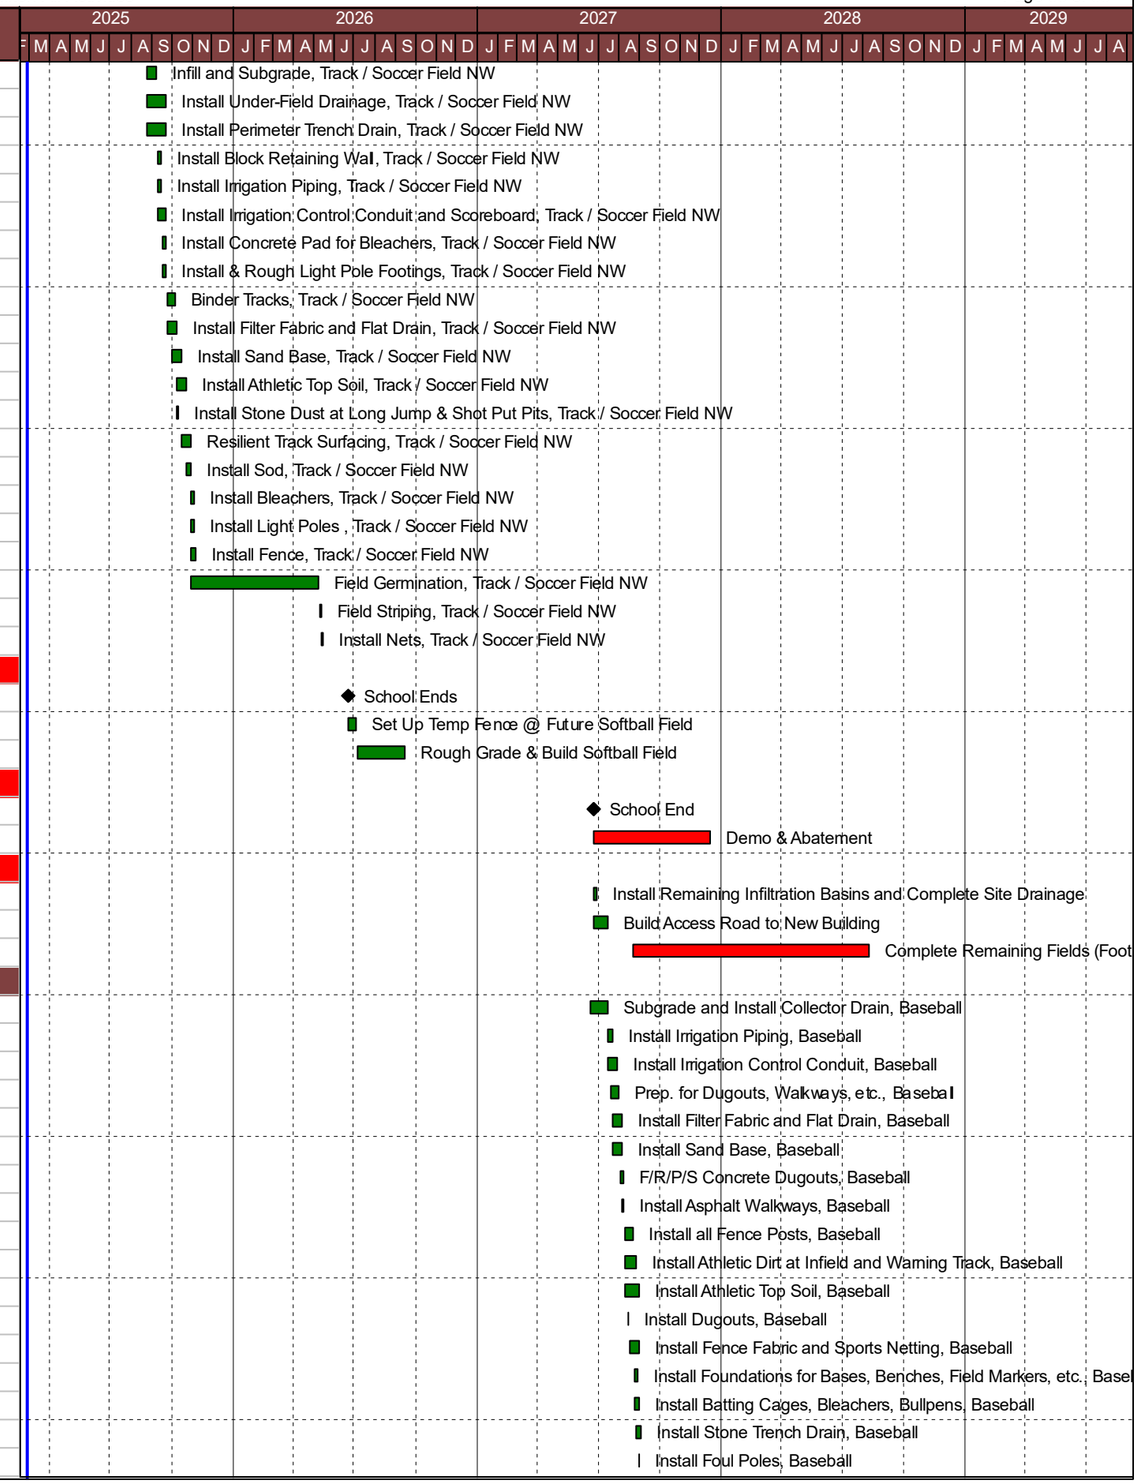

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A50360	Install Benches, Bases, Field Markers, etc., Baseball	2d	2d	02-Sep-27	03-Sep-27
A191420	Install Sod, Baseball	7d	7d	02-Sep-27	13-Sep-27
A191410	Install Sprinkler Heads, Baseball	5d	5d	03-Sep-27	10-Sep-27
Football					
A191440	Infill and Subgrade, Football	10d	10d	16-Dec-27	29-Dec-27
A191470	Install Collector Drain, Football	20d	20d	16-Dec-27	12-Jan-28
A191520	Install Irrigation Piping, Football	5d	5d	30-Dec-27	05-Jan-28
A191740	Install Segmented Retaining Wall, Football	10d	10d	30-Dec-27	12-Jan-28
A191480	Prep. Asphalt Walkways, Football	10d	10d	13-Jan-28	27-Jan-28
A191500	Install Irrigation Control, Scoreboard, & Lighting Conduit, Football	10d	10d	28-Jan-28	10-Feb-28
A191660	FRP Pad / Foundations for Bleachers, Press Box & Ramps, Football	15d	15d	28-Jan-28	17-Feb-28
A191490	Install all Fence Posts, Football	10d	10d	11-Feb-28	25-Feb-28
A191690	Install Press Box Framing & Structure, Football	15d	15d	18-Feb-28	10-Mar-28
A191530	Install Scoreboard and Field Marker Footings, Football	2d	2d	28-Feb-28	29-Feb-28
A191590	Install Scoreboard, Football	1d	1d	01-Mar-28	01-Mar-28
A191550	Install Filter Fabric and Flat Drain, Football	11d	11d	02-Mar-28	16-Mar-28
A191560	Install Sand Base, Football	11d	11d	02-Mar-28	16-Mar-28
A191700	MEP Rough Press Box, Football	10d	10d	13-Mar-28	24-Mar-28
A191680	Install Bleachers, Football	20d	20d	13-Mar-28	07-Apr-28
A191600	Install Athletic Top Soil, Football	10d	10d	17-Mar-28	30-Mar-28
A191710	Finishes Press Box, Football	15d	15d	27-Mar-28	14-Apr-28
A191610	Install Mow Strip, Football	2d	2d	03-Apr-28	04-Apr-28
A191620	Install Sprinkler Heads, Football	5d	5d	05-Apr-28	11-Apr-28
A191980	Pave Walkways, Football	5d	5d	18-Apr-28	24-Apr-28
A191540	Install Fence Fabric and Sports Netting, Football	10d	10d	25-Apr-28	08-May-28
A191630	Install Sod, Football	5d	5d	09-May-28	15-May-28
A191640	Install Nets, Football	3d	3d	16-May-28	18-May-28
Multi-Purpose					
A191650	Infill and Subgrade, Multi-Purpose	10d	10d	13-Jan-28	27-Jan-28
A191670	Install Collector Drain, Multi-Purpose	20d	20d	13-Jan-28	10-Feb-28
A191730	Install all Fence Posts, Multi-Purpose	10d	10d	11-Feb-28	25-Feb-28
A191720	Install Filter Fabric and Flat Drain, Multi-Purpose	11d	11d	28-Feb-28	13-Mar-28
A191770	Install Sand Base, Multi-Purpose	11d	11d	28-Feb-28	13-Mar-28
A191810	Install Athletic Top Soil, Multi-Purpose	10d	10d	14-Mar-28	27-Mar-28
A191840	Install Hyrdo-Seed, Multi-Purpose	5d	5d	28-Mar-28	03-Apr-28
A191790	Install Fence Fabric and Sports Netting, Multi-Purpose	10d	10d	28-Mar-28	10-Apr-28
A191850	Germination Period for Grass, Multi-Purpose	86d	86d	04-Apr-28	04-Aug-28
A191860	Install Nets, Multi-Purpose	3d	3d	07-Aug-28	09-Aug-28
Entry Drive					
A192000	Excavate & Set DMH - Entry Drive	5d	5d	17-Jun-27	23-Jun-27
A192010	Install UG Drain Piping - Entry Drive	5d	5d	24-Jun-27	30-Jun-27
A192020	Install Light Pole Bases + UG Conduit - Entry Drive	5d	5d	01-Jul-27	08-Jul-27
A192110	Strip Existing Asphalt - Entry Drive	2d	2d	09-Jul-27	12-Jul-27
A192030	Subgrade for Asphalt + Install Curbing - Entry Drive	12d	12d	13-Jul-27	28-Jul-27
A192120	Install Temp Sidewalks - Entry Drive	10d	10d	29-Jul-27	11-Aug-27
A192040	FRPS Concrete Sidewalks - Entry Drive	12d	12d	29-Jul-27	13-Aug-27
A192050	Install Binder - Entry Drive	3d	3d	16-Aug-27	18-Aug-27
A192060	Set Light Poles - Entry Drive	1d	1d	19-Aug-27	19-Aug-27
A192090	Final Pave - Entry Drive	3d	3d	20-Aug-27	24-Aug-27
A192100	Line Stripe - Entry Drive	2d	2d	25-Aug-27	26-Aug-27

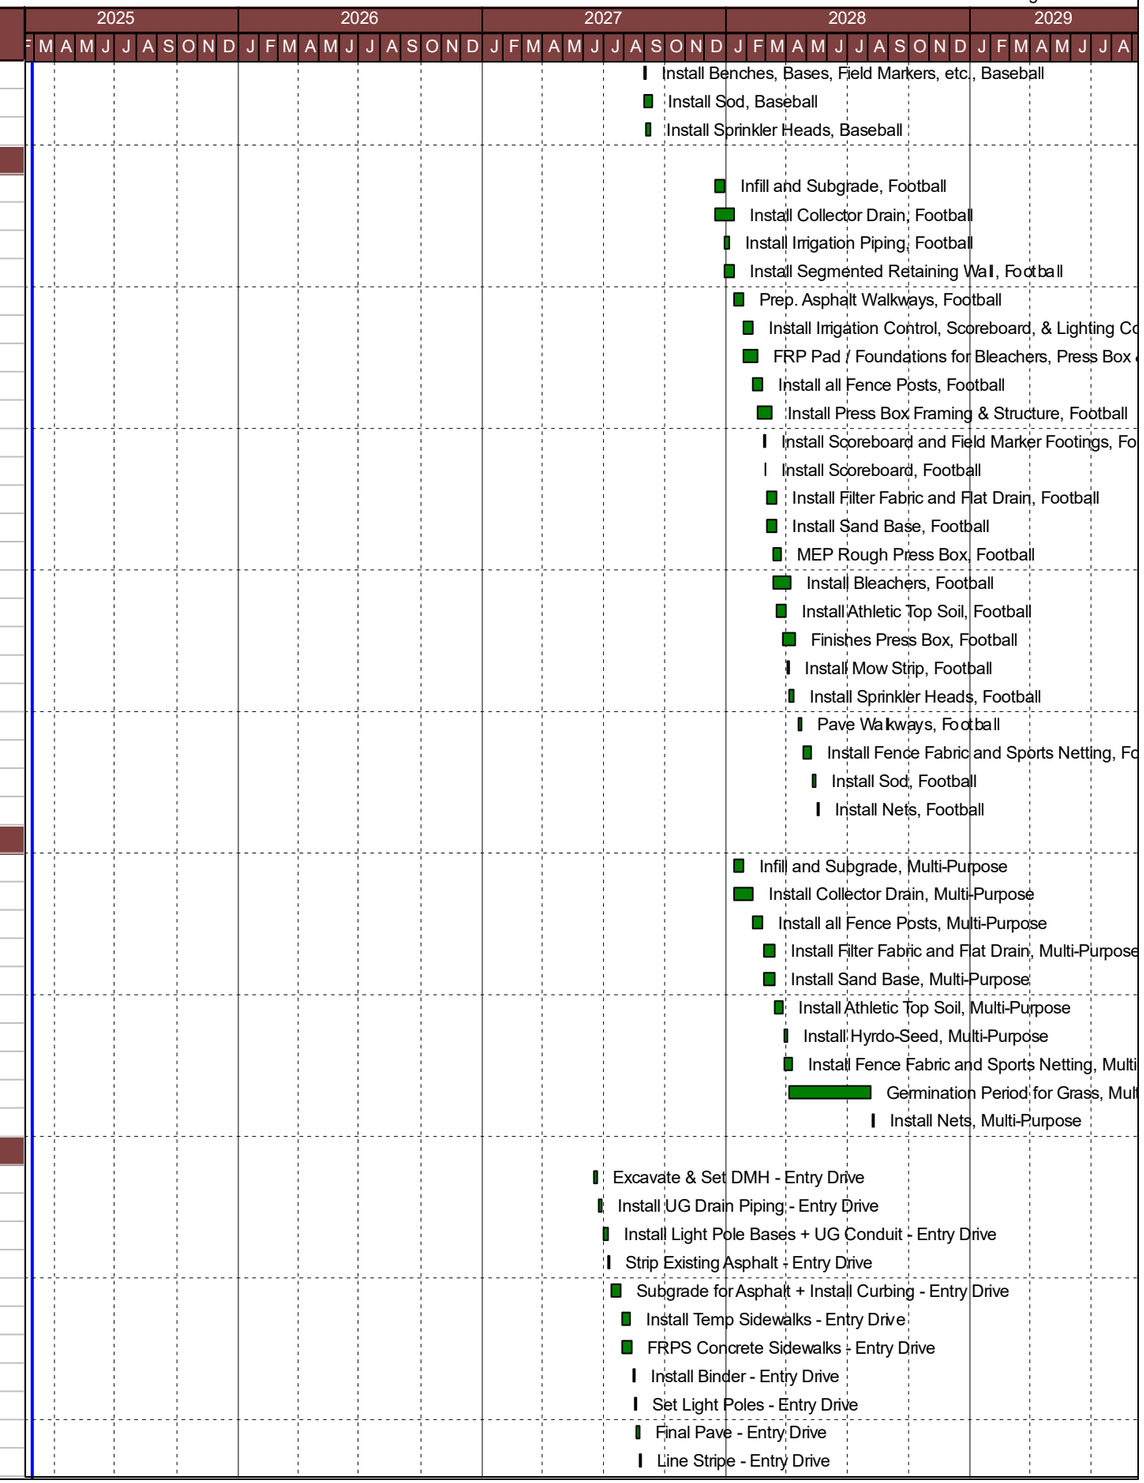

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish
A192070	Loam Planting Areas - Entry Drive	5d	5d	01-May-28	05-May-28
A192080	Install Landscaping + Accessories - Entry Drive	5d	5d	08-May-28	12-May-28
Central Parking					
A2570	Install Infiltration System - Central Parking	12d	12d	16-Dec-27	31-Dec-27
A2500	Excavate & Set DMH - Central Parking	5d	5d	03-Jan-28	07-Jan-28
A2510	Install UG Drain Piping - Central Parking	5d	5d	10-Jan-28	14-Jan-28
A2580	Install Light Pole Bases + UG Conduit - Central Parking	5d	5d	18-Jan-28	24-Jan-28
A2620	Subgrade for Asphalt + Install Curbing - Central Parking	12d	12d	20-Mar-28	04-Apr-28
A2660	FRPS Concrete Sidewalks - Central Parking	12d	12d	05-Apr-28	21-Apr-28
A2630	Install Binder - Central Parking	3d	3d	24-Apr-28	26-Apr-28
A2700	Set Light Poles - Central Parking	1d	1d	27-Apr-28	27-Apr-28
A2710	Loam Planting Areas - Central Parking	5d	5d	01-May-28	05-May-28
A2720	Install Landscaping + Accessories - Central Parking	5d	5d	08-May-28	12-May-28
A2740	Final Pave - Central Parking	3d	3d	15-May-28	17-May-28
A2730	Line Stripe - Central Parking	5d	5d	18-May-28	24-May-28

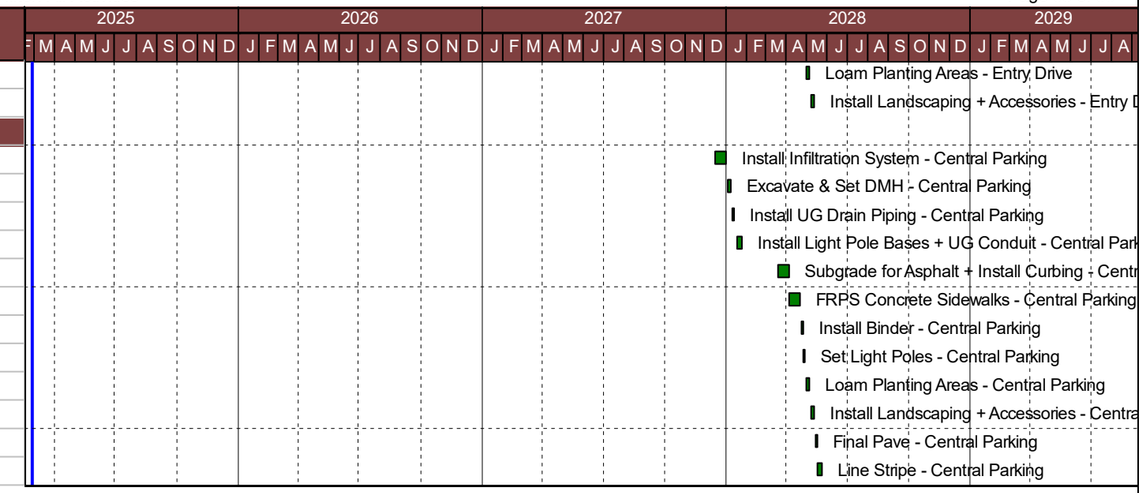

Section 7 - Submittal Log

Milford, MA

Printed on Wed Mar 5, 2025 at 10:22 am EST

Job #: 2983 Tri County Reg. Voc. Tech HS
147 Pond Street
Franklin, Massachusetts 02038

Submittals By Spec Section

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
312316 CONTROLLED BLASTING															
312316-045	0	TR: Blast Report 12/4/24	Test Report	Pending	Northeast Contractors, Inc.		Brandon Gauthier	12/04/2024	Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Stephen McLaughin (O'Reilly, Talbot & Okun Engineering Associates (OTO))	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Stephen McLaughin (O'Reilly, Talbot & Okun Engineering Associates (OTO)) Mike Talbot (O'Reilly, Talbot & Okun Engineering Associates (OTO))	Approved Pending Pending Pending Pending Approved	12/09/2024 12/09/2024 12/09/2024 12/09/2024	12/09/2024 01/02/2025	12/23/2024	
312316-044	0	TR: Blast Report 12/3/24	Test Report	Pending	Northeast Contractors, Inc.		Brandon Gauthier	12/03/2024	Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Stephen McLaughin (O'Reilly, Talbot & Okun Engineering Associates (OTO))	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Stephen McLaughin (O'Reilly, Talbot & Okun Engineering Associates (OTO)) Mike Talbot (O'Reilly, Talbot & Okun Engineering Associates (OTO))	Approved Pending Pending Pending Pending Approved	12/09/2024 12/09/2024 12/09/2024 12/09/2024	12/09/2024 01/02/2025	12/23/2024	
260000 Electrical															
260000-005	0	PD: Precast Pre-fab Conduit and Boxes	Material Delivery	Pending	Wayne J. Griffin Electric Inc.	02/26/2025	Nate Bernen	02/25/2025	Robert Bravo (Griffith & Vary, Inc.) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Robert Bravo (Griffith & Vary, Inc.) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending	02/26/2025 02/26/2025 02/26/2025	02/26/2025	03/12/2025	
260000-004	1	SD: Electrical Coordination in Architectural Precast	Construction	Pending	Consigli Construction Co., Inc.	02/26/2025	Tim Barrow	02/24/2025	Robert Bravo (Griffith & Vary, Inc.) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Robert Bravo (Griffith & Vary, Inc.) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending	02/26/2025 02/26/2025 02/26/2025	02/26/2025	03/12/2025	
235125 Closed Loop Geothermal Piping System															

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
235125-003	1	PD: Geothermal Vault & Manifold	Material Delivery	Pending	Allied Environmental Services, Inc. DBA Allied Drilling LLC	02/27/2025	Kyle Sweeney	02/27/2025	John Adkins (RFS (Rist-Frost-Shumway Engineering)) Darcy Gibson (RFS (Rist-Frost-Shumway Engineering)) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Joeseph Reid (RFS (Rist-Frost-Shumway Engineering))	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) John Adkins (RFS (Rist-Frost-Shumway Engineering)) Darcy Gibson (RFS (Rist-Frost-Shumway Engineering)) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Joeseph Reid (RFS (Rist-Frost-Shumway Engineering))	Approved Pending Pending Pending Pending Pending Pending	02/27/2025 02/27/2025 02/27/2025 02/27/2025 02/27/2025	02/27/2025	03/13/2025	
235125-001	2	PD: Geothermal Piping and Accessories	Material Delivery	Pending	Allied Environmental Services, Inc. DBA Allied Drilling LLC	03/03/2025	Kyle Sweeney	03/03/2025	John Adkins (RFS (Rist-Frost-Shumway Engineering)) Darcy Gibson (RFS (Rist-Frost-Shumway Engineering)) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Joeseph Reid (RFS (Rist-Frost-Shumway Engineering))	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) John Adkins (RFS (Rist-Frost-Shumway Engineering)) Darcy Gibson (RFS (Rist-Frost-Shumway Engineering)) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Joeseph Reid (RFS (Rist-Frost-Shumway Engineering))	Approved Pending Pending Pending Pending Pending Pending	03/03/2025 03/03/2025 03/03/2025 03/03/2025 03/03/2025	03/03/2025	03/17/2025	
142150 Gearless Machine Roomless Traction Elevator															
142150-003	0	PD/SD: Elevator 1	Material Delivery	Pending	Delta Beckwith Elevator Co.	02/27/2025	Mike Lee	02/21/2025	Robert Bravo (Griffith & Vary, Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Robert Bravo (Griffith & Vary, Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending Pending	02/27/2025 02/27/2025 02/27/2025 02/27/2025 02/27/2025	02/27/2025	03/13/2025	
142150-002	0	D: Sample Elevator Hoistway Ventilation Letter	Document	Pending	Delta Beckwith Elevator Co.	02/27/2025	Mike Lee	02/21/2025	Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending	02/27/2025 02/27/2025	02/27/2025	03/13/2025	

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
142150-001	0	PD/SD: Elevator 2	Material Delivery	Pending	Delta Beckwith Elevator Co.	02/27/2025	Mike Lee	02/21/2025	Robert Bravo (Griffith & Vary, Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Robert Bravo (Griffith & Vary, Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/27/2025 02/27/2025 02/27/2025 02/27/2025 02/27/2025	02/27/2025	03/13/2025	
071300 Sheet Waterproofing															
071300-003	1	PD: Below Pit Slab Composite Sheet Waterproofing	Material Delivery	Pending	Superior Caulking & Waterproofing Co., Inc.	02/18/2025	Jim Shaw	02/18/2025	Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending	02/18/2025 02/18/2025	02/18/2025	03/04/2025	
071100 Bituminous Dampproofing															
071100-001	0	PD: Bituminous Dampproofing	Material Delivery	Pending	Superior Caulking & Waterproofing Co., Inc.	01/28/2025	Jim Shaw	01/27/2025	Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Daniel Glazer (Drummey Rosane Anderson Inc.) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending	01/28/2025 01/28/2025	01/28/2025	02/11/2025	
053100 Steel Decking															
053100-001	0	PD: Steel Decking Fasteners	Construction	Pending	Sturo Metal Inc.	02/18/2025	Jérôme Dubé	02/18/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/18/2025 02/18/2025 02/18/2025 02/18/2025	02/18/2025	03/04/2025	
051200 Structural Steel Framing															
051200-007	0	SD: Sequences 201-206 Connection Design Calculations	Construction	Pending	Sturo Metal Inc.	02/28/2025	Jérôme Dubé	02/26/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/28/2025 02/28/2025 02/28/2025 02/28/2025	02/28/2025	03/14/2025	

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
051200-006	0	SD: Structural Steel Shop Drawings Sequences 201-206	Material Delivery	Pending	Sturo Metal Inc.	02/28/2025	Jérôme Dubé	02/26/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/28/2025 02/28/2025 02/28/2025 02/28/2025	02/28/2025	03/14/2025	
051200-005	0	SD: Anchor Bolt Shop Drawings for Buildings D & E	Material Delivery	Pending	Sturo Metal Inc.	01/23/2025	Jérôme Dubé	01/23/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/27/2025 01/27/2025 01/27/2025 01/27/2025	01/27/2025	02/10/2025	
051200-004	0	SD: Structural Steel Erection Sequence Plan	Construction	Pending	Sturo Metal Inc.	01/24/2025	Jérôme Dubé	01/23/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/24/2025 01/24/2025 01/24/2025 01/24/2025	01/24/2025	02/07/2025	
051200-002	0	PD: Shop Primer (2.5)	Construction	Pending	Sturo Metal Inc.	01/16/2025	Jérôme Dubé	01/16/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/16/2025 01/16/2025 01/16/2025 01/16/2025	01/16/2025	01/30/2025	
034500 Architectural Precast Concrete															

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
034500-011	0	SD: FOR RECORD Architectural Pre-Cast Shop Drawings	Material Delivery	Pending	Coreslab Structures	02/18/2025	Ylber Voci	02/17/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/18/2025 02/18/2025 02/18/2025 02/18/2025	02/18/2025	03/04/2025	
034500-005	0	PD: Galv Rebar Certificates	Construction	Pending	Coreslab Structures	01/24/2025	Ylber Voci	01/23/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Anjeza Gjata (Consigli Construction Co., Inc.) Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Pending Approved Pending Pending Pending Pending Pending	01/24/2025 01/24/2025 01/24/2025 01/24/2025	01/24/2025	02/07/2025	
034500-003	0	PD: Admixtures	Construction	Pending	Coreslab Structures	01/24/2025	Ylber Voci	01/23/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Anjeza Gjata (Consigli Construction Co., Inc.) Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Pending Approved Pending Pending Pending Pending Pending	01/24/2025 01/24/2025 01/24/2025 01/24/2025	01/24/2025	02/07/2025	
034113 Precast and Prestressed Concrete Plank															
034113-003	0	PD: Cement Mill Test Report	Document	Pending	Boccella Precast	02/14/2025	Steve Biernacki	02/13/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/14/2025 02/14/2025 02/14/2025 02/14/2025	02/14/2025	02/28/2025	

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
034113-002	0	PD: Plant Certification	Document	Pending	Boccella Precast	02/14/2025	Steve Biernacki	02/13/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/14/2025 02/14/2025 02/14/2025 02/14/2025	02/14/2025	02/28/2025	
034113-001	0	PD: Mix Design (2.2)	Construction	Pending	Boccella Precast	02/14/2025	Steve Biernacki	02/13/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/14/2025 02/14/2025 02/14/2025 02/14/2025	02/14/2025	02/28/2025	
033300 Architectural Concrete															
033300-026	0	FOR RECORD - PD: Patching at Tie Holds	Product Information	Pending	Riggs Contracting, Inc.	02/07/2025	Anthony Cheschi	02/06/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/07/2025 02/07/2025 02/07/2025 02/07/2025	02/07/2025	02/21/2025	
033000 Cast-In-Place Concrete															
033000-040	0	SD/PD: Building D Roof Slab on Deck	Material Delivery	Pending	Rebars and Mesh	03/03/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	03/03/2025 03/03/2025 03/03/2025 03/03/2025	03/03/2025	03/17/2025	

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
033000-039	0	SD/PD: Building D Level 3 Slab on Deck	Material Delivery	Pending	Rebars and Mesh	03/03/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	03/03/2025 03/03/2025 03/03/2025 03/03/2025	03/03/2025	03/17/2025	
033000-038	0	SD/PD: Buildings D & E Level 2 Slab on Deck	Material Delivery	Pending	Rebars and Mesh	03/03/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	03/03/2025 03/03/2025 03/03/2025 03/03/2025	03/03/2025	03/17/2025	
033000-037	0	SD/PD: Buildings D & E Mezzanine Slab on Deck	Material Delivery	Pending	Rebars and Mesh	03/03/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	03/03/2025 03/03/2025 03/03/2025 03/03/2025	03/03/2025	03/17/2025	
033000-036	0	SD/PD: Building C Roof Slab on Deck	Material Delivery	Pending	Rebars and Mesh	03/03/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	03/03/2025 03/03/2025 03/03/2025 03/03/2025	03/03/2025	03/17/2025	
033000-035	0	SD/PD: Building C Level 2 Slab on Deck	Material Delivery	Pending	Rebars and Mesh	03/03/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	03/03/2025 03/03/2025 03/03/2025 03/03/2025	03/03/2025	03/17/2025	

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
033000-034	0	SD/PD: Building C Mezzanine Slab on Deck	Material Delivery	Pending	Rebars and Mesh	03/03/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	03/03/2025 03/03/2025 03/03/2025 03/03/2025	03/03/2025	03/17/2025	
033000-033	0	SD/PD: Building B Roof Slab on Deck	Material Delivery	Pending	Rebars and Mesh	02/28/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/28/2025 02/28/2025 02/28/2025 02/28/2025	02/28/2025	03/14/2025	
033000-032	0	SD/PD: Building B Level 3 Slab on Deck	Material Delivery	Pending	Rebars and Mesh	02/28/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/28/2025 02/28/2025 02/28/2025 02/28/2025	02/28/2025	03/14/2025	
033000-031	0	SD/PD: Building B Level 2 Slab on Deck	Material Delivery	Pending	Rebars and Mesh	02/28/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/28/2025 02/28/2025 02/28/2025 02/28/2025	02/28/2025	03/14/2025	
033000-030	0	SD/PD: Building B Mezzanine Level Slab on Deck	Material Delivery	Pending	Rebars and Mesh	02/28/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/28/2025 02/28/2025 02/28/2025 02/28/2025	02/28/2025	03/14/2025	

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
033000-029	0	SD/PD: Building A Level 3 Slab on Deck	Material Delivery	Pending	Rebars and Mesh	02/28/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/28/2025 02/28/2025 02/28/2025 02/28/2025	02/28/2025	03/14/2025	
033000-028	0	SD/PD: Building A Level 2 Slab on Deck	Material Delivery	Pending	Rebars and Mesh	02/28/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/28/2025 02/28/2025 02/28/2025 02/28/2025	02/28/2025	03/14/2025	
033000-027	0	SD/PD: Building A Mezzanine Slab on Deck	Material Delivery	Pending	Rebars and Mesh	02/28/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/28/2025 02/28/2025 02/28/2025 02/28/2025	02/28/2025	03/14/2025	
033000-026	0	PD: Epoxy	Construction	Pending	Riggs Contracting, Inc.	02/24/2025	Anthony Cheschi	02/24/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/24/2025 02/24/2025 02/24/2025 02/24/2025	02/24/2025	03/10/2025	
033000-025	0	SD: SOG Building E	Material Delivery	Pending	Rebars and Mesh	01/31/2025	Garibaldi Castellanos	01/28/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/31/2025 01/31/2025 01/31/2025 01/31/2025	01/31/2025	02/14/2025	

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
033000-024	0	SD: SOG Building D	Material Delivery	Pending	Rebars and Mesh	01/31/2025	Garibaldi Castellanos	01/28/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/31/2025 01/31/2025 01/31/2025 01/31/2025	01/31/2025	02/14/2025	
033000-023	0	SD: SOG Building C	Material Delivery	Pending	Rebars and Mesh	01/31/2025	Garibaldi Castellanos	01/28/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/31/2025 01/31/2025 01/31/2025 01/31/2025	01/31/2025	02/14/2025	
033000-022	0	SD: SOG Building B	Material Delivery	Pending	Rebars and Mesh	01/31/2025	Garibaldi Castellanos	01/28/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/31/2025 01/31/2025 01/31/2025 01/31/2025	01/31/2025	02/14/2025	
033000-021	0	SD: SOG Building A	Material Delivery	Pending	Rebars and Mesh	01/31/2025	Garibaldi Castellanos	01/28/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/31/2025 01/31/2025 01/31/2025 01/31/2025	01/31/2025	02/14/2025	
033000-020	0	PD: Concrete Mix Design [Metal Pan Stair Fill]	Product Information	Pending	Dauphinais Concrete	01/24/2025	Robert Roncarati	01/23/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/24/2025 01/24/2025 01/24/2025 01/24/2025	01/24/2025	02/07/2025	

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
033000-019	0	PD: Concrete Mix Design [Mezzanine Topping Slab] (1.5)	Material Delivery	Pending	Dauphinais Concrete	01/24/2025	Robert Roncarati	01/23/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/24/2025 01/24/2025 01/24/2025 01/24/2025	01/24/2025	02/07/2025	
033000-015	1	PD: Concrete Mix Design [Site Concrete & Exterior Paving]	Product Information	Pending	Dauphinais Concrete	01/21/2025	Robert Roncarati	01/16/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/28/2025 01/28/2025 01/28/2025 01/28/2025	01/28/2025	02/11/2025	
033000-005	0	SD/PD: Reinforcement Shop Drawings [Building E] (1.5)	Material Delivery	Pending	Rebars and Mesh	01/14/2025	Eduardo Gonzalez	01/13/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	01/14/2025 01/14/2025 01/14/2025 01/14/2025	01/14/2025	01/28/2025	
033000-003	1	SD/PD: FOR RECORD Reinforcement Shop Drawings [Building C]	Material Delivery	Pending	Rebars and Mesh	02/24/2025	Eduardo Gonzalez	02/24/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/24/2025 02/24/2025 02/24/2025 02/24/2025	02/24/2025	03/10/2025	
033000-002	1	SD/PD: FOR RECORD Reinforcement Shop Drawings [Building B]	Shop Drawing	Pending	Rebars and Mesh	02/24/2025	Eduardo Gonzalez	02/19/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/24/2025 02/24/2025 02/24/2025 02/24/2025	02/24/2025	03/10/2025	

#	Rev.	Title	Type	Status	Responsible Contractor	Submit By	Received From	Received Date	Ball In Court	Approvers	Response	Sent Date	Returned Date	Final Due Date	Distributed Date
033000-001	3	SD/PD: FOR RECORD Reinforcement Shop Drawings [Building A]	Material Delivery	Pending	Rebars and Mesh	02/24/2025	Eduardo Gonzalez	02/05/2025	Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mehul Dhruv (Engineers Design Group) Daniel Glazer (Drummey Rosane Anderson Inc.) Tim Hill (Engineers Design Group) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.)	Approved Pending Pending Pending Pending Pending	02/24/2025 02/24/2025 02/24/2025 02/24/2025	02/24/2025	03/10/2025	
012400 Schedule Of Values															
012400-009	0	RIGGS Concrete Proposed Schedule of Values	Document	Pending	Riggs Contracting, Inc.		Sean Russell	02/14/2025	Mike Cox (Dore and Whittier) Trip Elmore (Dore and Whittier) Daniel Glazer (Drummey Rosane Anderson Inc.) Elias Grijalva (Dore and Whittier) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Dan Wiedeman (Dore and Whittier)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mike Cox (Dore and Whittier) Trip Elmore (Dore and Whittier) Daniel Glazer (Drummey Rosane Anderson Inc.) Elias Grijalva (Dore and Whittier) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Dan Wiedeman (Dore and Whittier)	Pending Approved Pending Pending Pending Pending Pending Pending	02/18/2025 02/18/2025 02/18/2025 02/18/2025 02/18/2025 02/18/2025	02/18/2025	03/04/2025	
012400-006	0	Allied Drilling LLC Proposed Schedule of Values	Document	Pending	Allied Environmental Service, Inc DBA Allied Drilling,LLC	02/04/2025	James Mosher	02/04/2025	Mike Cox (Dore and Whittier) Trip Elmore (Dore and Whittier) Daniel Glazer (Drummey Rosane Anderson Inc.) Elias Grijalva (Dore and Whittier) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Dan Wiedeman (Dore and Whittier)	Carly Hundertmark (Consigli Construction Co., Inc.) Tristen Moore (Consigli Construction Co., Inc.) Mike Cox (Dore and Whittier) Trip Elmore (Dore and Whittier) Daniel Glazer (Drummey Rosane Anderson Inc.) Elias Grijalva (Dore and Whittier) Vladimir Lyubetsky (Drummey Rosane Anderson Inc.) Dan Wiedeman (Dore and Whittier)	Pending Approved Pending Pending Pending Pending Pending Pending	03/03/2025 03/03/2025 02/04/2025 02/04/2025 02/04/2025 02/04/2025 02/04/2025 02/04/2025	03/03/2025 03/03/2025	02/18/2025	

Section 8 - RFI Log

Milford, MA

Printed on Wed Mar 5, 2025 at 10:21 am EST

Job #: 2983 Tri County Reg. Voc. Tech HS
147 Pond Street
Franklin, Massachusetts 02038

RFI LOG

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
77	Steel Missing Information	Open	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng... Glazer, Daniel (D...	03/04/2025	Carly Hundertmark	03/09/2025		Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng... Glazer, Daniel (D...				
76	Doweling Wall Rebar At Intersection of 3.3 and A.4	Closed	Northeast Contrac...	Chelo, Chris (Northeast Contractors, Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	02/28/2025	Carly Hundertmark	03/05/2025	03/03/25					
75	Exposed Round HSS Moment Connection	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	02/28/2025	Carly Hundertmark	03/05/2025	03/05/25					
74	Welded Connections at the Gym	Open	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng... Glazer, Daniel (D...	02/28/2025	Carly Hundertmark	03/05/2025		Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng... Glazer, Daniel (D...				
73	Grid A.2 Location	Open	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng... Glazer, Daniel (D...	02/21/2025	Carly Hundertmark	02/26/2025		Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng... Glazer, Daniel (D...				
72	Loads for Trusses in T2 and T3	Closed	Sturo Metal	Dubé, Jérôme (Sturo Metal	Dhruv,	02/19/2025	Carly	02/24/2025	03/03/25					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
			Inc.	Inc.)	Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...		Hundertmark							
71	Steel Plate Embed For Overhead Door Hardware Mounting	Open	Consigli Construc...	Feraco, Will (Consigli Construction Co., Inc.)	Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng... Glazer, Daniel (D...	02/13/2025	Carly Hundertmark	02/18/2025		Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng... Glazer, Daniel (D...				
70	Stiffeners at Rod Precast Connection	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	02/10/2025	Carly Hundertmark	02/15/2025	02/13/25					
69	Electrical in Early Masonry Walls	Closed	Consigli Construc...	Barrow, Tim (Consigli Construction Co., Inc.)	Lyubetsky, Vladim... Bravo, Robert (Gr... Glazer, Daniel (D...	02/10/2025	Carly Hundertmark	02/15/2025	03/03/25					
68	Sprinkler Bigger than 4" Incorporated into Trusses	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Hoekstra, Christo... Dhruv, Mehul (Eng... Vincent, Ray (C.A... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	02/07/2025	Carly Hundertmark	02/12/2025	02/13/25					
67	Mat Hoist Locations	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng...	02/07/2025	Carly Hundertmark	02/12/2025	02/26/25					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...									
66	Building A - Edge of Slab Clarifications	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	02/06/2025	Carly Hundertmark	02/11/2025	02/12/25					
65	Damp Proofing Termination Location	Closed	Consigli Construc...	Feraco, Will (Consigli Construction Co., Inc.)	Lyubetsky, Vladim... Glazer, Daniel (D...	02/05/2025	Carly Hundertmark	02/10/2025	02/13/25					
64	ASI-004 [-7'] Symbol by Certain Footings	Closed	Rebars and Mesh	Gonzalez, Eduardo (Rebars and Mesh)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	02/05/2025	Carly Hundertmark	02/10/2025	02/11/25					
63	Stiffeners at Bent Plates at Roof Clarifications	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	02/04/2025	Carly Hundertmark	02/09/2025	02/19/25					
62	Steel Beam Connections at Precast Panel Connections	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	02/03/2025	Carly Hundertmark	02/08/2025	02/06/25					
61	Clarifications and Missing Dimensions in Steel	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul	01/31/2025	Carly Hundertmark	02/05/2025	02/06/25					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					(Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...									
60	Misc. Engineering Confirmations for Steel	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/31/2025	Carly Hundertmark	02/05/2025	03/03/25					
59	HSS Beam Shear Loads at Bracing Frame	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/31/2025	Carly Hundertmark	02/05/2025	02/11/25					
58	Under Slab Drainage Piping Slope	Closed	Consigli Construc...	Barrow, Tim (Consigli Construction Co., Inc.)	Hoekstra, Christo... Vincent, Ray (C.A... Lyubetsky, Vladim... Glazer, Daniel (D...	01/31/2025	Carly Hundertmark	02/05/2025	01/31/25					
57	Anchor Bolt Repair Plan	Closed	Riggs Contracting...	Cheschi, Anthony (Riggs Contracting, Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/30/2025	Carly Hundertmark	02/04/2025	02/05/25					
56	Foundation Wall Thickness Clarifications Along Grid Line P from Grid Line 1 to Grid Line 2	Closed	Rebars and Mesh	Gonzalez, Eduardo (Rebars and Mesh)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky,	01/29/2025	Carly Hundertmark	02/03/2025	01/30/25					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					Vladim... Glazer, Daniel (D...									
55	Wall Hydrant Non Cast in Place for Arch. Precast	Closed	Consigli Construc...	Barrow, Tim (Consigli Construction Co., Inc.)	Hoekstra, Christo... Dhruv, Mehul (Eng... Vincent, Ray (C.A... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/27/2025	Carly Hundertmark	02/01/2025	02/04/25					
54	Reinforcement Requirements at the Precast Connection Boxouts	Closed	Riggs Contracting...	Cheschi, Anthony (Riggs Contracting, Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/27/2025	Carly Hundertmark	02/01/2025	02/04/25					
53	Bent Plate Joints	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/27/2025	Carly Hundertmark	02/01/2025	02/04/25					
52	FOR RECORD: Future Switchgear Vault Stub Up Alternative	Closed	Wayne J. Griffin ...	Bernen, Nate (Wayne J. Griffin Electric Inc.)	SC, CA (Samiotes ... Glazer, Daniel (D... Melnyk, Greg (Sam... Pilat, Jeffrey (S... Hadley, Kyle (Sam... Powers, Stephen (... Lyubetsky, Vladim... Bravo,	01/24/2025	Carly Hundertmark	01/29/2025	01/30/25					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					Robert (Gr...									
51	Steel Locations and Clarifications	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/24/2025	Carly Hundertmark	01/29/2025	01/30/25					
50	Moment Connection Loads	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/24/2025	Carly Hundertmark	01/29/2025	01/28/25					
49	New Proposed Electric Vault Locations	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Bravo, Robert (Gr... Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... SC, CA (Samiotes ... Glazer, Daniel (D...	01/23/2025	Carly Hundertmark	01/28/2025	01/28/25					
48	FOR RECORD: Temporary Expansion of Goat Path to Accommodate Construction Vehicles	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	SC, CA (Samiotes ... Melnyk, Greg (Sam... Pilat, Jeffrey (S... Hadley, Kyle (Sam... Powers, Stephen (... Lyubetsky, Vladim... Glazer, Daniel (D...	01/23/2025	Carly Hundertmark	01/28/2025	01/24/25					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
47	Building A MEP Sleeve Locations with Proposed Dropped Footings	Closed	Consigli Construc...	Barrow, Tim (Consigli Construction Co., Inc.)	Dhruv, Mehul (Eng... Vincent, Ray (C.A... Hill, Tim (Engine... Lyubetsky, Vladim... Hoekstra, Christo... Glazer, Daniel (D...	01/23/2025	Carly Hundertmark	01/28/2025	01/29/25					
46	Moment Connections - Sections vs. Typical Details	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/21/2025	Carly Hundertmark	01/26/2025	01/24/25					
45	Domestic Water Service Entrance Location	Closed	Consigli Construc...	Barrow, Tim (Consigli Construction Co., Inc.)	Hoekstra, Christo... Lyubetsky, Vladim... Vincent, Ray (C.A... Glazer, Daniel (D...	01/17/2025	Carly Hundertmark	01/22/2025	01/22/25					
44	Steel Finished Clarifications	Open	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng... Glazer, Daniel (D...	01/16/2025	Carly Hundertmark	01/21/2025		Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng... Glazer, Daniel (D...				
43	Bolt Type in Bracing Clarification	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/16/2025	Carly Hundertmark	01/21/2025	01/24/25					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
42	Trusses Clarifications	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/16/2025	Carly Hundertmark	01/21/2025	01/24/25					
41	LM Vault Relocation	Closed	Wayne J. Griffin ...	Bernen, Nate (Wayne J. Griffin Electric Inc.)	SC, CA (Samiotes ... Melnyk, Greg (Sam... Pilat, Jeffrey (S... Hadley, Kyle (Sam... Powers, Stephen (... Lyubetsky, Vladim... Glazer, Daniel (D...	01/16/2025	Carly Hundertmark	01/21/2025	01/24/25					
40	Bracing Connection Clarifications	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/15/2025	Carly Hundertmark	01/20/2025	01/29/25					
39	Detail 2/S0-0-7 Clarifications	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/15/2025	Carly Hundertmark	01/20/2025	01/22/25					
38	Clarifications on Structural Drawings	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer,	01/15/2025	Carly Hundertmark	01/20/2025	01/27/25					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					Daniel (D...									
37	Steel Framing Connection Clarifications	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/10/2025	Carly Hundertmark	01/15/2025	01/16/25					
36	Gage of Form Deck at Monumental Stair	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/10/2025	Carly Hundertmark	01/15/2025	01/16/25					
35	Missing Steel Dimensions	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/09/2025	Carly Hundertmark	01/14/2025	02/26/25					
34	Bolted Splices at Joists	Closed	Sturo Metal Inc.	Dubé, Jérôme (Sturo Metal Inc.)	Dhruv, Mehul (Eng... Hill, Tim (Engine... Lyubetsky, Vladim... Glazer, Daniel (D...	01/09/2025	Carly Hundertmark	01/14/2025	02/11/25					
33	Ledge Interrupts Frost Wall Condition	Closed	Consigli Construc...	Feraco, Will (Consigli Construction Co., Inc.)	Wiedeman, Dan (Do... Grijalva, Elias (... Dhruv, Mehul (Eng... Cox, Mike (Dore a... Talbot, Mike (O'R...	12/31/2024	Carly Hundertmark	01/05/2025	01/09/25					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					McLaughin, Stephe... Hill, Tim (Engine... Elmore, Trip (Dor... Glazer, Daniel (D...									
32	Low Voltage Lines in One Trench	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Bravo, Robert (Gr... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... SC, CA (Samiotes ... Lyubetsky, Vladim... Glazer, Daniel (D...	12/27/2024	Carly Hundertmark	01/01/2025	12/31/24					
31	Fire Protection Service Piping Size	Closed	Consigli Construc...	Barrow, Tim (Consigli Construction Co., Inc.)	Vincent, Ray (C.A... Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... SC, CA (Samiotes ... Hoekstra, Christo...	12/18/2024	Carly Hundertmark	12/23/2024	01/08/25					
30	Utility Corridor Under Drain	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Powers, Stephen (... Lyubetsky, Vladim... Hadley, Kyle (Sam... Pilat, Jeffrey (S...	12/17/2024	Carly Hundertmark	12/22/2024	01/09/25					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					Melnyk, Greg (Sam... SC, CA (Samiotes ... Glazer, Daniel (D...									
29	Lowering Height of Interior Frost Walls for Crane Path	Closed	Consigli Construc...	Feraco, Will (Consigli Construction Co., Inc.)	Lyubetsky, Vladim... Hill, Tim (Engine... Powers, Stephen (... Dhruv, Mehul (Eng... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... SC, CA (Samiotes ... Glazer, Daniel (D...	12/12/2024	Carly Hundertmark	12/17/2024	01/09/25					
28	Transformer Pad Orientation and Conduit Entrance Detail	Closed	Wayne J. Griffin ...	Kaiser, Kevin (Wayne J. Griffin Electric Inc.)	SC, CA (Samiotes ... Melnyk, Greg (Sam... Pilat, Jeffrey (S... Hadley, Kyle (Sam... Powers, Stephen (... Lyubetsky, Vladim... Bravo, Robert (Gr... Glazer, Daniel (D...	12/10/2024	Carly Hundertmark	12/15/2024	12/18/24					
27	Confirming RFI: Utility Corridor Road Shift	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	SC, CA (Samiotes ... Melnyk, Greg (Sam... Pilat, Jeffrey (S... Hadley, Kyle (Sam... Lyubetsky,	12/10/2024	Carly Hundertmark	12/15/2024	12/18/24					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					Vladim... Powers, Stephen (... Glazer, Daniel (D...									
26	Confirming RFI: Pre-Cast Plank Spanning	Closed	Consigli Construc...	Lyons, Kristy (Consigli Construction Co., Inc.)	Lyubetsky, Vladim... Glazer, Daniel (D...	12/05/2024	Tristen Moore	12/10/2024	12/05/24			TBD		TBD
25	Electric Manhole Grounding Detail	Closed	Wayne J. Griffin ...	Kaiser, Kevin (Wayne J. Griffin Electric Inc.)	Glazer, Daniel (D... Lyubetsky, Vladim... Bravo, Robert (Gr...	11/26/2024	Tristen Moore	12/01/2024	12/11/24					
24	Confirming RFI: BP #3 Concrete Descope Clarifications	Closed	Consigli Construc...	Moore, Tristen (Consigli Construction Co., Inc.)	Lyubetsky, Vladim... Glazer, Daniel (D...	11/22/2024	Tristen Moore	11/27/2024	12/18/24					
23	Confirming RFI: Sewer Man Hole Conflict With Existing Electrical	Closed	Northeast Contrac...	Rodegher, John (Northeast Contractors, Inc.)	SC, CA (Samiotes ... Melnyk, Greg (Sam... Pilat, Jeffrey (S... Hadley, Kyle (Sam... Lyubetsky, Vladim... Powers, Stephen (... Glazer, Daniel (D...	11/22/2024	Tristen Moore	11/27/2024	11/25/24					
22	Proposed Grid Position	Closed	Brennan Consultants	Bodwell, Jamie (Brennan Consultants)	SC, CA (Samiotes ... Melnyk, Greg (Sam... Pilat, Jeffrey (S... Hadley, Kyle (Sam... Lyubetsky, Vladim... Powers, Stephen (... Glazer, Daniel (D...	11/19/2024	Tristen Moore	11/24/2024	11/25/24					
21	Confirming RFI: Civil Changes Made Post ASI#002	Closed	Northeast	Gauthier, Brandon	SC, CA	11/15/2024	Tristen	11/20/2024	12/18/24					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
			Contrac...	(Northeast Contractors, Inc.)	(Samiotes ... Melnyk, Greg (Sam... Pilat, Jeffrey (S... Hadley, Kyle (Sam... Lyubetsky, Vladim... Powers, Stephen (... Glazer, Daniel (D...		Moore							
20	Proposed Grease Trap Dimensions	Closed	Northeast Contrac...	Rodegher, John (Northeast Contractors, Inc.)	Vincent, Ray (C.A... Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... Hoekstra, Christo... SC, CA (Samiotes ...	11/11/2024	Tristen Moore	11/16/2024	11/13/24					
19	Structural CAD File Request	Closed	Brennan Consultants	Bodwell, Jamie (Brennan Consultants)	Glazer, Daniel (D... Lyubetsky, Vladim... Hill, Tim (Engine... Dhruv, Mehul (Eng...	10/31/2024	Tristen Moore	11/05/2024	11/15/24					
18	Water Line & Road Shift in Utility Access Corridor	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Powers, Stephen (... Lyubetsky, Vladim... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam...	10/29/2024	Tristen Moore	11/03/2024	11/05/24			Yes (Unknown)		TBD

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					Glazer, Daniel (D... SC, CA (Samiotes ...									
17	Confirming RFI: Softball Field Backstop Footings	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Johnson, Ti (Warn... Lyubetsky, Vladim... Glazer, Daniel (D...	10/16/2024	Tristen Moore	10/21/2024	11/05/24					
16	Electrical Site Plans Per Meetings with NGrid	Closed	Northeast Contrac...	Rodegher, John (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Bravo, Robert (Gr... Glazer, Daniel (D...	10/16/2024	Tristen Moore	10/21/2024	12/27/24					
15	Confirming RFI: Outlet Control Structure Weir Locations	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Powers, Stephen (... Lyubetsky, Vladim... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... SC, CA (Samiotes ...	10/01/2024	Tristen Moore	10/06/2024	10/10/24					
14	Proposed Drainage Shift in the Utility Access Corridor	Closed	Northeast Contrac...	Rodegher, John (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... SC, CA (Samiotes ... Glazer, Daniel (D...	09/19/2024	Tristen Moore	09/24/2024	10/07/24					
13	Parking Lot Grading Measures (For Record)	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	SC, CA (Samiotes ... Melnyk, Greg (Sam...	08/27/2024	Tristen Moore	09/01/2024	09/09/24					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					Pilat, Jeffrey (S... Hadley, Kyle (Sam... Powers, Stephen (... Lyubetsky, Vladim... Glazer, Daniel (D...									
12	Existing DMH D2-03 Pitch Request	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	SC, CA (Samiotes ... Melnyk, Greg (Sam... Pilat, Jeffrey (S... Hadley, Kyle (Sam... Powers, Stephen (... Lyubetsky, Vladim... Glazer, Daniel (D...	08/22/2024	Tristen Moore	08/27/2024	08/22/24					
11	Timeclock Schedule	Closed	Wayne J. Griffin ...	Bernen, Nate (Wayne J. Griffin Electric Inc.)	Lyubetsky, Vladim... Bravo, Robert (Gr... Glazer, Daniel (D...	08/22/2024	Tristen Moore	08/27/2024	11/05/24					
10	Confirming RFI: Infiltration System Stone Depth	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... SC, CA (Samiotes ... Glazer, Daniel (D...	08/06/2024	Tristen Moore	08/11/2024	09/09/24					
9	Confirming RFI: Water Line Location	Closed	Northeast Contrac...	Quiterio, Angelo (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle	08/02/2024	Tristen Moore	08/07/2024	08/06/24			TBD		No

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					(Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... SC, CA (Samiotes ...									
8	Submittal Clarification (334000-003.1) Pre-Cast Structures after ASI #001	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... SC, CA (Samiotes ...	08/02/2024	Tristen Moore	08/07/2024	08/20/24			28 days		TBD
7	Temporary Lighting Clarifications	Closed	Wayne J. Griffin ...	Kaiser, Kevin (Wayne J. Griffin Electric Inc.)	Lyubetsky, Vladim... Bravo, Robert (Gr... Glazer, Daniel (D...	08/01/2024	Tristen Moore	08/06/2024	08/05/24					
6	ADS Manufacturing Concerns: Infiltration System #4	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... SC, CA (Samiotes ...	07/26/2024	Tristen Moore	07/31/2024	09/09/24			TBD		
5	Franklin Water Department Request: Additional Gate Valve at Tri-County Drive	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam...	07/26/2024	Tristen Moore	07/31/2024	07/29/24					

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
					Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... SC, CA (Samiotes ...									
4	Sanitary Manhole Inside/Outside Drop	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... SC, CA (Samiotes ...	07/24/2024	Tristen Moore	07/29/2024	07/26/24					
3	Confirming RFI: HDPE Pipe Sizing in ASI #001	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... SC, CA (Samiotes ...	07/23/2024	Tristen Moore	07/28/2024	08/02/24			TBD		TBD
2	Additional Gate Valve for the Utility Access Road	Closed	Northeast Contrac...	Rodegher, John (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... SC, CA (Samiotes ...	07/19/2024	Tristen Moore	07/24/2024	07/26/24			No		$4,000.00

Milford, MA

Printed on Wed Mar 5, 2025 at 10:21 am EST

Job #: 2983 Tri County Reg. Voc. Tech HS
147 Pond Street
Franklin, Massachusetts 02038

#	Subject	Status	Responsible Contractor	Received From	Assignee	Date Initiated	RFI Manager	Due Date	Closed Date	Ball In Court	Location	Schedule Impact	Cost Code	Cost Impact
1	Water Quality Units and Water Main	Closed	Northeast Contrac...	Gauthier, Brandon (Northeast Contractors, Inc.)	Lyubetsky, Vladim... Moore, Tristen (C... Powers, Stephen (... Hadley, Kyle (Sam... Pilat, Jeffrey (S... Melnyk, Greg (Sam... Glazer, Daniel (D... SC, CA (Samiotes ...	07/16/2024	Tristen Moore	07/21/2024	07/16/24			TBD		TBD

Section 9 - Progress Photos
